

3-201-10
1422



INTEROFFICE MEMORANDUM

To:	Distribution	Date:	April 16, 1998
Location:	Various	Reference:	N/A
From:	Lyle Hampshire <i>L.H.</i>	FD Fernald #:	M:FCDP(FDP):98-0011
Location:	Fernald	Client:	DOE DE-AC24-92OR21972
Extension:	648-4109	Subject:	AMENDMENT TO OU3 INTEGRATED RD/RA WORK PLAN REGULATORY MILESTONES

c: File Record Storage Copy 106.4.33.7

Attached, please find the amended pages of the OU3 Integrated Remedial Design/Remedial Action (RD/RA) Work Plan, May 1997, which contain the revised milestones (Table 6-1) and the revised OU3 Base Remediation Schedule (Figure 6-1). Please replace pages 6-3 and 6-7 of the OU3 Integrated RD/RA Work Plan with the attached yellow pages.

This amendment incorporates revised implementation plan submittal dates for each of the OU3 decontamination and dismantlement (D&D) complexes. The bases for the revisions are:

- the disparity between the previous regulatory agency-approved milestones and the rescheduling of baseline D&D activities, which has been done as a result of adjustments made to actual and anticipated site funding levels;
- improved project cost estimates based on field actuals and lessons learned; and
- the resultant changes in priorities due to these funding levels based on an integrated but fully constrained schedule.

In a letter to the Department of Energy, dated March 18, 1998, the United States Environmental Protection Agency (U.S. EPA) concurred with the revised OU3 implementation plan submittal dates. These dates are enforceable milestones under the 1991 Amended Consent Agreement.



INTEROFFICE MEMORANDUM


FD Fernald No. M:
April 16, 1998
Page 2

It should be noted that no other remedial priorities have been significantly altered at this time relative to implementation schedules.

Inquiries regarding the content of this document may be directed to me at 648-4109.

2503-WP-0023 K/UPC/N1

FY96 FY97 FY98 FY99 FY00 FY01 FY02 FY03 FY04 FY05

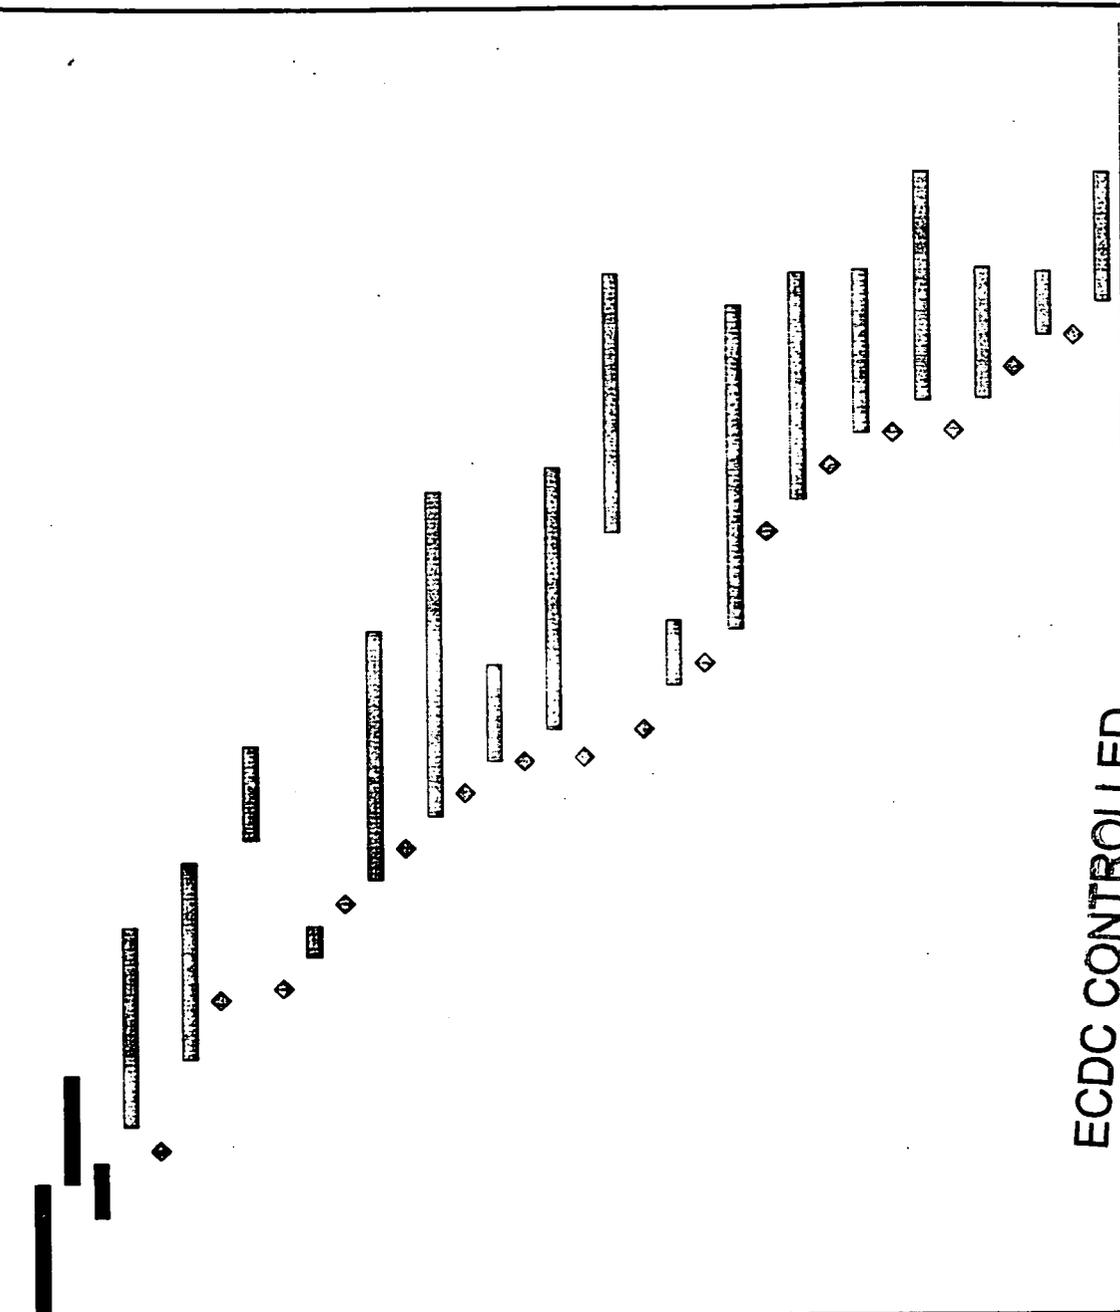

ECDC CONTROLLED
COPY NO. 7031

Activity Description	FY96	FY97	FY98	FY99	FY00	FY01	FY02	FY03	FY04	FY05
OU3 COMPLEX D&D										
BUILDING 4A D&D										
PLANT 1 COMPLEX - PHASE I D&D										
HIGH & LOW NITRATE TANKS										
BOILER & WATER PLANT COMPLEX D&D										
PLANT 9 IMPLEMENTATION PLAN TO EPA										
THORIUM/PLANT 9 COMPLEX D&D										
MAINT/TANK FARM D&D IMPLEMENTATION PLAN TO EPA										
MAINTENANCE/TANK FARM COMPLEX D&D										
STP IMPLEMENTATION PLAN TO EPA										
SEWAGE TREATMENT PLANT COMPLEX D&D										
PLANT 3 IMPLEMENTATION PLAN TO EPA										
PLANT 3 COMPLEX D&D										
PLANT 5 IMPLEMENTATION PLAN TO EPA										
PLANT 5 COMPLEX D&D										
PLANT 1 PHASE II IMPLEMENTATION PLAN TO EPA										
PLANT 1 COMPLEX PHASE II D&D										
PLANT 6 COMPLEX IMPLEMENTATION PLAN TO EPA										
PLANT 6 COMPLEX D&D										
PILOT PLANT COMPLEX IMPLEMENTATION PLAN TO EPA										
PILOT PLANT COMPLEX D&D										
EAST WAREHOUSE IMPLEMENTATION PLAN TO EPA										
EAST WAREHOUSE COMPLEX D & D										
PLANT 2 COMPLEX IMPLEMENTATION PLAN TO EPA										
PLANT 2 COMPLEX D&D										
PLANT 8 COMPLEX IMPLEMENTATION PLAN TO EPA										
PLANT 8 COMPLEX D&D										
GENERAL SUMP COMP. IMPLEMENTATION PLAN TO EPA										
GENERAL SUMP COMPLEX D&D										
ADMIN. COMPLEX IMPLEMENTATION PLAN TO EPA										
ADMINISTRATION COMPLEX D&D										
LABORATORY COMPLEX IMPLEMENTATION PLAN TO EPA										
CHEMICAL LAB COMPLEX D&D										
LIQUID STOR COMPLEX IMPLEMENTATION PLAN TO EPA										
LIQUID STORAGE COMPLEX D&D										
ELECTRICAL COMPLEX IMPLEMENTATION PLAN TO EPA										
ELECTRICAL STATION COMPLEX D&D										
OTHER STRUCTURAL D&D										
OU1 COMPLEX IMPLEMENTATION PLAN TO EPA										
OU1 COMPLEX D&D										
OU4 COMPLEX D&D (*)										

Sheet 1 of 1

REVISOR: []

DATE: []

Checked: [] Approved: []

Project Start: 01OCT94
 Project Finish: 31MAY06
 Data Date: 01OCT94
 Run Date: 26FEB98

3

© Primavera Systems, Inc.

TABLE 6-1 OU3 Remedial Design Regulatory Milestones

Complex	Implementation Plan Submittal Dates
Building 4A	19 Sep 94 ^(a)
Plant 1 Complex - Phase I	3 Nov 95 ^(a)
High and Low Nitrate Tanks	20 Feb 96 ^(a)
Boiler Plant/Water Plant Complex	12 Sep 96 ^(a)
Thorium/Plant 9 Complex	2 Jan 97 ^(a)
Tank Farm Complex	5 Mar 98 ^(b)
Maintenance Complex	5 Mar 98 ^(b)
Sewage Treatment Plant Complex	2 Apr 98
Plant 3 Complex	2 Dec 98
Plant 5 Complex	2 May 99
Plant 1 Complex - Phase II	6 Oct 99
Plant 6 Complex	2 Jan 00
Pilot Plant Complex	17 Jan 00
East Warehouse Complex	2 Apr 00
Plant 2 Complex	1 Oct 00
Plant 8 Complex	3 Oct 01
General Sump Complex	4 Apr 02
Administration Complex	4 Jul 02
Laboratory Complex	7 Jul 02
Liquid Storage Complex	1 Jan 03
Electrical Complex	3 Apr 03
OU1 Complex	3 Jul 04
OU4 Complex	(c)

- (a) actual submittal date
- (b) Maintenance and Tank Farm Complexes are planned to be remediated as a combined project (i.e., Maintenance/Tank Farm Complex), resulting in the submittal of a single, joint implementation plan.
- (c) to be determined; submittal date pending resolution of OU4 milestone rescheduling effort.
