

**Department of Energy**

**Ohio Field Office
Fernald Closure Project
175 Tri-County Parkway
Springdale, Ohio 45246
(513) 648-3155**



SEP 13 2005

Mr. James A. Saric, Remedial Project Manager
United States Environmental Protection Agency
Region V-SRF-5J
77 West Jackson Boulevard
Chicago, Illinois 60604-3590

DOE-0326-05

Mr. Thomas Schneider, Project Manager
Ohio Environmental Protection Agency
Southwest District Office
401 East Fifth Street
Dayton, Ohio 45402-2911

Dear Mr. Saric and Mr. Schneider:

**SCHEDULE CHANGE FOR SUBMITTAL OF THE ABOVE- GRADE
DECONTAMINATION AND DISMANTLEMENT OF THE SILOS 1&2 COMPONENTS
34A (SILO 2), 34B (SILO 1) AND SILOS 1&2 BRIDGES PROJECT COMPLETION
REPORT AND PAGE CHANGE NOTICE 3**

According to the Operable Unit 4 Complex Silos 1&2 Components 34A (Silo 2), 34B (Silo 1) and Silos 1&2 Bridges Implementation Plan for Above-Grade Decontamination and Dismantlement (D&D), the project completion report was due on August 29, 2005.

Although demolition of the silos and bridges was completed in early July 2005, due to attempting to gain operational and equipment utilization efficiencies, additional implementation plan demolition scope remains. Remaining scope includes the Decant Sump Tank (Component F34-4) unearthing and demolition along with demolition of the remaining 600 feet of the K-65 Trench (Component 22E).

The Fluor Soil Disposal Facility Project will remove the remaining K-65 Trench and the scope of this activity is covered under the Excavation Plan for Area 7 Silos and General Area.

Excavation of the decant sump tank is in process and demolition by the Fluor Fernald Self-Perform D&D group is expected to be complete by September 23, 2005. Therefore, the Silos 1&2 Components 34A (Silo 2), 34B (Silo 1) and Silos 1&2 Bridges Above-Grade Decontamination and Dismantlement (D&D) Project Completion Report will be submitted no later than November 22, 2005 (Sixty days after field work completion).

Mr. James A. Saric
Mr. Thomas Schneider

-2-

DOE-0326-05

Pursuant to Section XVIII A, DOE respectfully requests an extension for submittal of the OU4 above referenced project completion report from August 29, 2005 until November 22, 2005. The majority of physical work has been completed. DOE believes that the operational efficiencies to be gained by coordinating the work between the D&D group and the Soils groups will result in a better quality remediation of the facilities and area.

This letter transmits Page Change Notice 3 (PCN3) for the implementation plan. PCN3 identifies the D&D schedule changes within Figure 4-1 of the implementation plan. Please remove the existing implementation plan pages affected by PCN3 and replace them with the enclosure.

If there are any questions concerning this information, please contact Johnny Reising at (513) 648-3139.

Sincerely,



for William J. Taylor
Director

FCP:Reising

Enclosure

cc w/enclosure:

J. Reising, OH/FCP
E. Skintik, OH/FCP
G. Jablonowski, USEPA-V, SR-6J
T. Schneider, OEPA-Dayton (three copies of enclosure)
F. Bell, ATSDR
M. Cullerton, Tetra Tech
M. Shupe, HIS GeoTrans
R. Vandergrift, ODH
AR Coordinator, Fluor Fernald, Inc./MS78

cc w/o enclosure:

K. Alkema, Fluor Fernald, Inc./MS01
D. Arico, Fluor Fernald, Inc./MS88
B. Edmondson, Fluor Fernald, Inc./MS64
J. Fry, Fluor Fernald, Inc./MS64
F. Johnston, Fluor Fernald, Inc./MS52-5
F. Miller, Fluor Fernald, Inc./MS88
C. Murphy, Fluor Fernald, Inc./MS01
P. O'Neill, Fluor Fernald, Inc./MS52-1
D. Sizemore, Fluor Fernald, Inc./MS02
ECDC Fluor Fernald Inc./MS52-7 Project Number 40900.2.1

5995

**OPERABLE UNIT FOUR COMPLEX SILOS 1&2
COMPONENTS 34A (SILO 2), 34B (SILO 1) AND SILOS
1&2 BRIDGES IMPLEMENTATION PLAN**

DOCUMENT NUMBER 40900-PL-0003 (REV. 0) PCN3

PAGE CHANGES

INCLUDES:


COVER PAGE/RECORD OF REVISION

PAGE 31/32

5995

OPERABLE UNIT 3

**OPERABLE UNIT 4 (OU4) COMPLEX SILOS 1&2
COMPONENTS 34A (SILO 2), 34B (SILO 1) AND
SILOS 1&2 BRIDGES
IMPLEMENTATION PLAN FOR ABOVE-GRADE
DECONTAMINATION AND DISMANTLEMENT**



SEPTEMBER 2005

**FERNALD CLOSURE PROJECT
FERNALD, OHIO**

**U. S. DEPARTMENT OF ENERGY
FERNALD AREA OFFICE**

FINAL

DOCUMENT CONTROL NO. 40900-PL-0003 (REV. 0) PCN3

RECORD OF ISSUE/REVISION

<u>DATE</u>	<u>REVISION NO.</u>	<u>DESCRIPTION AND AUTHORITY</u>
3/16/05	Rev. 0	Issued Final Implementation Plan
3/29/05	PCN1	Section 2.6, "Phase 4 D&D Activities" - inserted text inadvertently omitted to address demolition of the Silo 2 concrete structure (ten bullets starting at the top of Page 24).
4/14/05	PCN2	Per USEPA comments, changes incorporated into Figure 1-1, and Subsections 1.2, 1.3, 2.2, 2.3.4, 2.4, 2.5.4, 3.1 and 3.2. Per OEPA, added Appendix H, titled "Fenceline Particulate Impact of Silos 1&2 D&D". Changes and additions are identified as "PCN2" or Page Change Notice 2.
9/12/05	PCN3	Figure 4-1 changed to identify the "Completion of Field Activities" date as September 23, 2005, the "Prepare Project Completion Report" duration to extend from September 24, 2005 to November 22, 2005 and to identify the "Submit Project Completion Report to USEPA/OEPA" date as November 22, 2005.

4.0 SCHEDULE

5995

This section presents the planning and implementation schedule for the OU4 Complex Silos 1&2 Components 34A (Silo 2), 34B (Silo 1) and Silos 1&2 Bridges D&D project. Figure 4-1 presents the schedule for implementation of field activities beginning with the Project Start and ending with the submittal of the Project Completion Report. The primary milestones of the project include the following: 1) Project Start; 2) Completion of Field Activities; and 3) submittal of the Project Completion Report to U.S. EPA and Ohio EPA. The content for the Project Completion Report is outlined in Section 4.5 of the OU3 Integrated RD/RA Work Plan.

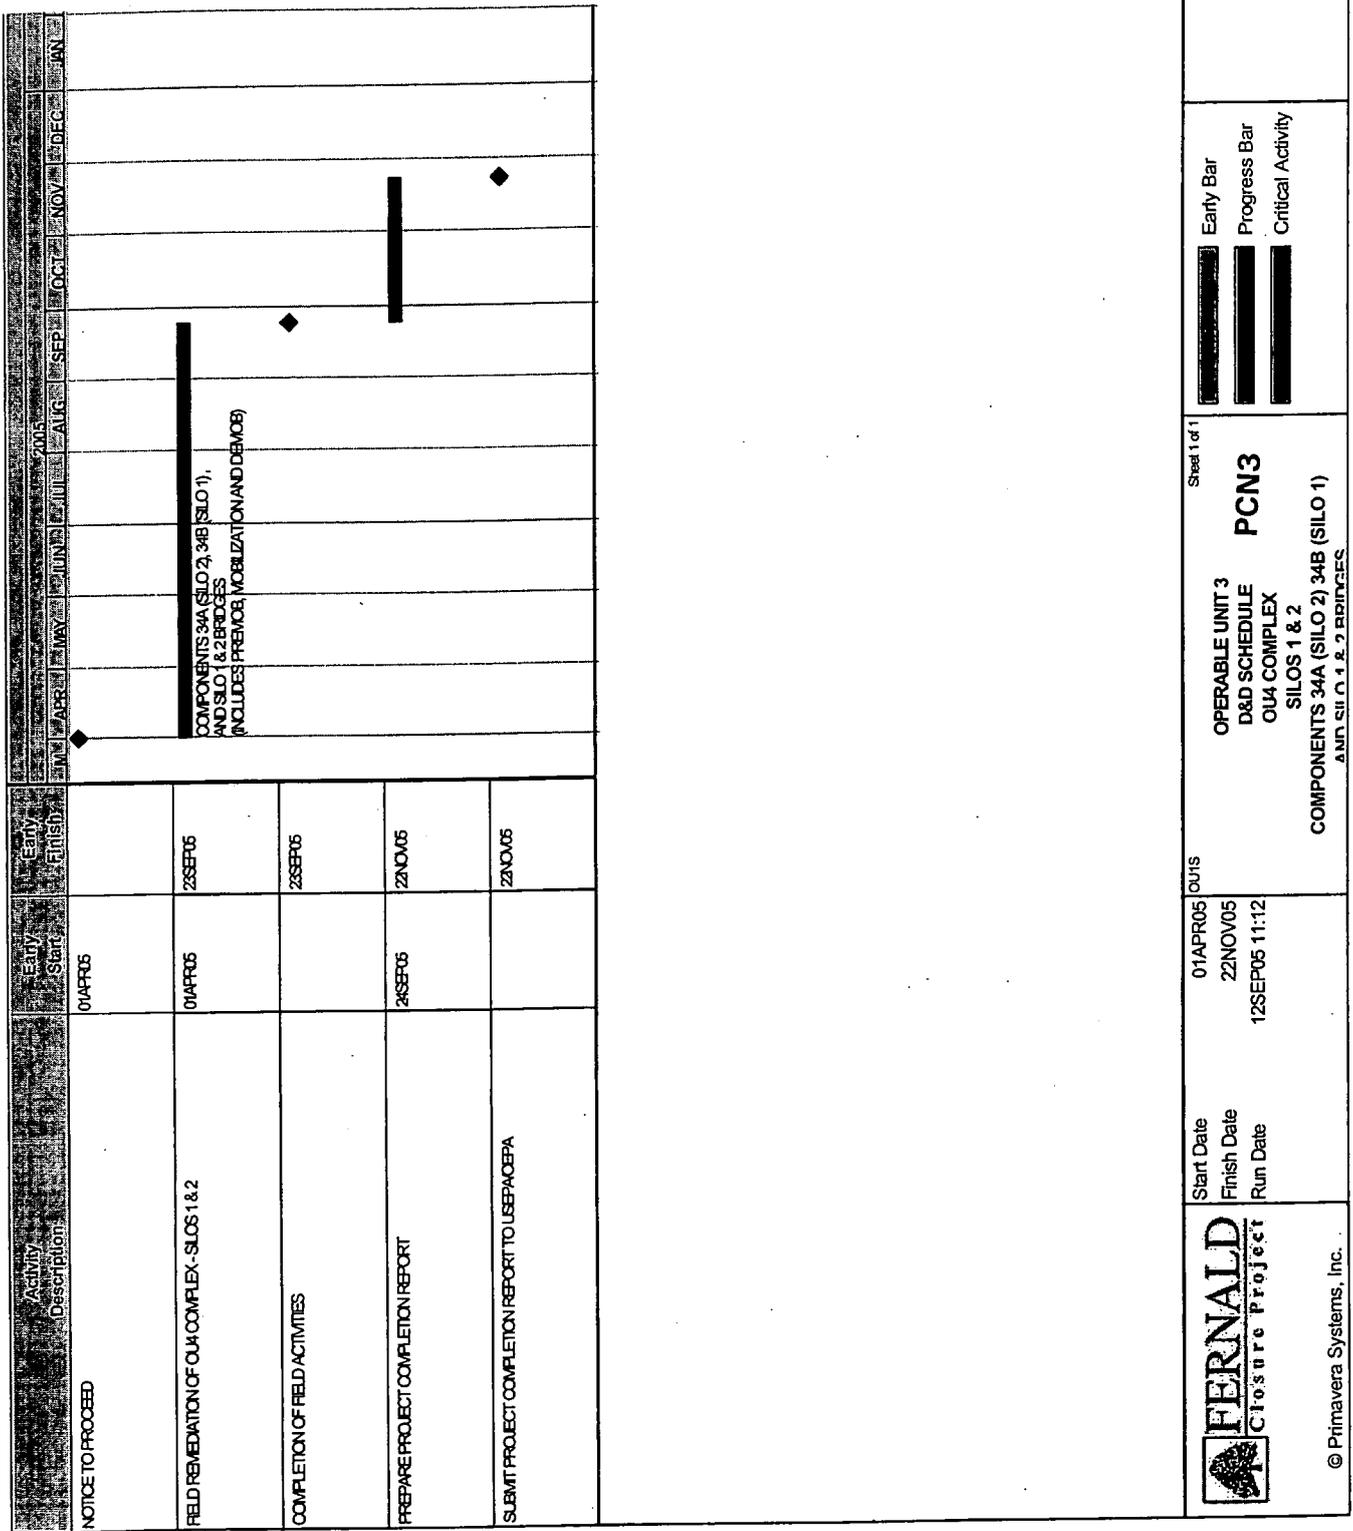


FIGURE 4-1 Components 34A, 34B and Silos 1&2 Bridges Remediation Schedule
