

00558 RF 94

DUE
DATE



Department of Energy



000022262

ROCKY FLATS OFFICE
P O BOX 928
GOLDEN COLORADO 80402-0928

FEB 08 1994

94 DOE 00164

ACTION	DIST	NC
	BFNEDETTI R L	
	P NJAMIN A	
	B R AN H S	
	CARNIVAL G J	
	COPP R D	
	CORDOVA R C	
	DAVIS J G	
	ERRERA D W	
	RANZ W A	
	HANNI B J	
	ALY T J	
	HEDAHL T G	
	HILBIG J G	
	UTCHINS N M	
	KIRBY W A	
	KUESTER A W	
	HAHAFFEY J W	
	HANN H P	
	MARX G E	
	M KENNA F G	
	MORGAN R V	
	IZZUTO V M	
	OTTER G L	
	ANDLIN N B	
	ATTERWHITE D G	
	CHUBERT A L	
	ETLOCK G H	
	ULLIVAN M T	
	WANSON E R	
	WILKINSON R B	
	WILSON J M	
	Busby W X Y	
	Steger S X Y	
	Houk R X Y	

Mr Martin Hestmark
U S Environmental Protection Agency Region VIII
ATTN Rocky Flats Project Manager 8HWM FF
999 18th Street Suite 500
Denver Colorado 80202 2405

Mr Gary Baughman
Hazardous Waste Facilities Unit Leader
Colorado Department of Health
4300 Cherry Creek Drive South
Denver Colorado 80222 1530

Gentlemen

The purpose of this letter is to clarify recent activities which have impacted Interagency Agreement (IA) Table 6 milestones for Operable Unit (OU) No 1 and to provide an extension request based on the Department of Energy's (DOE) position regarding these impacts. This request is based on Part 42 Paragraph 222 of the IA. The DOE believes that the series of events discussed in this letter constitutes good causes. There are four main constituents which were considered in compiling this extension request:

1. A previous DOE extension request dated October 7 1993 (Ref 93 DOE 10200) has not been acted on by the Environmental Protection Agency (EPA) and the Colorado Department of Health (CDH)
2. There was a stop work order which was applied to the Baseline Risk Assessment (BRA) on Operable Unit No 1 between June 21 and November 3 1993
3. The Draft Technical Memo (TM) No 10 *Development of Remedial Action Objectives* was submitted to the agencies on August 27 1993 however official comments on this TM had not been received from CDH as of February 1 1994
4. DOE would like to incorporate recent efforts by DOE EG&G EPA and CDH to develop a consistent programmatic approach for conducting Corrective Measures Studies/Feasibility Studies (CMS/FS) across all OUs at Rocky Flats

These items have caused inextinguishable schedule impacts and were discussed on the staff level in a meeting on January 28 1994 between DOE EPA and CDH personnel. The discussion of the above items in a meeting prior to DOE submitting a formal extension request was suggested by CDH personnel so that these items could be clarified.

For background purposes Enclosure 1 contains a detailed discussion of the above items and their potential impacts on the IA milestone schedule for OU 1.

Although many of the above constituents were considered this extension request is primarily based on the use of the Programmatic Approach for conducting CMS/FS studies and on the discussions of the January 28 1994 meeting. A detailed discussion

CORRESPONDENCE CONTROL	
ATS/T130G	
ADMIN RECORD/080	X 2

w d f Add ss e
C es Co t ol RFP

2-11-94
DATE BY

R f l t #

CE ORDER 5400 1

IN RECORD

M Hestmark & G Baughman
94 DOE 00164

2

FEB 08 1994

and background of the Programmatic Approach is included in Enclosure 1. In general the Programmatic Approach for conducting CMS/FS studies assumes that a series of interim working meetings will be held for DOE to present interim/draft results from the FS to EPA and CDH for comment. The approach then assumes that a Draft CMS/FS report can be reviewed by EPA and CDH in 20 days. In effect, this approach shortens the assumed duration between a Draft and Final CMS/FS report.

For your convenience a detailed GANT chart for conducting the CMS/FS study is included as Enclosure 2. This chart is based on the Programmatic Approach model. Please note the interim meetings and the 20 day review time for the Draft CMS/FS report by EPA and CDH reflected in this schedule. It should also be noted from the chart that the DOE review times for the draft and final reports are also due in 20 days.

Enclosure 3 shows the proposed milestone dates for eight Table 6 IA Milestones for OU 1. The first column of Enclosure 2 shows the original dates or the previously approved extension dates for the eight Table 6 IA milestones. The second column shows the proposed schedule for these milestones. The submittal dates for the Draft and Final CMS/FS reports are November 7, 1994 and February 8, 1995 respectively. If you have any questions regarding this material please contact Jen Pepe of my staff at 966 2184.

Sincerely


Martin McBride
Acting Assistant Manager for
Environmental Restoration

Enclosure

M Hestmark & G Baughman
94 DOE 00164

3

FEB 08 1994

cc w/enclosure
A Rampertaap EM 453
J Ciocco EM 453
S Grace ERD RFO
T Reeves ERD RFO
R Houk EG&G
W Busby EG&G
G Kleeman EPA
J Scheffelin CDH
J Swanson CDH

Enclosure 1

Background Discussion of IA Schedule Impacts

Previous Extension Request

The October 7 1993 DOE letter (Ref 93 DOE 10200) requested extension of 8 Interagency Agreement (IA) milestones. This DOE letter requested an extension for the submittal of the draft and final Corrective Measures Study/Feasibility Study (CMS/FS) reports to March 24 1994 and September 20 1994 respectively indicating that sufficient time would be required to transfer critical information between the Baseline Risk Assessment (BRA) in the Resource Conservation and Recovery Act Facility Investigation/Remedial Investigation (RFI/RI) report and Technical Memorandum (TM) No 10. The letter further requested subsequent extensions for the Draft Proposed Plan (PP) Final PP Draft Responsiveness Summary (RS) Final RS Draft Corrective Action Decision/Record of Decision (CAD/ROD) and Final CAD/ROD. These extensions were requested because the IA milestone for submittal of the Final RFI/RI Report had been extended from January 4 1993 to November 15 1993.

Stop Work Order

The August 12 1993 Environmental Protection Agency (EPA) letter concurred that work would be stopped on the schedule for Operable Units 1 through 7 on efforts to prepare Baseline Risk Assessments and prepare the RFI/RI reports. The Colorado Department of Health (CDH) letter dated October 22 1993 acknowledged the DOE October 7 1993 extension request (Ref 93 DOE 10200) for OU 1 and stated that the agencies would delay action on this request until the work stoppage on OU 1 was rescinded.

The work stoppage for OU 1 was rescinded via the CDH letter dated October 21 1993 and signed for concurrence by DOE on November 3 1993. Based on this letter the work stoppage for OU 1 was 135 days (June 21 1993 to November 3 1993). As of the date of this letter the DOE extension request had not been acted on by the agencies.

CDH Review of Technical Memoranda No 10

The Draft TM 10 (Development of Remedial Action Objectives) was submitted to the agencies on August 27 1993 (Ref 93 DOE 10202). This draft was submitted despite the work stoppage which had been imposed on the BRA for the RFI/RI report. As of the date of this letter DOE had not received written comments on TM 10 from CDH. The EPA comments on TM 10 were received November 17 1993. It should be noted that DOE has proceeded with work to address the EPA comments and that initial work is being conducted to screen remediation alternatives. This work however is proceeding with a certain amount of risk and approval of TM 10 is becoming a very crucial path item for progression of work on the CMS/FS.

Programmatic Approach for CMS/FS Studies

On December 23 1993 January 6 and January 13 1994 meetings were held with personnel from EPA CDH DOE and EG&G. The purpose of these meetings were for DOE and EG&G to present a draft model which outlines a detailed programmatic

Enclosure 1
page 2

approach for conducting CMS/FS studies at Rocky Flats There are three major advantages to developing this detailed programmatic approach in concurrence with the regulators

- 1 CMS/FS studies will be conducted using similar logistic procedures and approaches across all OUs resulting in greater efficiency
- 2 Potential problems associated with procedures review times legal determinations etc may be easily identified before hand and potentially avoided
- 3 It may be possible to compress an FS schedule depending on the particular circumstances for the OU

Although the CMS/FS process for OU 1 is in progress DOE feels that it would be beneficial to follow the proposed Programmatic Approach for finishing the CMS/FS process for this OU This would aid DOE EG&G EPA and CDH in testing modifying and further developing this approach Potential logistic problems which may exist would be identified by using OU 1 as the test case This could only improve the efficiency with which the CMS/FS studies are conducted for the other OUs at Rocky Flats

Enclosure 2

ACTIVITY ID	ACTIVITY DESCRIPTION	DRIG DUR	EARLY START	EARLY FINISH
88828C1070	SUBCONTRACTOR DEVELOPS INTERNAL WORK PLAN	18	3JUN92A	26JUN92A
88828C1000	FEASIBILITY STUDY START	0	11AUG93	
88828C1170	SITEWIDE TREATABILITY STUDIES DATA	1	11AUG93	11AUG93
88828C1060	IDENTIFY COLLECT AND DELIVER RI DATA TO SUBCONT	4	11AUG93	16AUG93
88828C1100	REVIEW AND ASSESS POTENTIAL ARAR	5	11AUG93	17AUG93
88828C1480	DRAFT BRA	8	11AUG93	20AUG93
88828C1080	CONDUCT RI DATA SUFFICIENCY REVIEW	4	17AUG93	20AUG93
88828C2268	UPDATE OF ARARs DATA	80	18AUG93	10DEC93
88828C1140	DEVELOP RARs	4	23AUG93	26AUG93
88828C1490	APPROVAL OF FINAL BRA	82	23AUG93	17DEC93
88828C1150	DEVELOP GRA	4	27AUG93	1SEP93
88828C1155	DEVELOP PRGS	4	2SEP93	8SEP93
88828C1210	DEVELOP DRAFT TM #10	4	9SEP93	14SEP93
88828C1220	EGG REVIEW AND COMMENT TM #10	4	15SEP93	20SEP93
88828C1290	EG&G AND DOE REVIEW AND COMMENT DRAFT TM#10	4	21SEP93	24SEP93
88828C1300	INCORPORATE COMMENTS & PRODUCE DRAFT FINAL TM#10	4	27SEP93	30SEP93
88828C1305	EPA/CDH REVIEW OF TM#10	34	10CT93	17NOV93
88828C1320	COMMENT RESOLUTION ON TM#10	20	18NOV93	17DEC93
88828C1180	DEVELOP COMP LIST OF TECH	5	20DEC93	3JAN94
88828C1500	REVISE TM#10	23	20DEC93	27JAN94
88828C1230	CONDUCT INITIAL SCREENING OF TECH	5	4JAN94	10JAN94
88828C1260	DEVELOP ALTERNATIVE LIST	5	11JAN94	17JAN94
88828C1275	MEETING WITH EPA/CDH	1	18JAN94	18JAN94
88828C1380	SCREEN ALTERNATIVES	5	19JAN94	25JAN94
88828C1390	DEVELOP TM#11	18	26JAN94	18FEB94
88828C1510	SUBMIT TM#10 TO EPA/CDH	1	28JAN94	28JAN94
88828C1400	DELIVER TASK 9 DRAFT TM#11	1	21FEB94	21FEB94
88828C1403	EG&G REVIEW OF TM#11	5	22FEB94	28FEB94
88828C1406	INCORPORATE COMMENTS	5	1MAR94	7MAR94
88828C1410	DOE REVIEW & COMMENT ON PRELIMINARY DRAFT TM#11	20	8MAR94	5APR94


1993 1994 1995

TREATABILITY/FEASIBILITY STUDY

ACTIVITY ID	ACTIVITY DESCRIPTION	ORIG DUR	EARLY START	EARLY FINISH
88828C1420	INCORPORATE DOE COMMENTS	10	6APR94	19APR94
88828C1440	FINAL DOE REVIEW ON DRAFT TM#11	5	20APR94	26APR94
88828C1450	INCORPORATE COMMENTS	5	27APR94	3MAY94
88828C1460	DELIVER TM#11 TO EGS/DOE, EPA/CDII	1	4MAY94	4MAY94
88828C1462	EPA/CDII REVIEW OF TM#11	10	5MAY94	18MAY94
88828C1464	MEETING WITH EPA/CDII	1	19MAY94	19MAY94
88828C1466	COMMENT RESOLUTION	10	20MAY94	3JUN94
88828C2270	ANALYZE ALTERNATIVES AGAINST 9 CRITERIA (TASK 10)	20	6JUN94	1JUL94
88828C2290	NEPA REVIEW OF ALTERNATIVES	20	6JUN94	1JUL94
88828C2272	COMPARATIVE ANALYSIS OF ALTERNATIVES AGAINST 9 CRITERIA	10	5JUL94	18JUL94
88828C2274	MEETING WITH EPA/CDII	1	19JUL94	19JUL94
88828C2276	PREPARE RECOMMENDED RAP	7	20JUL94	28JUL94
88828C2300	PREPARE PRELIMINARY DRAFT CMS/FS EA REPORT	20	29JUL94	25AUG94
88828C2320	EG&G/DOE REVIEW OF PREL. DRAFT CMS/FS EA REPORT	20	26AUG94	23SEP94
88828C2330	ADDRESS COMMENTS & PREPARE DRAFT CMS/FS EA RPT	10	26SEP94	7OCT94
88828C2340	RE SUBMIT DRAFT CMS/FS EA REPORT TO DOE	0		7OCT94
88828C2350	FINAL DOE REVIEW OF CMS/FS EA REPORT	20	10OCT94	4NOV94
88828C2170	SUBMIT DRAFT CMS/FS EA REPORT TO EPA/CDII	5	7NOV94	11NOV94
88828C4000	PREPARE PRELIMINARY DRAFT PROPOSED PLAN	15	7NOV94	24NOV94
88828C2180	EPA/CDII REVIEW OF DRAFT CMS/FS EA REPORT	20	14NOV94	13DEC94
88828C4010	DOE REVIEW PRELIMINARY DRAFT PROPOSED PLAN	20	30NOV94	4JAN95
88828C2190	PREPARE DRAFT FINAL CMS/FS EA RPT	15	14DEC94	11JAN95
88828C4020	INCORPORATE COMMENTS	10	5JAN95	18JAN95
88828C2200	DOE REVIEW DRAFT FINAL CMS/FS EA REPORT	20	12JAN95	8FEB95
88828C4022	FINAL DOE REVIEW DRAFT PROPOSED PLAN	10	19JAN95	1FEB95
88828C4025	INCORPORATE COMMENTS	5	2FEB95	8FEB95
88828C2210	DOE TRANSMITTAL OF DRAFT FINAL CMS/FS EA REPORT	0		8FEB95
88828C4030	SUBMIT DRAFT PROPOSED PLAN	0		8FEB95

1993 1994 1995

TREATABILITY/FEASIBILITY STUDY

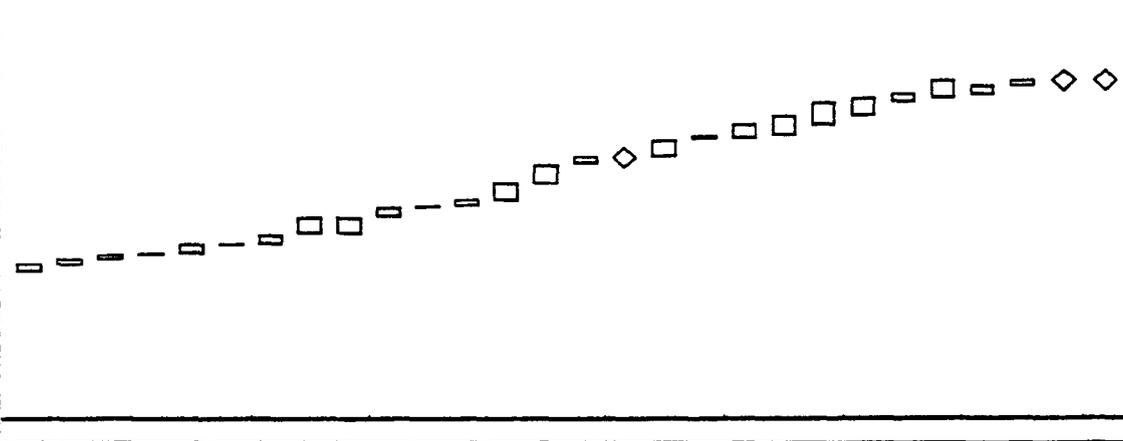

Enclosure 3

Proposed IA Milestone Schedule

IA Deliverable	IA Table 6 Milestone Date	Proposed Schedule
Draft CMS/FS	11 Feb 94 *	7 Nov 94 **
Final CMS/FS	3 Aug 94 *	8 Feb 94 **
Draft PP	27 Sep 93	8 Feb 94
Final PP	4 Jan 94	18 May 94
Draft RS	6 May 94	28 Aug 95
Final RS	3 Aug 94	25 Nov 95
Draft CAD/ROD	3 Aug 94	25 Nov 95
Final CAD/ROD	1 Nov 94	23 Feb 96

CMS/FS Corrective Measures Study/Feasibility Study

PP Proposed Plan

RS Responsiveness Summary

CAD/ROD Corrective Action Decision/Record of Decision

* An extension to the original Table 6 milestone date was granted April 2 1993

** Proposed Schedule based on the CMS/FS Programmatic Approach model and the IA Schedule Assumptions. A detailed gant chart is attached for the proposed CMS/FS study. This schedule assumes that the Draft CMS/FS Report can be reviewed by EPA and CDH in 20 days. It also assumes 20 days for DOE review prior to the submittal of the draft and final reports. An expedited or concurrent review by DOE would result in an early finish date for the CMS/FS report.
