

Internal Memorandum


Date: December 10, 2003
To: Building Notification File T760A
From: Steve Nesta
Subject: ADDITIONAL INFORMATION FOR CLOSEOUT REPORTS

CDPHE has provided comments to DOE concerning Type 1 Closeout Reports. To address CDPHE's comments, this memorandum documents the additional information identified by CDPHE for Trailer 760A.

Trailer 760A (Type 1 Facility)

- Sanitary sewer line was flushed with clear water from the trailer to the main system line. The sanitary sewer line raiser was cut and plugged 4 ft below grade and plugged at the manhole. This section of the sanitary sewer line remains.
- Domestic water line was isolated at grade under the trailer and cut/capped 4 feet below grade.
- Propane service was provided through an above ground tank and gas line located west of the trailer. The tank and line were removed.
- Electrical service was provided through above ground power pole and wires. The electrical wires and pole were removed.
- T760A did not have telephone service or an alarm system.
- T760A was demolished and disposed of as sanitary waste. Concrete anchor points, and concrete slabs were removed and disposed of as sanitary waste. Site restoration will be performed during the final land configuration for Rocky Flats.


See Attachment 1, Trailer 760A, for location of domestic water line and sanitary sewer line.



ADMIN RECORD

1/3
DOCUMENT CLASSIFICATION
REVIEW WAIVER PER
CLASSIFICATION OFFICE

IA-A-001923

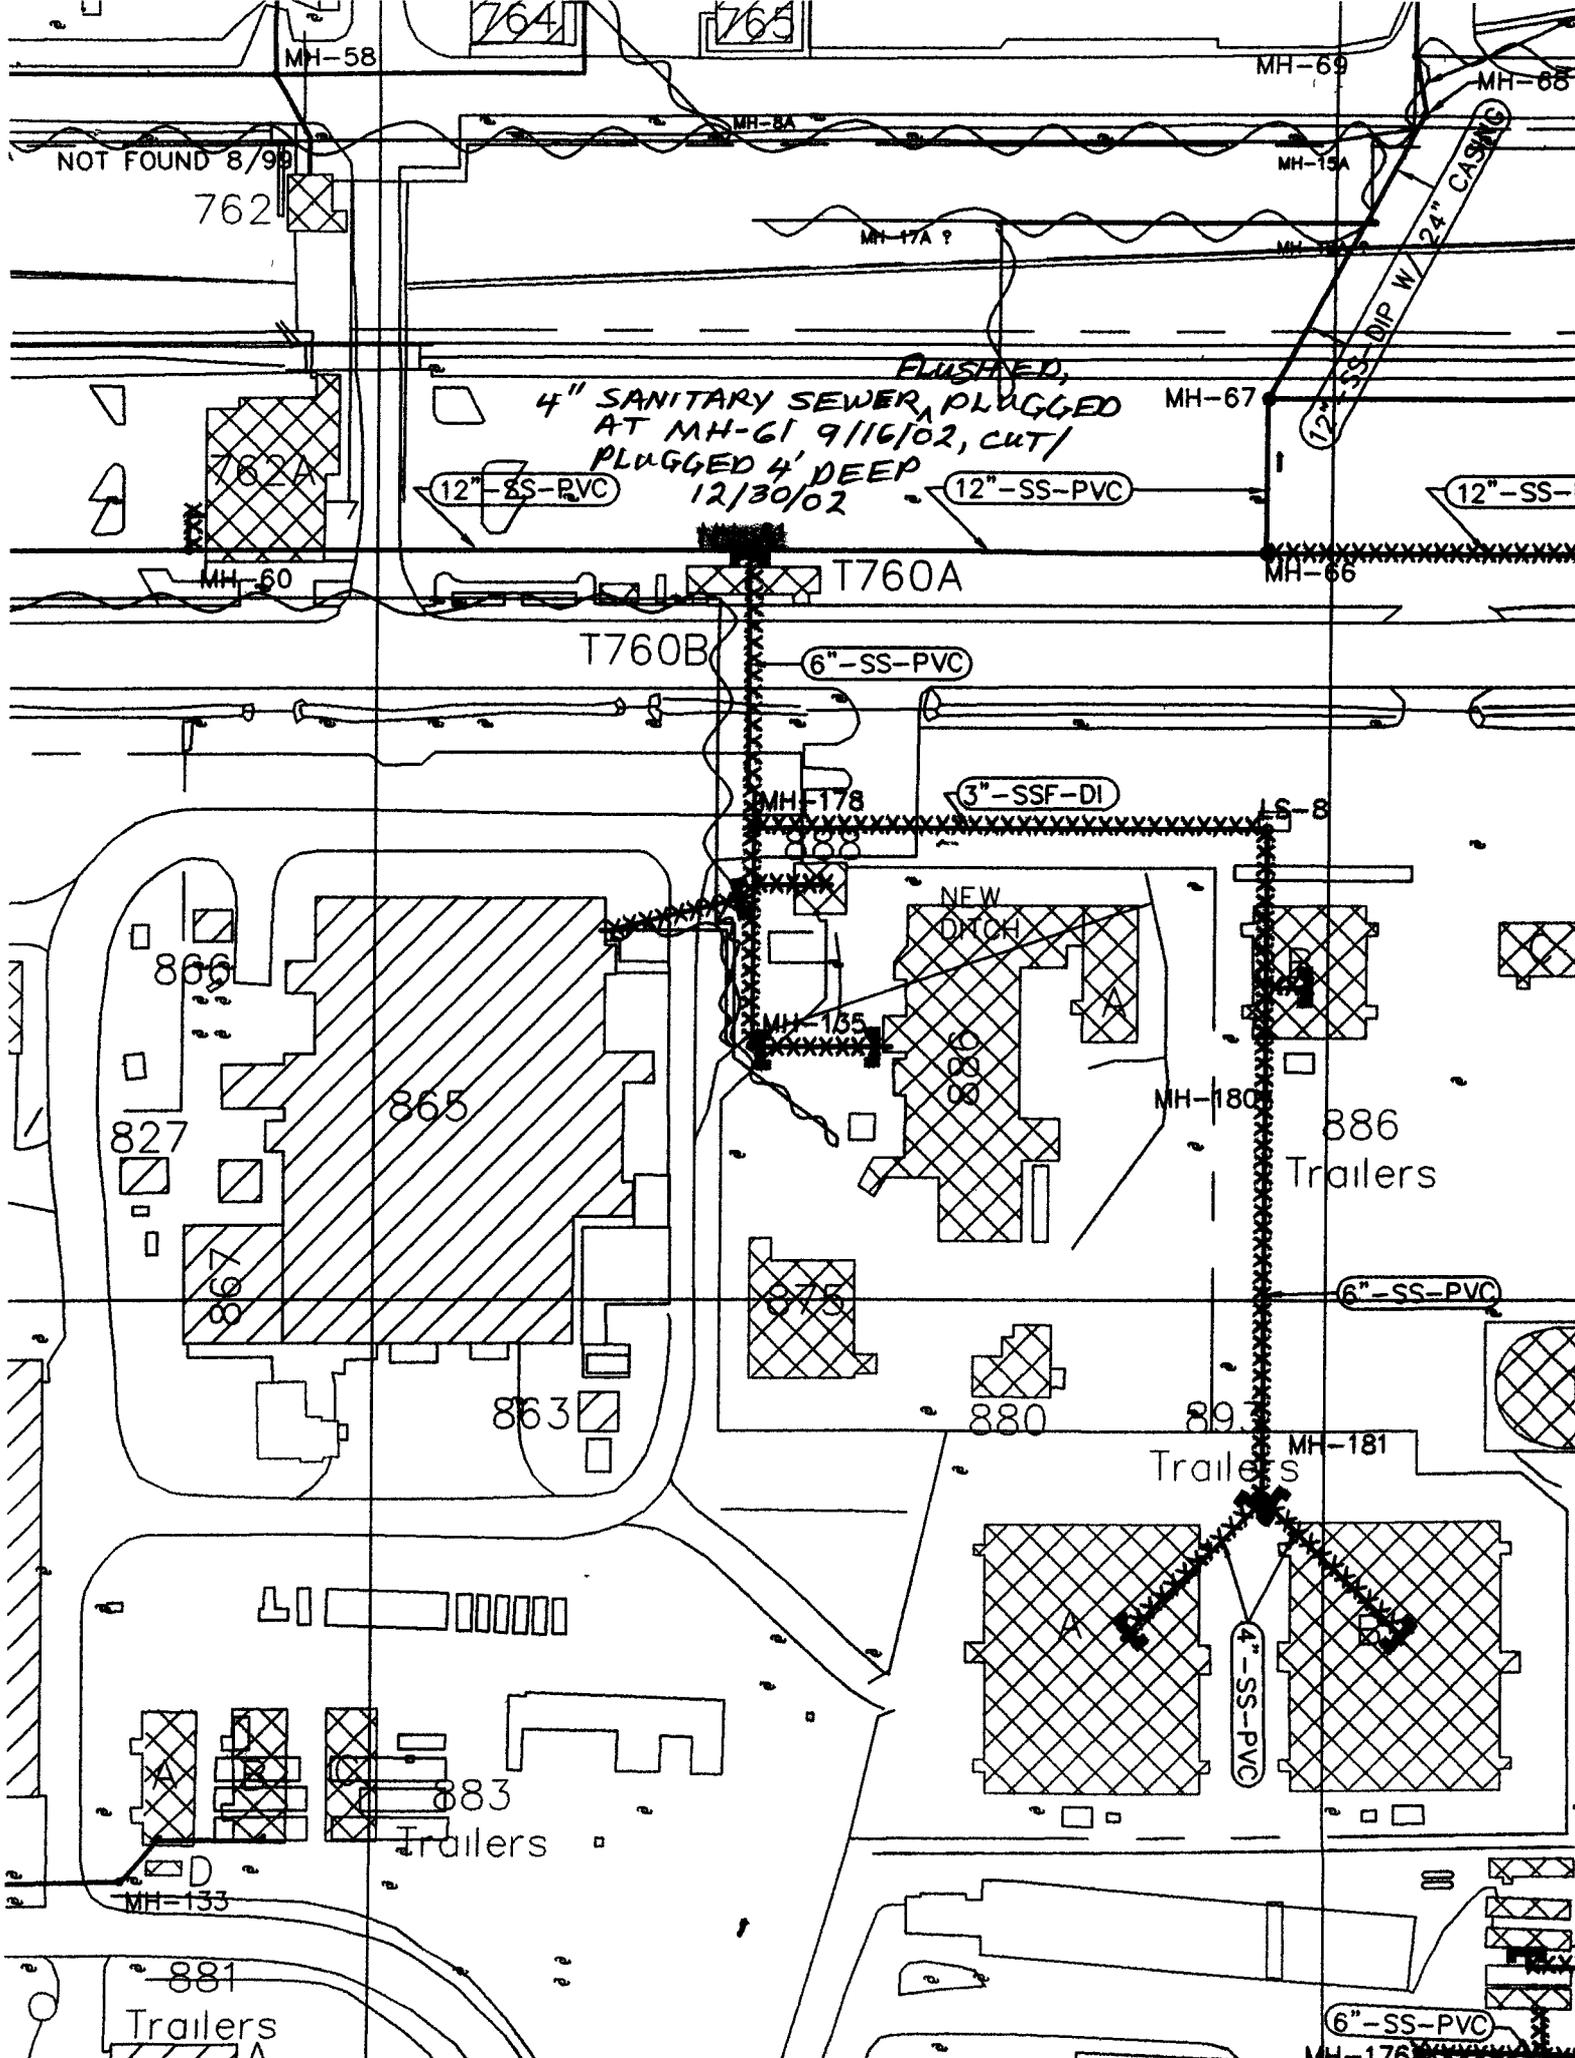

MH-58

764

765

MH-69

MH-68

MH-8A

NOT FOUND 8/99

762

MH-17A ?

MH-15A

MH-17

12" SS DIP W/ 24" CASING

FLUSHED,
4" SANITARY SEWER, PLUGGED
AT MH-61 9/16/02, CUT/
PLUGGED 4' DEEP
12/30/02

MH-67

12"-SS-PVC

12"-SS-PVC

12"-SS-P

MH-60

T760A

MH-66

T760B

6"-SS-PVC

MH-178

3"-SSF-DI

NEW
DITCH

MH-135

MH-180

886
Trailers

866
827
868

865

863

873

880

89

MH-181

Trailers

LI

883
Trailers

4"-SS-PVC

MH-133

881
Trailers

6"-SS-PVC

MH-176
