

# Type 1 Facility Closeout Report

<b>Section A. Facility Data</b>	
Facility No.	T130A
Facility Descriptor:	Office Trailer, 15,400 square feet
Project:	RISS – Area 5 D&D
Date of Demolition:	August 1, 2005
Additional Information:	Modular corrugated metal office trailer demolished and disposed of as sanitary waste.
<i>(Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)</i>	

<b>Section B. Final Characterization Data</b>	
Reconnaissance Level Characterization Report <i>(concurrence received)</i>	Reconnaissance Level Characterization Report – Concurrence, Steven H. Gunderson to Joseph A. Legare, dated August 03, 2005.
In-process Characterization	N/A
Pre-Demolition Survey Report <i>(approval received)</i>	N/A
Post-Demolition Survey Report <i>(as necessary)</i>	N/A

<b>Section C. Waste Data <i>(complete categories as appropriate)</i></b>	
<u>Sanitary Disposal</u>	
Disposal Site:	BFI Foothills Landfill, Golden, Colorado
Waste Volume (m <sup>3</sup> ):	2354.8
Waste Weight (tons):	986.4 tons
Additional Information:	Above grade building debris
<u>Hazardous Disposal</u>	
Disposal Site:	Kettleman Hills Facility, Kettleman City, CA or Bethlehem Apparatus Co, Hellertown, PA
Waste Volume (m <sup>3</sup> ):	Minor amounts
Additional Information:	Electronic circuit boards, thermostats, exit signs, batteries, fluorescent light bulbs and any other RCRA hazardous components were removed and taken to the RFCA temporary unit for combination with like waste streams for disposal.
<u>TSCA Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	N/A
Additional Information:	
<u>Asbestos Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	N/A
Additional Information:	
<u>Low-Level Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	N/A
Additional Information:	
<u>Low-Level Mixed Waste Disposal</u>	
Disposal Site:	
Waste Volume (m <sup>3</sup> ):	N/A
Additional Information:	
<u>Recycled Material</u>	
Recycle Facility:	
Waste Volume (m <sup>3</sup> ):	
Additional Information:	

ADMIN RECORD

IA-A-002820

# Type 1 Facility Closeout Report

## Property Disposition

Receiver Locations (major items only): N/A

Volume (m<sup>3</sup>): \_\_\_\_\_

Weight (tons): \_\_\_\_\_

Additional Information: \_\_\_\_\_

## Section D. Approvals

Kaiser-Hill Project Manager

[Signature]  
Name/Signature

9/1/05


Date

## Additional Facility Information

Building T130A was an approximately 15,400 square foot modular trailer acquired in 1991. The structure was corrugated metal siding with corrugated metal skirting. The entrances had wooden stairs leading to a wooden enclosure.

Building T130A had the following utilities: electrical, plant water, plant sanitary and fire protection provided by an overhead sprinkler system and wall mounted fire extinguishers.

The entire T130A structure was removed during D&D activities, and sent offsite for disposal. The utilities were disconnected and removed to at least three feet below final grade as indicated on the attached map. There are no remaining structural components, utility lines, or parts of the foundation. The buildings are not in an IHSS or PAC therefore no soil sampling is required.






4" SEWER LINE  
REMOVED TO 4  
FEET BELOW GRADE  
AND GROUTED

4" WATERLINES REMOVED TO 4  
FEET BELOW GRADE


SEWER MANHOLES REMOVED  
AND GROUTED

ELECTRICAL CABLE AND  
CONDUIT REMOVED FROM  
AREA

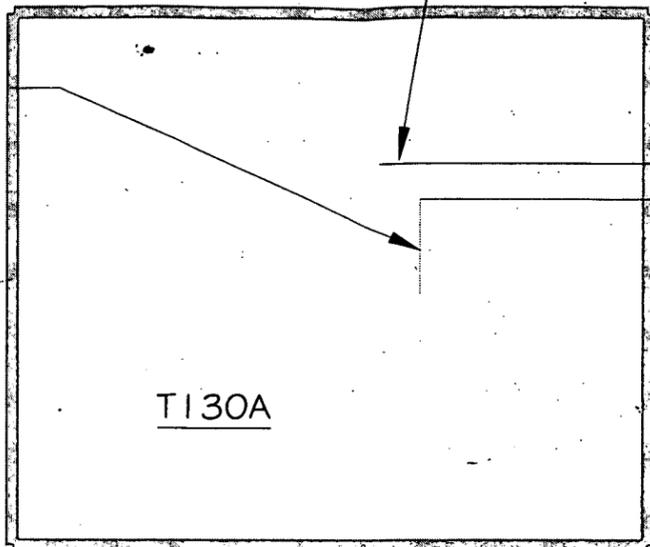

PIV VALVES  
REMOVE FOR  
WATER ISOLATION

4" WATERLINES REMOVED TO 4"  
BELOW GRADE

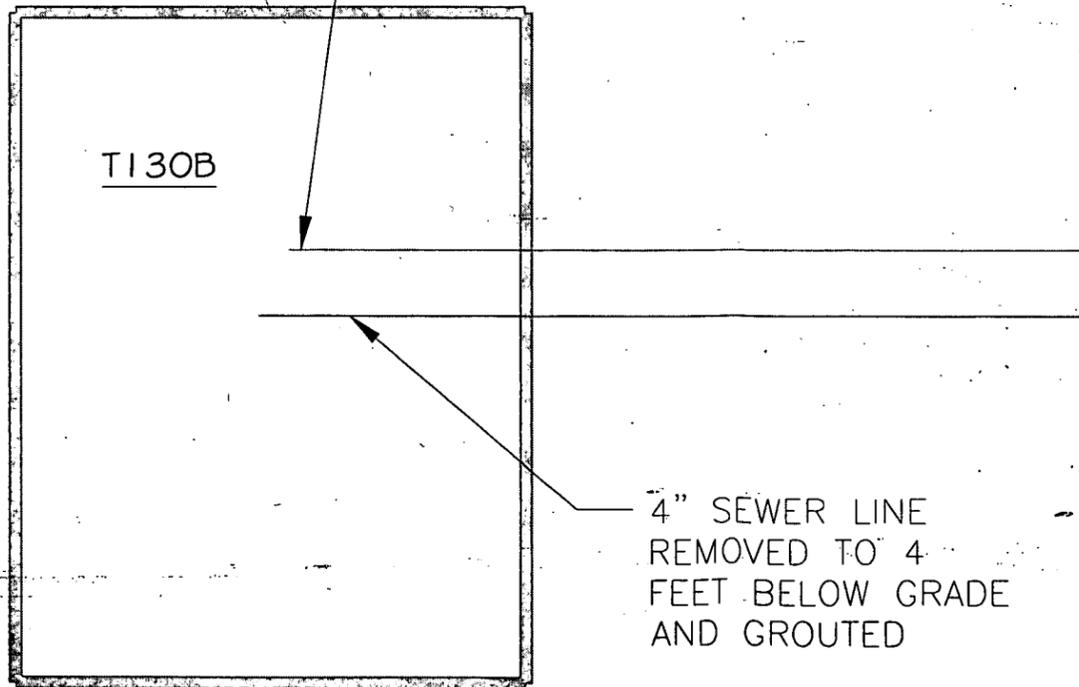

4" SEWER LINE  
REMOVED TO 4  
FEET BELOW GRADE  
AND GROUTED

T130A AND T130B
