

CORRES CONTROL
OUTGOING LTR #

DOE ORDER #

05-RF-00868

DIST	LTR	ENC
CROCKETT, G		
FERRERA, D.W.	X	X
GILPIN, H.E.		
LONG, J.W.		
LINDSAY, D. C.		
SHELTON, D.C.		
TUOR, N.R.		
SNYDER, D		
MCGRORY, M		
KAISER, M.		
BEAN, C.		
LINSINBGLER, H		
NESTA, S.	X	X
PRIMROSE, A		
WIEMELT, K		



September 19, 2005

05-RF-00868

Richard J. Schassburger, Director
Headquarters Cadre Project Management
DOE, RFPO

TRANSMITTAL OF CLOSE OUT REPORT FOR OFFICE TRAILERS T130D, T130F AND
T130H -- DWF-095-05

Attached is the Closeout Report for the Type 1 facility for office trailers T130D, T130F and
T130H. Also included are six color copies of the removal map. Please note that a copy of the
report has been submitted to the CERCLA AR by the Kaiser-Hill RISS project.

Please contact Steve Nesta at extension 6386 with questions or concerns.

Dennis Ferrera

Dennis W. Ferrera
Vice President and Project Manager
Remediation, Industrial D&D, and Site Services

CORRES CONTROL	X	X
ATS		
DMN. RECORD	X	X
ASTE REC CTR		
RAFFIC		

Attachment:
As Stated

CLASSIFICATION:		
CNI		
NCLASSIFIED		
CONFIDENTIAL		
SECRET		

SMN:rlm

AUTHORIZED CLASSIFIER
SIGNATURE:

Orig. and 1 cc - Richard J. Schassburger

A _____ CC:
ate: _____ John Rampe
IN REPLY TO RFP CC #:

ACTION ITEM STATUS:

- ☐ PARTIAL/OPEN
☐ CLOSED

LTR APPROVALS:


ast Name) _____
ast Name) _____

ORIG. & TYPIST INITIALS:

SMN:rlm

Letter # DWF-095-05

Kaiser-Hill Company, L.L.C.
Rocky Flats Environmental Technology Site, 12101 Airport Way, Unit B, T130F, Golden, CO 80403-8200 ♦ (303) 966-6386



ADMIN RECORD

IA-A-002843

Type 1 Facility Closeout Report

Section A. Facility Data

Facility No.	T130D, F, H
Facility Descriptor:	Office Trailers, 46,200 square feet
Project:	RISS - Area 5 D&D
Date of Demolition:	August 31, Sept. 6, Sept. 8, 2005 (respectfully)
Additional Information:	Modular corrugated metal office trailers demolished and disposed of as sanitary waste.

(Must include information on environmental releases and conditions of site at turnover to Environmental Restoration)

Section B. Final Characterization Data

Reconnaissance Level Characterization Report (concurrence received)	Reconnaissance Level Characterization Report - Concurrence, Steven H. Gunderson to Richard DiSalvo, dated April 17, 2003.
--	---

In-process Characterization	N/A
-----------------------------	-----

Pre-Demolition Survey Report (approval received)	N/A
--	-----

Post-Demolition Survey Report (as necessary)	N/A
--	-----

Section C. Waste Data (complete categories as appropriate)

Sanitary Disposal

Disposal Site:	BFI Foothills Landfill, Golden, Colorado
Waste Volume (m ³):	10,910.1 m ³
Waste Weight (tons):	2851.3 tons
Additional Information:	Above grade building debris, and surrounding asphalt infrastructure.

Hazardous Disposal

Disposal Site:	Kettleman Hills Facility, Kettleman City, CA or Bethlehem Apparatus Co, Hellertown, PA
Waste Volume (m ³):	Minor amounts
Additional Information:	Electronic circuit boards, thermostats, exit signs, batteries, fluorescent light bulbs and any other RCRA hazardous components were removed and taken to the RFCA temporary unit for combination with like waste streams for disposal.

TSCA Waste Disposal

Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	

Asbestos Waste Disposal

Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	

Low-Level Waste Disposal

Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	

Low-Level Mixed Waste Disposal

Disposal Site:	
Waste Volume (m ³):	N/A
Additional Information:	

Recycled Material

Recycle Facility:	
Waste Volume (m ³):	
Additional Information:	

Type 1 Facility Closeout Report

Property Disposition

Receiver Locations (major items only): N/A

Volume (m³): _____

Weight (tons): _____

Additional Information: _____

Section D. Approvals

Kaiser-Hill Project Manager

Robert A. Ferrera / R.A. Ferrera ^{for Don Clark}

Name/Signature

9-13-05


Date

Additional Facility Information

Building T130D, F, and H each were approximately 15,400 square foot modular trailer acquired in 1991. The structures were corrugated metal siding with corrugated metal skirting. The entrances had wooden stairs leading to a wooden enclosure.

These trailers had the following utilities: electrical, plant water, plant sanitary and fire protection provided by an overhead sprinkler system and wall mounted fire extinguishers.

All three trailer structures were removed during D&D activities, and sent offsite for disposal. The utilities were disconnected and removed to at least three feet below final grade as indicated on the attached map. There are no remaining structural components, utility lines, or parts of the foundation. The buildings are not in an IHSS or PAC therefore no soil sampling is required.

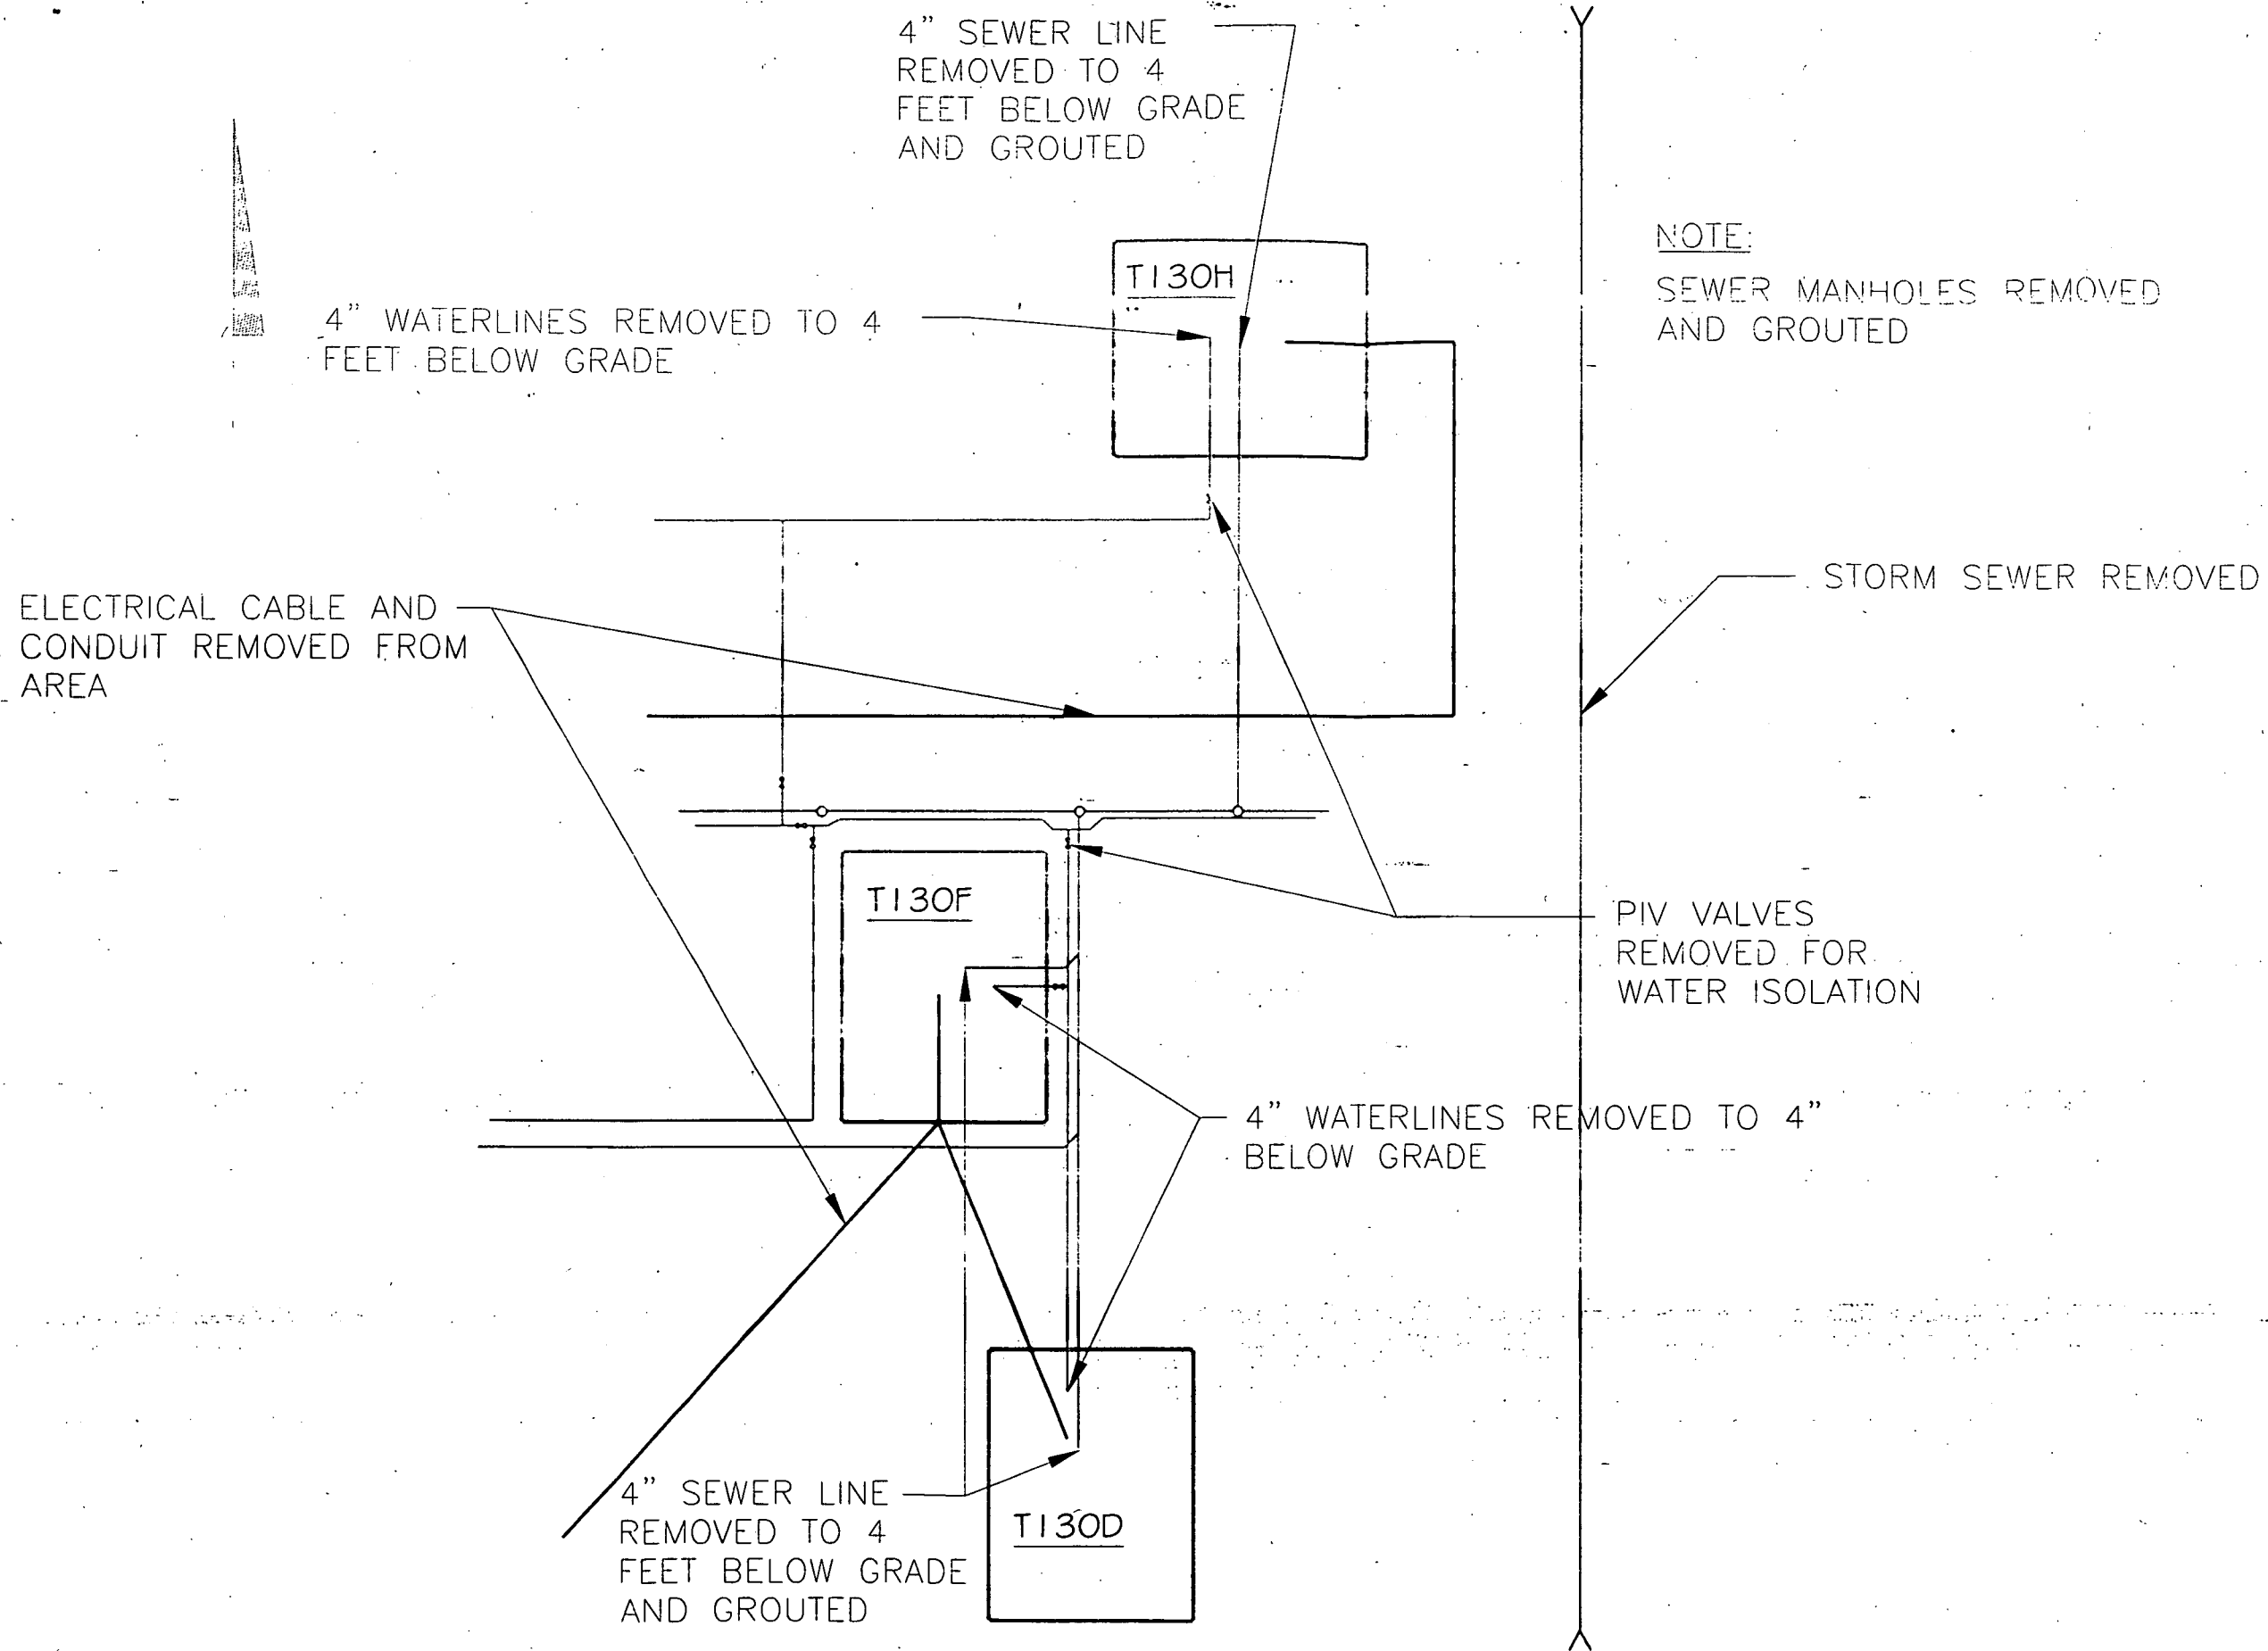

T130 TRAILERS - D, F & H
