
Overview of the Rocky Flats Site Annual Report of Site Surveillance and Maintenance Activities

Calendar Year 2008

Rocky Flats Stewardship Council
June 1, 2009



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Surface Water Monitoring and Operations



Third Quarter 2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Pond Operations – Third Quarter 2008

- Terminal Pond Discharges:
 - None
- Transfers:
 - None
- Pond Levels:
 - As of September 30, 2008, Ponds A-3, A-4, B-5, and C-2 and the Landfill Pond were holding approximately 14.4 MG (14.4% of capacity).



Recent Pond Levels (January 27, 2009):

- Landfill (22.5%)
- A-3 (11.5%)
- A-4 (8.3%)
- B-5 (22.1%)
- C-2 (16.2%)



Dam Breach Phase 1

- Dams A-1 and A-2 are nearly complete.
- Dams B-1, B-2, B-3, and B-4 are ongoing.
- All construction and erosion controls are expected to be installed by mid-March 2009.



*Dam A-1:
October 8, 2008*



*Dam A-1:
January 8, 2009*




Hydrologic Data – Third Quarter 2008

- Precipitation:
 - 4.3 inches total precipitation
 - 107% of WY 93–07 average
- Flow rates (percentage of average):
 - GS01 (no flow)
 - GS03 (no flow)
 - GS10 (9%)
 - SW027 (no flow)
 - SW093 (15%)




POC GS01

- Plutonium and Americium

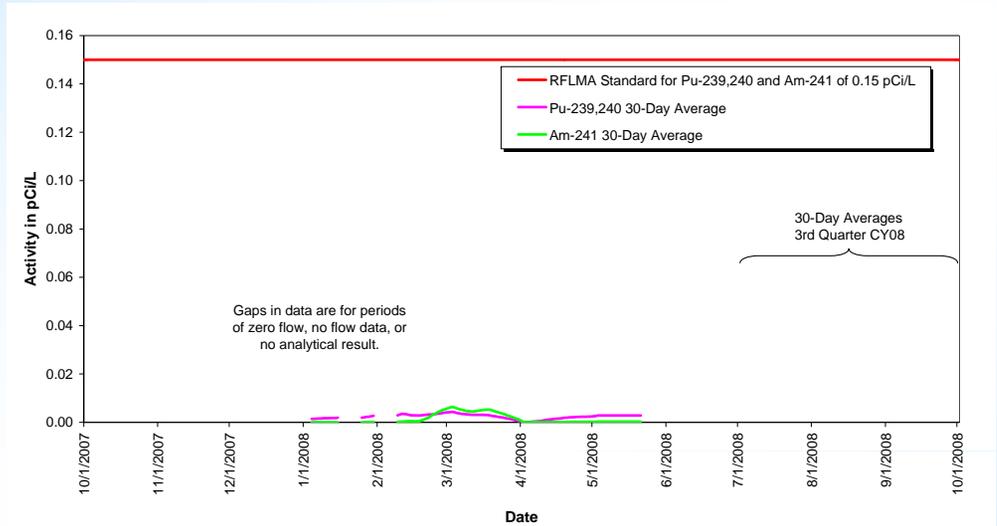



- Total Uranium

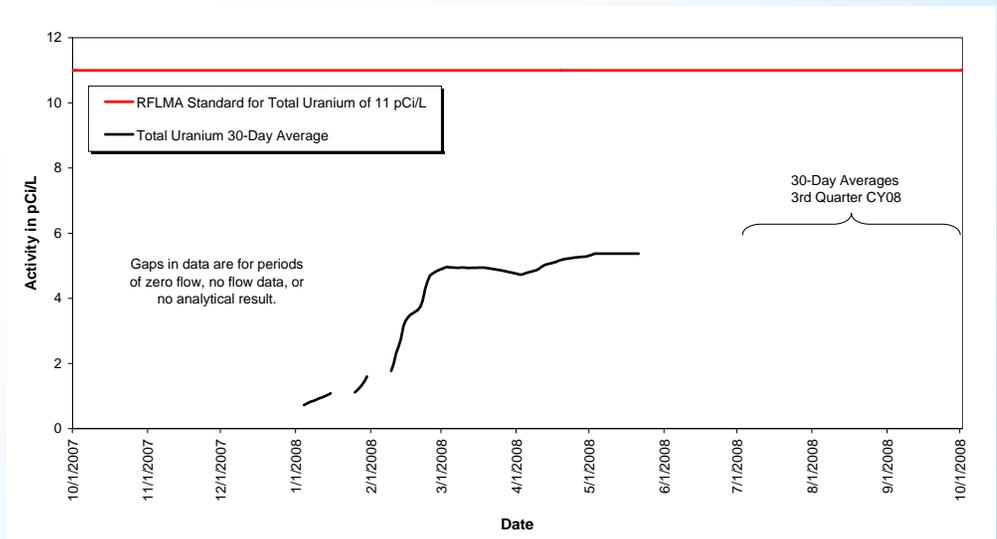

POC GS03

- Plutonium and Americium



- Total Uranium and Nitrate + Nitrite as Nitrogen

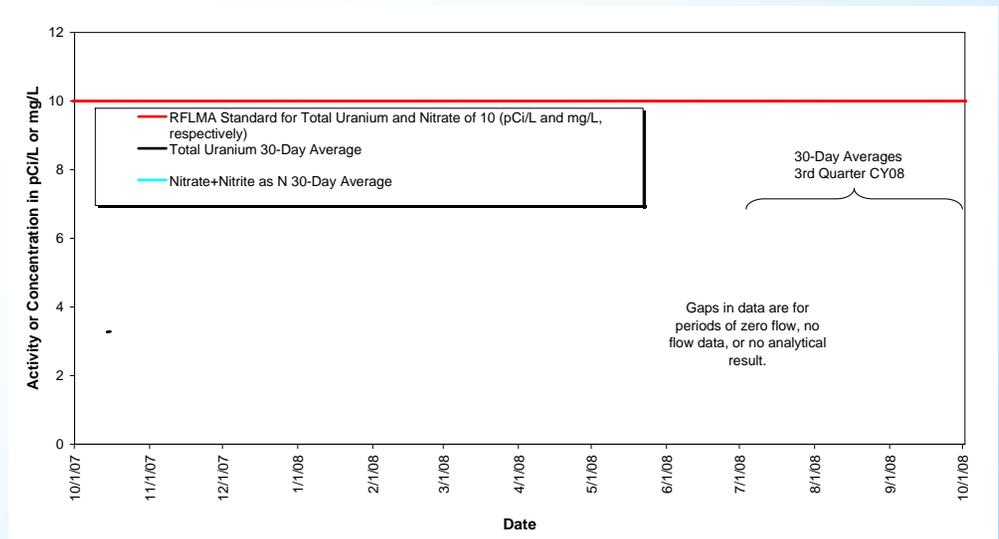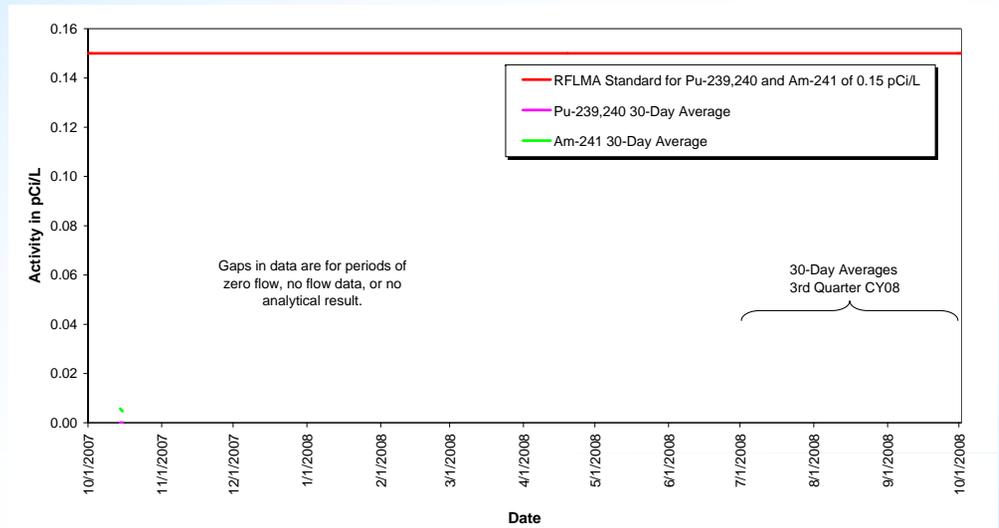

POC GS08

- Plutonium and Americium



- Total Uranium and Nitrate + Nitrite as Nitrogen

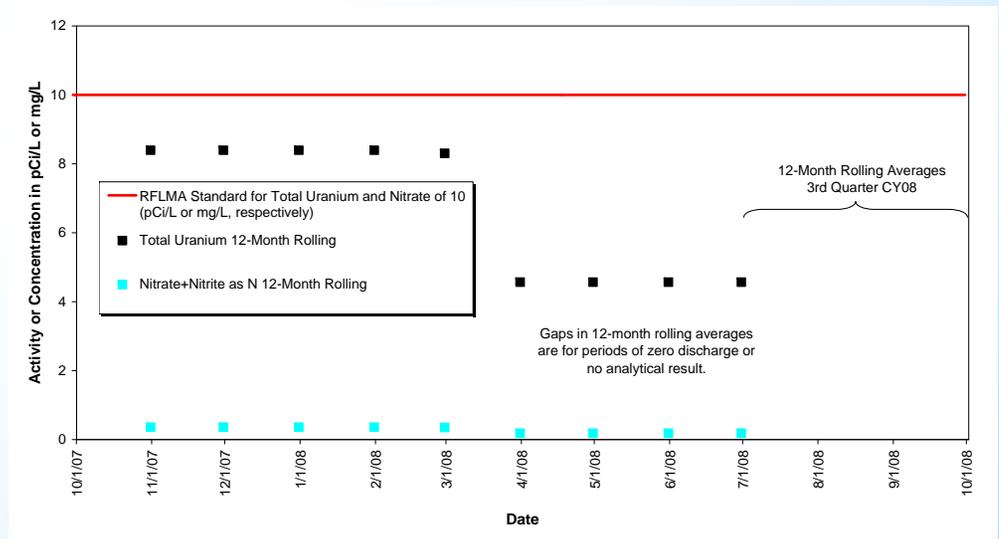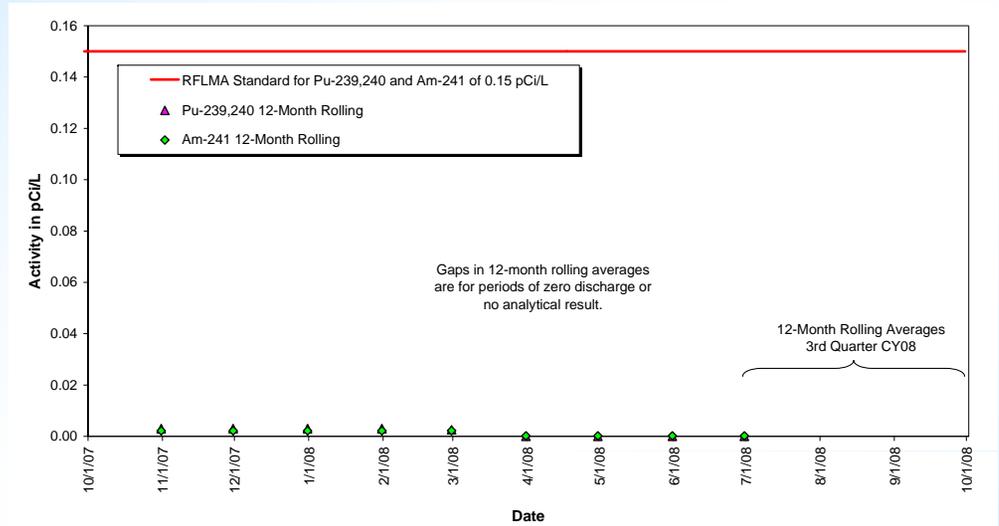

POC GS11

- Plutonium and Americium

- Total Uranium and Nitrate + Nitrite as Nitrogen

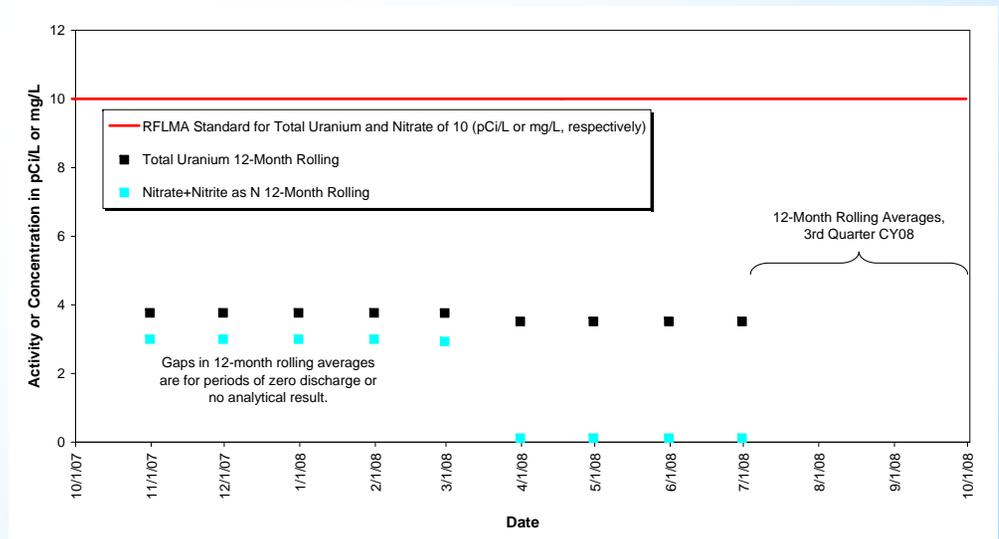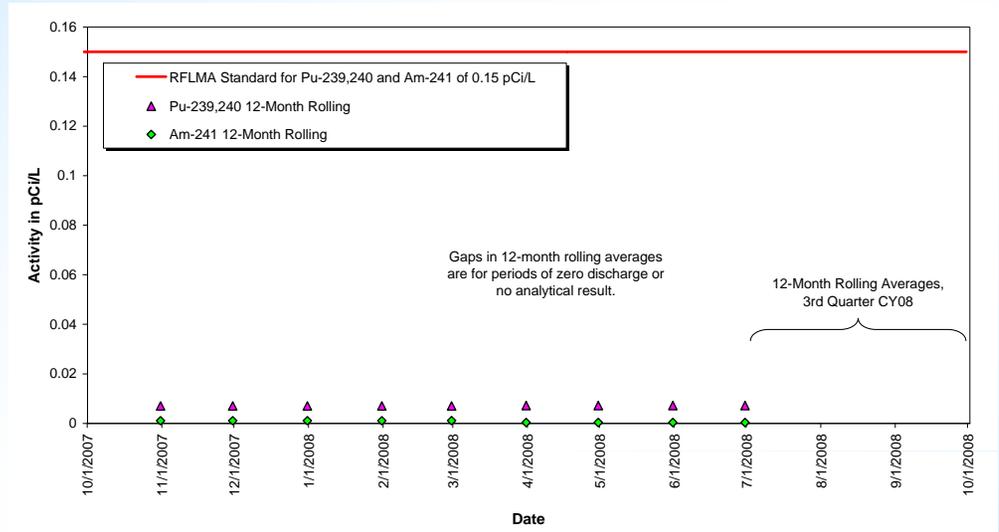

POC GS31

- Plutonium and Americium

- Total Uranium

No pond C-2 discharge during the last 12 months



Point of Evaluation Monitoring – Third Quarter 2008

- Water quality at all points of evaluation, except GS10, was below applicable standards.
 - Reportable values for total uranium at GS10 continue to be observed and are probably caused by groundwater contributions of naturally occurring uranium to South Walnut Creek.



Performance Monitoring – Third Quarter 2008 Original and Present Landfills

- Original Landfill: Surface water quality results during the second quarter of 2008 triggered monthly sampling for selenium.
 - Selenium was not detected in the third monthly sample collected during the third quarter of 2008; monthly sampling was discontinued.
- Present Landfill: Surface water quality results triggered monthly sampling for vinyl chloride.
 - Vinyl chloride was not detected in the first monthly sample; monthly sampling was discontinued.



Questions?



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Groundwater Monitoring and Operations



Third Quarter 2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

RFLMA Monitoring

- All RCRA wells were monitored.
- Results will be evaluated in the 2008 Annual Report.



SPPTS Update

- SPPTS effluent is now monitored at “SPOUT”.
- The effects of Phase I upgrades on effluent water quality include the following:
 - Flow to the SPPTS has approximately doubled, reducing residence time within the media.
 - Concentrations of nitrate have doubled to tripled (load has increased approximately 4 to 6 times).
 - Concentrations of uranium have increased by approximately 50% (load has increased approximately 2 times).



SPPTS Update (continued)

- Based on original treatment studies and SPPTS performance data, reduced treatment was anticipated.
 - Nitrate levels are now approximately 20 times those of University of Waterloo studies (which removed approximately 60% of nitrate).
 - We target approximately 98% removal.
 - Heavy snowmelt in winter 2006–2007 increased flow, thereby reducing treatment.
 - Current conditions include higher flow and higher concentrations.



SPPTS Update (continued)

- As a result of increased nitrate and uranium load and shortened treatment time:
 - Treatment effectiveness is reduced.
 - Effluent concentrations are above target levels.
- System effluent and discharge gallery water quality are essentially the same (effluent is no longer re-contaminated before discharge).
- DOE has consulted with the regulators.
- The phased path forward continues to be followed.
- The rejuvenation of existing media is being evaluated.



SPPTS Update (continued)

- The SPPTS phased path forward consists of four phases:
 - Phase I: Collect additional contaminated groundwater, and route it through treatment cells.
 - Status: Completed.
 - Phase II: Install new uranium treatment cell as first treatment step (so future downstream nitrate treatment media will not be “rad waste”).
 - Status: Construction to begin in mid-February and be completed by March 31, 2009.



SPPTS Update (continued)

- Phase III: Define and perform a pilot-scale study to identify preferred nitrate treatment media.
 - Current sawdust/ZVI media would require a treatment cell of at least 5 times the current quantity to achieve adequate treatment.
 - The study will evaluate two pilot-scale cells: inert (plastic) media with brewery byproduct as carbon source, and walnut shells infused with vegetable oil.
 - Status: Construction to begin in March and be completed in late April.
- Phase IV: Combine findings from Phase III (media) and flows measured since the completion of Phase I to design and construct a full-scale nitrate treatment cell.





Questions?



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Update on WQCC Rulemaking

- Petition to adopt the statewide basic uranium standard (MCL 30 $\mu\text{g/L}$ approximately 20 pCi/L). Hearing: January 12, 2009
 - WQCC recognized that changed conditions warranted revision.
 - WQCD said that a mistake was made in promulgating uranium's statewide standard in 2005:
 - The range should be from 16.8 to 30 $\mu\text{g/L}$ (“hyphenated standard”).
 - Many analytes have the hyphenated standard.
 - The statewide uranium standard will be clarified.
 - The higher number applies as the end-of-pipe limit for discharge permits.



Update on WQCC Rulemaking (continued)

- The lower number is a health-based goal value derived using WQCC methodology per Policy 96-2.
 - 10⁻⁶ incremental lifetime cancer risk
 - 2 liters drunk per day over a lifetime
- WQCC revised the site-specific uranium standard to the 16.8 µg/L (approximately 11.5 pCi/L) health-based standard.
- A higher ambient-based standard may be addressed in the future, based on data and what is practical.
- Gross alpha and gross beta standards were removed; specific radionuclides (uranium, plutonium, and americium) are being monitored.



Update on WQCC Rulemaking (continued)

- Expiring Temporary Modifications (TMs) Annual Review—Hearing: December 2008
 - Current Rocky Flats TMs (six VOCs, nitrate/nitrite) and the expiration date (December 31, 2009) were retained.
- Triennial Review South Platte River Basin
 - Issues Formulation Hearing: November 10, 2008; Rulemaking Hearing: June 2009
 - Potential Rocky Flats Issues:
 - Rocky Flats TMs expire on December 31, 2009.
 - The SPPTS upgrade should reduce nitrate loading to North Walnut Creek, but it may not meet 10 $\mu\text{g/L}$ by December 31, 2009.
 - New statewide basic standard for arsenic (0.02–10 $\mu\text{g/L}$) below site-specific standard (50 $\mu\text{g/L}$).



2008 Ecological Monitoring Summary



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Project Assistance

- Project support for ecological issues was provided for the:
 - 2008 Roads Projects
 - Dam Breach Project
 - Annual Dam Mowing and Riprap Spraying Project
 - Solar Ponds Sump Installation and Phase II/III Project




Ecological Monitoring

- OLF and PLF vegetation surveys
- Monthly weed surveys in the mitigation wetlands
- Revegetation monitoring
- Weed monitoring/mapping
- Preble's mouse mitigation monitoring
- Wetland mitigation monitoring




Weed Control

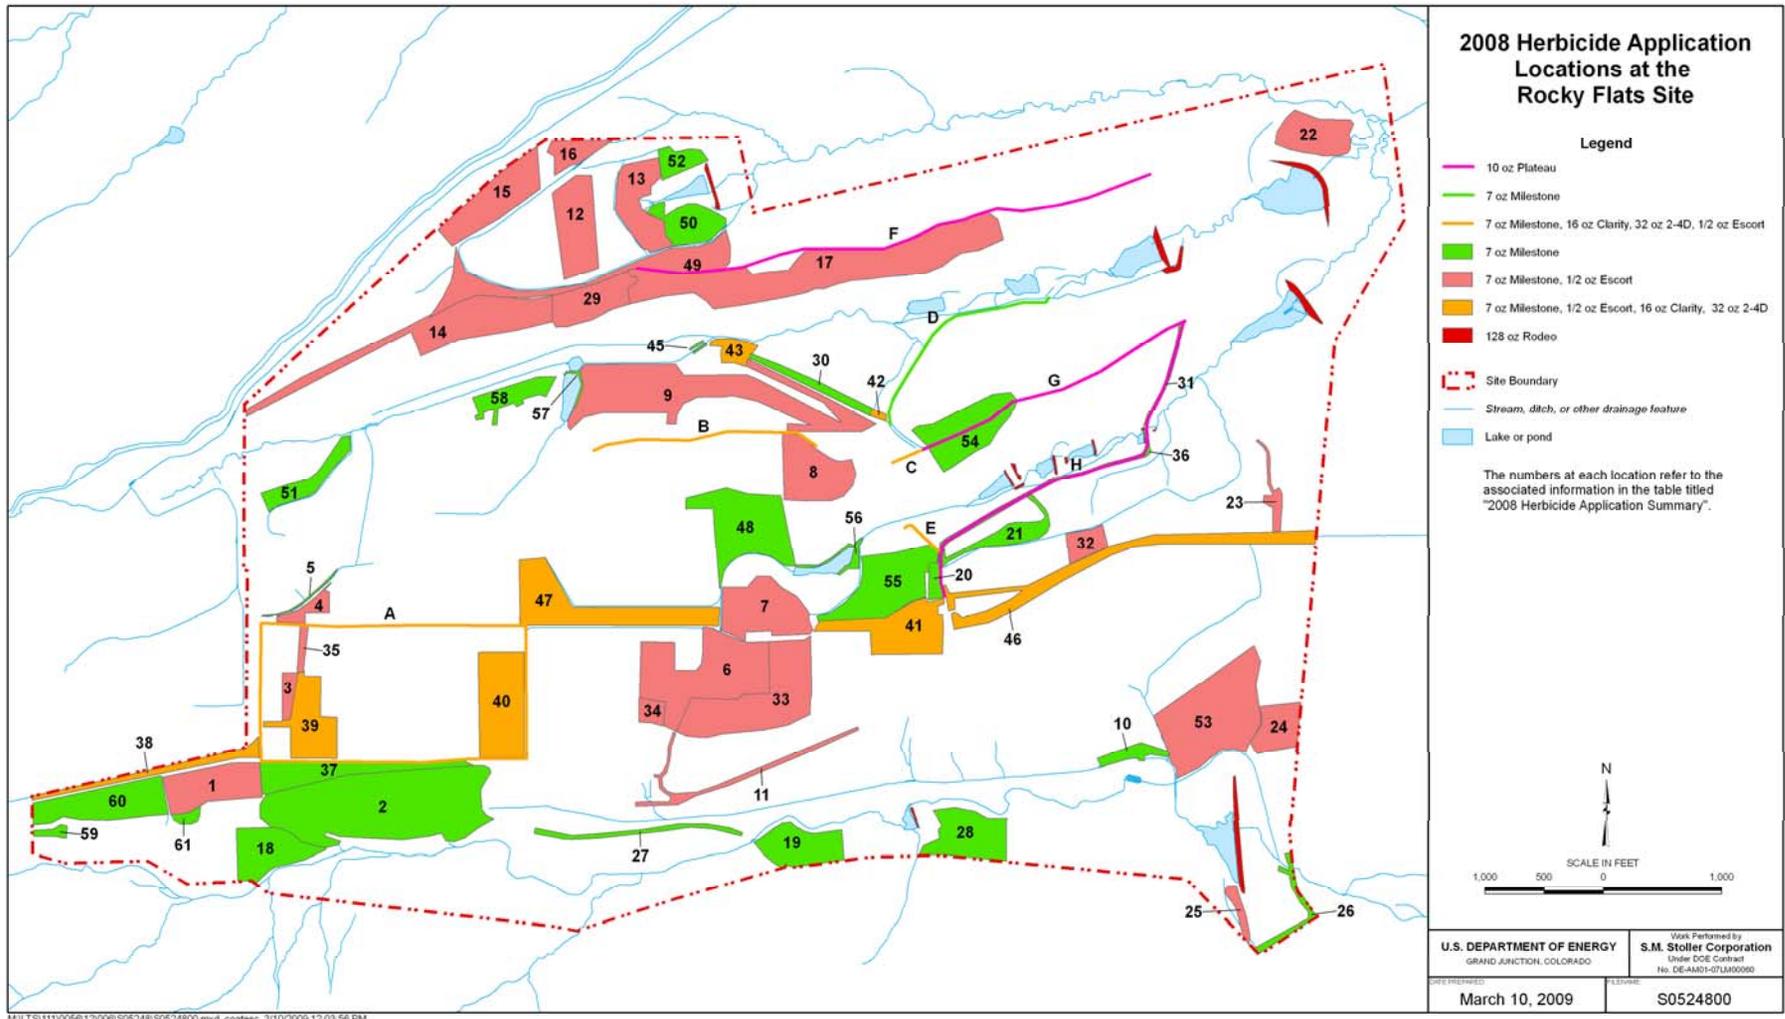

U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Revegetation Activities

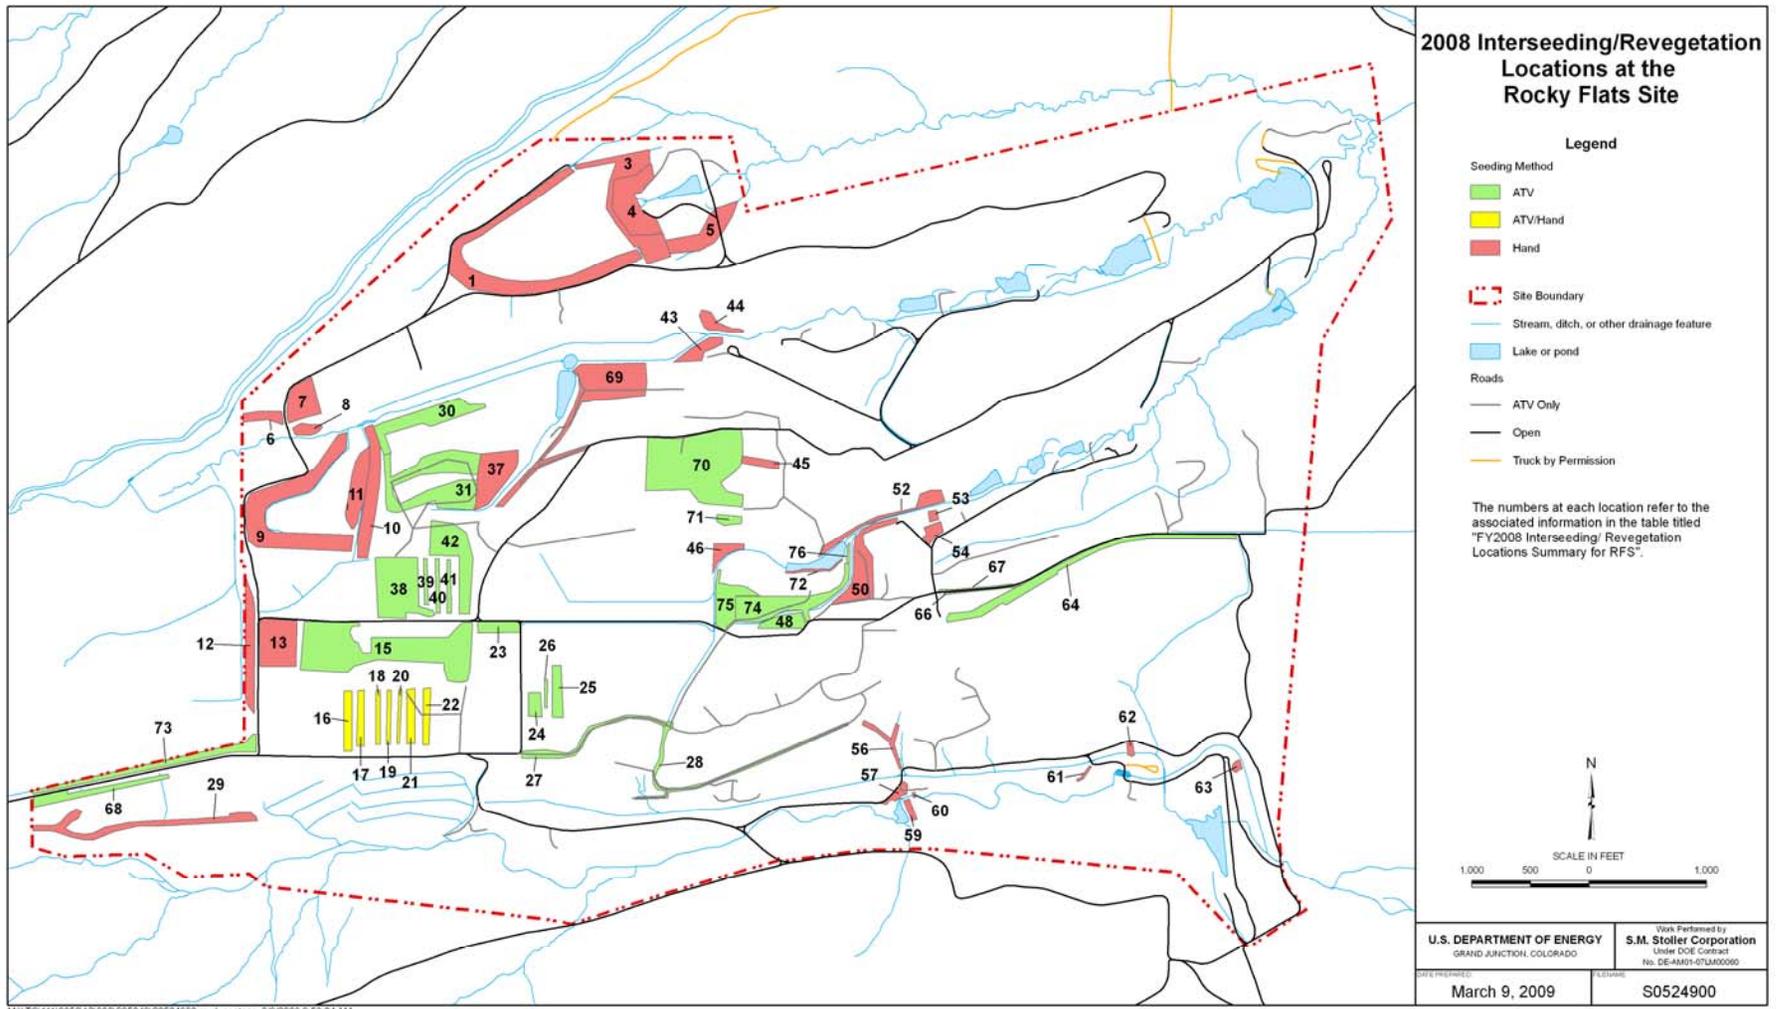

U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

2003



2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

2005



2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

2004




2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

2003

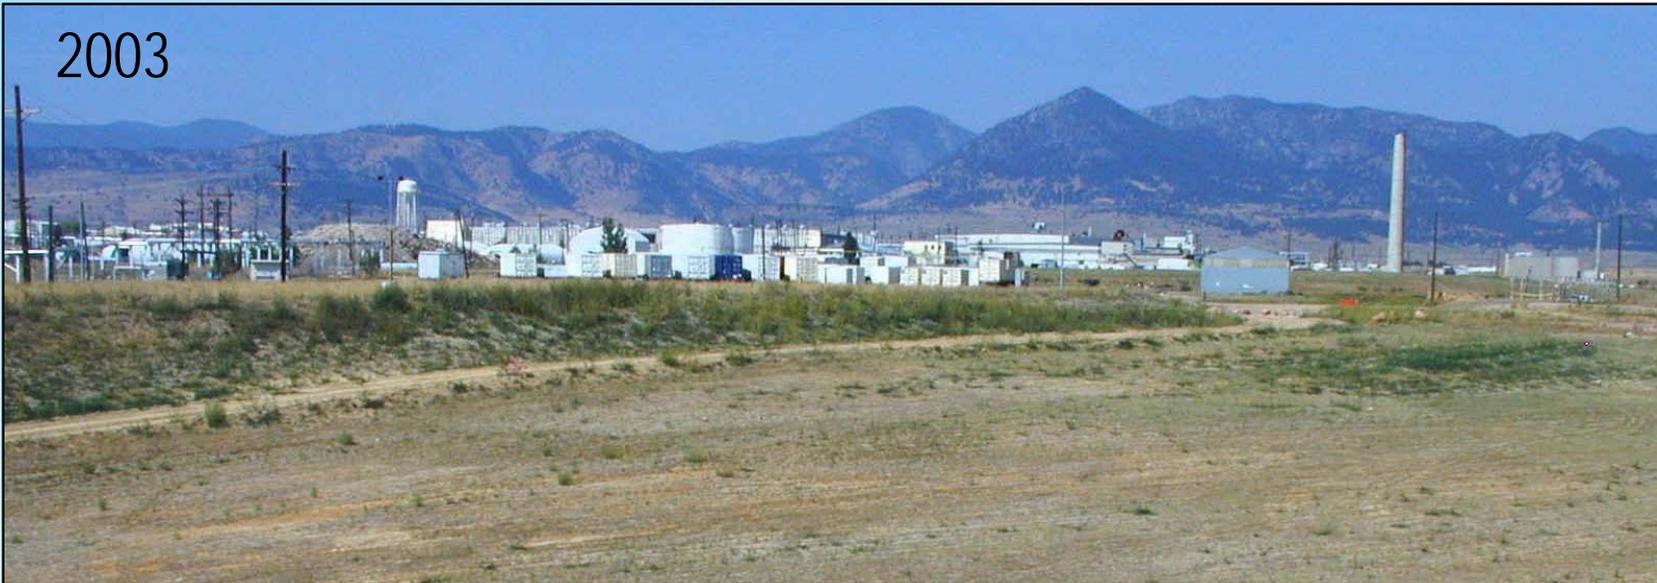

2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management



2005




2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Wildlife Monitoring

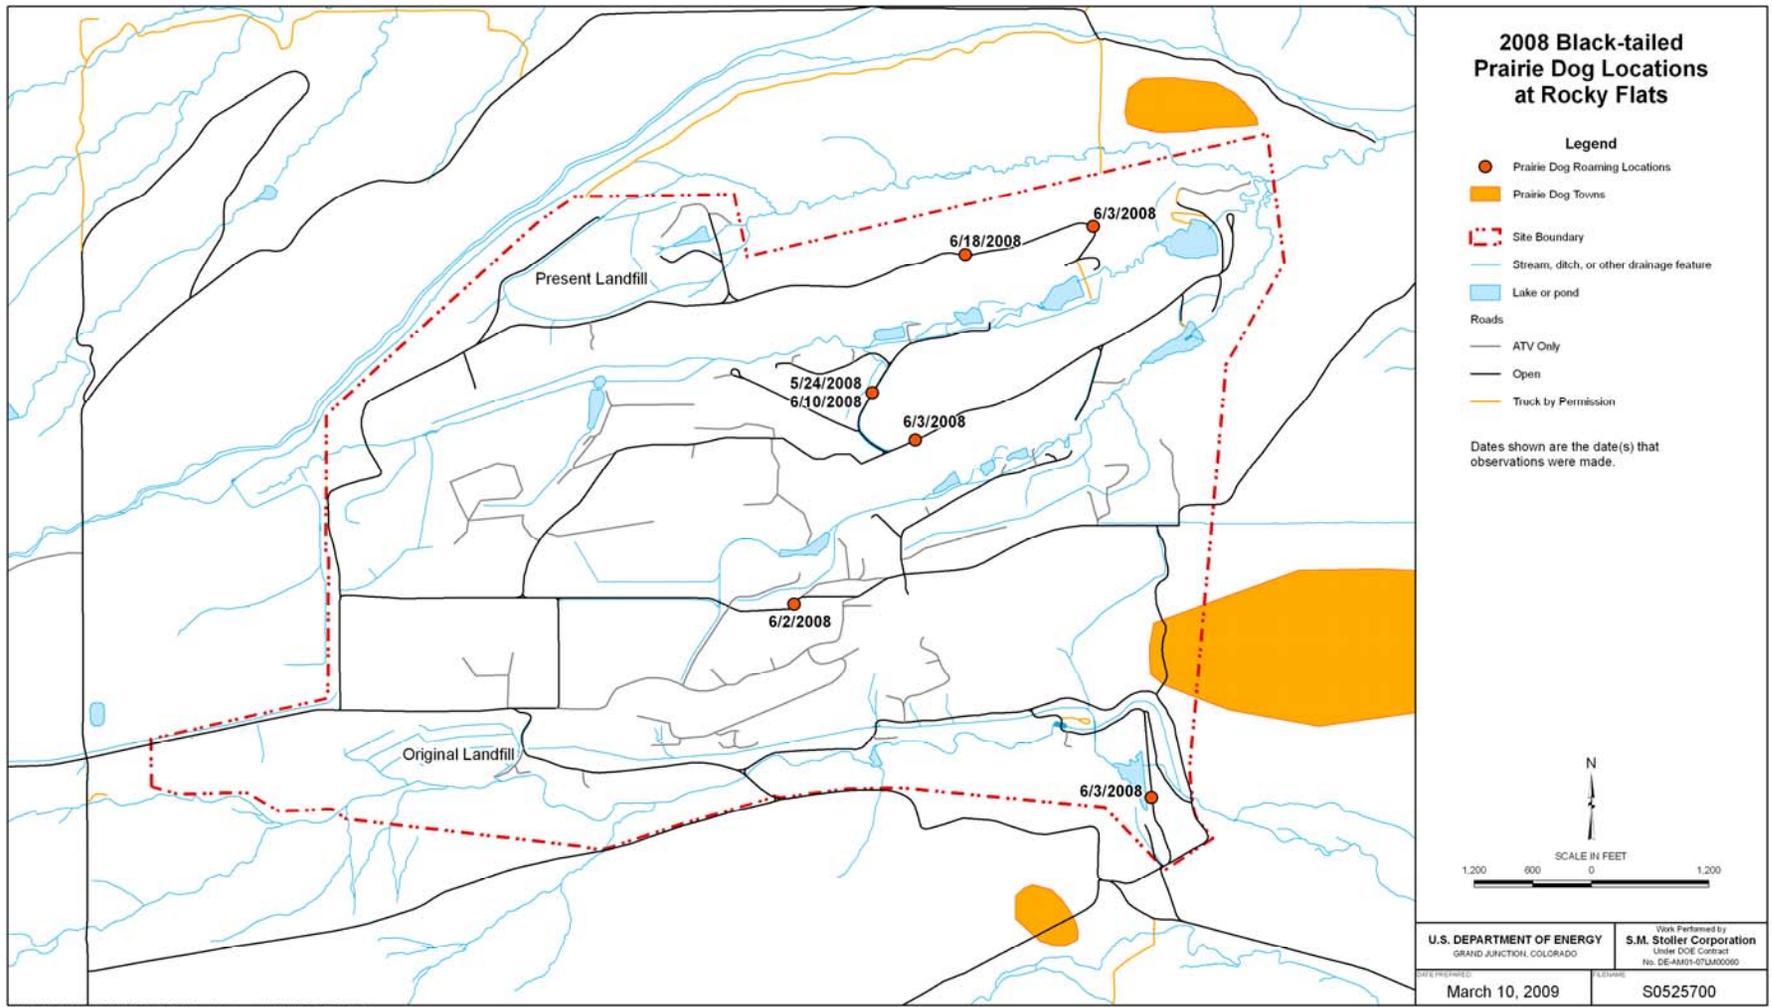

U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Questions?



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Site Operations



Third Quarter 2008



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Site Operations – Third Quarter 2008

Original Landfill – Inspections

Landfill inspections were completed on July 30, 2008, August 25, 2008, and September 30, 2008.

A vegetation inspection was completed on August 8, 2008.



Site Operations – Third Quarter 2008 (continued)

Original Landfill – Seeps

Seep #7 was dry throughout the third quarter.

Seep #4 was saturated during July and August and showed a surface flow of approximately 1 gpm during September.

Seep #8 showed a surface flow of approximately 1–2 gpm throughout the third quarter.



Site Operations – Third Quarter 2008 (continued)

Original Landfill Seep #7 Drain Extension

CDPHE approved the design on September 2, 2008.

The project was started on September 3, 2008, and completed on September 10, 2008.

The Seep #7 drain was extended and tied in with the existing drain.



Site Operations – Third Quarter 2008 (continued)

Original Landfill Seep #7 Drain Extension



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management

Site Operations – Third Quarter 2008 (continued)

- Original Landfill Berm Regrade Project
- Rocky Flats Alluvium was added to the tops of berms to obtain minimum berm height requirements.
- Troughs of berms, where ponding was occurring, were regraded.
- The project was started on September 16, 2008, and finished on September 24, 2008.



Site Operations – Third Quarter 2008 (continued)

- Original Landfill – Settlement Monuments and Inclinometers
- Settlement monument E was installed on September 11, 2008.
- Settlement monuments were surveyed on September 11, 2008; data are within the expected range per the Original Landfill Monitoring and Maintenance Plan.
- Consolidation monitors were removed in July.
- Inclinometers were measured on July 17, 2008, on August 27, 2008, and from September 25, 2008 through September 30, 2008. No significant displacement was observed.



Site Operations – Third Quarter 2008 (continued)

- Present Landfill – Inspections and Surveys
- The quarterly inspection was completed on August 24, 2008.
- The vegetation inspection was completed on August 18, 2008.
- The settlement monument surveys were completed on June 21, 2008.



Questions?



U.S. DEPARTMENT OF
ENERGY

Office of
Legacy Management
