ENGINEERS
AND
CONSTRUCTORS

MORRISON KNUDSEN CORPORATION

MK - FERGUSON GROUP

WELDON SPRING SITE REMEDIAL ACTION PROJECT
7295 HIGHWAY 94 SOUTH
ST. CHARLES, MISSOURI U.S.A. 63304
PHONE: (636) 441-8086

86738

LTSM007967

APRIL 07 2000

U. S. Department of Energy
Weldon Spring Site
Remedial Action Project
ATTN: Mr. Stephen H. McCracken
Project Manager
7295 Highway 94 South
St. Charles, MO 63304

SUBJECT: Contract No. DE-AC05-86OR21548
TRANSMITTAL OF THE POST REMEDIAL ACTION REPORT FOR VICINITY PROPERTY MDC-6

Dear Mr. McCracken:

Attached is a copy of the Post Remedial Action Report for Vicinity Property MDC-6 entitled *Confirmation Results for Vicinity Property MDC-6 (RU12/CU141)* dated May 6, 1999. This report was written in an IOC format due to the extremely small area comprising Remedial Unit 12, which required only two samples. Please forward copies of this IOC to ORISE, ANL, the EPA, and the MDNR.

If you have any questions or need further information, please call Melissa Lutz at extension 3544.

Sincerely,

Douglas E. Steffen
Project Director

DES/ml/lac

Enclosure: as stated

cc: Pamela Thompson

MORRISON KNUDSEN CORPORATION
MK-FERGUSON GROUP

INTER-OFFICE CORRESPONDENCE

86738

DATE: May 6, 1999

TO: Distribution

FROM: Melissa Lutz

SUBJECT: CONFIRMATION RESULTS FOR VICINITY PROPERTY MDC-6 (RU12/CU141)

Confirmation soil samples were collected from Vicinity Property MDC-6 in accordance with the *Confirmation Sampling Plan Details for Vicinity Property MDC No. 6 (DOE/OR/21548-631)*. A summary of the results and associated field activities is presented below. There were no deviations from the sampling plan. Additional information about MDC-6, including characterization results, can be found in the *Close Out Report for Vicinity Properties MDC6 and MDC9 (DOE/OR/21548-775)*.

Vicinity Property MDC-6 was designated as Remedial Unit (RU) 12 and Confirmation Unit (CU) 141. During removal of Quarry bulk waste, MDC-6 was remediated. The initial walkover surveys for this vicinity property were conducted immediately after excavation, but no documentation could be found. Therefore, the gravel was removed in June 1996 and another walkover was conducted. The NaI detector (2x2) background reading was 3,500 CPM and was taken at the Weldon Spring Quarry telephone pole along Highway 94. The readings ranged between 3 to 6 K, with the majority being 3-4K. Walkover results were documented on the Radiation Survey Form.

Once the walkover was completed, the confirmation soil sampling locations were staked by the surveyors according to the sampling plan. Confirmation soil samples were collected at the 2 designated locations as designated in the sampling plan (Doc 631). Final results are summarized in Table 1.

Table 1 Summary of Confirmation Results for RU12 (CU141)

Parameter	Range (pCi/g)	Average (pCi/g)	ALARA GOAL	CLEANUP CRITERIA
Radium-226	1.11 - 1.29	1.2	5.0	6.2
Radium-228	0.43 - 1.05	0.74	5.0	6.2
Total Radium	1.72 - 2.16	1.94	5.0	6.2
Thorium-230	1.10 - 1.76	1.43	5.0	6.2
Uranium-238	All results ND	NA	30	120

ND Non detect NA Not applicable

PAGE 2: CONFIRMATION RESULTS FOR VICINITY PROPERTY MDC-6 (RU12/CU141)

These results met the cleanup standards as detailed in the *Chemical Plant Area Cleanup Attainment Confirmation Plan (DOE/OR/21548-491)*. This CU was released as unrestricted on July 08, 1996. A copy of the disposition form, which includes results and a figure, has been attached.

Quality control samples for confirmation were collected in accordance with the *Attainment Plan*. Although there were no QC samples specifically associated with SC-14101-C and SC-14102-C, QC samples were collected during that week for overall confirmation sampling activities as detailed in the WP-420 Post Remedial Action Reports (*DOE/OR/21548-666*). QC results collected during this period met the DQRs.

ML/jn

Attachments: as stated

ES&H Manager	5/7/99 Date	Data Administration Mgr.	5/7/99 Date
Quarry Project Mgr.	7MAY99 Date	Engineering Manager	5-11-99 Date
Quality Assurance Mgr.	PDC 5/7/99 Date	Deputy Project Director	5/11/99 Date

Distribution:

Dan Hoffman
Randy Thompson
Phil Cate
Marj Wesley
Phil Cate
Steve Warren
Eric Ripp

Weldon Spring Site Remedial Action Project
7295 Highway 94 South, St. Charles, Missouri, 63304

86738

ES&H 1.2.1.1, Rev. 1, 03/96

SOIL CONFIRMATION REMEDIATION DISPOSITION FORM

SECTION I

1. Work Package Number: —
2. Date: 7-2-96
3. Review Form #: 96-023
4. Remediation Unit Number: RU012
5. Confirmation Unit Number: CU141 (map attached)
6. Contaminants of Concern: X U-238 X Th-230 X Th-232 X Ra-226 X Ra-228 ___ TNT ___ PCB ___ PAH ___ As ___ Cr ___ Pb ___ Tl

7. Results average below ALARA goal(s)?	X Yes ___ No
8. All results below cleanup criteria?	X Yes ___ No
9. Any results greater than 3X criteria?	___ Yes X No
10. Hotspots present (less than 3X criteria)?	___ Yes X No

Parameter	Size	Concentration	Complies with Plan?
			___ Yes ___ No
			___ Yes ___ No
N/A			___ Yes ___ No
			___ Yes ___ No

11. Reviewer: Mel H. Lutz Date: 7/2/96

12. Reviewer Disposition Recommendation:
X Release for Unrestricted Use (Section II)
___ Additional Excavation Required (Section IV)
___ ALARA Committee Required (Section III)

SECTION II

Results are ALARA. CU is released for unrestricted use.

14. ES&H Manager: [signature] Date: 7/2/96
15. DOE Project Manager/Engineer: Thomas C. Pauling Date: 7/2/96
16. Project Manager: [signature] Date: 7-2-96
17. Construction Engineer: [signature] Date: 7-8-96

SEE ATTACHED RESULTS AND MAP

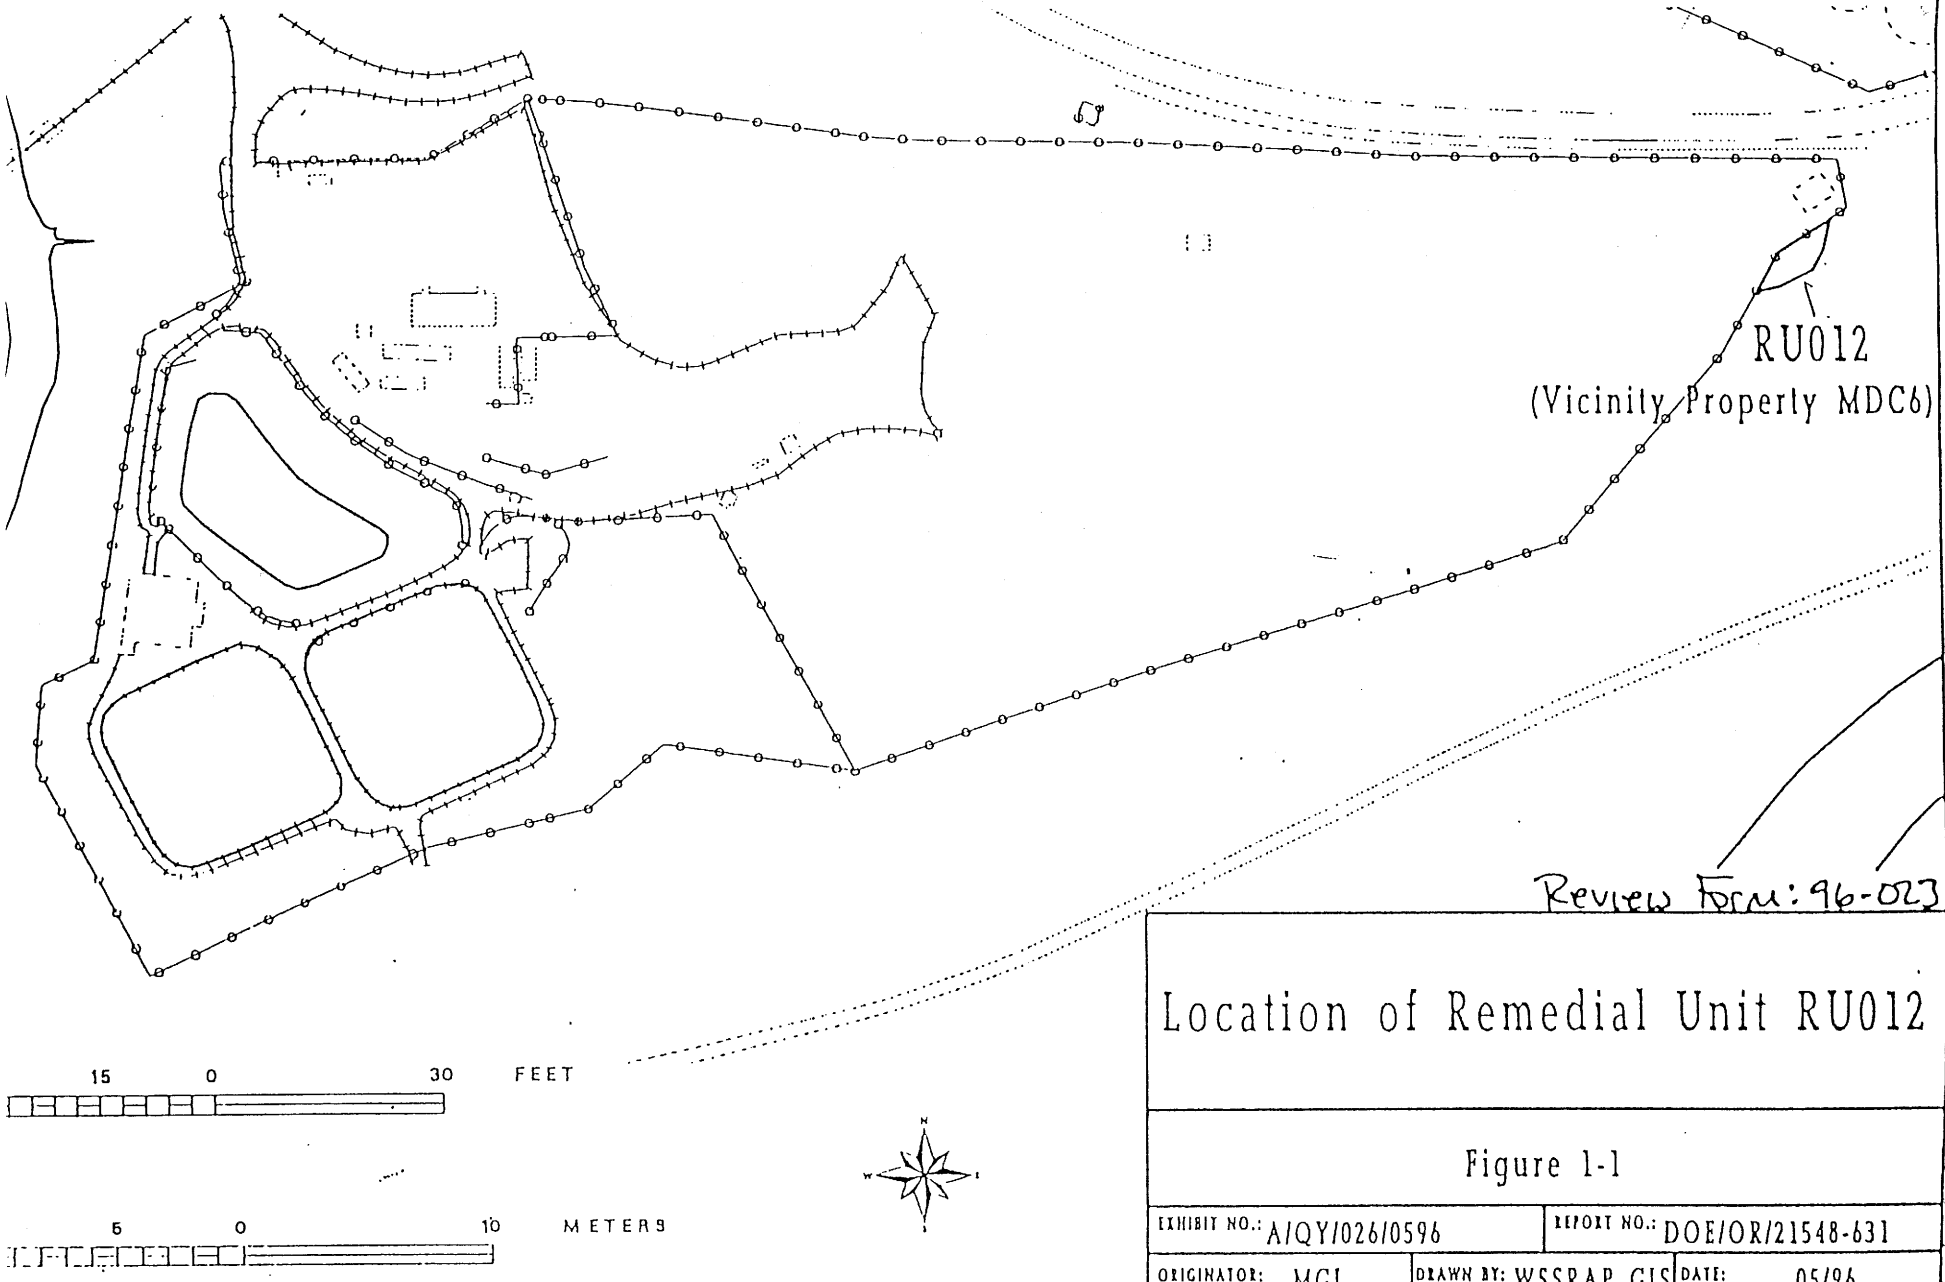

Review Form: 96-023

Location of Remedial Unit RU012

Figure 1-1

EXHIBIT NO.: A/QY/026/0596	REPORT NO.: DOE/OR/21548-631	
ORIGINATOR: MGL	DRAWN BY: WSSRAP GIS	DATE: 05/96

86738

86738

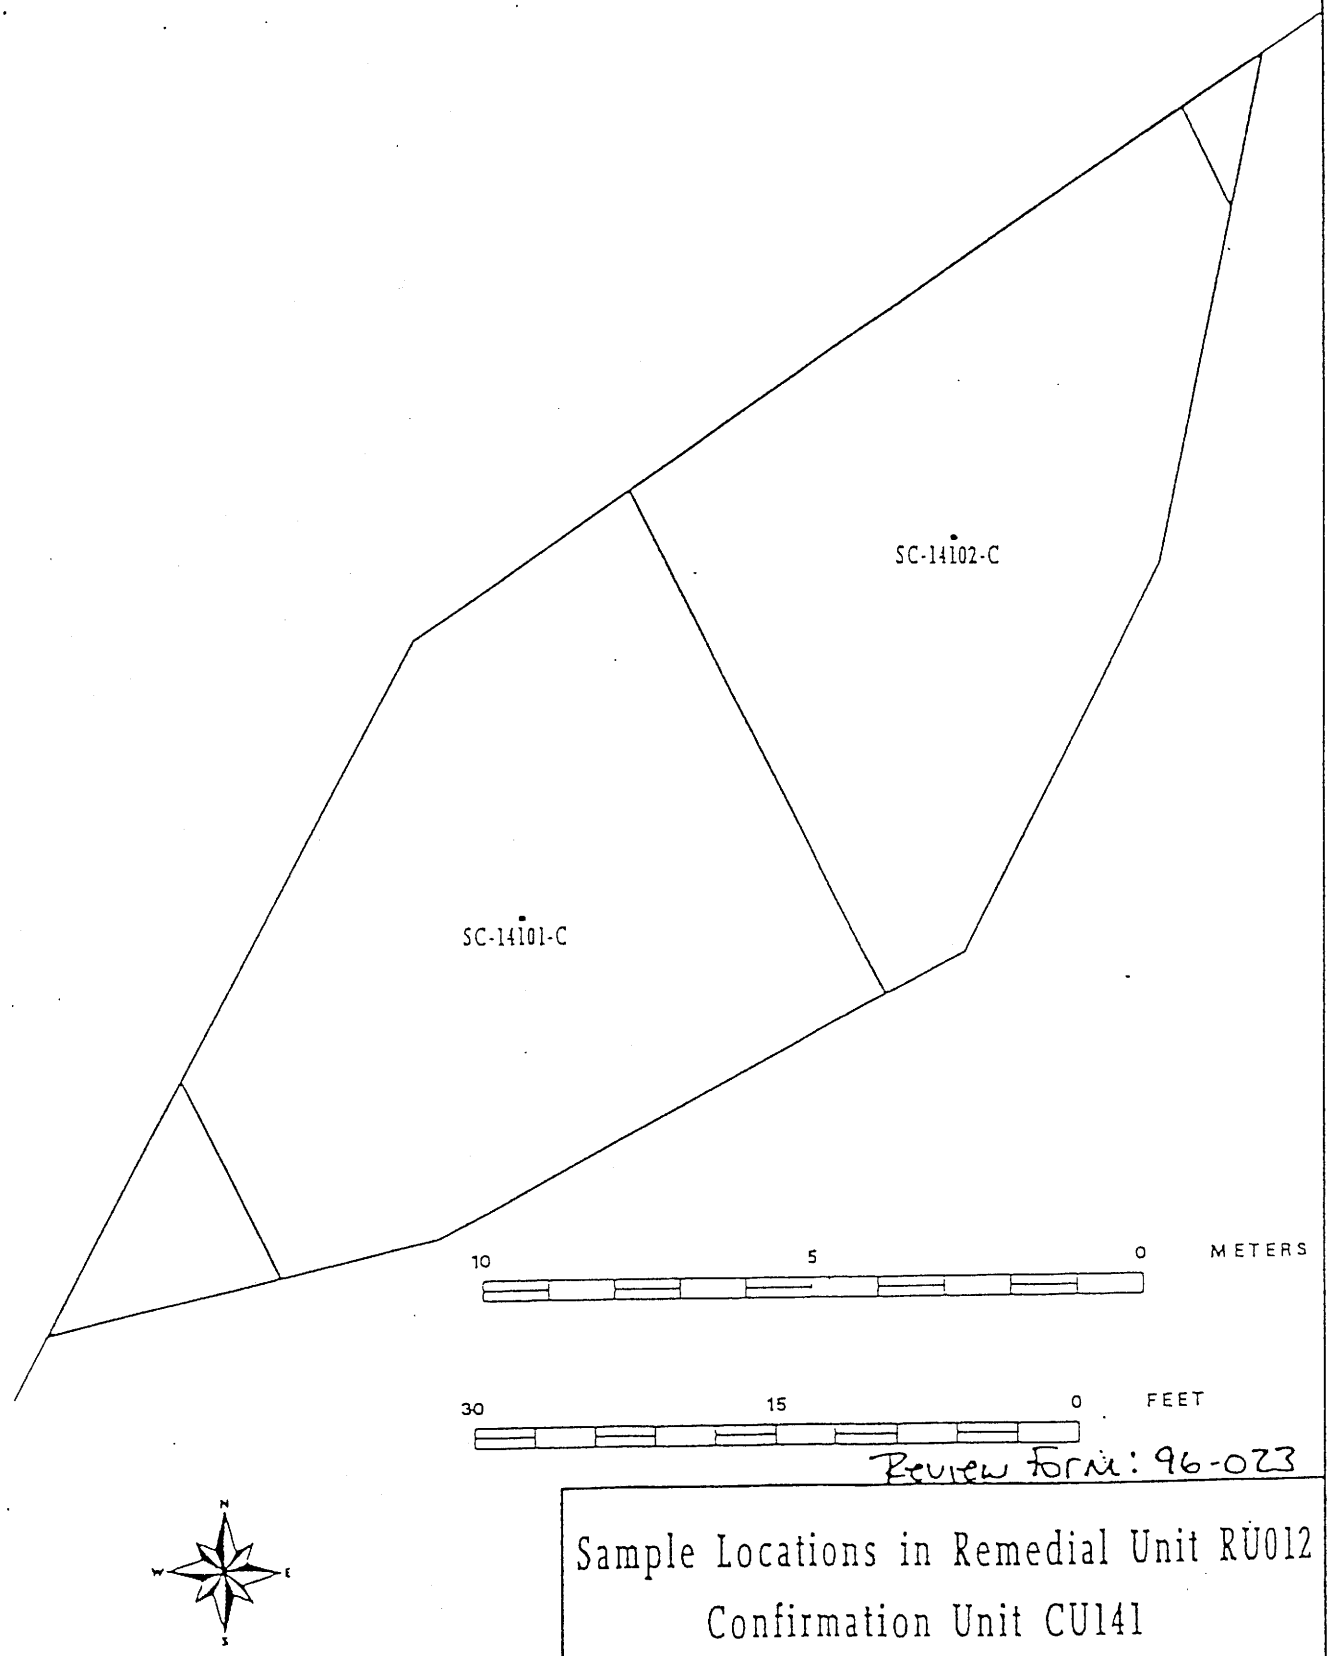

Review form: 96-023

Sample Locations in Remedial Unit RU012
Confirmation Unit CU141

Figure 2-1

EXHIBIT NO.: A/QY/028/0596

REPORT NO.: DOE/OR/21548-631

Confirmation Results for RU012CU141

Location ID	Parameter	Concen	Units	Lab Request
SC-14101-C	Uranium-238	<3.21	pCi/g	WP093
	Radium-226	1.77	pCi/g	WP093
	Radium-228	0.64	pCi/g	WP093
	Thorium-230	1.10	pCi/g	QT1406
	Thorium-232	0.66	pCi/g	WP093
SC-14102-C	Uranium-238	<2.85	pCi/g	WP093
	Radium-226	1.91	pCi/g	WP093
	Radium-228	1.01	pCi/g	WP093
	Thorium-230	1.76	pCi/g	QT1406
	Thorium-232	1.04	pCi/g	WP093

Emi-96-023

REV 45

DOCUMENT CONTROL SYSTEM - CORRESPONDENCE FILE

WELDON SPRING SITE REMEDIAL ACTION PROJECT
MK-FERGUSON CO., INC. WO 3589 (314) 441-8086
7295 Highway 94 South
St. Charles, MO 63304

Document Number: 86738

▸▸Document Type: LR-MKFW-DOEW

Originators DCN:

▸SUBJECT TRANSMITTAL OF THE POST REMEDIAL ACTION REPORT FOR VICINITY PROPERTY MDC-6

▸AUTHOR STEFFEN, DOUGLAS E. ▸▸TO MCCRACKEN, STEPHEN H. ▸▸DATE 4/7/00

▸SUBJECT CODE/WORK PACKAGE NUMBER 0-3010

REFERENCED DOCUMENT(S)

ACTION ITEM TRACKING

INITIATE ACTION ITEM

INDIVIDUAL ASSIGNED TO ACTION DEPARTMENT

ACTION REQUIRED

DUE DATE / / ACTION ITEM LOG NUMBER

CLOSE ACTION ITEM

ACTION ITEM LOG NUMBER INITIATING DOCUMENT DIN

COMPLETION DATE APPROVAL

COMMENTS

DISTRIBUTION	ATTACH W	ATTACH W/O	APPRVL. ROUTE ORDER	INITIAL
D.E. STEFFEN			5	
K.M. GREENWELL				
S.D. WARREN			4	SAW
J. HEITKAMP				
D.K. MURANO				
P.D. CATE				
S.L. HODGES				
W.W. JOHNSON				
G.E. MCKAY				
D.S. HIXSON			2	
M. MITCHELL				
A.D. SISSON				
C.R. SAVAGE				
D.C. WIGTON				
M.L. WESELY				
S.D. ANDERSON				
G.L. VALETT				

DISTRIBUTION	ATTACH W	ATTACH W/O	APPRVL. ROUTE ORDER	INITIAL
DOCUMENT CONTROL:				
CORRESPONDENCE FILE				
WORK PACKAGE FILE				
TECH EDITOR			3	
ORIGINATOR: Lutz	X		1	

DISTRIBUTION	W	W/O
DOE		
S.H. MCCRACKEN		
G.A. NEWTOWN		
P.S. THOMPSON		
J.R. ENRIGHT		
K.A. REED		
T.C. PAULING		
A.D. PICKETT		
PAI		
M.B. BALLEW		
S. RICHARDSON		
Y. DEYO		
W.R. OWEN		
J. MARTIN		
