7221 R-028-204.10

REMOVAL ACTION NUMBER 17 WORK PLAN, REVISION 3, IMPROVED STORAGE OF SOIL AND DEBRIS

10/10/95

DOE-0019-96
DOE-FN EPAS
75
WORK PLAN

Department of Energy
Fernald Environmental Management Project
P. O. Box 398705
Cincinnati, Ohio 45239-8705
(513) 648-3155

OCT 10 1995

DOE-0019-96

Mr. James A. Saric, Remedial Project Director
U.S. Environmental Protection Agency
Region V - 5HRE-8J
77 W. Jackson Blvd.
Chicago, IL 60604-3590

Mr. Tom Schneider, Project Manager
Ohio Environmental Protection Agency
401 East 5th Street
Dayton, OH 45402-2911

Dear Mr. Saric and Mr. Schneider:

REMOVAL ACTION NUMBER 17 WORK PLAN, REVISION 3, IMPROVED STORAGE OF SOIL AND DEBRIS

Enclosed is the subject revision to the Removal Action Number (RA) 17 Work Plan. This document reflects an effort to develop a work plan that is consistent with the approaches being taken in the approved Operable Units (OU) 3 Interim Record of Decision (IROD), 1, 4 and 2, and draft Operable Unit 5 (OU5) Records of Decision (RODs) for the management of soil and debris. It also reflects changes/reduction in scope that had been previously approved by the regulatory agencies to the existing Revision 2 of the RA 17 Work Plan. The two actions that were to be accomplished under the revised scope of Phase II activities of the existing RA 17 Work Plan (the Soil and Rubble Pile North of Third Street and the Scrap Metal Pile Residue/Debris Removal) are described and incorporated into this revision, thereby satisfying the requirement for the final/closeout report for these activities. Finally, a sitewide policy for non-aqueous investigation derived waste is established. This work plan is intended to be an interim measure for managing soil and debris, and will be in effect until the on-property disposal facility is in operation and the appropriate remedial action plans are implemented.

Recycled and Recyclable

The key concepts/assumptions that are addressed in the revised RA 17 Work Plan include:

- Whether soil and debris stockpiles need cover;
- Use of the Corrective Action Management Unit concept from the OU5 Feasibility Study/Proposed Plan and draft ROD;
- Staging/storage criteria based on the final remediation levels (FRLs)/preliminary remediation levels (PRLs) and waste acceptance criteria (WACs); and
- The criteria to determine the amount of sampling and analysis that will be required.

The objectives are to assure that the actions are field-implementable, are protective of human health and the environment and are consistent with the remedial actions that are selected or anticipated, but retain flexibility in the selection of the final design of the remedial actions selected in the RODs.

The overall approach used in preparing Revision 3 to the RA 17 Work Plan was discussed in a meeting with the U.S. Environmental Protection Agency (U.S. EPA) and the Ohio Environmental Protection Agency (OEPA) on May 23, 1995.

If you or your staff have any questions, please contact Pete Yerace at 648-3161.

Sincerely,

Johnny Reising
Fernald Remedial Action
Project Manager

FN:Yerace

Enclosure: As Stated

cc w/enc:

K. Chaney, EM-423/GTN
B. Skokan, EM-243/GTN
G. Jablonowski, USEPA-5, 5HRE-8J
Manager, TSPP/DERR, OEPA-Columbus
L. Parsons, DOE-FN
J. Sattler, DOE-FN
F. Bell, ATSDR
D. Ward, GeoTrans
R. Vandegrift, ODOH
S. McClellan, PRC
R. George, FERMCO/52-2
T. Hagen, FERMCO/65-2
L. Goidell, FERMCO/52-3
AR Coordinator, FERMCO

cc w/o enc:

C. Little, FERMCO
M. Yates, FERMCO

REMOVAL ACTION 17 WORK PLAN
(REVISION NO.3)

SEPTEMBER 1995

FERNALD ENVIRONMENTAL MANAGEMENT PROJECT

FERNALD, OHIO

U.S. DEPARTMENT OF ENERGY

FERNALD FIELD OFFICE

DRAFT

7221

REMOVAL ACTION 17 WORK PLAN
(REVISION NO. 3)

FERNALD ENVIRONMENTAL MANAGEMENT PROJECT

FERNALD, OHIO

SEPTEMBER 1995

U.S DEPARTMENT OF ENERGY
FERNALD AREA OFFICE

DRAFT

000005

7221

TABLE OF CONTENTS

Table of Contents i

List of Appendices iii

List of Tables iii

List of Figures iii

List of Acronyms iv

Executive Summary ES-1

1.0 INTRODUCTION 1-1
- 1.1 PURPOSE 1-1
- 1.2 CONTENT 1-1

2.0 BACKGROUND AND JUSTIFICATION FOR REVISION 2-1
- 2.1 SUMMARY OF PREVIOUS RvA 17 (REVISION NO. 2) ACTIVITIES 2-1
- 2.2 CLOSEOUT OF PHASE II FIELD ACTIVITIES 2-2
  - 2.2.1 Soil and Rubble Pile (SRP) North of Third Street 2-2
  - 2.2.2 Scrap Metal Pile (SMP) Residue/Debris Removal 2-5
- 2.3 RvA 17 REVISION JUSTIFICATION 2-10
- 2.4 REVISED REMOVAL ACTION SCOPE 2-10
  - 2.4.1 Soil Management 2-11
  - 2.4.2 Debris Management 2-11
  - 2.4.3 Sources and Quantification of Soil and Debris 2-13
- 2.5 BACKFILL POLICY 2-13

3.0 INTERIM SOIL MANAGEMENT PLAN 3-1
- 3.1 INTRODUCTION 3-1
- 3.2 SCOPE 3-1
- 3.3 INTEGRATION OF OPERABLE UNIT REQUIREMENTS 3-1
- 3.4 SOIL STAGING CRITERIA 3-2
  - 3.4.1 Location Restrictions for Staging Areas 3-2
  - 3.4.2 Staging Area for On-Site Treatment 3-2
  - 3.4.3 Staging Area for On-Property Disposal 3-2
  - 3.4.4 Staging Areas for Off-Site Disposal 3-2
- 3.5 SUMMARY OF OPERABLE UNIT REMEDIAL ACTIVITIES THAT REQUIRE SOIL STAGING 3-3
- 3.6 SOIL MANAGEMENT 3-4
  - 3.6.1 Soil Stockpiles to be Created During the Interim Period 3-4
  - 3.6.2 Existing Stockpiles 3-5
- 3.7 WASTE MINIMIZATION 3-5

4.0 INTERIM DEBRIS MANAGEMENT PLAN 4-1
- 4.1 INTRODUCTION 4-1
- 4.2 OPERABLE UNIT 3 SCOPE 4-1
- 4.3 DEBRIS DESCRIPTION 4-2

000006

4.3.1 OU3 Debris Categories 4-2
4.3.2 Staging Sub-Categories 4-4
4.4 DEBRIS MANAGEMENT 4-4
4.4.1 Implementing Debris Staging 4-5
4.4.2 Operable Unit 3 Decontamination Activities 4-6
4.4.3 Interim Storage of Debris 4-6
4.4.4 Monitoring/Sampling Issues 4-9

5.0 MATERIAL CHARACTERIZATION 5-1
5.1 OBJECTIVES 5-1
5.2 ANALYTICAL PARAMETERS 5-1
5.2.1 Operable Unit 1 5-2
5.2.2 Operable Unit 2 5-2
5.2.3 Operable Unit 3 5-2
5.2.4 Operable Unit 4 5-3
5.2.5 Operable Unit 5 5-3
5.3 SOIL AND DEBRIS SAMPLING 5-4
5.4 FIELD SCREENING 5-4
5.5 FIELD AND LABORATORY QUALITY ASSURANCE 5-5
5.6 CHAIN-OF-CUSTODY 5-5
5.7 ANALYTICAL METHODS 5-5
5.8 DATA VALIDATION, MANIPULATION, AND MANAGEMENT 5-5

6.0 NON-AQUEOUS IDW MANAGEMENT PLAN 6-1
6.1 BACKGROUND 6-1
6.2 NON-AQUEOUS IDW MANAGEMENT 6-2
6.2.1 RCRA-Hazardous Non-Aqueous IDW 6-2
6.2.2 Soil From Drilling Boreholes and Soil and Debris From Field Sampling 6-3
6.2.3 Waste From Drilling Boreholes and Field Sampling 6-4
6.2.4 Sample Material for Laboratory Analysis 6-4
6.2.5 PPE 6-5
6.2.6 Treatment Technology Testing Waste 6-5

DRAFT

LIST OF TABLES

2-1 Statistical Summary of Data - SRP North of 3rd St. 2-4
4-1 OU3 Debris Categories 4-3
4-2 Debris Segregation Approach 4-6

LIST OF FIGURES

2-1 Photograph of the SRP 2-7
2-2 Photograph of the SMP Prior to Residue/Debris Removal 2-8
2-3 Photograph of the SMP After Residue/Debris Removal 2-10
2-4 Flowchart of General Soil & Debris Management Strategies 2-13
4-1 Material Flowchart for Debris Categories 4-7

LIST OF APPENDICES

Appendix A Operable Unit Milestones/Dates

Appendix B Applicable or Relevant and Appropriate Requirements (ARARs)

Appendix C FEMP Soil Piles and Debris Estimated Quantities

Appendix D Support Documentation

Appendix E Remediation Levels and Waste Acceptance Criteria

DRAFT

LIST OF ACRONYMS

ALARA	As Low As Reasonably Achievable
ARARs	Applicable or Relevant and Appropriate Requirements
AWWT	Advanced Wastewater Treatment
BTVs	biological toxicity values
CAMU	Corrective Action Management Unit
CERCLA	Comprehensive Environmental Response, Compensation, and Liability Act
CFR	Code of Federal Regulations
COC	constituent of concern
D&D	decontamination and dismantlement
DOE	United States Department of Energy
DOE-FN	United States Department of Energy-Fernald Area Office
EPA	Environmental Protection Agency
FEMP	Fernald Environmental Management Project
FRL	final remediation level
FS	Feasibility Study
ft^3	cubic feet
HEPA	high efficiency particulate air
HQ	hazard quotient
IDW	investigation-derived waste
ILCR	incremental lifetime cancer risk
IROD	Record of Decision for Interim Remedial Action; a.k.a., Interim Record of Decision
MCLs	maximum contaminant levels
mg/kg	milligrams per kilogram
NTS	Nevada Test Site
OAC	Ohio Administrative Code
OEPA	Ohio Environmental Protection Agency
PCBs	polychlorinated biphenyls
pCi/g	picoCuries per gram
PPE	personal protective equipment
ppm	parts per million
PRL	preliminary remediation level
QC	Quality Control
RA	Remedial Action
RCRA	Resource Conservation and Recovery Act
RDWP	Remedial Design Work Plan
RI	Remedial Investigation
RI/FS	Remedial Investigation/Feasibility Study
ROD	Record of Decision
RSE	Removal Site Evaluation
RTLs	Regulatory Threshold Levels
RvA	removal action (Note: The "v" is used to differentiate from remedial action (RA) pursuant to a ROD.)
RvA 17	Removal Action No. 17
RvAWP	Removal Action Work Plan
SCQ	Sitewide CERCLA Quality Assurance Program Specific Plan
SMP	Scrap Metal Pile
SRP	Soil and Rubble Pile (North of Third Street)
SWIFTS	Sitewide Waste Information, Forecasting, and Tracking System
TCLP	Toxicity Characteristic Leaching Procedure

DRAFT

TSS	tension support structure
TU	temporary unit
WAC	waste acceptance criteria
U.S.	United States
U.S. EPA	United States Environmental Protection Agency
VOC	Volatile Organic Compounds

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK.

EXECUTIVE SUMMARY

In February 1993, Revision 2 of the Removal Action (RvA) 17 Work Plan, Improved Storage of Soil and Debris, was issued. This plan provided a sitewide management concept and implementation strategy for improved storage and management of excess soil and debris over the period required to design and construct improved storage facilities. Since that time, several events have occurred:

- With the concurrence of the regulatory agencies, DOE has determined that the new storage facilities are not needed.
- The Records of Decision (RODs) for each of the Operable Units have either been issued or are to be issued within the near term.

Because of this, the RvA 17 Work Plan is being revised to:

- Amend current RvA 17 management concepts to be consistent with current Fernald Environmental Management Project (FEMP) response actions, and
- Develop an interim site-wide soil and debris management concept that will integrate implementation of RODs or anticipated RODs and individual remedial action plans, including use of the CAMU Rule.

The objectives of the RvA 17 revised work plan are to identify the practical means of soil and debris management prior to disposal in the on-property disposal facility or at an approved off-site treatment/disposal facility, and to define the necessary means to transfer soil and debris managed under the existing RvA 17 document into the remedial management requirements specified in this document. The intent is to assure these actions are field-implementable and are protective of human health and the environment. In accordance with U.S. Department of Energy (DOE) policy, National Environmental Policy Act (NEPA) values have been incorporated into Sections 3.0 and 4.0 of this work plan.

Under the interim soil management plan being implemented here, efficient soil management practices for the site are being developed while allowing the flexibility to perform remedial actions within the realm of the respective operable unit selected remedy. The goals of the plan are to minimize the total number of soil staging areas for the FEMP by providing an integrated implementation strategy for all operable units, and to set guidelines for management practices for staging/storage facilities, based on regulatory guidelines and protection of health and the environment.

The interim debris management plan addresses the management of construction debris that will be generated mainly from the decontamination and dismantlement activities that may require on-property storage/staging. The projected staging needs were developed based on estimated volumes of materials that will need to be dispositioned upon building dismantlement compared to the schedule for availability of the on-property disposal facility.

The prerequisites for staging locations are addressed in the respective sections of the Interim Soil Management Plan (Section 3.0) and the Interim Debris Management Plan (Section 4.0). The guidelines are based on the final remediation levels (or preliminary remediation levels where final remediation levels are not yet available) contained in the appropriate operable unit RODs and the waste acceptance criteria for the potential receiving facility. Additionally, run-on/run-off control and erosion control needs are identified.

There are two actions that were to be accomplished under Phase II of the existing RvA 17 Work Plan (Revision 2). Summary information for the Soil and Rubble Pile North of Third Street and for the Scrap Metal Pile Residue/Debris Removal is being provided within this work plan to serve as the final report for these RvA 17 field activities; a final report was to have been submitted to the Agencies on December 5, 1995. Incorporating this information into this revision of the RvA 17 Work Plan streamlines the reporting process.

This work plan will be in effect until the on-property disposal facility is in operation and the appropriate remedial action plans are implemented. It is anticipated that the remedial action plans could utilize this work plan as the bases for soil and debris management actions.

DRAFT

7221

1.0 INTRODUCTION

1.1 PURPOSE

The purposes of the *Revised* Removal Action No. 17 (RvA 17) Work Plan (Revision No. 3) are to:

- Provide for the interim management of debris and like material generated before the establishment of approved remedial design documentation that will otherwise address this issue.
- Provide for ongoing management of existing soil piles prior to their ultimate disposition as provided for in the Operable Unit 5 Remedial Design.
- Provide for interim management of any soil or soil-like material to be generated before the establishment of approved remedial design documentation that will otherwise address this issue.
- Establish a comprehensive policy for management of solid investigation-derived waste.
- Satisfy reporting requirements related to activities already completed under Removal Action 17.

Per the above, this document is an interim measure to manage soil and debris between the approval of this revised Work Plan and the time that approved design documentation issued pursuant to an operable unit ROD is established which otherwise addresses a related issue. A schedule of operable unit Final RODs and associated Remedial Design and Remedial Action Work Plan(s) has been provided as Appendix A. In accordance with DOE policy, NEPA values have been incorporated into Sections 3.0 and 4.0 of this Work Plan.

It is important to note that the need for soil and debris management areas (e.g., stockpiles, staging areas) during remedial activities will be kept to a minimum as remedial activities will be sequenced such that direct placement (in the on-property disposal facility) or shipment (off-site) will be performed to the extent possible. Again, the main function of this Revised Work Plan is to guide the management of soil and debris occurring during construction and prior to operation of the on-property disposal facility and/or remedial transportation activities (i.e., transportation of remedial action-generated waste to an off-site disposal facility).

1.2 CONTENT

This removal action work plan is structured as follows:

DRAFT

- Section 2.0 provides background information about previous RvA 17 activities (including final reports for previous RvA17 activities), justification for revisions to the current RvA 17 Work Plan (Revision No. 2, February 1993) and the scope of this *Revised* Work Plan, and general soil and debris management concepts.

- Section 3.0 discusses the general management strategy for soils while addressing contaminant and category determinations. Additionally, Section 3.0 addresses the management of existing stockpiles.

- Section 4.0 discusses general debris management.

- Section 5.0 presents an overview of the sampling and analysis requirements to determine if soil piles and debris meet waste acceptance criteria (WAC) and/or FRLs.

- Section 6.0 discusses the management of non-aqueous Investigation-Derived Waste (IDW).

- Appendix A presents Final ROD milestones and associated Remedial Design and Remedial Action Work Plan(s) schedules.

- Appendix B includes a table of the ARARs. This appendix also includes a general statement regarding permitting requirements (i.e., crosswalks within operable unit Remedial Design or Remedial Action Work Plans).

- Appendix C contains estimated quantities of soil piles and debris.

- Appendix D contains support and reference documentation.

- Appendix E contains the final remediation levels for soil and the waste acceptance criteria for the on-property disposal facility.

DRAFT

7221

2.0 BACKGROUND AND JUSTIFICATION FOR REVISION

2.1 SUMMARY OF PREVIOUS RvA 17 (REVISION NO. 2) ACTIVITIES

The current version (Revision No. 2) of RvA 17 is divided into two phases. Phase I addresses soil and debris management from the conceptual design of improved storage facilities through construction of these facilities. Phase II addresses soil and debris management from the time the construction of these facilities is completed until the selection of operable unit final remedial alternatives or selected remedies.

None of the improved storage structures, scoped as a part of RvA 17, have been constructed at the FEMP to date. As a result (and in accordance with the RvA 17 Work Plan, Revision No. 2), all excess soil and debris generated since the inception of RvA 17 have been managed in accordance with the policies established in Phase I of the RvA 17 Work Plan, Revision No. 2. A summary of Phase I methodologies as presented in the RvA 17 Work Plan, Revision No. 2, is located in Appendix D.

As anticipated, most of the excess material managed under Phase I management policies of RvA 17 has been radiologically contaminated soil. Only a small amount of debris and excess soil containing hazardous material has required Phase I management policies.

As a result of the evolving soil and debris management policy at the FEMP and through discussions and written correspondence between the DOE and the U.S. and Ohio Environmental Protection Agency (Ohio EPA) [see "Proposed Actions for RvA 17" letter dated November 18, 1994 in Appendix D], the U.S. and Ohio EPAs concurred with the FEMP proposal to revise the scope of the RvA 17 Work Plan (Revision No. 2) to exclude construction of three tension support structures (TSSs) (see letter, HRE-8J, dated January 4, 1995 in Appendix D). A summary of the scope changes approved January 4, 1995 is provided below:

- Delete construction of two (2) improved storage structures or TSSs; namely the scrap metal pile (SMP) structure and the decontamination facility pad structure;
- Defer construction of the Central Storage Facility and evaluate its need as new soil and debris management strategies evolve and waste acceptance criteria for on-property disposal are established;
- Complete remaining field actions in the RvA 17 scope which include regrading and seeding (including runon/runoff controls) the Soil and Rubble Pile (SRP) North of Third Street (SRP) and the removal of the residues/debris remaining in the former SMP area;

DRAFT

- Revise milestone date for the completion of the above two field actions from May 31, 1995 to August 31, 1995; and

- Continue utilizing Phase I methodologies for soil and debris management (e.g., utilizing improved storage facilities as they become available) until further details regarding on-property disposal are known.

Due to the exclusion of construction of the three (3) new improved storage structures, or TSSs, most Phase II activities of the RvA 17 Work Plan, Revision No. 2 (e.g., placement of soil and debris into improved storage facilities) could no longer be implemented as presented in the Work Plan. However, two of the field actions, as indicated in the third bullet above, were a part of the original Phase II activities and have been implemented.

2.2 CLOSEOUT OF PHASE II FIELD ACTIVITIES

The following information summarizes the two field actions performed as part of the Phase II field activities scope identified in Revision No. 2. This summary information is being provided within this revision (No. 3) of the RvA 17 Work Plan to serve as the final report and close-out for the two RvA 17 field activities discussed below. According to Revision No. 2 of the RvA 17 Work Plan, a final report was to be submitted to the U.S. and Ohio EPA on December 5, 1995. As a result of discussions and a meeting held with the DOE and the EPAs on May 23, 1995, the closeout information is incorporated into this revision (No. 3) of the RvA 17 Work Plan, thus streamlining the reporting process.

2.2.1 Soil and Rubble Pile (SRP) North of Third Street

The SRP is located in the northwest corner of the FEMP former production area and consists of approximately 23,000 cubic yards of material primarily consisting of uncompacted soil and construction debris rubble. The pile, which served as a construction soil and rubble staging/stockpile area for nonhazardous, radiologically-contaminated soil and debris (including large slabs and blocks of concrete, piping, and rock from the Laboratory Upgrade, Rotary Kiln, Drum Reconditioner, Tank Farm, Derby Breakout Milling Slag, and Plant 1 Pad Extension projects), was vulnerable to water and wind erosion. Following completion of a Removal Site Evaluation on June 18, 1990, the DOE issued an Action Memorandum stating the need for a removal action and an evaluation of proposed methods to mitigate any release of contamination from the pile.

Originally, a TSS was proposed as the management strategy for the SRP, based on the assumption that portions of the pile were radiologically-contaminated and periodic access to portions of the pile would

be necessary. In October 1992, however, the pile was secured with a fence to discontinue acceptance of material and to control access. Because of the large increase in size of the pile from previous years, a letter addendum to Revision No. 2 of the Removal Action 17 Work Plan (see Appendix D, letter dated November 23, 1993) was submitted to the EPAs. The addendum proposed that a TSS should not be constructed and that selection of the best management option should be based on analytical results from sampling the pile.

Results from previous sampling and analyses and process knowledge indicated that the SRP contained no hazardous waste and was below the existing Removal Action 17 radiological disposition limits for a controlled stockpile. Additional sampling and analysis was conducted to determine the nature and extent of the contamination contained within the pile; forty-two (42) samples were collected. A 95-percent confidence level was used to determine whether the sample mean of each constituent exceeded the regulatory threshold or disposition limit. Regulatory Threshold Levels (RTLs) for non-radiological constituents were taken from the Ohio Administrative Code 3745-51-24, Table 1. RTLs for radiological constituents were taken from the approved Work Plan. A statistical summary of data is presented in Table 2-1.

Based on the data summarized below in Table 2-1, the following conclusions were made:

- The stockpile waste materials are nonhazardous based on statistical analysis and evaluation of toxicity characteristic leaching procedure (TCLP) and total concentration analytical data;
- The levels of radiological activity concentrations for uranium, thorium, and radium are significantly below the prescribed threshold levels established in the Work Plan for RvA 17, Revision No. 2; and
- TCLP selenium and lead results indicate that additional samples are not required.

The above conclusions are supported by the Sitewide Characterization Report (1993) indicating that the pile does not contain Resource Conservation and Recovery Act (RCRA) regulated hazardous waste and the radiological activity concentration levels are below the RvA 17 (Revision 2) management policy limits of 100 pCi/g total uranium, 5 pCi/g total radium, and 50 pCi/g total thorium. Therefore, the SRP satisfied the controlled stockpile criteria and an engineered impermeable cover (TSS or tarped fabric) would not be required. A proposal was then submitted to the U.S. and Ohio EPAs for the pile to be regraded, removing accessible and exposed debris and rubble, and seeded to form a vegetative cover that would be maintained until the pile contents were remediated under the OU5 ROD (for the soils) and the

TABLE 2-1 STATISTICAL SUMMARY OF DATA - SRP NORTH OF 3RD ST.

Analyte (Units)	RTL*	Number of Samples	Mean	Standard Deviation	Sample Variance	Standard Error	Upper Limit of CI (95%)
TCLP Metals - Actual + Derived							
Arsenic (mg/L)	5	41	0.1992	0.2300	0.0529	0.0359	0.2597
Barium (mg/L)	100	41	2.3364	1.8404	3.3869	0.2874	2.8204
Cadmium (mg/L)	1	41	0.0229	0.0157	0.0002	0.0024	0.0270
Chromium (mg/L)	5	41	0.4506	0.3467	0.1202	0.0541	0.5417
Lead (mg/L)	5	41	0.6392	1.0444	1.0908	0.1631	0.9138
Mercury (mg/L)	0.2	41	0.0066	0.0150	0.0002	0.0023	0.0106
Selenium (mg/L)	1	41	0.0923	0.1206	0.0146	0.0198	0.1240
Silver (mg/L)	5	41	0.0637	0.1028	0.0106	0.0161	0.0908
Transformed Actual + Derived							
Barium (mg/L) arcsine transformation	0.0001	41	1.992 E-7	6.03 E-8	3.634 E-15	9.4 E-9	2.151 E-7
Lead (mg/L) arcsine transformation	0.000005	41	6.392 E-7	7.11 E-8	5.06 E-15	1.11 E-8	6.579 E-7
Total Metals							
Arsenic (mg/kg)	100	31	5.1356	4.7476	22.5398	0.8527	6.5827
Barium (mg/kg)	2000	31	58.9561	34.0661	1160.4995	6.1185	69.3391
Cadmium (mg/kg)	20	31	0.5894	0.2401	0.0577	0.0431	0.6625
Chromium (mg/kg)	100	31	11.8863	5.3972	29.1297	0.9694	13.5313
Lead (mg/kg)	100	26	27.3296	40.0192	1601.5372	7.8484	40.7347
Mercury (mg/kg)	4	31	0.1748	0.3361	0.1130	0.0604	0.2773
Selenium (mg/kg)	20	31	7.0274	25.5078	650.6453	4.5813	14.8019
Silver (mg/kg)	100	31	1.0694	0.2690	0.0724	0.0483	1.1513
TCLP Metals - Actual Only							
Arsenic (mg/L)	5	10	0.0209	0.0236	0.0006	0.0075	0.0345
Barium (mg/L)	100	10	0.4402	0.3131	0.0980	0.0990	0.6217
Cadmium (mg/L)	1	10	0.0025	0.0000	0.0000	0.0000	0.0025
Chromium (mg/L)	5	10	0.0053	0.0018	0.0000	0.0006	0.0063
Lead (mg/L)	5	16	0.0045	0.0068	0.0000	0.0017	0.0075
Mercury (mg/L)	0.2	10	0.0001	0.0001	0.0000	0.0000	0.0002
Selenium (mg/L)	1	11	0.0074	0.0109	0.0001	0.0033	0.0134
Silver (mg/L)	5	10	0.0055	0.0017	0.0000	0.0005	0.0065
TCLP Volatile Organics							
MEK (mg/L)	200	41	0.1512	0.0412	0.0017	0.0064	0.1620
Tetrachloroethylene (mg/L)	0.7	41	0.0314	0.0130	0.0002	0.0020	0.0348
Radiological							
Total U (ppm dry)		39	43.2308	43.9091	1928.0108	7.0311	55.0894
Total U (pCi/g dry)	100	39	29.2100	29.6683	980.2092	4.7507	37.2226
U-234 (pCi/g dry)		38	14.3038	14.2849	204.0593	2.3173	18.2152
U-235 (pCi/g dry)		38	0.7477	0.7119	0.5068	0.1155	0.9426
U-236 (pCi/g dry)		39	0.2568	0.3631	0.1318	0.0581	0.3548
U-238 (pCi/g dry)		39	17.5590	19.6003	384.1698	2.3186	22.8525
Total Th (ppm dry)		39	11.4872	10.6891	114.2564	1.7116	14.3740
Total Th (pCi/g dry)	50	41	5.4685	2.8711	8.2433	0.4484	6.2236
Th-228 (pCi/g dry)		41	1.5578	0.5058	0.2558	0.0790	1.6908
Th-230 (pCi/g dry)		41	2.6939	2.7779	7.7169	0.4338	3.4245
Th-232 (pCi/g dry)		40	1.2473	0.4566	0.2085	0.0722	1.3689
Total Ra (pCi/g dry)	5	39	1.3897	0.8613	0.7418	0.1379	1.6224
Ra-226 (pCi/g dry)		39	0.9679	0.8655	0.7491	0.1386	1.2017
Ra-228 (pCi/g dry)		39	0.4218	0.1872	0.0350	0.0300	0.4723
Alpha Activity (pCi/g)		41	28.8207	28.6516	820.9150	4.4746	36.3560
Beta Activity (pCi/g)		41	25.6829	26.2410	688.5876	4.0981	32.5842

* Regulatory Threshold Levels (RTLs) for non-radiological constituents were taken from Table 1 of Chapter 3745-51-24 of the Ohio Administrative Code. RTLs for radiological constituents were taken from Removal Action 17, Improved Storage of Soil and Debris.

OU3 ROD (for the debris). The regrading of the pile slopes and vegetative cover reduced the vulnerability of the pile to wind and water erosion. In a January 14, 1994 letter (Appendix D), the U.S. EPA approved the vegetative cover approach and emphasized that the pile material was not to be used as backfill.

The SRP has been regraded and seeded with a vegetative cover to prevent erosion and to mitigate airborne migration of soil. A concrete curb and gutter berm has been constructed around the pile that prevents water from running onto the pile (run-on) and ensures that precipitation (run-off) flows through the gutter trench system to the controlled stockpile storm catch basins (see Figure 2-1 for a photograph of the SRP). The berm begins in the southwest corner, encloses the dirt pile on three sides, and ends in the southeast corner. Run-off from the south edge of the pile flows into existing catch basins which flow directly to the FEMP stormwater retention basin.

The drainage control systems were designed to accommodate a minimum of a 25-year, 24-hour storm event. A chain-linked fence was reinstalled around the perimeter of the pile to control access. All field construction activities for the SRP were completed on May 18, 1995. This pile will be managed similar to a controlled stockpile as defined according to the RvA 17 (Revision 2) Work Plan with the exception that no soil will be removed from or added to this pile. This exception (to not use the SRP material for backfill) is being implemented in order to comply with the U.S. and Ohio EPA's conditional acceptance of the vegetative cover approach. Furthermore, not adding or removing material from this pile will preserve the vegetative and grass cover over this soil pile.

2.2.2 Scrap Metal Pile (SMP) Residue/Debris Removal

The SMP at the FEMP had been used for storage of contaminated scrap metal awaiting decontamination/disposal. It is located in the northeastern part of the FEMP former process area and is adjacent Building 69. A photograph of the SMP, prior to the residue/debris removal, has been included in Figure 2-2). The pile of scrap metal was removed from the concrete pad and recycled in 1993 as part of RvA 15.

Residues and small debris had remained from the former SMP on portions of the Building 69 outdoor pad. The removal and containerization of this remaining material was to be a part of initial activities conducted in order to construct the new SMP TSS. Although the SMP TSS was deleted from the scope of RvA 17, it was determined that the remaining residues should be removed as part of the

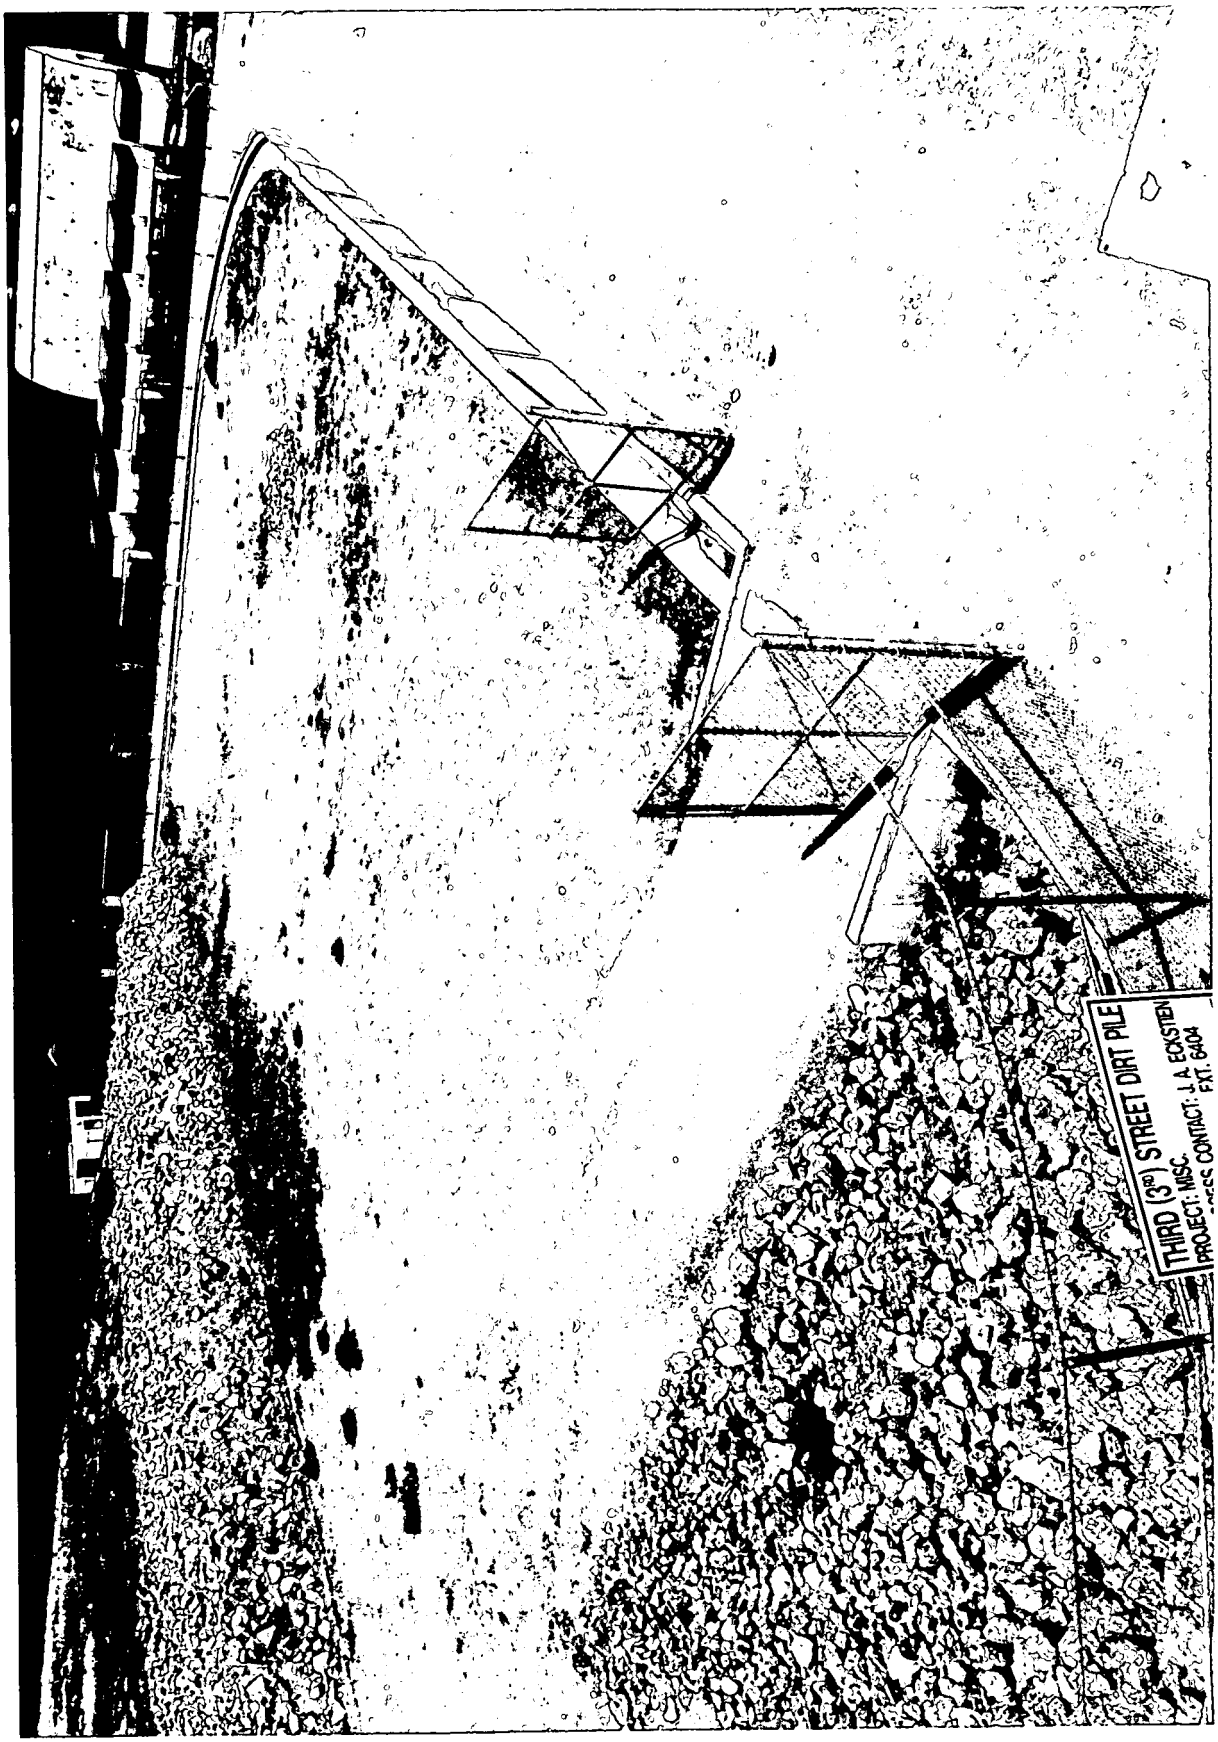

FIGURE 2-1 PHOTOGRAPH OF THE SRP

FIGURE 2-2 PHOTOGRAPH OF SMP PRIOR TO RESIDUE/DEBRIS REMOVAL

RvA 17 scope to mitigate the potential for airborne radiological contamination release and clear this pad area for possible future staging.

The residue and debris material was composed of soil, rust, small metal fragments/residue, asphalt chunks, and reinforcing steel pieces (most less than two inches long). Because of the fine particle size of some of this material, it presented a potential for airborne radiological contamination, although none of the existing air monitoring stations within this area had indicated an increased airborne activity. The suspected contaminants, reflected in the original sampling and analysis request, were: uranium, thorium, and their associated isotopes; heavy metals; Volatile Organic Compounds (VOCs), semi-VOCs, and PCBs. The analytical data from this sampling effort indicated that the debris and residue are nonhazardous. A material evaluation form (MEF) No. 2384 has been completed for the material and is part of the documentation that is now maintained with the small white metal containers in which the material is stored.

Residue and debris removed from the area (approximately 200 feet by 112 feet) filled 115 small white metal boxes (approximately 3 ft. x 4 ft. high x 6 ft. long). The equipment used to remove the residue and debris included a front-end loader, a Bobcat (small front-end loader for filling boxes), forklifts, high efficiency particulate air (HEPA) wet/dry vacuums, personal protective equipment (PPE), poly film, tarps. Barricade fencing and radiological contamination/caution signs were utilized at the east edge of the work area around the decontamination pad to segregate the construction/removal work area from the ongoing decontamination operations work area adjacent to Building 69. Any dust-like residues were kept damp to minimize radiological airborne contamination. HEPA-filtered vacuum systems were also used to remove the fine residue. High-pressure washers (using biodegradable detergent) were used to wash the pad once the bulk of the material was removed. Wet vacuums and squeegees were used to control runoff. Wash water and rinseate was controlled and directed into the sump drain located at the southeast corner of the pad. This sump drain is tied into an existing dedicated decontamination rinse water system that is piped to the FEMP's wastewater treatment system.

Removal and containerization of this residue and debris was completed on August 4, 1995. A photograph of the cleaned pad is shown in Figure 2-3. The containers filled with this material have been placed in storage on the Plant 1 pad until final disposition (on-property cell or offsite shipment to NTS) is determined, via the OU3 Final ROD, and implemented.

DRAFT

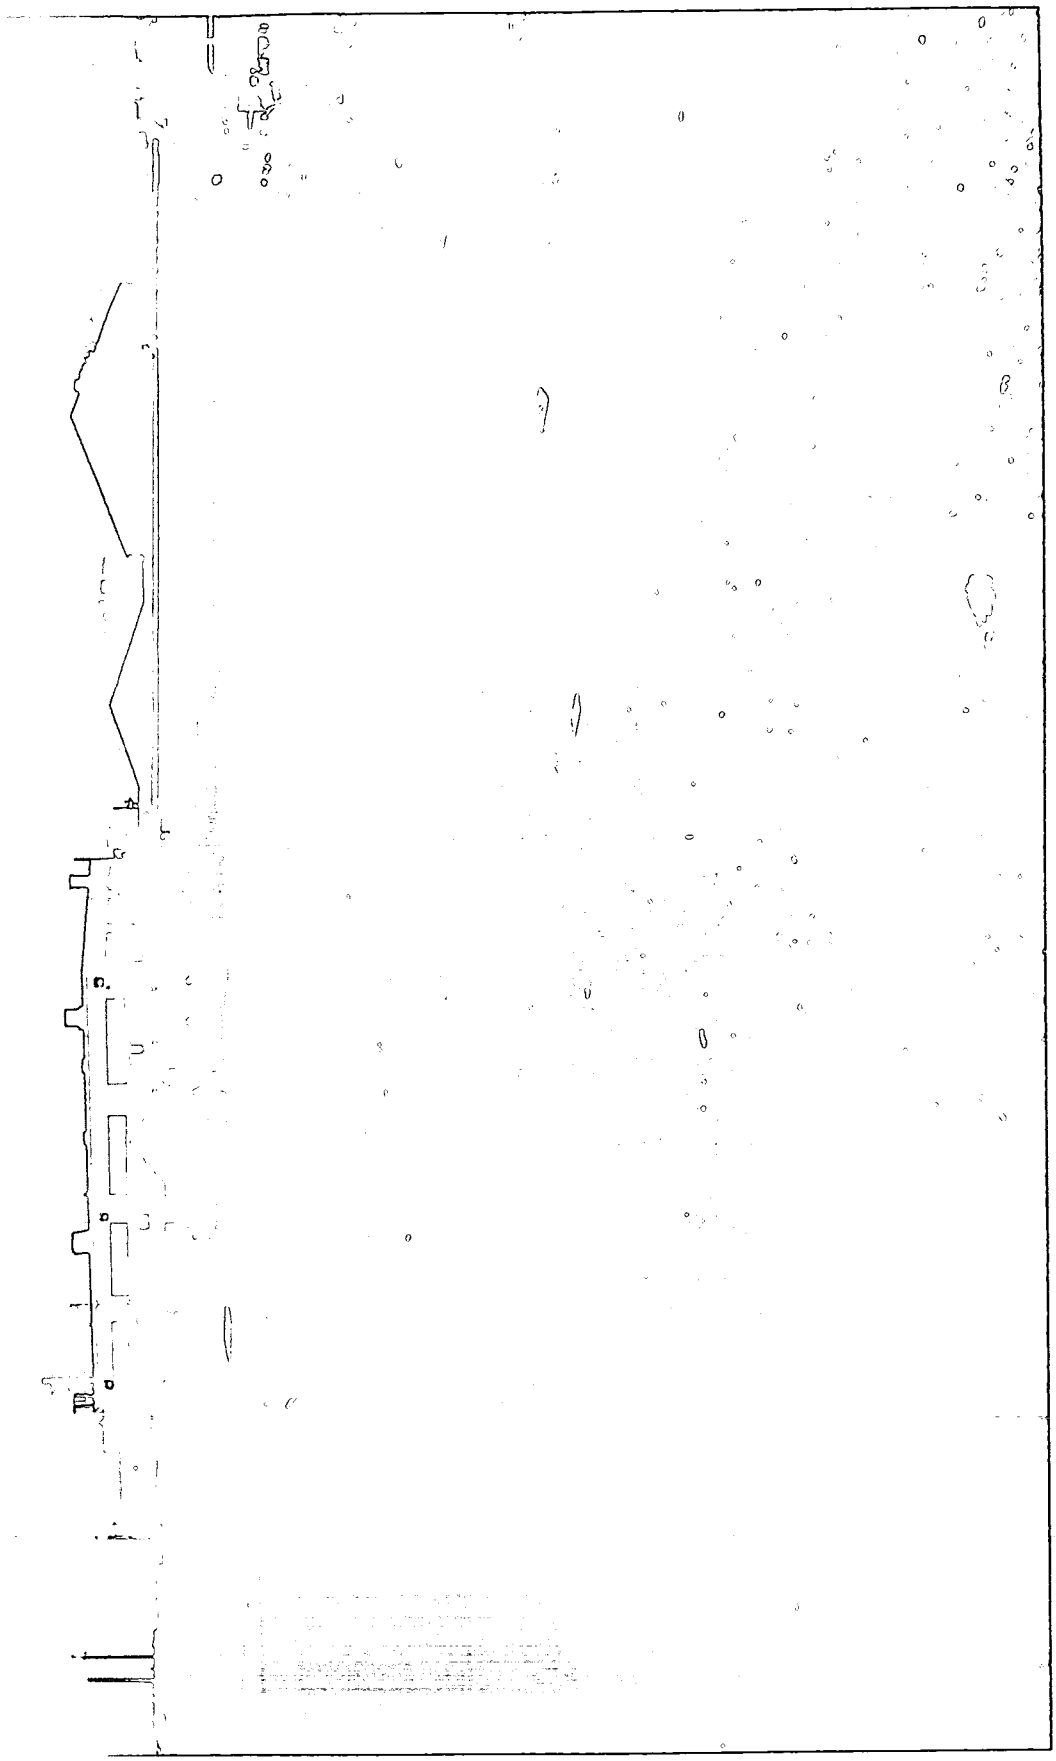

FIGURE 2-3 PHOTOGRAPH OF SMP AFTER DEBRIS/RESIDUE REMOVAL

In 1984, a concrete pad extension was placed adjacent to and west of the old decontamination pad area where the scrap metal was once located. This concrete section of the pad is free of embedded debris and residue and is in structurally sound condition. The older portion of the pad (once covered by the residue and debris), is considered marginally intact in terms of structural integrity based on visual inspections. A radiological survey was conducted to measure the loose and fixed radiological contamination since the debris and residue were removed and water-washed from the pad. The results of the radiological survey indicated that the area can now be down-posted from a "High Contamination Area" to a "Contamination Area". Furthermore, high-volume boundary air samplers (also utilized in the radiological survey) indicated that this area no longer presents a radiological airborne hazard. The newly cleaned pad could potentially be used for container storage contingent upon the structural integrity of the pad and according to FEMP waste management strategies.

2.3 RvA 17 REVISION JUSTIFICATION

The U.S. and Ohio EPA's January 1995 concurrence (Appendix D) on the proposed changes to the RvA 17 Work Plan, Revision No. 2, deleted a large portion of the scope of RvA 17. This reduction in scope, however, effected Phase II field/construction activities only. This reduction in scope did not alter the sitewide management strategies and concepts currently being utilized at the FEMP. All Phase I soil and debris management concepts adopted in the RvA 17 Work Plan, Revision No. 2, were to continue to be applicable regardless of the reduced scope.

It is necessary to expeditiously revise the strategy utilized for soil and debris currently managed under the existing RvA 17 Work Plan (Revision No. 2) into soil and debris management concepts that reflect consistency with the final RODs or anticipated RODs. This revision (No. 3) of the RvA 17 Work Plan is being provided as an interim measure to manage soil and debris until Final RODs and associated remedial action work plans supersede this work plan.

2.4 REVISED REMOVAL ACTION SCOPE

The revised RvA 17 Work Plan (i.e., Revision No. 3) will not implement a two-phased approach. The work plan will, however, retain its basic format that devises a separate soil management plan and a debris management plan as in the revision No. 2 of the work plan. Components of the interim soil management plan include criteria for stockpiles, storage areas, and management strategies. Components for the debris management plan include the method used for determining whether debris will meet the on-property disposal facility WAC, the type of process and material that certain equipment (process vs. non-process) originated from, and the ability to remove contamination from equipment or debris. Below is a listing

of these components and principles that provide the conceptual framework and discuss the major changes incorporated into the revised (rev. No. 3) RvA 17 Work Plan scope. Additionally, a flowchart of general soil and debris management strategies has been included as Figure 2-4.

2.4.1 Soil Management

The contaminant concentrations currently in the RvA 17 Work Plan (Revision No. 2), which serve as criteria dictating interim soil management practices, are being replaced with the criteria defined in the final approved OU2 ROD and the OU5 Proposed Plan (e.g., Waste Acceptance Criteria (WAC), FRLs). Upon finalization of the OU5 ROD, the criteria contained therein will be incorporated into this document by reference, replacing those in the Proposed Plan. With respect to the FRLs, this revised Work Plan (Revision No. 3) discourages interim management of soil containing contaminant concentrations below these soil remediation (cleanup) levels established in the appropriate RODs. With respect to the on-property disposal facility and associated WACs, the revised Work Plan (Revision No. 3) categorizes soil designated for interim management based on either meeting or not meeting the on-property WACs. Details of this soil management plan are provided in Section 3 of this Work Plan. The revised Work Plan also addresses (see Section 6.0) management of Investigative Derived Waste (IDW) which is not addressed in the current revision (No. 2) of the RvA 17 Work Plan.

2.4.2 Debris Management

The current RvA 17 Work Plan (Revision No. 2) establishes the management of debris based on whether the material is recoverable (able to be decontaminated for recycle, reuse, or sale) or nonrecoverable (disposal required). The revised Work Plan (Revision No. 3) manages debris based on the ability of the material to meet the WAC for the on-property disposal facility, although recycle/reuse is not precluded if it is economically feasible (consistent with the draft OU3 RI/FS Proposed Plan).

Additionally, the current RvA 17 Work Plan (Revision No. 2) utilizes the disposition criteria (recoverable or nonrecoverable) as the only categorization criteria for debris generated. The revised RvA 17 Work Plan (Revision No. 3) introduces the categorization philosophy presented in the draft OU3 Remedial Investigation and Feasibility Study (RI/FS) Report. These categories (which are presented in Section 4.3.1) are primarily determined from the type of contamination (process vs. non-process) and the physical/dimensional aspects as it relates to the ability to decontaminate debris (e.g., accessible vs. inaccessible metals) in order to meet the on-property disposal facility WAC.

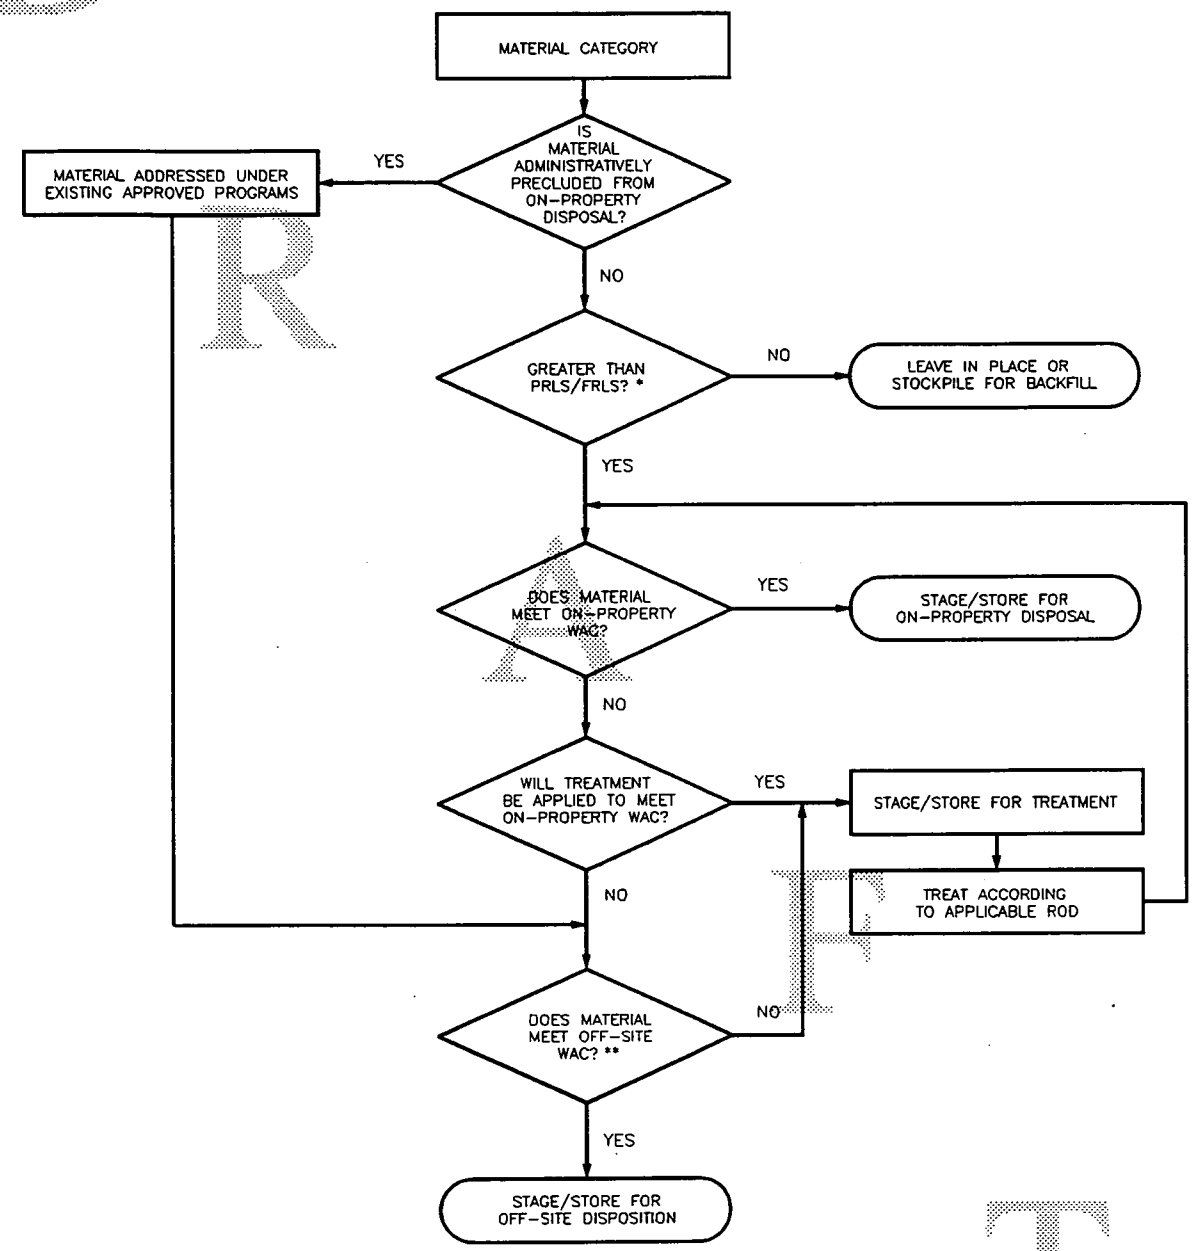

* EVALUATE DIVERGENT FRLS AND BTVS AS WELL
** DISPOSAL AND RECEIPT CRITERIA, INCLUDING LDRS

FIGURE 2-4 FLOWCHART OF GENERAL SOIL & DEBRIS MANAGEMENT STRATEGIES

2.4.3 Sources and Quantification of Soil and Debris

Many activities at the FEMP have generated soil and debris requiring controlled staging/storage. Activities to date have produced several soil piles that will likely require additional handling, possible real-time verification sampling, laboratory analysis, and temporary storage until final disposition is determined. These existing piles are primarily radiologically contaminated (determined through limited sampling results, field screening, and process knowledge), yet some materials (by process knowledge) may also be contaminated with petroleum products, PCBs, hazardous waste, or other mixed wastes.

Appendix C provides estimated quantities and sources of soil and debris on site as well as their locations on the FEMP site. These quantities represent soil and debris that either currently exist in some managed pile configuration at the FEMP or are currently being generated as part of field activities. Future sources and estimated quantities of soil and debris are identified to the extent possible.

Although is it difficult to identify all future soil and debris sources, the information presented in Appendix C is an estimate of the volume of soil and debris that may be created and the potential storage that may be needed for planning purposes. The generation schedule for these quantities will vary as additional structures may become available as waste inventories are removed. It should be noted that future-generated materials not identified in Appendix C should be managed according to the concepts presented in this Work Plan.

2.5 BACKFILL POLICY

The FEMP has established a backfill policy to: (1) minimize the amount of soil excavated during a construction project; (2) to minimize the need to bring soils from off-site locations; and (3) to identify criteria for the construction of new facilities. The backfill policy is effected by the determination of whether a facility is temporary or permanent.

Temporary facilities are defined as those that will be removed during remedial activities. Temporary facilities may be constructed without prior detailed characterization if the site is not expected to pose a significant risk to health or the environment. During construction, soil will be returned to the excavation or the surrounding area when possible. If it is not possible to reuse the soil at the point of excavation, the excess soil will be managed in accordance with the selected remedy in the OU5 ROD. Should soil be required as backfill for construction of a temporary facility, the feasibility of using soil from a controlled stockpile or another area on site will be evaluated. This evaluation will be based on the amount of soil required and the project location. These temporary facilities may also be considered TUs

DRAFT

under the CAMU rule. The design details of these TUs, as needed, will be designated in the appropriate remedial design and/or remedial action documentation.

Permanent structures (i.e., structures that will remain after the completion of final remedial action) will require that any contaminated soil under the proposed building be excavated and the area clean-backfilled prior to construction of that facility. Excavation of soil will occur to meet FRLs for that area. If soil is required for the construction of a permanent building, fill materials below the FRLs may be brought in from a non-contaminated borrow area (potentially off-site). However, the quantity of clean soil brought on site from off-site sources will be minimized. Hydraulic barriers may be utilized to prevent contamination of clean soils. Few permanent buildings are expected to be constructed at the FEMP during remedial activities.

DRAFT

3.0 INTERIM SOIL MANAGEMENT PLAN

3.1 INTRODUCTION

The intent of this interim soil management plan is to provide a policy on efficient soil management practices for the FEMP during the period between approval of this plan (Revision No. 3) and availability of approved design documentation issued pursuant to an operable unit ROD which otherwise addresses a related issue. Concurrently this management plan is intended to be consistent with the anticipated remedial action plans. The goals of this interim management plan are to:

- Define the scope of this plan;
- Minimize the total number of soil staging areas for the FEMP by providing an integrated implementation strategy for all operable units (which can be achieved through the application of soil staging criteria); and
- Set guidelines for management practices of staging facilities, such as buildings and stockpiles, that are based on ARARs and protection of health and the environment.

3.2 SCOPE

This integrated soil management plan is limited to the on-site interim management of soil. This plan should be considered relevant upon excavation of soil, and inclusive of soil management activities until the soil is properly stockpiled or disposed. Pertinent soil management activities are based on the staging criteria established in Section 3.4 of this plan, and the knowledge of the anticipated staging needs for each of the operable units where soil will be managed.

3.3 INTEGRATION OF OPERABLE UNIT REQUIREMENTS

Information from the selected remedies or preferred alternatives for each operable unit will determine the potential to combine and reduce soil staging or storage areas, which includes knowledge of:

- Planned final disposition (e.g., on-property or off-site disposal);
- Location and mode of transport to off-site disposal facility(ies) as applicable;
- Total number of soil staging/storage areas projected during remediation;
- Projection of on-site treatment requirements for on-property/off-site disposal; and
- Types of staging areas required (e.g., stockpiles, container storage areas, construction of new facilities, use of existing facilities/structures).

The intent of this interim plan is to employ methodologies from the pertinent remedy descriptions to maintain consistency from this transition period into remedial action. The soil staging criteria presented below were developed on this basis.

3.4 SOIL STAGING CRITERIA

Guidelines for creating staging areas require several general criteria. The strategy for segregating or combining soil within an operable unit (or from several operable units) creates a commitment to manage each staging area according to the common planned disposition of the soil in that staging area. The general criteria are discussed below. In addition, several criteria will be required for management practices for all soil stockpiles, such as run-on and run-off controls. These criteria will be developed in more detail after approval of this plan. In the event that new staging areas are created, moved, or consolidated, appropriate notices will be provided to the U.S. EPA and Ohio EPA.

3.4.1 Location Restrictions for Staging Areas

Areas to be avoided for staging locations include designated wetlands and floodplains, areas that will not require remediation by any operable unit, or areas where combining soil from other operable units would exceed the FRLs of that location. Appendix B includes a table of location-specific ARARs.

3.4.2 Staging Area for On-Site Treatment

Selected remedies where on-site treatment technologies are to be employed to meet the on-property WAC should combine the use of the treatment facilities and soil staging areas where common treatment technologies are being considered. The anticipated locations, facilities/staging requirements, and treatment technologies planned during remedial action have been included in Section 3.5.

3.4.3 Staging Area for On-Property Disposal

Soil that meets the on-property WAC may be combined into one designated central staging area for the on-property disposal facility if direct transport into the on-property disposal facility is not possible. The on-property disposal facility WAC are provided in Section 5.0.

3.4.4 Staging Areas for Off-Site Disposal

Two off-site disposal facilities are currently designated to receive soil from the FEMP; others may become available at a future date. These include Nevada Test Site (NTS) and a representative licensed commercial disposal facility in Clive, Utah. Each of these facilities has specific WAC and transportation options that must be met in order to receive the FEMP's remediation waste. NTS can only receive

shipments by truck. NTS accepts low-level radioactive waste, but will not accept waste regulated under RCRA or waste containing 55 parts per million (ppm) or more of PCBs under the Toxic Substance Control Act. Sampling and analysis plans must be submitted prior to acceptance at NTS. Therefore, at least one staging area is anticipated for soil, pending analysis for acceptance at NTS, based on the ability to ship material directly to the off-site disposal facility.

The representative licensed commercial disposal facility will accept both low-level mixed waste and low level radioactive waste. Hazardous wastes on its permit include D-characteristic waste, and most F-, P-, U-, and K-listed wastes. The licensed commercial disposal facility is not permitted to accept F-listed dioxins. Waste profiles must be submitted prior to shipment. Therefore, a minimum of two staging areas is assumed for shipment to the licensed commercial disposal facility, based on the presence/absence of RCRA constituents in the soil. Transportation options to the licensed commercial disposal facility include rail and truck. Remedial actions that may include on-site treatment to meet the licensed commercial disposal facility WAC prior to off-site shipment by rail should combine the use of the staging/treatment areas and manage soil in conjunction, or perform these activities separately in the same treatment/staging facilities (if operable unit ownership is necessary to maintain). Similarly, soil to be shipped by truck should be combined in another staging area when direct transport is not possible.

3.5 SUMMARY OF OPERABLE UNIT REMEDIAL ACTIVITIES THAT REQUIRE SOIL STAGING

The anticipated soil-related remedial activities for each operable unit relative to soil staging is summarized below. Specifics will be provided in subsequent remedial design packages and remedial action plans.

- OU1 - Soil excavated from beneath the pits will be stockpiled near the excavation area. The soil will be transferred to an on-site treatment facility. It is anticipated that the soil will be staged at two locations within this treatment facility: 1) preparation for feeding the materials into the treatment system, and 2) preparation for loading rail cars for shipment to an off-site disposal facility.

- OU2 - Staging areas are currently being considered for remedial action, and will be developed as needed. These areas will support OU2 waste excavation activities. Soil that does not meet the on-property WAC will be directly loaded and transported to the staging area planned for rail transportation activities.

- OU3 - No soil staging areas are within the scope of this remedial action.

- OU4 - Two soil staging areas are anticipated during these remedial activities : 1) soil staging for on-property disposal (i.e., meets the WAC), and 2) soil for treatment prior to disposal (i.e., does not meet the WAC). The first staging area mentioned will be constructed through the OU2 selected remedy; hence, only one soil staging area (if

necessary) is anticipated for OU4. Backfill soil will be managed as discussed in Section 2.5 of this plan.

- OU5 - Four types of areas are being considered for soil staging, as follows: 1) remediation wastes to be excavated during the winter may have to be stockpiled when the on-property disposal facility is closed during inclement weather conditions; 2) soil that contains vegetation in excess volumes for the on-property WAC may have to be staged or treated until the WAC is met; 3) soil that must be treated prior to on-property disposal will require a staging area; and 4) soil to be shipped off-site.

3.6 SOIL MANAGEMENT

Soil staging requirements apply to drummed soils, pads, buildings, or any structures or containers that may be used to hold soil. Some of these units may serve as Temporary Units (TUs) under the CAMU rule, as documented in the OU3 Remedial Investigation (RI)/FS Report and the OU5 FS and ROD. TUs are defined in 40 CFR §264.553(a) as temporary tanks and container storage areas which are used for treatment or storage of hazardous remediation wastes, during remedial activities. The U.S. EPA may allow for an applicable design, operating, or closure standard to be replaced by alternative requirements which are protective of human health and the environment. TUs or existing facility design standards must be designated in the remedial design or remedial action plan of the operable unit that intends to incorporate them. Many of the soil staging requirements are driven by action-specific ARARs, which are documented in Appendix B. It is the intent to use these designated units when necessary to facilitate interim soil management practices. Application of the CAMU and the designated criteria are designated in the OU5 ROD and described in the OU5 Feasibility Study.

Two generations of soil stockpiles from the FEMP will be managed differently: 1) stockpiles to be created during the interim period, and 2) existing stockpiles.

3.6.1 Soil Stockpiles to be Created During the Interim Period

Stockpiles to be created during the interim period will be segregated by their final disposition (e.g., on-property disposal or off-site disposal) and by their need for treatment and proposed method of shipment. The number of potential stockpiles needed for off-site disposal will be dependent on the number of facilities to receive waste from the FEMP, method of transport, and possible delays in being able to ship waste. Section 3.5 discusses *potential* stockpiles to be created during remedial activities.

3.6.2 Existing stockpiles

Currently there are several soil stockpiles, containing either Category I or Category II soil (per the RvA 17 Work Plan, Revision No. 2), which are staged at various locations across the FEMP. The contaminant concentrations from these categorized stockpiles will be compared to the on-property WAC to determine the potential disposition of the soil. Disposition confirmation of the soil stockpiles will be completed based on currently available sampling and analytical results from the stockpiles, as appropriate. The three options for soil disposition are: 1) on-property disposal, 2) treatment of soil to meet the on-property WAC, or 3) off-site disposal of soil.

3.7 WASTE MINIMIZATION

Waste minimization principles will be applied during FEMP remedial activities and within the scope of this plan. The FEMP will minimize the generation of waste soil by returning excavated soil to the environment, when appropriate (i.e., contamination levels do not exceed approved FRLs for that location). The combination of returning soil to the excavation and using soil from a controlled stockpile as backfill (see Section 2.5), when appropriate, will reduce the amount of clean backfill that is brought on site and potentially mixed with contaminated soils that would require treatment/disposal during the remedial action. Additionally, any material brought to the FEMP will be handled in accordance with the provisions of this work plan.

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK

4.0 INTERIM DEBRIS MANAGEMENT PLAN

4.1 INTRODUCTION

This section addresses the interim management of FEMP construction debris that may require on-property storage/staging until approved design documentation issued pursuant to an operable unit ROD is established which otherwise addresses a related issue. This debris will be generated primarily from the decontamination and dismantlement (D&D) of OU3 structures; however, small amounts of debris may be generated during the remediation of other operable units. Interim storage of construction debris to be generated during the OU3 interim remedial action currently falls within the scope of the OU3 Record of Decision for Interim Remedial Action (IROD), but will be integrated into the OU3 ROD for Final Remedial Action. In order to integrate the scope of this work plan into the current scope of forthcoming OU3 activities, a brief discussion of the OU3 scope is presented in Section 4.2.

The majority of information contained within Section 4.0 relates primarily to OU3 activities. However, small volumes of debris will be generated during the remedial actions selected in the respective RODs for OUs 1, 2, 4, and 5. The sizing and packaging specifications, based on final disposition, will be incorporated into the waste management plan for the on-property disposal facility. These specifications will also be incorporated into remedial action plans. In addition, the staging of this debris will also be managed according to this revised RvA 17 Work Plan, until it is superseded by remedial action plans.

In addition to integration between remedial actions for debris management, the integrated remediation of below-grade materials (e.g., soil, below-grade piping, concrete foundations, etc.) is currently planned between the remedial actions for OUs 3 and 5 in order to reduce overall remediation schedules and costs, and to prevent double-handling of contaminated materials. This integrated approach includes utilizing one subcontractor to excavate the subgrade debris and soil from the former production area. The integration approach will be detailed in the planning documents to be developed to implement the OU5 ROD-selected remedial action.

4.2 OPERABLE UNIT 3 SCOPE

The OU3 IROD provides that the final remedial action ROD for OU3 will establish the strategy for the final disposition of the debris generated during the interim remedial action. The OU3 IROD specifies that all buildings, equipment and other above- and below-grade improvements undergo D&D. The IROD also specifies that only ten percent of the total volume of debris to be generated during the OU3 interim remedial action may be dispositioned off-site with the remaining portion of OU3 debris to be placed in

interim storage until a final remedial decision is approved. The interim and final remedial actions will be coordinated to provide a unified remediation approach to OU3.

The forthcoming OU3 Proposed Plan for Final Remedial Action will identify the preferred remedial alternative that considers the disposal of a majority of the OU3 remediation debris in an on-property disposal facility along with OU2 and OU5 materials, as discussed in their respective RODs. Any debris removed from buildings and structures, as well as any debris generated during the interim and final remedial actions that requires storage will be supported by the debris management criteria/requirements discussed in the following sections. Again, the focus of this section is OU3 debris as the D&D of site structures will be the main generator of such debris.

4.3 DEBRIS DESCRIPTION

As with soil, guidelines for combining staging areas require several general criteria. The strategy for segregating or combining debris within an operable unit (or from several operable units) creates a commitment to manage each staging area according to the common disposition of the debris in that staging area.

4.3.1 OU3 Debris Categories

OU3 RI/FS debris categories were developed as a management strategy to handle the diverse debris generated in OU3 as a result of ongoing and proposed D&D activities. The categorization of OU3 construction debris into nine debris categories was based on potential treatment and disposition options (including the ability to recycle and recover materials), possible dismantling techniques, and existing debris management strategies, as well as the regulatory drivers for segregation and disposition of debris. The estimated weights and volumes of debris, analytical characterization data, and process knowledge were also considered in the definition and categorization of debris. The debris categories provide a cross-walk to link volume estimates in the Sitewide Waste Information, Forecasting, and Tracking System (SWIFTS) database, RI/FS characterization data, WAC development, and potential process options.

Estimates of the weights and volumes of OU3 construction debris were compiled in the SWIFTS database. Details of the assumptions and methodology used in determining these estimates are provided in the draft OU3 Estimated Material Quantities Report, June 1995. A summary of the OU3 debris categories and their respective estimated volumes (in unbulked cubic feet) are provided in Table 4-1.

TABLE 4-1 OU3 DEBRIS CATEGORIES

Category Designator	Category Title	Category Description	Estimated Unbulked Volume (ft³)
A	Accessible Metals	Structural steel and steel decking having large accessible surface areas and thicknesses which are greater than one-quarter inch. The surface of accessible metals can be easily decontaminated using physical surface decontamination techniques and subsequently surveyed prior to disposition.	63,400
B	Inaccessible Metals	Non-process piping, equipment in non-process areas, decontaminated process equipment, conduit/wire, electrical fixtures, miscellaneous electrical items, doors, and other miscellaneous metals are included in this category. These debris have surfaces which cannot be easily decontaminated or surveyed, and thus are considered inaccessible.	1,710,000
C	Process-Related Metals	Process equipment, electrical equipment not included in Category B, and process piping which are assumed to be highly contaminated. Treatment of these debris is not expected to be cost-effective.	191,000
D	Painted, Light-Gauge Metals	Ductwork, louvers, metal wall and roof panels, and sheet lead (painted metals less than one-eighth inch thick) are included in this category. Metals in this category are assumed to be painted with lead-based paint, or in the case of lead sheeting, to be made of lead themselves.	7,150
E	Concrete	Concrete, masonry, asphalt, and clay piping are all porous construction debris.	4,800,000
F	Brick	Acid brick was used extensively to line floors, drain areas, and trenches in process areas utilizing corrosive chemicals, and thus is expected to be highly contaminated.	20,700
G	Non-Regulated Asbestos-Containing Materials (ACM)	Transite walls and roofs, refractory (fire brick and insulating brick) debris, ceiling demolition, floor tile, and feeder cable are debris which are non-friable.	60,300
H	Regulated ACM	Piping insulation, ductwork insulation, and personal protective equipment (PPE), which are classified as regulated ACM because either the debris matrix is potentially friable ACM (e.g., insulation), or in the case of PPE, contaminated with asbestos fibers during asbestos abatement activities.	80,200
I	Miscellaneous Debris	Other miscellaneous items present in the structures and buildings in OU3 including windows, wood, built-up roofing, building insulation (non-ACM), drywall, process area and non-process area trailers, polyvinyl chloride (PVC) pipe, fabric roofs and walls, PPE, and other miscellaneous debris.	564,000
TOTAL			7,500,000

NOTE: The source of Table 4-1 is the draft OU3 Proposed Plan; however, Category J (Product, Residues, and Special Materials) is not included as it is excluded from the scope of RvA 17.

4.3.2 Staging Sub-Categories

Within each debris category, sub-categories have been defined to facilitate effective staging. For most of the debris categories, several potential dispositions exist contingent upon level of contamination and types of contaminants (e.g., disposal in the proposed on-property disposal facility, disposal at an off-site permitted facility, free release of non-contaminated material to a public landfill, recycling/reuse off-site, or requiring treatment prior to disposition). These sub-categories are important facets of debris management, as they identify future disposition, and will help in the determination of staging needs. For example, Category E (Concrete) debris will typically exhibit a variety of levels of fixed radiological contamination and may be destined for on-property disposal. This debris may be bulk staged to facilitate disposal operations. However, some concrete may be encountered with hazardous constituents, indicating off-site disposal or the potential need for treatment prior to disposal. This debris would be staged separately from the concrete acceptable for on-property disposal. Typically, this debris would be containerized according to the requirements for its ultimate disposition.

Based on current approaches incorporated into the draft OU3 RI/FS Report, debris will be segregated for on-property or off-site disposal. Debris remaining for on-property disposal will be placed in interim storage until such time that permanent disposal is possible. Debris that are to be sent off-site for disposal will be containerized at the point of generation. Interim on-property storage of these debris will be minimized to the extent practical.

4.4 DEBRIS MANAGEMENT

Given the nature of OU3 debris, the most efficient segregation of debris will be identified prior to the D&D based on current RI/FS data, process knowledge, and other supporting information. Given the nature of production activities at the FEMP, it is logical to attempt to segregate debris prior to removal. In its current state, RI/FS data and process knowledge can be used to determine the extent of contamination, the type of contaminants, and the condition of contamination (e.g., fixed or removable). Once the debris from the D&D efforts are bulk-stored or containerized, the traceability of the RI/FS data and process knowledge, as applied to the specific debris, will essentially be lost. Additionally, due to the extreme heterogeneity of the OU3 debris, any sampling approach implemented would not be representative of potential residual contamination. The sub-categories established to facilitate effective staging of debris are further discussed below with respect to effect on the staging process.

Within the interim remedial action, all materials will be evaluated to determine its disposition in accordance with the proposed final disposition. As stated earlier, all materials to be dispositioned off-site

will be containerized at the point of generation and staged under RvA 17 until shipment off-site can occur. All other materials will be staged under RvA 17 for potential on-property disposal under the final remedial action. Similar segregation decision will be made within the remedial action scopes of each operable unit generating debris at or before the time of generation.

A variety of other disposition options are available for debris depending on characterization and economic factors. Debris that meets radiological criteria for unrestricted release may be staged separately from debris acceptable for on-property disposal to facilitate unrestricted release actions. Also, based on levels/types of contamination and economic considerations, recycling of some debris streams may be feasible. These streams would generally be identified prior to execution of a D&D action to facilitate separate staging of this debris from others.

4.4.1 Implementing Debris Staging

For each separately identified debris stream, a variety of specific requirements will apply to assure environmental compliance and efficient management. Debris identified as acceptable for on-property disposal will be segregated from those destined for off-site disposal. Debris to be dispositioned off-site will be containerized at the point of generation and shipped off-site as soon as practical. For debris proposed to be disposed on-property, some debris will be bulk-staged to permit the most effective handling of these media. In cases where bulk staging is desired, the debris will be managed to assure minimization of airborne emissions, and staging will occur to assure control of runoff. These debris will be staged in a manner to minimize double handling, minimize costs by optimizing container use, and minimize labor associated with maintenance. Debris categories considered for bulk staging include accessible metals, inaccessible metals, painted light-gauge metals, concrete, and transite. All debris will be staged as detailed in Table 4-2. Container selection would be accomplished as a function of appropriateness based on debris sizing and containment needs. Debris determined to be RCRA characteristic or listed hazardous waste would require continued management as hazardous debris until actual disposal occurs.

The following sections provide further detail relative to implementing the debris management strategy, including decontamination activities, interim storage, and monitoring/sampling issues. These sections are written to reflect the management of OU3 debris, in that OU3 is expected to be the primary source of debris during the effective period for this interim plan. The practices reflected in the following sections will be similarly imparted on any debris generated by other operable units during this effective period.

TABLE 4-2 DEBRIS SEGREGATION APPROACH

	Debris Category	Storage Configuration [1]	Disposition
A	Accessible Metals	Stockpile	On-Property
B	Inaccessible Metals	Stockpile	On-Property
C	Process Related Metals	Containerize	Off-Site
D	Painted Light-Gauge Metals	Stockpile	On-Property
E	Concrete	Stockpile	On-Property
F	Brick	Containerize	Off-Site
G	Non-Regulated ACM [2,3]	Stockpile	On-Property
H	Regulated ACM	Containerize	On-Property
I	Miscellaneous Materials [3]	Containerize	On-Property

Notes:
[1] Typical approach for storage of predominant materials. All hazardous and mixed waste debris will be containerized.
[2] Transite will be handled separate from other Non-Regulated ACM. Transite is to be band-wrapped to pallets and stored in stockpile configuration.
[3] Miscellaneous Materials can be containerized with other Non-Regulated ACM materials.

DRAFT

4.4.2 Operable Unit 3 Decontamination Activities

The categories that were introduced in Section 4.3 have been established for segregation of debris during the OU3 interim remedial action that are consistent with the potential disposition options available. Segregation of debris will occur during the interim remedial action according to potential disposition options. The segregation will be based on OU3 RI/FS sampling program data, process knowledge, and the results of the Safe Shutdown and the interim remedial action decontamination efforts. The decontamination activities to take place under Safe Shutdown and the interim remedial action will include removal of residues, vacuuming loose media, water washing, and scabbling of concrete to remove localized contamination "hot spots." The anticipated levels of contamination after the Safe Shutdown and interim remedial action activities should allow for the interim storage of OU3 debris in various configurations, as needed. Figure 4-1 shows the debris flow from post-interim remedial action to final disposition.

4.4.3 Interim Storage of Debris

As shown in Figure 4-1, debris that will be staged in stockpiles include structural steel, equipment, miscellaneous metals, painted light-gauge metals, and concrete. In addition, transite panels used for

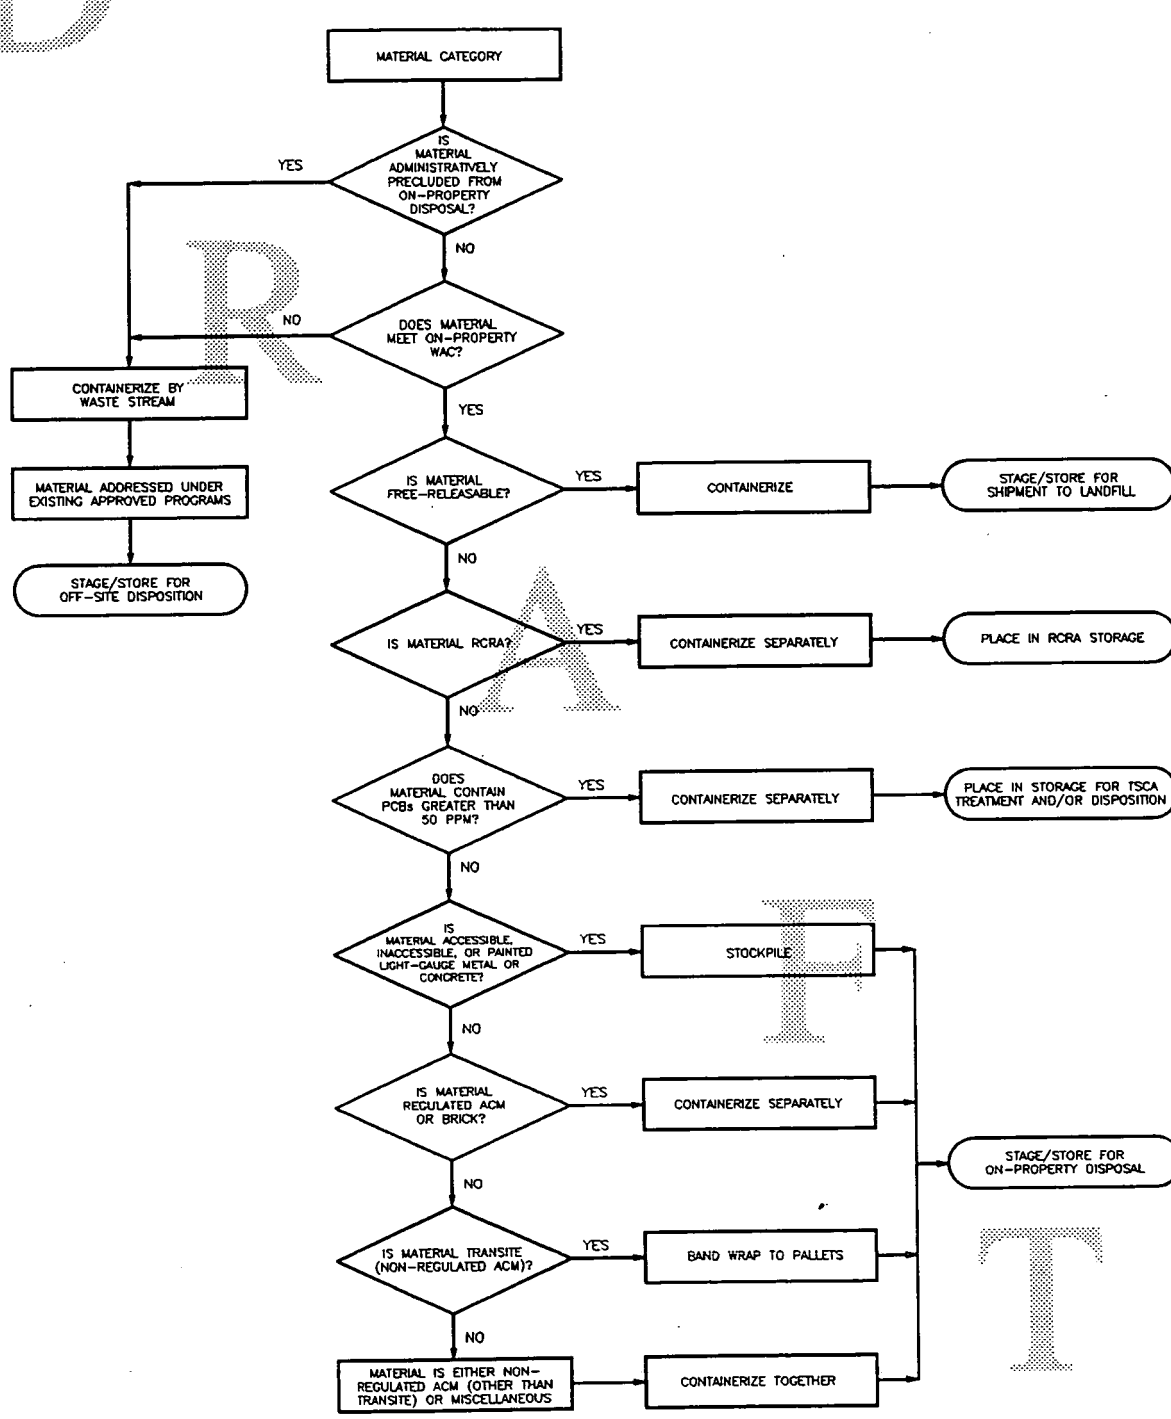

FIGURE 4-1 MATERIAL FLOWCHART FOR DEBRIS CATEGORIES

building roofing and siding would be stacked on pallets to an appropriate height. The stacked transite panels would then be banded to the pallet and placed in interim storage. The interim staging would be required since current and forthcoming OU3 D&D activities are expected to generate the aforementioned debris prior to the completion of the FEMP on-property disposal facility. It is currently expected that the D&D activities of Plant 4A, Plant 1A, Plant 9A, and Plant 10A will generate debris that will require interim staging until the on-property disposal facility is completed and functioning (currently scheduled for late 1997). Once the on-property facility is functional, the interim-staged materials would be placed in the facility in a sequential manner. Until such time, debris requiring interim staging will be placed on the Plant 1 Storage Pad (74T), other existing storage pads, and/or foundations of dismantled buildings.

The combination of the OU3 decontamination efforts and stormwater runoff collection systems would address potential leachate of fixed contamination from the stockpiled debris. Loose contamination is anticipated to be minimal due to the water wash that will be performed as part of the OU3 component D&D activities. Although all materials to be considered for stockpiling will have been water washed during D&D operations and subsequently inspected, it is assumed that because these materials may be staged uncovered for up to approximately four years, weathering conditions may cause small amounts of residual contaminants to be released.

To protect the environment from the migration of contaminated leachate, a polymer sealant has been applied to the surface of the Plant 1 Pad to create an impermeable barrier between the concrete and stormwater runoff. The runoff from these debris piles will be collected and treated, as necessary, in the site wastewater treatment system.

Likewise, airborne contaminant concentrations from the stockpiled debris are expected to be negligible based on reduced surface contamination after high-pressure water washing. However, if a determination is made that the debris requires additional treatment, the FEMP possesses the capability to treat the stockpiled debris with an amended water spray. The amended water would consist of ordinary water mixed with a commercial surfactant. The amended water could be applied to the stockpiles using fire-fighting equipment. This application would create a thin coating on the surfaces of the stockpiled debris to reduce the potential for airborne releases. This practice is common at uranium mill-tailing sites to suppress airborne emissions.

Worker protection (e.g., individuals involved with stockpiling of OU3 debris, etc.) requirements will be addressed by the site health and safety plan, which implements engineering and administrative controls

to ensure that the inhalation and radiation doses received will not exceed occupational standards and are kept as low as reasonably achievable. Therefore, no significant impacts to human health (either on-site worker or off-site resident) or the environment are anticipated as a result of stockpiling debris.

4.4.4 Monitoring/Sampling Issues

Since OU3 debris has been characterized based on conservative, biased sampling approaches ("hot spot" identification), the resulting disposition of the debris, represented by the OU3 RI sampling data, can be identified in advance of the OU3 D&D efforts. As discussed in Section 5, further characterization to support disposition should generally not be necessary. However, any additional monitoring/sampling that may be required will be defined in project-specific D&D implementation plans.

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK.

5.0 MATERIAL CHARACTERIZATION

Prior to excavation of soil and segregation of debris, existing analytical data (i.e., analytical data resulting from RIs, safe shutdown activities, legacy waste characterization, and interim remedial action decontamination efforts) will be assessed to determine whether the soil or debris contains constituents greater than FRLs or WAC, as applicable. If analytical data and process knowledge does not exist to make this determination, sampling and analysis and/or field screening shall be performed. This section discusses the methods and activities necessary to collect that data.

5.1 OBJECTIVES

The primary objective of this sampling and analysis plan is to guide the collection of representative samples that will allow both accurate and precise measurements of the chemical and radiological contaminants in the soil and debris. The analytical data will be used to determine if material meets the requirements for waste management and disposal in the on-property disposal facility and at off-site facilities.

This sampling and analysis plan provides a general framework for sampling soil and debris, and describes the procedures that will be undertaken to obtain analytical data and/or field screen results of sufficient quality and quantity to characterize the soil and debris generated at the FEMP. Sampling and analysis shall only be performed when sufficient quality and quantity of data do not exist. All sampling and analysis (including field screening) will be conducted to determine if the soil/debris meets or exceeds the established WACs for the on-property disposal facility and to segregate into staging areas. Debris shall be dispositioned using data presented in the OU3 RI.

Project-specific sampling and analysis plans, developed in accordance with the Site-Wide CERCLA Quality Assurance Plan (SCQ), shall be prepared to provide details of the sampling effort (e.g., the number of samples to be collected, analytical requirements, and sampling procedures.) The project-specific sampling and analysis plans shall be submitted to the regulatory agencies for approval within or as a supplement to operable unit remedial action plans.

5.2 ANALYTICAL PARAMETERS

Process knowledge and analytical results generated during RI, safe shutdown activities, and legacy waste characterization will be relied upon to determine disposition and the need for staging; however, if existing analytical data are not of sufficient quality or quantity, additional sampling will be required. Analytical

parameters will be consistent with Constituents of Concern (COCs) listed in the final RODs. This section discusses the COCs and sampling requirements for each operable unit. The list of analytes may be changed based on the specific requirements of each project.

Sampling and analysis requirements associated with operable unit remediation have not yet been developed, and will not be until the remedial action plans are developed; however, the soil cleanup levels (i.e., PRLs, FRLs, primary/secondary cleanup levels) for each operable unit are identified in discussions below.

5.2.1 Operable Unit 1

The levels identified in Tables E-1 and E-2 in Appendix E, are appropriate only to OU1 waste remediation activities. For disposal, sampling will be conducted to adhere to the WAC for the on-property or off-site disposal facility.

5.2.2 Operable Unit 2

The OU2 cleanup levels, or FRLs, have been divided into primary and secondary cleanup levels, which are presented in Table E-3 and Table E-4 in Appendix E, respectively. The COCs for the primary cleanup levels contribute over 90 percent of the risk from OU2 and over 99 percent of the volumes to be excavated under the selected alternative. The COCs for the secondary cleanup levels pose risks that are close to the 10^{-6} point of departure and contribute a small percentage to the overall risk from OU2. Based on existing analytical results from the RI and the volume calculations from the FS, secondary cleanup levels will most likely be achieved by remediation to the primary levels; however, this will be confirmed through post-remediation sampling.

OU2 material with concentrations above FRLs but at or below 346 pCi/g of uranium-238, or 1,030 (mg/kg) ppm of total uranium, will be accepted at the on-property disposal facility.

5.2.3 Operable Unit 3

The COC for OU3, as summarized in the draft OU3 RI/FS, is technetium-99. Segregation of the debris will occur consistent with the available disposal options.

DRAFT

5.2.4 Operable Unit 4

Table E-5 in Appendix E provides FRLs for soil cleanup in the soils. Specific details on the development of these FRLs are provided in the FS Report for OU4. Based on the contaminant concentrations found in OU4 soils, FRLs were not required for non-radionuclide (chemical) contaminants.

5.2.5 Operable Unit 5

The WAC were derived to establish mass-based or activity-based operation limits for soil or sludge contaminant concentrations to ensure the long term protection of the Great Miami Aquifer underlying and downgradient of the on-property disposal facility. The OU5 on-property WAC were derived to ensure that the water quality in those portions of the aquifer potentially impacted by the on-property disposal facility do not exceed the groundwater FRLs over the long term. The OU5 on-property disposal facility WAC are provided in Table E-8 in Appendix E.

The proposed remediation levels for the individual carcinogenic contaminants for on-property soil represent the 1 x 10^{-6} Incremental Lifetime Cancer Risk (ILCR) level to a hypothetical undeveloped park user. For the noncarcinogenic constituents, the final remediation levels for each constituent present in on-property soil represent a concentration equivalent to an Hazard Quotient (HQ) of 0.2 to a hypothetical undeveloped park user. As identified in Table E-6 and E-7 in Appendix E, FRLs are presented for soil and sediment for uranium present in both leachable and relatively nonleachable forms. Soil exhibiting relatively leachable forms of uranium have been detected within the former production area beneath the retired processing buildings. For on-property soil exhibiting less leachable forms of uranium, the proposed OU5 remedy has adopted an As Low As Reasonably Achievable (ALARA) goal of 50 ppm (mg/kg) of uranium in soil. The FEMP will apply available hand-held instrumentation to help guide excavation and assist in identifying any isolated areas of higher contamination to help attain this ALARA goal.

The FRLs for off-property soil represent the 1 x 10^{-5} ILCR level (3.5 x 10^{-5} for uranium to the resident farmer receptor) for individual carcinogenic constituents. The FRLs for the Great Miami Aquifer represent the Safe Drinking Water Act maximum contaminant levels (MCLs) or, in the absence of MCLs, the 1 x 10^{-5} ILCR or HQ of 0.2 values for individual constituents to recreational users of surface water resources.

5.3 SOIL AND DEBRIS SAMPLING

The characterization process for soil and debris will rely heavily on existing data and field surveying results. Supplemental verification sampling may be completed to increase the confidence levels of the field surveying results. Guidelines for soil and debris sampling protocols are contained in Section 6 and Appendix K of the SCQ. Project specific sampling and analysis plans will be developed to define the actual sampling and analytical needs.

Sampling equipment shall be decontaminated following use at each sampling location to prevent the transfer of contaminants from equipment to sampled media and to limit cross-contamination between sampling locations. Equipment shall be decontaminated according to requirements outlined in Appendix K.11 of the SCQ.

Sample collection documentation shall be completed for all sampling activities. Required documentation include a daily field activity log and sample collection log. Pertinent information contained on these forms include activities and measurements conducted in the field by the sampling team, unique sample location identifier, collector initials, sample volumes, sample preservation, equipment calibration information, sample data and time, and chain-of-custody information.

Soil samples shall be collected using trowels, shovels, hand augers, or hydraulically operated soil probing equipment composed of inert material relative to the analytes of interest. Intrusive sample collection methodology for debris differs depending upon the sampled media. Collection methods include needle scaler, coring devices, rotary drill and coring bit, and paint scrapers. Samples shall be carefully transferred to the appropriate sample containers and sealed with custody tape. The samples will be preserved according to the requirements of the analytes of interest. Samples requiring compositing shall be composited according to the guidelines specified in Appendix K of the SCQ. Samples collected for volatile organics analyses shall not be composited. IDW generated from sampling activities will be handled per Section 6.0.

5.4 FIELD SCREENING

Real-time field instrumentation may be utilized for chemical and radiological screening of the soil. Concentrations for some contaminants may require determination in the laboratory as field instruments may not detect the FRL and WAC concentrations with the high level of confidence and accuracy needed. Specific instrumentation shall be outlined in the applicable operable unit Remedial Action Work Plans or Project Specific Sampling Plans. Field screening instrumentation will be calibrated according to

manufacturer's specifications. Any equipment that fails calibration shall be tagged and removed from service.

5.5 FIELD AND LABORATORY QUALITY ASSURANCE

Duplicate samples and trip, field, and rinseate blanks may be collected during sampling for Quality Assurance/Quality Control (QA/QC) purposes. Frequency and applicability of field and laboratory QC sample collection are in Section 4.0 and Appendix G of the SCQ. The field and laboratory QC samples shall be collected consistent with the on-property and off-site facility WACs and the requirements for the collection of field QC samples shall be documented in the project specific sampling and analysis plans.

The following types of laboratory QC samples shall be analyzed as applicable for analytical methods: laboratory control samples, method blanks, matrix spikes, matrix spike duplicates, surrogate spikes, blind and double blind QC samples, and interlaboratory comparison study samples. Guidelines for laboratory QC are contained in Appendices A and G of the SCQ.

5.6 CHAIN-OF-CUSTODY

An essential component of the soil and debris sampling and analysis plan is ensuring the integrity of the sample from collection and analysis to data reporting. A chain-of-custody procedure will be utilized to ensure this traceability. The chain-of-custody program is presented in Section 7.0 of the SCQ.

5.7 ANALYTICAL METHODS

When field screening methods are not feasible, hazardous waste constituents will be analyzed according to the U.S. EPA Test Methods for Evaluating Solid Waste Physical/Chemical Methods (SW-846) procedures. Additionally, when field screening methods are not feasible radionuclide activities will be performance-based as specified in Appendix G of the SCQ.

5.8 DATA VALIDATION, MANIPULATION, AND MANAGEMENT

Guidelines for analytical data validation, consisting of an independent review of all sampling and analytical information and qualifying the data results (if necessary), are contained in Appendix D of the SCQ and as otherwise required to meet disposal facility WAC.

Statistical analysis between the calculated mean value and the limit may be required to determine whether there is a significant difference at a 95 percent confidence level. If that is the case, a student's "t" test

will be used to perform the statistical analysis and the analytical results will be entered into a computerized database.

DRAFT

7221

6.0 NON-AQUEOUS IDW MANAGEMENT PLAN

This section establishes the site-wide principles for management of all non-aqueous IDW. The non-aqueous IDW includes drilling muds and cuttings from soil borings and well installation; soil, debris, and other materials from the collection of samples; residues (e.g., ash, spent carbon) from testing of treatment technologies and treatment systems; and contaminated PPE used during investigations. This section addresses IDW that is currently stored in containers and stockpiles, as well as IDW that will be generated during field activities.

The non-aqueous IDW includes waste materials generated from CERCLA field investigation activities, (e.g., RI/FS and Remedial Designs), that may pose a risk to human health and the environment. The RvA17 implementation and Remedial Action (RA) phases of the FEMP cleanup, although not an investigative phase, will likely generate investigative wastes (e.g., verification and certification samples, drill cuttings from installing pumping wells) similar to the IDW-wastes covered by this policy. The removal action or remedial action plans will therefore incorporate these waste management principles for IDW-type wastes generated during the removal or remedial action (e.g., PPE, excess verification samples, etc.).

The management principles identified in this Section should be considered for any IDW generated during CERCLA activities conducted at the FEMP. All removal or remedial action plans that involve IDW should specify the methods for managing IDW. These methods should be consistent with the IDW management principles included in this section.

6.1 BACKGROUND

Two FEMP policies currently exist for non-aqueous IDW: the OU2 plan for soil and waste drill cuttings, and the OU5 plan for soil drill cuttings (Attachment D).

The OU2 plan is for managing soil and waste drill cuttings generated from the OU2 RI Phase II sampling program. The plan specifies areas within OU2 where cuttings are to be placed. The OU5 policy involves drummed soil drill cuttings from previous OU5 field investigations conducted in 1993. The plan states that the drummed soil is to be placed in a shallow surface depression near the sampling location or is to be managed per (previous) RvA 17 methodologies, depending on the nature and amount of contamination. Both the OU2 and OU5 plans are superseded by this non-aqueous management plan.

DRAFT

Note that a policy currently exists for aqueous IDW — the FEMP's Policy for Management of Aqueous IDW. The FEMP's aqueous IDW which includes purge water from sampling monitoring wells, development water from the installation of monitoring wells, and wastewater from decontaminating PPE and sampling equipment, will be treated through the Advanced Wastewater Treatment (AWWT) facility. The policy should be used for all aqueous IDW generated during the RI/FS and RD phases of cleanup, and its principles should be incorporated into all removal and remedial action plans, as appropriate.

6.2 NON-AQUEOUS IDW MANAGEMENT

Non-aqueous IDW should be managed in a manner to: 1) minimize the generation of new waste-streams, 2) be consistent with the management of the source waste, and 3) be consistent with the remedial action for the site. The preferred management options for non-aqueous IDW is to return the IDW to or near its source, if possible, or to manage it in accordance with Sections 3.0 and 4.0 of this work plan.

The management method of the IDW is dependent on the type and amount of contamination in the source material from which the IDW is generated. Knowledge of the type and amount of contamination can be based on one of the following information sources: existing data from the RI Reports and other projects, data from field screening performed while the IDW is generated, or laboratory analytical data. This information is sufficient to determine the type and amount of contamination in the IDW, including whether or not the IDW contains a listed hazardous waste and/or has the potential to exhibit a hazardous waste characteristic.

6.2.1 RCRA-Hazardous Non-Aqueous IDW

Any IDW from investigations of known or suspected RCRA-hazardous soil, debris, or waste should be identified. If the IDW contains a listed hazardous waste or exhibits a characteristic it should be managed in the manner described in this sub-section. If the IDW does not contain a listed hazardous waste or exhibit a characteristic then it should be handled according to Sections 6.2.2 through 6.2.5 of this Plan.

RCRA-hazardous soil/debris/waste is subject to regulation under RCRA (and Ohio Hazardous Waste rules) if: (1) the soil/debris/waste contains a listed hazardous waste, or (2) the soil/debris/waste is contaminated enough to exhibit a hazardous waste characteristic such as corrosivity, reactivity, ignitability, or toxicity. Mixed waste/soil/debris is both RCRA-hazardous and radioactive.

To contain a listed hazardous waste, the IDW must be contaminated with a hazardous constituent that resulted from contact with or leakage of RCRA-hazardous waste from a Hazardous Waste Management

7221

Unit (HWMU), or must be from sampling waste within a HWMU. Merely containing contamination of a hazardous substance that is listed in RCRA does not render a soil, debris, or waste RCRA-hazardous. The source of the hazardous substance must be from a HWMU that managed listed hazardous waste in order to be considered a listed hazardous waste. Any IDW associated with soil/debris/waste containing a listed hazardous waste to be disposed in the on-property disposal facility should be handled in the same manner as non-RCRA hazardous IDW, per Sections 6.2.2 through 6.2.6 of this plan. IDW containing listed hazardous waste that will be disposed off-site should be containerized and stored on-site in a RCRA storage area until it is disposed.

To be characteristically hazardous, the IDW must be contaminated enough to exhibit a hazardous waste characteristic. The source of the contamination that causes the soil/debris/waste to exhibit the characteristic is not relevant, unlike listed hazardous wastes. IDW that may be contaminated enough to exhibit a hazardous waste characteristic (regardless of the source of contamination) will be considered to be potentially characteristically hazardous and should be containerized until the source material and/or the IDW has been sampled. If the IDW or its source material exhibits one or more of the four aforementioned characteristics, then it should continue to be containerized and stored in an approved RCRA storage facility on-property for subsequent treatment and/or disposal. If the IDW does not exhibit one or more of the four characteristics then it should be managed in the same manner as non-hazardous IDW, per Sections 6.2.2 through 6.2.6.

Note that some hazardous waste may meet regulatory exclusions for management as a hazardous waste. IDW from investigations of such excluded waste would also be excluded from management as a hazardous waste.

6.2.2 Soil From Drilling Boreholes and Soil and Debris From Field Sampling

Drilling boreholes for subsurface geotechnical investigations and/or for monitoring well installation will generate IDW in the form of soil drill cuttings and excess soil from split spoon samples. Shallow hand augers and surface soil sampling will generate IDW in the form of excess soil sample material. Such IDW should be returned to the source if the contaminant concentration in the IDW meets or is less than the FRL for that area. If the IDW contaminant concentration is greater than the FRL for the source area, the IDW can be returned to the source area only if the IDW contaminant concentration does not exceed or significantly differ from the average surface soil contamination at the source location. If the IDW contaminant concentration exceeds or significantly differs from the average surface soil contamination at

DRAFT

the source location, then the IDW should be placed in an appropriate stockpile in accordance with Section 3.0 of this Plan.

IDW generated from excess field samples of debris should be returned to the sample source, if possible, or in appropriate debris stockpile in accordance with Section 4.0.

6.2.3 Waste From Drilling Boreholes and Field Sampling

Investigations of wastes in the units to be remediated (e.g., waste pits, landfills, etc.) will result in excess waste samples and waste drill cuttings. Where possible, such IDW should be returned to the source unit under investigation provided that the returned IDW will not pose an increased risk to human health and the environment.

6.2.4 Sample Material for Laboratory Analysis

Soil/debris/waste samples will be taken to verify the extent and nature of contamination and to certify that cleanup goals have been achieved. Such sampling will generate IDW (from both on- and off-site laboratories) in the form of unused samples and sample fractions, used sample fractions, contact wastes from laboratory analysis, and residues from sample analysis.

Unused and unpreserved soil/debris/waste samples and sample fractions that are no longer needed may be returned to the samples' source or to an adjacent location, if possible. If the source has since been excavated or removed, then the sample material should be managed in accordance with Sections 3.0 and 4.0 of this Plan.

The IDW from soil/debris/waste sample fractions that have been analyzed in the laboratory include associated sampling equipment and containers (contact waste), used lab samples, and associated residues (extracts, leachates, acid digests) from sample analysis. Such IDW from laboratory analysis may be often contaminated with chemicals after the laboratory analysis (e.g., the sample may be purged with organics to extract the analytes.) Hence, this IDW, which may be contaminated by these chemicals, should be containerized and managed on-site for appropriate disposition.

6.2.5 PPE

The PPE (e.g., respirators and clothing articles) used during field activities will be decontaminated to allow re-use, if possible. If contaminated PPE are to be disposed, they should be containerized and stored on-site pending disposition either in the on-property disposal cell or at an off-site facility.

Decontaminated PPE will be baled and placed in site dumpsters for disposal off-site at a solid waste landfill.

6.2.6 Treatment Technology Testing Waste

Testing treatment technologies for treating contaminated soil/debris/waste will generate IDW in the form of excess unused sample material, treated sample material, and non-aqueous residues such as ash or spent carbon. Treated and unused soil/debris/waste samples should be returned to the source or an adjacent location, where possible, or managed according to Sections 3.0 and 4.0 of this Plan.

Some waste might come to the FEMP from another site for treatability study. Treatability samples and other wastes resulting from treatability testing of such waste are not covered under this section. Management of such waste must be defined in the appropriate plan for the treatability study.

DRAFT

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

000057

DRAFT

APPENDIX A

OPERABLE UNIT MILESTONES/DATES

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK

~~72221~~ 7221

RvA 17 REVISED WORK PLAN SCHEDULE & ASSOCIATED OPERABLE UNIT (OU) MILESTONES/DATES

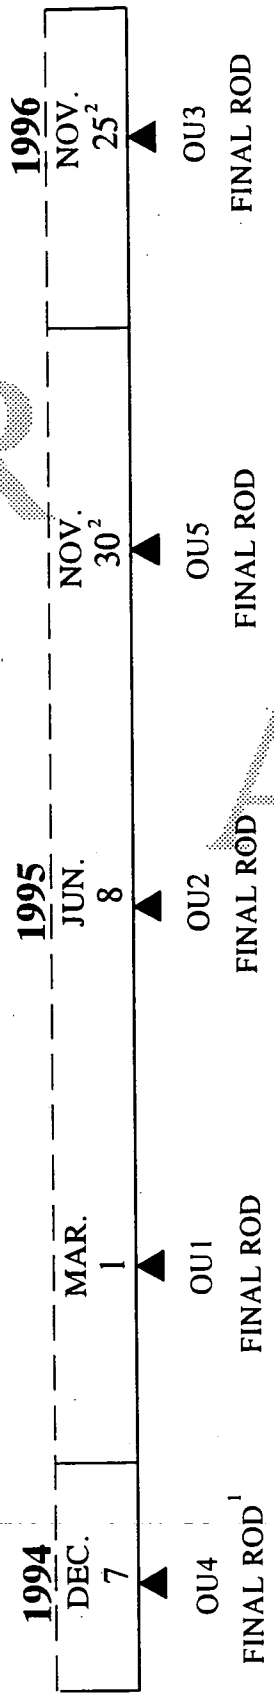

[1] Draft RD Work Plan submitted to EPA 0 to 60 days following Final ROD. Draft RA Work Plan(s) submitted to EPA 2 to 7 months from Draft RD Work Plan submittal

[2] Projected schedule

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK

DRAFT

APPENDIX B

APPLICABLE OR RELEVANT AND APPROPRIATE REQUIREMENTS (ARARs)

DRAFT

TABLE B-1 RvA17 ARARs

CHEMICAL SPECIFIC ARARs

AIR	
40 CFR Subpart H	National Emission Standards for Emissions of Radionuclides Other Than Radon From DOE Facility
40 CFR 61 Subpart Q	National Emission Standard for Hazardous Air Pollutants, Radon - 222 Emissions
OEPA Proposed Policy January 1994	Ohio De Minimis Emission Levels
OAC 3545-21-07(G)(2)	Organic Air Emissions
TOXIC SUBSTANCE CONTROL ACT	
40 CFR 761.125	Requirements for PCB Spill Cleanup
RADIATION LIMITS	
DOE Order 5400.5 (proposed 10 CFR 834)	Radiation Protection of the Public and the Environment

LOCATION-SPECIFIC ARARs

THREATENED AND ENDANGERED SPECIES	
16 USC §1531 et seq.	Endangered Species Act
50 CFR 17.21, 17.31, 17.61, 17.71 and 17.94	Endangered and Threatened Wildlife and Plants
50 CFR 402.01	Interagency Cooperation - Endangered Species Act
FLOOD PLAINS AND WETLANDS	
10 CFR 1022.3(a)(b)(1),(2),(3),(5),(6),(c)(d)(e)	DOE Compliance with Flood Plains/Wetlands Environmental Review Requirement

DRAFT

TABLE B-1 RvA17 ARARs (Cont'd)

ACTION-SPECIFIC ARARs

GENERAL

40 USC §4901 et seq.	Noise Control Act
42 USC §7641	Noise Pollution and Abatement Act
	Hamilton County Earthwork Regulations Erosion Control Specifications

HAZARDOUS WASTE MANAGEMENT (GENERAL FACILITY STANDARDS)

40 CFR 262.11 OAC 3745-52-11	RCRA Hazardous Waste Determination
40 CFR 265.13 - .16 OAC 3745-65-13 - 16	Interim Status: Treatment, Storage, and Disposal General Facility Standards
40 CFR 265.31 - .35, .37 OAC 3745-65-31 - 35, 37	Interim Status: Treatment, Storage, and Disposal Facility Preparedness and Prevention
40 CFR 265.51, .52 and .55 - .56 OAC 3745-65-51, -52, and -55 through -56	Interim Status: Treatment, Storage, and Disposal Facility Contingency Plan and Emergency Procedures
40 CFR 264.251 through .259 OAC 3745-56-51, 54, 58	RCRA Waste Piles

HAZARDOUS WASTE MANAGEMENT (CORRECTIVE ACTION)

40 CFR 264.552, .553	Subpart S: Corrective Action Management Unit 58 FR 865829 (16 FEB 93) - (See Table C-5 for additional discussion)

RADIOACTIVE

10 CFR 835	Occupational Radiation Protection
10 CFR 20	Standards for Protection Against Radiation

SURFACE WATER RUN-OFF

40 CFR 122.26	Discharge of Stormwater Run-off
OAC 3745-38	Discharge of Stormwater Run-off

AIR

OAC 3745-15-07	General Provisions on Air Pollution Control Prevention of Air Pollution Nuisance
40 CFR 5.6(a),(b),(c) OAC 3745-17-07(A)	Control of Visible Emissions From Stationary Sources
OAC 3745-17-08	Restriction of Emission of Fugitive Dust

DRAFT

TABLE B-2 RvA 17 OTHER REQUIREMENTS

29 CFR 1904 and 1910	Occupational Safety and Health Act (OSHA) Worker Protection Requirements
DOE Order 5440.1E	NEPA Compliance Program
DOE Order 5480.1B	Environmental, Safety, and Health Program for DOE Operations
DOE Order 5480.4	Environmental Protection, Safety, and Health Protection Standards
DOE Order 5483.1A	Occupational Safety and Health Programs for DOE Employees at Government Owned, Contractor Operated Facilities
DOE Order 5700.6C	Quality Assurance

DRAFT

DRAFT

APPENDIX C

FEMP SOIL PILE AND DEBRIS QUANTITY ESTIMATES

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK.

APPENDIX C

FEMP SOIL PILE AND DEBRIS QUANTITY ESTIMATES

This appendix summarizes the in situ soil volumes generated at the FEMP during various removal actions, maintenance, and construction projects. Table C-1 lists these projects, the locations where the soil was excavated and stored, the operable unit responsible for the generation, the associated category (i.e., I or II), and the volume in cubic yards.

This appendix also provides summary information concerning unbulked and bulked volumes and their associated weights for materials (i.e., debris) to be generated from the dismantlement of OU3 components during the OU3 interim remedial action. Estimates for the OU3 FS material categories, as defined during the development of the OU3 RI/FS Report, are provided for each component and are summed to provide complex totals. The complexes are listed in the same order as the sequence for the base schedule provided in the final OU3 Remedial Design Prioritization and Sequencing Report (June 1995).

Table C-2 lists unbulked volumes of OU3 materials for each component and complex. These volume estimates have been taken from the FEMP Sitewide Waste Information, Forecasting, and Tracking System (SWIFTS) database, which is the official FEMP database for material estimates and is constantly being updated with improved, more detailed volume estimates.

Table C-3 provides bulked volume estimates for OU3 materials. These numbers were calculated by multiplying media-specific bulking factors with the unbulked volume estimates provided in Table C-2. These bulking factors originated during the development of the OU3 Proposed Plan/Environmental Assessment for the Interim Remedial Action (December 1993) and have been further refined from data gathered from Removal No. 19 (Plant 7 Dismantling) and from construction industry standards.

The estimates of OU3 material tonnage in Table C-4 are calculated by multiplying unbulked material densities to unbulked volume estimates provided in Table C-2. These material densities are either generally well-known chemical properties (e.g., the density of steel is 490 pounds per cubic foot) or were provided by the manufacturer of the material (e.g., the density of transite is 112 pounds per cubic foot).

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

TABLE C–1 Volumes of FEMP Soil Piles

Project	Location Generated	OU	Category	Location Moved From Longitude	Location Moved From Latitude	Location Moved To Longitude	Location Moved To Latitude	Volume (CY)
AWWT Area	North Side	5	I	84° 41' 32.5"	39° 17' 46.5"	84° 41' 25"	39° 17' 30"	190
AWWT Area IV	East Side of Building 51	3	I	84° 41' 29.5"	39° 17' 46.5"	84° 41' 31"	39° 17' 59.5"	200
AWWT Area III	South Ammonia Tank Farm	5	I	84° 41' 29.5"	39° 17' 46.3"	84° 41' 25"	39° 17' 30"	2,667
AWWT Area II	Pipeline from Building 51 to SWRB	5	I	84° 41' 25"	39° 17' 42"	84° 41' 25"	39° 17' 30"	150
Checkpoint Awning Project	West Side of T–50	3	I	84° 41' 10.4"	39° 17' 47.5"	84° 41' 31"	39° 17' 59.5"	10
Laundry Sump Project	North of Services Building	3	I	84° 41' 16.3"	39° 17' 49.5"	84° 41' 31"	39° 17' 59.5"	
Lab Hoist Installation Project	Northwest Corner of Northern Lab Courtyard	3	I	84° 41' 23.4"	39° 17' 48.7"	84° 41' 31"	39° 18' 00.5"	5
Site Consolidation Parking Lot	West of Building 45	5	I	84° 41' 25"	39° 17' 20"	Along the road base from:		4,500
EDR Trailer Project	South Side of Building 20B (West Tank H)	3	I	84° 41' 16"	39° 18' 03"	84° 41' 25"	39° 17' 59"	2
Horizontal Grout Project Soils	North of Sewage Treatment Plant	5	I	84° 40' 50"	39° 18' 05"	84° 41' 25"	39° 17' 20"	1,243
Waste Plant Brine Pit	Northwest Corner of Building 10A	3	I	84° 41' 17.3"	39° 18' 06"			8
South Plume Recovery Well Cutting	Floodplain	5	I			84° 41' 25"	39° 17' 30"	39
Building 10 Excavation	Building 10 Northwest of Boiler Plant	3	I	84° 41' 18"	39° 18' 07"	84° 41' 15.5"	39° 18' 00.5"	4
Container Staging Area	Northeast of Building 82 (Buffer Zone)	5	I	Area Bounded on E and W by:		84° 41' 25"	39° 17' 30"	7,407
Building 78 Southeast	Southeast of Building 78	3	I	84° 41' 03"	39° 18' 03.3"	84° 41' 17"	39° 18' 15.5"	
Nitric Acid Tank Car	Rail Siding Northeast of Building 64	3	I	84° 41' 09.8"	39° 18' 10.8"	84° 41' 29.2"	39° 17' 48"	1
Nitric Acid Tank Car	Rail Siding Northeast of Building 64	3	I	84° 41' 09.8"	39° 18' 10.8"	84° 41' 12"	39° 18' 09"	3
Great Miami River Chr. Project	18 Sample Points at Outfall	5	I			84° 41' 25"	39° 17' 30"	3
RvA 14	Sewage Treatment Plant	3	I	84° 40' 43"	39° 17' 55"	84° 41' 25"	39° 17' 30"	2,257
Common Carrier Staging	Southeast of Building 82	5	I	84° 41' 01.9"	39° 17' 49.9"	84° 41' 25"	39° 17' 30"	500
BDN Pipe Repair	West Side of Building 18H	3	I	84° 41' 26.8"	39° 17' 52.6"	84° 41' 29.9"	39° 17' 57.6" (9yd)	14
Water Main Repair at Laundry	North Side of Building 11 (Laundry)	3	I	84° 41' 16.3"	39° 17' 49.7"	84° 41' 07.4"	39° 18' 01.6"	10
SPIT Project	Northwest Corner of SWRB (18E)	5	I	84° 41' 21.5"	39° 17' 39"	84° 41' 25"	39° 17' 30"	100
Electrical Sub–Station	Main Electrical Station (16A)	3	I	84° 41' 04"	39° 17' 48"	84° 41' 31"	39° 17' 59"	14
UST #5	Northwest Corner of Building 46	3	I (UST)	84° 41' 07.7"	39° 17' 49.9"	84° 41' 17"	39° 18' 09"	3
Oil Spill at Building 53A	South Side of Building 53A	3	PCS I	84° 41' 14"	39° 17' 48"	84° 41' 16"	39° 18' 10"	2
AWWT Area IV	East Side of Building 51	3	II	84° 41' 31"	39° 18' 00.5"	84° 41' 31"	39° 18' 00.5"	198
AWWT Area VI	Pipeline from BDN to Building 51	3	II	84° 41' 19"–29"	39° 17' 50.5"	84° 41' 31"	39° 17' 00.5"	30
AWWT Area VI (cont.)				84° 41' 19"	39° 17' 49.3"–55"			
Laundry Sump Project	North of Services Building	3	II	84° 41' 16.3"	39° 17' 49.5"	84° 41' 31"	39° 18' 00.5"	3
Fuel Loading Station Project	Northwest Corner of Building 82	3	II	84° 41' 03"	39° 17' 52"	84° 41' 31"	39° 17' 00.5"	17
Building 78 Soils North Side	North Side of Building 78	3	II	84° 41' 03.5"	39° 18' 05"	84° 41' 25"	39° 17' 30"	100
Plant 7 Utilities Capping	West Side of Plant 7	3	II	84° 41' 91"	39° 17' 53"	84° 41' 12"	39° 18' 09"	5
Waste Water Sump Pump	South Side of Building 20B and Piping	3	II	84° 41' 90"	39° 17' 53"	84° 41' 31"	39° 18' 00.5"	2
Lab Upgrade	Northwest Side of Building 15A	3	II	84° 41' 25"	39° 17' 49"	84° 41' 31"	39° 17' 00.5"	1,200
EPA/Parsons Trailer Project	East Side of Building 46	3	II	84° 41' 06.5"	39° 17' 48"	84° 41' 12"	39° 18' 09"	86
Plant 1 Pad Upgrade	North of Plant 1	3	II	Trench E to W :		84° 41' 31"	39° 18' 00.5"	140
RvA 14	Sewage Treatment Plant	3	II	84° 40' 53"	39° 17' 50"	84° 41' 12"	39° 18' 09"	400
Storm Sewer Upgrade	A Street West of BDN Faciliy	3	II					100
Storm Sewer Upgrade	Intersection of A and 101st	3	II					309
Storm Sewer Upgrade	Northwest Corner of Plant 6	3	II	84° 41' 09"	39° 17' 57.5"	Pending Relocation		341
Waste Pit 5 Construction Activity	Waste Pit 5	1	II Th	84° 41' 45"	39° 18' 10"	84° 41' 35"	39° 18' 13"	3
Water Supply Tie–In Project						84° 41' 25"	39° 17' 30"	
RvA 14						Currently stored in WMB at FEMP		500
ISA #3	Southeast of Plant 5	3		84° 41' 13"	39° 17' 50.5"	Pending Characterization and Relocation		10
SWRB Excess								17,000
Total								**39,775**

020000

7221

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

TABLE C-2 Operable Unit 3 Unbulked Material Volume Estimates (in cubic feet)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component/ Complex Totals
Building 4A											
Green Salt Plant	4 A	5,844	82,467	8,873	195	0	0	5,017	866	11,907	115,168
External Complex											
Skeet Range Building	28 F	0	22	0	2	0	0	0	0	0	24
Sewage Treatment Plant Incinerator	39 D	10	643	0	0	203	0	189	23	112	1,179
Decontamination Building	69	156	401	28	17	5,625	0	0	116	1,513	7,855
External Complex Total		165	1,065	28	19	5,628	0	189	139	1,625	9,058
Thorium/Plant 9 Complex											
Special Products Plant	9 A	2,010	63,984	6,816	441	233	0	3,599	1,011	13,365	91,460
Plant 9 Sump Treatment Facility	9 B	33	852	92	4	81	0	161	46	524	1,794
Plant 9 Dust Collector	9 C	6	46	0	3	0	0	0	14	32	102
Plant 9 Substation	9 D	18	112	0	0	0	0	221	10	700	1,060
Plant 9 Cylinder Shed	9 E	1	0	0	0	0	0	6	3	16	26
Electrostatic Precipitator	9 F	4	65	3	3	0	0	12	15	48	152
Magnesium Storage Building	32 A	99	311	0	2	5,023	0	0	40	1,791	7,267
Building 32 Covered Loading Dock	32 B	17	19	0	0	0	0	0	3	293	332
Thorium Warehouse	64	197	1,423	0	106	1,200	0	25	74	1,489	4,514
(Old) Plant 5 Warehouse	65	269	640	0	72	0	0	0	54	789	1,824
D & D Building	78	239	4,333	418	49	8,160	0	44	88	4,961	18,291
Plant 9 Warehouse	81	81	376	0	40	0	0	0	49	120	665
Thorium/Plant 9 Complex Total		2,975	72,160	7,330	721	14,698	0	4,068	1,406	24,128	127,486
Boiler Plant/Water Plant Complex											
Boiler Plant	10 A	1,800	55,837	6,006	117	5,480	0	4,612	378	2,951	77,180
Boiler Plant Maintenance Building	10 B	41	174	4	21	580	0	43	21	138	1,023
Wet Salt Storage Bin	10 C	7	19	2	0	1,598	0	0	25	123	1,775
Utilities Heavy Equipment Building	10 E	12	109	1	13	0	0	0	10	381	526
Pump Station & Power Center	20 A	56	622	58	4	0	0	202	87	780	1,809
Water Plant	20 B	224	5,032	540	23	328	0	165	265	1,612	8,188
Cooling Towers	20 C	23	177,399	0	268	0	0	434	85	4,971	183,181
Process Water Storage Tank	20 H	0	47	0	0	8,100	0	0	182	928	9,257
Railroad Scale House	24 A	0	4	0	0	360	0	0	3	67	433
Coal Pile[1]	P-005	0	0	0	0	0	0	0	0	0	0
Boiler Plant/Water Plant Complex Total		2,163	239,243	6,611	446	16,446	0	5,457	1,054	11,952	283,371
Tank Farm Complex											
Main Tank Farm	19 A	221	21,241	0	0	2,430	0	0	140	327	24,358
Tank Farm Control House	19 C	12	323	29	2	1,300	0	28	14	545	2,254
Old North Tank Farm	19 D	0	12,006	0	0	486	0	0	59	311	12,856
Tank Farm Lime Slitter Building	19 E	28	585	60	6	0	0	0	22	104	805
Tank Farm Complex Total		261	34,149	89	9	4,216	0	28	234	1,286	40,273
Plant 1 Complex											
Preparation Plant	1 A	1,647	40,300	4,325	339	5,019	0	2,757	1,290	9,924	65,600
Plant 1 Storage Shelter	1 B	124	69	0	32	0	0	0	40	336	602
Chemical Warehouse	30 A	620	1,156	0	1	320	0	1,871	167	3,144	7,279
Drum Storage Warehouse	30 B	8	80	0	5	0	0	0	21	129	242
CP Storage Warehouse	56 A	134	301	0	53	0	0	11	71	933	1,503
Storage Shed (West)	56 B	0	17	0	4	0	0	0	31	303	355
Storage Shed (East)	56 C	0	17	0	6	0	0	0	24	323	370
Quonset Hut #1	60	46	148	0	17	0	0	0	9	54	274
Quonset Hut #2	61	25	106	0	14	0	0	0	11	70	226
Quonset Hut #3	62	25	106	0	14	0	0	333	6	43	527
KC-2 Warehouse	63	371	899	0	0	9,146	0	50	106	7,211	17,782
Drum Reconditioning Building	66	51	5,463	580	24	0	0	21	127	619	6,884
Plant 1 Thorium Warehouse	67	117	157	0	24	0	0	0	52	411	760
General In-Process Warehouse	71	231	569	0	0	5,376	0	0	104	6,565	12,845
Drum Storage Building	72	51	64	0	0	0	0	113	48	280	556
Tension Support Structure #4	TS-004	408	764	0	0	0	0	0	33	335	1,541
Tension Support Structure #5	TS-005	408	797	0	0	0	0	0	33	335	1,574
Tension Support Structure #6	TS-006	45	129	0	0	0	0	0	11	74	259
Plant 1 Complex Total		4,312	51,138	4,905	534	19,860	0	5,156	2,184	31,089	119,179
Maintenance Complex											
Main Maintenance Building	12 A	1,454	8,855	718	82	26,554	0	5,426	295	19,214	62,598
Cylinder Storage Building	12 B	13	41	0	83	1,556	0	0	29	542	2,264
Lumber Storage Building	12 C	24	28	0	12	0	0	0	16	196	276
Maintenance Building Warehouse	12 D	53	257	0	34	0	0	0	53	1,634	2,031
Railroad Engine House	24 B	12	141	7	0	1,733	0	0	30	470	2,395
Propane Storage	38 A	11	415	38	0	1,421	0	0	93	288	2,266
Cylinder Filling Station	38 B	2	2,022	0	1	0	0	0	57	279	2,361
Maintenance Complex Total		1,570	11,760	763	212	31,264	0	5,426	574	22,623	74,191
East Warehouses Complex											
Elevated Potable Storage Tank	20 D	521	224	0	0	0	0	0	35	347	1,127
Finished Products Warehouse (4A Warehouse)	77	205	762	0	84	0	0	0	88	144	1,284
Plant 6 Warehouse	79	171	696	0	74	0	0	0	64	96	1,101
Receiving/Incoming Materials Inspection	82	122	791	33	64	2,400	0	55	63	427	3,956
East Warehouses Complex Total		1,020	2,474	33	222	2,400	0	55	251	1,014	7,469
Plant 3 Complex											
Ozone Building	3 B	31	45	1	0	0	0	119	36	193	425
NAR Control House	3 C	71	8,012	0	0	0	0	407	89	1,637	10,217
NAR Towers	3 D	380	42,257	0	2	0	0	18	331	637	43,626
Hot Raffinate Building	3 E	195	22,790	2,479	17	5,940	0	543	229	928	33,121
Harshaw Digestion Fume Recovery	3 F	122	1,140	0	1	0	0	0	55	195	1,514
Refrigeration Building	3 G	21	914	98	6	0	0	130	30	531	1,730
Combined Raffinate Tanks	3 J	100	16,516	0	0	0	0	0	138	454	17,208
Old Cooling Water Tower	3 K	0	36	0	0	78	0	0	37	195	347
Incinerator Building	39 A	186	365	18	0	0	0	568	94	1,007	2,239
Incinerator Sprinkler Riser House	39 C	2	316	6	0	241	0	0	17	90	672
Plant 3 Complex Total		1,109	92,392	2,603	25	6,259	0	1,786	1,057	5,866	111,098
Plant 2 Complex											
Ore Refinery Plant	2 A	3,718	139,030	14,842	252	8,889	400	4,061	813	11,592	183,597
Metal Dissolver Building	2 D	134	8,733	912	4	0	0	347	142	1,855	12,127
NFS Storage and Pump House	2 E	31	7,232	0	0	518	0	0	120	255	8,128
Cold Side Ore Conveyor	2 F	44	5,171	0	1	0	0	91	42	207	6,557
Hot Side Ore Conveyor	2 G	39	8,038	0	0	0	0	62	41	178	8,357
Waste Oil Decant Shelter	39 B	24	18	1	3	0	0	0	14	64	124
Plant 2 Complex Total		3,963	169,221	15,755	260	9,407	400	4,561	1,172	14,150	218,891

TABLE C–2 Operable Unit 3 Unbulked Material Volume Estimates (in cubic feet)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component Complex Totals
Plant 8 Complex											
Recovery Plant	8 A	2,349	63,634	6,768	181	7,104	0	3,409	1,409	16,786	101,639
Plant 8 Maintenance Building	8 B	34	122	2	0	2,450	0	117	60	785	3,571
Rotary Kiln/Drum Reconditioning	8 C	1,557	34,468	3,760	189	3,800	0	0	132	6,817	50,724
Plant 8 Railroad Filter Building	8 D	4	45	4	1	0	0	0	13	48	115
Drum Conveyor Shelter	8 E	24	29	0	3	0	0	0	9	48	113
Plant 8 Old Drum Washer	8 F	0	0	0	2	0	0	0	10	32	44
Plant 8 Warehouse	80	102	304	0	53	0	0	0	92	386	937
Plant 8 Complex Total		4,070	98,602	10,534	430	13,354	0	3,526	1,725	24,902	157,142
General Sump Complex											
General/Refinery Sump Control Building	2 B	113	5,464	703	9	177	0	172	77	1,316	9,030
Bulk Lime Handling Building	2 C	31	2,126	233	0	0	0	91	41	248	2,770
Maintenance Building	3 A	96	8,823	959	10	0	0	440	84	1,728	12,139
Refinery Sump	3 H	65	13,106	0	0	0	0	0	136	370	13,677
Electrical Power Center Building	3 L	51	5,518	578	0	0	0	277	69	1,160	7,654
General Sump	18 B	65	1,876	0	2	0	0	0	230	713	2,886
Biodenitrification Towers	18 D	557	6,003	565	70	0	0	107	192	4,032	11,545
BDN Effluent Treatment Facility	18 H	9	34,217	3,790	14	0	0	0	68	758	38,855
General Sump Complex Total		986	78,133	6,848	104	177	0	1,087	896	10,325	98,555
Plant 5 Complex											
Plant 4 Warehouse	4 B	166	458	0	66	0	0	0	89	424	1,203
Metals Production Plant	5 A	5,088	174,751	18,916	477	19,243	0	6,693	1,653	16,797	243,620
Plant 5 Ingot Pickling	5 B	59	2,597	277	12	0	0	0	65	239	3,248
Plant 5 Electrical Substation	5 C	8	776	78	3	0	0	0	48	150	1,063
West Derby Breakout/ Slag Milling	5 D	1,553	22,336	2,410	83	223	0	0	267	777	27,648
Plant 5 Filter Building	5 E	38	93	0	20	0	0	0	27	264	442
Plant 5 Covered Storage Pad	5 F	143	219	0	27	0	0	0	30	280	699
Plant 5 Ingot Storage Shelter	5 G	26	33	0	7	0	0	0	8	69	143
Slag Recycling Building	55 A	310	6,193	660	16	0	0	501	116	2,149	9,945
Slag Recycling Pit/Elevator	55 B	56	482	50	5	0	0	100	40	143	877
Plant 5 Complex Total		7,446	207,938	22,390	716	19,466	0	7,294	2,343	21,293	288,888
Plant 6 Complex											
Metals Fabrication Plant	6 A	5,453	187,559	20,184	518	8,652	0	10,793	1,288	6,830	241,278
Plant 6 Covered Storage Area	6 B	44	19	0	9	0	0	0	32	104	207
Plant 6 Electrostatic Precipitator (South)	6 C	12	67	5	12	0	0	0	49	155	300
Plant 6 Electrostatic Precipitator (Central)	6 D	6	34	0	8	0	0	0	40	123	211
Plant 6 Electrostatic Precipitator (North)	6 E	12	568	61	12	0	0	0	48	155	856
Plant 6 Salt Oil Heat Treat Building	6 F	20	2,211	242	11	0	0	0	251	274	3,010
Plant 6 Sump Building	6 G	369	9,349	1,069	42	216	0	57	219	1,901	13,156
Plant 6 Complex Total		5,917	199,661	21,500	613	8,868	0	10,851	1,927	9,543	259,019
Liquid Storage Complex											
Methanol Tank	18 J	18	48	0	0	324	0	0	9	20	419
Low Nitrate Tank	18 K	8	459	0	0	0	0	0	5	20	492
High Nitrate Tank	18 L	8	459	0	0	0	0	0	6	24	497
Well House #1	20 E	0	61	6	0	299	0	0	20	147	533
Well House #2	20 F	0	72	7	0	301	0	0	20	147	546
Well House #3	20 G	2	340	37	2	395	0	0	18	180	974
Gas Meter Building	22 A	2	41	3	0	579	0	0	20	134	779
Storm Sewer Lift Station	22 B	2	252	27	2	255	0	0	25	98	661
Scale House & Weigh Scale	22 D	3	14	0	0	0	0	16	18	96	147
Pump House–HP Fire Protection	26 A	168	547	54	4	5,813	0	0	38	496	7,121
Elevated Water Storage Tank	26 B	1,763	480	0	0	540	0	0	66	135	2,985
Rust Engineering Building	45 A	169	2,396	0	111	3,028	0	513	188	489	6,891
Utility Shed East of Rust Trailers	45 B	0	6	0	0	0	0	0	18	170	194
Liquid Storage Complex Total		2,144	5,177	134	119	11,532	0	528	451	2,154	22,240
Pilot Plant Complex											
Pilot Plant Wet Side	13 A	170	16,754	1,809	13	10,429	0	407	457	3,958	33,997
Pilot Plant Maintenance Building	13 B	12	237	12	0	3,366	0	16	27	682	4,350
Sump Pump House	13 C	4	306	33	1	333	0	0	35	135	848
Pilot Plant Thorium Tank Farm	13 D	0	9,692	0	0	0	0	0	65	215	9,972
Pilot Plant Annex	37	144	10,610	1,137	0	6,200	0	0	100	1,834	20,026
Six to Four Reduction Facility #1	54 A	566	25,624	2,815	110	10,478	0	391	485	5,560	46,030
Pilot Plant Shelter	54 B	24	113	0	14	0	0	0	141	741	1,034
Pilot Plant Dissociator Shelter	54 C	24	1,525	154	47	0	0	0	21	20	1,801
Pilot Plant Warehouse	68	154	372	0	6	810	0	366	52	439	2,199
Pilot Plant Complex Total		1,100	65,233	5,970	190	31,616	0	1,180	1,383	13,585	120,256
Laboratory Complex											
Laboratory	15 A	893	33,073	3,126	561	84,815	0	4,363	2,220	27,054	156,105
Laboratory Chemical Storage Building	15 B	13	541	0	10	869	0	0	10	4	1,448
Laboratory Complex Total		906	33,614	3,126	572	85,684	0	4,363	2,230	27,058	157,552
Electrical Station Complex											
Main Electrical Station	16 A	96	4,152	0	0	1,836	0	0	23	414	6,523
Electrical Substation	16 B	3	1,785	97	21	884	0	0	0	219	3,000
Electrical Panels & Transformer	16 C	0	96	0	0	0	0	0	23	138	257
Main Electrical Switch House	16 D	3	492	51	0	758	0	16	23	120	1,462
Main Electrical Transformers	16 E	0	9,847	0	0	0	0	0	23	120	9,990
Trailer Substation #1	16 F	3	204	0	11	0	0	0	0	0	208
Trailer Substation #2	16 G	2	208	0	11	0	0	0	0	0	211
Main Electrical Strainer House	26 C	1	61	6	0	267	0	5	26	120	485
Engine House/Garage	31 A	127	794	43	0	4,527	0	0	40	2,312	7,843
Heavy Equipment Building	46	220	502	15	62	1,040	0	48	66	784	2,731
Electrical Station Complex Total		456	18,140	211	85	9,312	0	70	217	4,216	32,708
Sewage Treatment Plant Complex											
Chlorination Building	25 A	0	100	8	0	462	0	0	8	92	669
M.H. #175/Effluent Line/Sampling Building	25 B	0	159	15	1	0	0	0	8	40	223
Sewage Lift Station Building	25 C	4	99	10	2	529	0	0	9	123	776
U.V. Disinfection Building	25 D	0	139	13	0	335	0	0	10	40	538
Digester & Control Building	25 E	30	392	37	2	3,828	0	0	39	261	4,590
Sewage Treatment Plant Complex Total		35	890	83	6	5,153	0	0	74	556	6,796

TABLE C–2 Operable Unit 3 Unbulked Material Volume Estimates (in cubic feet)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component Complex Totals
Administration Complex											
Service Building	11	164	29,479	0	286	147,952	0	1,011	994	18,599	198,485
Administration Building	14 A	54	10,669	0	37	42,856	0	2,048	187	9,990	65,841
Building 14 EOC Generator Set	14 B	0	271	0	0	0	0	0	0	0	271
Security Building	28 A	10	895	0	16	8,178	0	0	29	3,730	12,859
Human Resources Building	28 B	235	1,097	0	30	3,198	0	554	57	3,727	8,897
Health & Safety Building	53 A	334	6,972	0	157	47,337	0	3,247	448	20,196	78,691
In-Vivo Building	53 B	24	1,347	0	26	0	0	141	25	1,719	3,282
Administration Complex Total		822	50,730	0	553	249,521	0	7,000	1,740	57,961	368,326
Miscellaneous Complex											
10-Plex North Substation	16 H	0	840	0	0	0	0	0	0	0	840
10-Plex South Substation	16 J	0	840	0	0	0	0	0	0	0	840
Clearwell Pump House	18 G	2	115	8	0	0	0	23	1	195	345
Meteorological Tower	23	8	36	0	0	0	0	0	0	0	44
10-Plex Sewage Lift Station	25 J	0	80	0	0	0	0	0	0	0	80
Guard Post on West End of 2nd Street	28 D	0	11	0	0	0	0	0	23	214	247
Guard Post East of T-81	28 E	2	6	0	1	0	0	0	0	51	61
Guard Post South of Building 51	28 G	1	9	0	1	0	0	0	0	50	61
Utility Lines	G-004	0	16,282	312	0	0	0	0	10,284	0	26,878
Process Trailers	G-006	0	0	0	0	0	0	0	0	71,136	71,136
Non-Process Trailers	G-007	0	0	0	0	0	0	0	0	305,136	305,136
Pipe Bridges	G-008	2,262	0	0	0	351	0	0	0	0	2,613
Miscellaneous Complex Total		2,275	18,220	320	3	351	0	23	10,308	376,782	408,281
Below Grade Components		9,752	43,576	13,949	0	3,952,270	20,292	3,373	19	27,421	4,070,652
Operable Unit 3 Total		59,269	1,576,124	132,054	6,033	4,497,662	20,692	71,036	32,249	701,436	7,096,596

[1] The quantities of stockpiled coal vary seasonally. No significant quantities of coal are expected to remain after the Boiler Plant/Water Plant Complex is shut down.

DRAFT

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

TABLE C-3 Operable Unit 3 Bulked Material Volume Estimates (in cubic feet)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component Complex Totals
Building 4A											
Green Salt Plant	4 A	97,590	281,893	30,741	390	0	0	6,054	2,922	16,626	436,215
External Complex											
Skeet Range Building	28 F	0	50	0	4	0	0	0	0	0	54
Sewage Treatment Plant Incinerator	39 D	162	2,218	0	0	263	0	241	34	134	3,052
Decontamination Building	69	2,599	821	57	33	7,313	0	0	235	2,249	13,307
External Complex Total		2,761	3,089	57	38	7,576	0	241	269	2,383	16,413
Thorium/Plant 9 Complex											
Special Products Plant	9 A	33,569	218,725	23,717	882	303	0	4,319	3,473	17,715	302,704
Plant 9 Sump Treatment Facility	9 B	559	2,759	302	8	105	0	193	125	685	4,736
Plant 9 Dust Collector	9 C	102	93	0	7	0	0	0	39	38	279
Plant 9 Substation	9 D	293	223	0	0	0	0	265	12	845	1,638
Plant 9 Cylinder Shed	9 E	14	0	0	0	0	0	7	4	19	44
Electrostatic Precipitator	9 F	68	148	9	7	0	0	15	35	57	339
Magnesium Storage Building	32 A	1,658	663	0	5	6,530	0	0	93	2,724	11,672
Building 32 Covered Loading Dock	32 B	290	37	0	0	0	0	0	4	426	757
Thorium Warehouse	64	3,297	3,720	0	212	1,560	0	40	215	2,758	11,802
(Old) Plant 5 Warehouse	65	4,497	1,315	0	144	0	0	0	166	1,505	7,626
D & D Building	78	3,985	14,023	1,431	97	10,608	0	88	265	7,395	37,893
Plant 9 Warehouse	81	1,347	761	0	80	0	0	0	132	143	2,463
Thorium/Plant 9 Complex Total		49,679	242,468	25,459	1,442	19,107	0	4,927	4,562	34,311	381,954
Boiler Plant/Water Plant Complex											
Boiler Plant	10 A	30,059	191,386	20,869	233	7,124	0	5,880	1,255	5,519	262,325
Boiler Plant Maintenance Building	10 B	687	376	10	42	754	0	82	45	219	2,215
Wet Salt Storage Bin	10 C	120	61	7	0	2,077	0	0	32	148	2,445
Utilities Heavy Equipment Building	10 E	204	222	2	26	0	0	0	17	464	935
Pump Station & Power Center	20 A	930	1,243	116	8	0	0	243	287	1,044	3,870
Water Plant	20 B	3,738	15,011	1,630	46	426	0	197	937	2,301	24,287
Cooling Towers	20 C	380	620,109	0	537	0	0	521	271	9,838	631,656
Process Water Storage Tank	20 H	0	94	0	0	10,530	0	0	232	1,114	11,970
Railroad Scale House	24 A	0	7	0	0	468	0	0	4	121	599
Coal Pile[1]	P-005	0	0	0	0	0	0	0	0	0	0
Boiler Plant/Water Plant Complex Total		36,119	828,509	22,634	892	21,380	0	6,923	3,080	20,767	940,303
Tank Farm Complex											
Main Tank Farm	19 A	3,694	72,752	0	0	3,159	0	0	384	392	80,380
Tank Farm Control House	19 C	204	1,041	102	5	1,690	0	57	16	726	3,841
Old North Tank Farm	19 D	0	42,000	0	0	632	0	0	71	373	43,076
Tank Farm Lime Slitter Building	19 E	461	1,974	269	13	0	0	0	32	124	2,814
Tank Farm Complex Total		4,359	117,766	372	18	5,481	0	57	503	1,615	130,111
Plant 1 Complex											
Preparation Plant	1 A	27,497	135,910	14,795	679	6,524	0	3,375	4,583	12,500	205,863
Plant 1 Storage Shelter	1 B	2,077	138	0	64	0	0	0	48	503	2,830
Chemical Warehouse	30 A	10,361	2,347	0	3	416	0	2,345	400	4,698	20,570
Drum Storage Warehouse	30 B	136	173	0	9	0	0	0	28	174	521
CP Storage Warehouse	56 A	2,237	609	0	106	0	0	18	147	1,662	4,778
Storage Shed (West)	56 B	0	33	0	8	0	0	0	37	476	555
Storage Shed (East)	56 C	0	33	0	13	0	0	0	28	548	623
Quonset Hut #1	60	773	304	0	34	0	0	0	11	71	1,193
Quonset Hut #2	61	412	211	0	28	0	0	0	14	93	758
Quonset Hut #3	62	412	212	0	28	0	0	433	7	60	1,152
KC-2 Warehouse	63	6,199	1,817	0	0	11,889	0	65	273	10,580	30,824
Drum Reconditioning Building	66	849	18,429	1,994	49	0	0	34	266	845	22,466
Plant 1 Thorium Warehouse	67	1,953	314	0	47	0	0	0	62	605	2,981
General In-Process Warehouse	71	3,858	1,177	0	0	6,989	0	0	204	9,576	21,804
Drum Storage Building	72	855	131	0	0	0	0	136	60	362	1,545
Tension Support Structure #4	TS-004	6,816	1,582	0	0	0	0	0	40	531	8,969
Tension Support Structure #5	TS-005	6,816	1,647	0	0	0	0	0	40	531	9,034
Tension Support Structure #6	TS-006	750	261	0	0	0	0	0	13	104	1,128
Plant 1 Complex Total		72,002	165,328	16,789	1,069	25,818	0	6,406	6,281	43,920	337,613
Maintenance Complex											
Main Maintenance Building	12 A	24,282	27,127	2,482	165	34,520	0	7,076	755	25,785	122,192
Cylinder Storage Building	12 B	215	82	0	167	2,023	0	0	35	765	3,286
Lumber Storage Building	12 C	409	56	0	23	0	0	0	19	324	832
Maintenance Building Warehouse	12 D	893	529	0	67	0	0	0	117	2,001	3,607
Railroad Engine House	24 B	206	363	23	0	2,253	0	0	45	665	3,555
Propane Storage	38 A	180	856	78	0	1,847	0	0	261	407	3,630
Cylinder Filling Station	38 B	27	7,046	0	2	0	0	0	80	335	7,490
Maintenance Complex Total		26,212	36,058	2,583	423	40,644	0	7,076	1,312	30,283	144,591
East Warehouses Complex											
Elevated Potable Storage Tank	20 D	8,698	528	0	0	0	0	0	90	416	9,732
Finished Products Warehouse (4A Warehouse)	77	3,430	1,536	0	169	0	0	0	280	181	5,595
Plant 6 Warehouse	79	2,855	1,401	0	147	0	0	0	307	315	4,725
Receiving/Incoming Materials Inspection	82	2,045	1,920	104	128	3,120	0	109	201	778	8,405
East Warehouses Complex Total		17,028	5,385	104	444	3,120	0	109	778	1,489	28,458
Plant 3 Complex											
Ozone Building	3 B	511	93	3	0	0	0	143	49	242	1,041
NAR Control House	3 C	1,193	27,539	0	0	0	0	488	166	2,040	31,427
NAR Towers	3 D	6,353	145,143	0	3	0	0	211	985	765	153,270
Hot Raffinate Building	3 E	3,257	78,527	8,619	34	7,722	0	652	571	1,339	100,722
Harshaw Digestion Fume Recovery	3 F	2,045	3,793	0	1	0	0	0	117	234	6,190
Refrigeration Building	3 G	348	3,134	341	11	0	0	156	42	637	4,669
Combined Raffinate Tanks	3 J	1,677	56,975	0	0	0	0	0	309	545	59,505
Old Cooling Water Tower	3 K	0	117	0	0	101	0	0	45	234	498
Incinerator Building	39 A	3,106	753	39	0	0	0	691	203	1,352	6,144
Incinerator Sprinkler Riser House	39 C	38	715	22	0	313	0	0	23	113	1,224
Plant 3 Complex Total		18,528	316,789	9,025	50	8,136	0	2,152	2,509	7,501	364,689
Plant 2 Complex											
Ore Refinery Plant	2 A	62,089	476,566	51,740	504	11,556	520	4,873	2,923	16,443	627,215
Metal Dissolver Building	2 D	2,239	29,616	3,174	9	0	0	417	274	2,470	38,198
NFS Storage and Pump House	2 E	49	24,786	0	0	674	0	0	358	326	26,192
Cold Side Ore Conveyor	2 F	743	21,474	0	2	0	0	109	63	254	22,645
Hot Side Ore Conveyor	2 G	654	27,965	0	0	0	0	74	74	222	29,010
Waste Oil Decant Shelter	39 B	409	37	1	6	0	0	0	23	76	553
Plant 2 Complex Total		66,183	580,465	54,916	521	12,229	520	5,474	3,715	19,791	743,814

TABLE C–3 Operable Unit 3 Bulked Material Volume Estimates (in cubic feet)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component/ Complex Totals
Plant 8 Complex											
Recovery Plant	8 A	39,220	211,459	22,890	362	9,235	0	4,091	5,184	24,257	316,698
Plant 8 Maintenance Building	8 B	563	245	5	0	3,185	0	234	92	1,347	5,671
Rotary Kiln/Drum Reconditioning	8 C	26,009	119,650	13,154	379	4,940	0	0	348	9,683	174,162
Plant 8 Railroad Filter Building	8 D	58	111	10	2	0	0	0	27	57	276
Drum Conveyor Shelter	8 E	399	58	0	6	0	0	0	11	57	531
Plant 8 Old Drum Washer	8 F	0	0	0	5	0	0	0	23	38	67
Plant 8 Warehouse	80	1,705	614	0	106	0	0	0	161	464	3,048
Plant 8 Complex Total		67,964	332,135	36,059	860	17,360	0	4,325	5,846	35,903	500,452
General Sump Complex											
General/Refinery Sump Control Building	2 B	1,885	22,405	2,459	18	230	0	206	103	1,699	29,005
Bulk Lime Handling Building	2 C	511	7,245	799	0	0	0	109	88	384	9,137
Maintenance Building	3 A	1,595	30,510	3,347	20	0	0	528	143	2,145	38,288
Refinery Sump	3 H	1,084	45,211	0	0	0	0	0	346	445	47,085
Electrical Power Center Building	5 L	852	18,839	2,023	0	0	0	332	86	1,407	23,539
General Sump	16 B	1,084	3,751	0	4	0	0	0	591	936	6,366
Biodenitrification Towers	16 D	9,304	19,537	2,006	139	0	0	214	444	5,443	37,088
BDN Effluent Treatment Facility	18 H	149	119,544	13,259	28	0	0	0	104	949	134,033
General Sump Complex Total		16,464	267,042	23,893	209	230	0	1,390	1,905	13,408	324,540
Plant 5 Complex											
Plant 4 Warehouse	4 B	2,767	923	0	131	0	0	0	197	609	4,627
Metals Production Plant	5 A	84,962	601,069	65,785	955	25,016	0	8,167	6,100	23,517	815,571
Plant 5 Ingot Pickling	5 B	981	8,850	960	24	0	0	0	131	287	11,233
Plant 5 Electrical Substation	5 C	136	2,490	260	6	0	0	0	116	189	3,198
West Derby Breakout/ Slag Milling	5 D	25,941	76,727	8,381	165	290	0	0	654	932	113,091
Plant 5 Filter Building	5 E	635	187	0	40	0	0	0	32	417	1,311
Plant 5 Covered Storage Pad	5 F	2,391	437	0	55	0	0	0	36	436	3,355
Plant 5 Ingot Storage Shelter	5 G	426	67	0	13	0	0	0	10	103	619
Slag Recycling Building	5 A	5,178	21,279	2,307	32	0	0	601	223	2,939	32,558
Slag Recycling Pit/Elevator	55 B	934	1,607	171	11	0	0	120	85	172	3,100
Plant 5 Complex Total		124,351	713,636	77,865	1,432	25,306	0	8,888	7,583	29,601	988,662
Plant 6 Complex											
Metals Fabrication Plant	6 A	91,068	642,818	70,112	1,037	11,248	0	13,040	4,820	12,920	847,064
Plant 6 Covered Storage Area	6 B	736	37	0	18	0	0	0	73	124	989
Plant 6 Electrostatic Precipitator (South)	6 C	204	168	13	25	0	0	0	113	186	710
Plant 6 Electrostatic Precipitator (Central)	6 D	102	93	0	16	0	0	0	94	148	453
Plant 6 Electrostatic Precipitator (North)	6 E	204	1,929	209	24	0	0	0	109	186	2,662
Plant 6 Salt Oil Heat Treat Building	6 F	341	6,436	708	23	0	0	0	858	331	8,699
Plant 6 Sump Building	6 G	6,161	31,031	3,389	84	281	0	95	743	2,290	44,074
Plant 6 Complex Total		98,817	682,515	74,431	1,227	11,529	0	13,136	6,810	16,187	904,651
Liquid Storage Complex											
Methanol Tank	18 J	307	103	0	0	421	0	0	25	24	879
Low Nitrate Tank	18 K	136	925	0	0	0	0	0	9	24	1,094
High Nitrate Tank	18 L	136	925	0	0	0	0	0	9	29	1,099
Well House #1	20 E	0	184	19	0	389	0	0	29	217	839
Well House #2	20 F	0	222	23	0	391	0	0	29	217	882
Well House #3	20 G	26	1,176	128	4	514	0	0	22	283	2,154
Gas Meter Building	22 A	27	105	8	0	753	0	0	27	191	1,111
Storm Sewer Lift Station	22 B	38	829	90	4	331	0	0	50	120	1,462
Scale House & Weigh Scale	22 D	53	34	1	0	0	0	19	22	115	243
Pump House–HP Fire Protection	26 A	2,808	1,608	154	9	7,557	0	0	103	723	12,972
Elevated Water Storage Tank	26 B	29,447	1,138	0	0	702	0	0	193	163	31,642
Rust Engineering Building	45 A	2,824	6,994	0	221	3,934	0	1,025	572	706	16,276
Utility Shed East of Rust Trailers	45 B	0	11	0	0	0	0	0	22	263	296
Liquid Storage Complex Total		35,803	14,254	435	238	14,992	0	1,044	1,110	3,073	70,949
Pilot Plant Complex											
Pilot Plant Wet Side	13 A	2,834	55,669	6,080	26	13,557	0	514	1,502	6,213	86,395
Pilot Plant Maintenance Building	13 B	197	592	37	0	4,376	0	311	67	1,054	6,354
Sump Pump House	13 C	58	986	107	11	433	0	0	93	197	1,886
Pilot Plant Thorium Tank Farm	13 D	0	33,739	0	0	0	0	0	146	258	34,143
Pilot Plant Annex	37	2,410	36,169	3,936	0	8,060	0	0	295	2,669	53,538
Six to Four Reduction Facility #1	54 A	9,458	86,689	9,790	220	13,622	0	504	1,172	7,863	131,419
Pilot Plant Shelter	54 B	409	233	0	28	0	0	0	169	889	1,728
Pilot Plant Dissociator Shelter	54 C	409	5,150	561	94	0	0	0	73	24	6,311
Pilot Plant Warehouse	68	2,577	760	0	11	1,053	0	444	62	662	5,568
Pilot Plant Complex Total		18,363	221,987	20,511	380	41,101	0	1,593	3,578	19,830	327,342
Laboratory Complex											
Laboratory	15 A	14,910	101,660	10,197	1,123	110,260	0	8,693	8,493	42,866	298,201
Laboratory Chemical Storage Building	15 B	221	1,824	0	20	1,129	0	0	39	5	3,238
Laboratory Complex Total		15,131	103,484	10,197	1,143	111,389	0	8,693	8,532	42,870	301,439
Electrical Station Complex											
Main Electrical Station	16 A	1,637	14,320	0	0	2,387	0	0	27	732	19,104
Electrical Substation	16 B	49	4,875	338	43	1,149	0	0	0	308	6,761
Electrical Panels & Transformer	16 C	0	231	0	0	0	0	0	27	180	439
Main Electrical Switch House	16 D	44	1,668	177	0	986	0	20	27	143	3,065
Main Electrical Transformers	16 E	0	19,695	0	0	0	0	0	27	143	19,865
Trailer Substation #1	16 F	45	519	0	2	0	0	0	0	0	566
Trailer Substation #2	16 G	42	625	0	2	0	0	0	0	0	669
Main Electrical Strainer House	26 C	19	176	17	0	347	0	6	40	143	748
Engine House/Garage	31 A	2,113	2,040	137	0	5,865	0	0	96	3,509	13,780
Heavy Equipment Building	46	3,674	1,029	32	124	1,352	0	97	148	1,427	7,883
Electrical Station Complex Total		7,623	45,277	702	171	12,105	0	123	393	6,586	72,980
Sewage Treatment Plant Complex											
Chlorination Building	25 A	0	300	26	0	500	0	0	10	152	1,088
M.H. #175/Effluent Line/Sampling Building	25 B	0	517	52	2	0	0	0	13	48	632
Sewage Lift Station Building	25 C	66	328	34	4	688	0	0	13	174	1,308
U.V. Disinfection Building	25 D	8	424	42	0	435	0	0	20	48	977
Digester & Control Building	25 E	504	1,171	118	5	4,976	0	0	96	365	7,234
Sewage Treatment Plant Complex Total		578	2,739	272	11	6,700	0	0	153	786	11,239

7221

TABLE C–3 Operable Unit 3 Bulked Material Volume Estimates (in cubic feet)

Component	Component Designation	A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component/ Complex Totals
		OU3 FS Material Category									
Administration Complex											
Service Building	11	2,736	91,695	0	572	192,338	0	1,422	3,975	27,281	320,019
Administration Building	14 A	908	33,653	0	75	55,712	0	3,945	749	17,529	112,571
Building 14 EOC Generator Set	14 B	0	949	0	0	0	0	0	0	0	949
Security Building	28 A	170	2,417	0	33	10,631	0	0	118	5,911	19,281
Human Resources Building	28 B	3,924	3,238	0	61	4,157	0	1,107	228	6,272	18,987
Health & Safety Building	53 A	5,580	19,714	0	314	61,538	0	6,166	1,791	36,522	131,625
In-Vivo Building	53 B	406	4,464	0	51	0	0	281	99	2,503	7,806
Administration Complex Total		13,726	156,130	0	1,106	324,377	0	12,921	6,960	96,019	611,238
Miscellaneous Complex											
10-Plex North Substation	16 H	2	2,940	0	0	0	0	0	0	0	2,942
10-Plex South Substation	16 J	2	2,940	0	0	0	0	0	0	0	2,942
Clearwell Pump House	18 G	42	329	27	0	0	0	28	5	389	819
Meteorological Tower	23	129	126	0	0	0	0	0	0	0	255
10-Plex Sewage Lift Station	25 J	1	275	0	0	0	0	0	0	0	276
Guard Post on West End of 2nd Street	28 D	0	23	0	0	0	0	0	27	332	382
Guard Post East of T-81	28 E	25	14	0	3	0	0	0	0	68	110
Guard Post South of Building 51	28 G	14	18	0	2	0	0	0	0	65	99
Utility Lines	G-004	0	34,534	625	0	0	0	0	41,136	0	76,294
Process Trailers	G-006	0	0	0	0	0	0	0	0	142,272	142,272
Non-Process Trailers	G-007	0	0	0	0	0	0	0	0	610,272	610,272
Pipe Bridges	G-008	37,776	0	0	0	456	0	0	0	0	38,232
Miscellaneous Complex Total		37,990	41,200	652	5	456	0	28	41,168	753,398	874,897
Below Grade Components		162,857	87,646	27,899	0	5,137,951	26,380	4,942	76	54,842	5,502,591
Operable Unit 3 Total		990,128	5,245,795	435,536	12,067	5,846,987	26,900	96,500	110,041	1,251,189	14,015,143

[1] The quantities of stockpiled coal vary seasonally. No significant quantities of coal are expected to remain after the Boiler Plant/Water Plant Complex is shut down.

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

7221

TABLE C-4 Operable Unit 3 Material Weight Estimates (in tons)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component Complex Totals
Building 4A											
Green Salt Plant	4 A	1,432	2,296	246	44	0	0	285	2	72	4,376
External Complex											
Skeet Range Building	28 F	0	0	0	1	0	0	0	0	0	1
Sewage Treatment Plant Incinerator	39 D	2	2	0	0	15	0	13	0	0	32
Decontamination Building	69	38	17	1	0	216	0	0	0	16	290
External Complex Total		41	20	1	1	231	0	13	0	16	323
Thorium/Plant 9 Complex											
Special Products Plant	9 A	492	1,167	116	104	6	0	201	2	80	2,168
Plant 9 Sump Treatment Facility	9 B	6	20	2	0	6	0	9	0	2	48
Plant 9 Dust Collector	9 C	2	4	0	1	0	0	0	0	0	6
Plant 9 Substation	9 D	4	6	0	0	0	0	12	0	2	24
Plant 9 Cylinder Shed	9 E	0	0	0	0	0	0	0	0	0	1
Electrostatic Precipitator	9 F	1	3	0	1	0	0	1	0	0	6
Magnesium Storage Building	32 A	24	14	0	1	138	0	0	0	24	202
Building 32 Covered Loading Dock	32 B	4	0	0	0	0	0	0	0	4	8
Thorium Warehouse	64	48	49	0	20	33	0	1	0	23	174
(Old) Plant 5 Warehouse	65	66	23	0	13	0	0	0	0	13	115
D & D Building	78	58	63	6	6	281	0	1	0	49	464
Plant 9 Warehouse	81	20	15	0	8	0	0	0	0	0	43
Thorium/Plant 9 Complex Total		729	1,364	124	154	465	0	225	3	196	3,260
Boiler Plant/Water Plant Complex											
Boiler Plant	10 A	441	893	93	10	300	0	302	1	45	2,086
Boiler Plant Maintenance Building	10 B	10	7	0	3	16	0	1	0	1	39
Wet Salt Storage Bin	10 C	2	1	0	0	120	0	0	0	0	123
Utilities Heavy Equipment Building	10 E	3	3	0	3	0	0	0	0	1	10
Pump Station & Power Center	20 A	14	27	3	0	0	0	11	0	4	59
Water Plant	20 B	55	202	22	4	25	0	9	1	16	334
Cooling Towers	20 C	6	214	0	5	0	0	24	0	73	322
Process Water Storage Tank	20 H	0	2	0	0	608	0	0	0	1	611
Railroad Scale House	24 A	0	0	0	0	10	0	0	0	1	11
Coal Pile[1]	P-005	0	0	0	0	0	0	0	0	0	0
Boiler Plant/Water Plant Complex Total		530	1,349	119	26	1,078	0	348	2	143	3,594
Tank Farm Complex											
Main Tank Farm	19 A	54	132	0	0	182	0	0	0	0	370
Tank Farm Control House	19 C	3	4	0	1	36	0	0	0	3	47
Old North Tank Farm	19 D	0	28	0	0	36	0	0	0	0	65
Tank Farm Lime Slitter Building	19 E	7	5	0	1	0	0	0	0	0	13
Tank Farm Complex Total		64	168	1	2	254	0	0	0	4	494
Plant 1 Complex											
Preparation Plant	1 A	403	433	43	88	368	0	150	3	32	1,521
Plant 1 Storage Shelter	1 B	30	3	0	8	0	0	0	0	2	44
Chemical Warehouse	30 A	152	47	0	1	9	0	99	0	25	333
Drum Storage Warehouse	30 B	2	2	0	1	0	0	0	0	1	6
CP Storage Warehouse	56 A	33	13	0	9	0	0	0	0	13	68
Storage Shed (West)	56 B	0	0	0	1	0	0	0	0	2	4
Storage Shed (East)	56 C	0	0	0	2	0	0	0	0	3	5
Quonset Hut #1	60	11	4	0	4	0	0	0	0	0	19
Quonset Hut #2	61	6	2	0	3	0	0	0	0	0	12
Quonset Hut #3	62	6	2	0	3	0	0	23	0	0	36
KC-2 Warehouse	63	91	34	0	0	252	0	3	0	94	474
Drum Reconditioning Building	66	12	54	4	6	0	0	11	0	3	81
Plant 1 Thorium Warehouse	67	29	4	0	5	0	0	0	0	3	40
General In-Process Warehouse	71	57	25	0	0	148	0	0	0	84	313
Drum Storage Building	72	13	2	0	0	0	0	6	0	1	22
Tension Support Structure #4	TS-004	100	17	0	0	0	0	0	0	5	123
Tension Support Structure #5	TS-005	100	18	0	0	0	0	0	0	5	124
Tension Support Structure #6	TS-006	11	3	0	0	0	0	0	0	1	15
Plant 1 Complex Total		1,056	664	47	131	777	0	284	4	276	3,240
Maintenance Complex											
Main Maintenance Building	12 A	356	129	7	14	820	0	271	1	107	1,706
Cylinder Storage Building	12 B	3	1	0	2	79	0	0	0	6	90
Lumber Storage Building	12 C	6	1	0	2	0	0	0	0	2	11
Maintenance Building Warehouse	12 D	13	11	0	8	0	0	0	0	4	36
Railroad Engine House	24 B	3	4	0	0	48	0	0	0	5	60
Propane Storage	38 A	3	21	2	0	69	0	0	0	3	98
Cylinder Filling Station	38 B	0	52	0	0	0	0	0	0	0	53
Maintenance Complex Total		385	220	10	26	1,015	0	271	1	127	2,054
East Warehouses Complex											
Elevated Potable Storage Tank	20 D	128	9	0	0	0	0	0	0	1	138
Finished Products Warehouse (4A Warehouse)	77	50	33	0	18	0	0	0	0	0	102
Plant 6 Warehouse	79	42	28	0	15	0	0	0	0	0	85
Receiving/Incoming Materials Inspection	82	30	25	1	15	56	0	1	0	5	143
East Warehouses Complex Total		250	94	1	48	56	0	1	1	6	467
Plant 3 Complex											
Ozone Building	3 B	6	2	0	0	0	0	7	0	1	17
NAR Control House	3 C	18	71	0	0	0	0	23	0	5	116
NAR Towers	3 D	93	378	0	0	0	0	1	1	1	474
Hot Raffinate Building	3 E	48	195	19	3	446	0	31	0	6	747
Hershaw Digestion Fume Recovery	3 F	30	17	0	0	0	0	0	0	0	48
Refrigeration Building	3 G	5	18	2	0	0	0	7	0	1	34
Combined Raffinate Tanks	3 J	25	143	0	0	0	0	0	0	1	168
Old Cooling Water Tower	3 K	0	0	0	0	6	0	0	0	0	6
Incinerator Building	39 A	46	15	1	0	0	0	33	0	5	100
Incinerator Sprinkler Riser House	39 C	1	6	0	0	9	0	0	0	0	15
Plant 3 Complex Total		272	843	23	4	460	0	101	2	20	1,725
Plant 2 Complex											
Ore Refinery Plant	2 A	911	1,313	110	62	667	28	227	2	76	3,396
Metal Dissolver Building	2 D	33	92	7	0	0	0	19	0	8	161
NFS Storage and Pump House	2 E	1	74	0	0	21	0	0	0	1	96
Cold Side Ore Conveyor	2 F	11	45	0	0	0	0	5	0	0	61
Hot Side Ore Conveyor	2 G	10	59	0	0	0	0	3	0	0	72
Waste Oil Decant Shelter	39 B	6	1	0	1	0	0	0	0	0	8
Plant 2 Complex Total		971	1,583	118	64	687	28	255	2	87	3,795

TABLE C–4 Operable Unit 3 Material Weight Estimates (in tons)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component/ Complex Totals
Plant 8 Complex											
Recovery Plant	8 A	575	929	88	34	533	0	190	3	119	2,471
Plant 8 Maintenance Building	8 B	8	4	0	0	125	0	1	0	11	150
Rotary Kiln/Drum Reconditioning	8 C	382	306	32	36	285	0	0	0	39	1,079
Plant 8 Railroad Filter Building	8 D	1	2	0	0	0	0	0	0	0	3
Drum Conveyor Shelter	8 E	6	1	0	1	0	0	0	0	0	8
Plant 8 Old Drum Washer	8 F	0	0	0	1	0	0	0	0	0	1
Plant 8 Warehouse	80	25	12	0	11	0	0	0	0	1	49
Plant 8 Complex Total		997	1,254	120	82	943	0	192	4	170	3,762
General Sump Complex											
General/Refinery Sump Control Building	2 B	28	51	5	2	13	0	10	0	5	113
Bulk Lime Handling Building	2 C	8	15	2	0	0	0	5	0	2	32
Maintenance Building	3 A	23	68	7	0	0	0	25	0	5	128
Refinery Sump	3 H	16	116	0	0	0	0	0	0	1	133
Electrical Power Center Building	3 L	13	56	4	0	0	0	15	0	3	91
General Sump	18 B	16	135	0	1	0	0	0	0	2	154
Biodenitrification Towers	18 D	136	85	6	13	0	0	1	0	21	262
BDN Effluent Treatment Facility	18 H	2	109	12	3	0	0	0	0	2	129
General Sump Complex Total		242	635	35	19	13	0	56	2	41	1,041
Plant 5 Complex											
Plant 4 Warehouse	4 B	41	18	0	11	0	0	0	0	2	72
Metals Production Plant	5 A	1,246	2,319	239	127	1,443	0	394	4	113	5,885
Plant 5 Ingot Pickling	5 B	14	35	4	2	0	0	0	0	0	56
Plant 5 Electrical Substation	5 C	2	16	1	1	0	0	0	0	0	20
West Derby Breakout/ Slag Milling	5 D	381	297	31	16	17	0	0	0	1	743
Plant 5 Filter Building	5 E	9	3	0	5	0	0	0	0	2	20
Plant 5 Covered Storage Pad	5 F	35	5	0	7	0	0	0	0	2	49
Plant 5 Ingot Storage Shelter	5 G	6	1	0	2	0	0	0	0	0	9
Slag Recycling Building	55 A	76	75	8	4	0	0	28	0	10	202
Slag Recycling Pit/Elevator	55 B	14	7	1	1	0	0	6	0	0	29
Plant 5 Complex Total		1,824	2,777	283	176	1,460	0	427	5	133	7,085
Plant 6 Complex											
Metals Fabrication Plant	6 A	1,336	2,573	256	88	244	0	602	3	104	5,206
Plant 6 Covered Storage Area	6 B	11	2	0	2	0	0	0	0	0	15
Plant 6 Electrostatic Precipitator (South)	6 C	3	4	0	3	0	0	0	0	0	11
Plant 6 Electrostatic Precipitator (Central)	6 D	2	2	0	2	0	0	0	0	0	6
Plant 6 Electrostatic Precipitator (North)	6 E	3	8	1	3	0	0	0	0	0	16
Plant 6 Salt Oil Heat Treat Building	6 F	5	77	8	3	0	0	0	1	1	94
Plant 6 Sump Building	6 G	90	161	17	6	16	0	2	0	4	296
Plant 6 Complex Total		1,450	2,826	282	107	260	0	604	4	110	5,643
Liquid Storage Complex											
Methanol Tank	18 J	5	2	0	0	24	0	0	0	0	31
Low Nitrate Tank	18 K	2	12	0	0	0	0	0	0	0	14
High Nitrate Tank	18 L	2	12	0	0	0	0	0	0	0	14
Well House #1	20 E	0	3	0	0	8	0	0	0	1	13
Well House #2	20 F	0	3	0	0	8	0	0	0	1	13
Well House #3	20 G	0	2	0	0	11	0	0	0	2	16
Gas Meter Building	22 A	0	1	0	0	24	0	0	0	1	27
Storm Sewer Lift Station	22 B	1	3	0	1	7	0	0	0	0	12
Scale House & Weigh Scale	22 D	1	0	0	0	0	0	1	0	0	2
Pump House–HP Fire Protection	26 A	41	23	2	0	263	0	0	0	6	335
Elevated Water Storage Tank	26 B	432	168	0	0	41	0	0	0	0	640
Rust Engineering Building	45 A	41	50	0	29	132	0	6	0	3	261
Utility Shed East of Rust Trailers	45 B	0	0	0	0	0	0	0	0	1	1
Liquid Storage Complex Total		525	278	3	29	519	0	7	1	16	1,380
Pilot Plant Complex											
Pilot Plant Wet Side	13 A	42	193	20	4	674	0	22	1	52	1,007
Pilot Plant Maintenance Building	13 B	3	8	0	0	170	0	0	0	9	190
Sump Pump House	13 C	1	6	1	0	9	0	0	0	1	18
Pilot Plant Thorium Tank Farm	13 D	0	36	0	0	0	0	0	0	0	36
Pilot Plant Annex	37	35	83	8	0	170	0	0	0	23	320
Six to Four Reduction Facility # 1	54 A	139	169	18	24	577	0	15	1	49	991
Pilot Plant Shelter	54 B	6	4	0	3	0	0	0	0	1	14
Pilot Plant Dissociator Shelter	54 C	6	15	1	3	0	0	0	0	0	25
Pilot Plant Warehouse	58	38	5	0	0	61	0	20	0	3	127
Pilot Plant Complex Total		269	520	48	34	1,661	0	57	3	138	2,730
Laboratory Complex											
Laboratory	15 A	219	604	51	154	4,508	0	54	5	425	6,020
Laboratory Chemical Storage Building	15 B	3	6	0	2	24	0	0	0	0	35
Laboratory Complex Total		222	610	51	156	4,532	0	54	5	425	6,055
Electrical Station Complex											
Main Electrical Station	16 A	24	41	0	0	138	0	0	0	5	207
Electrical Substation	16 B	1	15	1	1	24	0	0	0	3	45
Electrical Panels & Transformer	16 C	0	4	0	0	0	0	0	0	0	4
Main Electrical Switch House	16 D	1	5	0	0	21	0	1	0	0	28
Main Electrical Transformers	16 E	0	222	0	0	0	0	0	0	0	222
Trailer Substation # 1	16 F	1	3	0	0	0	0	0	0	0	4
Trailer Substation #2	16 G	1	3	0	0	0	0	0	0	0	4
Main Electrical Strainer House	26 C	0	1	0	0	7	0	0	0	0	10
Engine House/Garage	31 A	31	37	2	0	150	0	0	0	31	251
Heavy Equipment Building	46	54	20	1	15	29	0	1	0	11	130
Electrical Station Complex Total		112	350	4	17	369	0	2	0	50	904
Sewage Treatment Plant Complex											
Chlorination Building	25 A	0	2	0	0	20	0	0	0	1	23
M.H. # 175/Effluent Line/Sampling Building	25 B	0	2	0	0	0	0	0	0	0	2
Sewage Lift Station Building	25 C	1	1	0	0	22	0	0	0	1	25
U.V. Disinfection Building	25 D	0	2	0	0	25	0	0	0	0	28
Digester & Control Building	25 E	7	10	1	0	193	0	0	0	2	214
Sewage Treatment Plant Complex Total		8	16	1	1	260	0	0	0	5	292

7221

TABLE C–4 Operable Unit 3 Material Weight Estimates (in tons)

Component	Component Designation	OU3 FS Material Category A Accessible Metals	B Inaccessible Metals	C Process-Related Metals	D Painted Light-Guage Metals	E Concrete	F Brick	G Non-Regulated ACM	H Regulated ACM	I Misc. Materials	Component Complex Totals
Administration Complex											
Service Building	11	40	447	0	53	7,066	0	39	21	240	7,918
Administration Building	14 A	13	147	0	10	2,645	0	31	0	200	3,048
Building 14 EOC Generator Set	14 B	0	2	0	0	0	0	0	0	0	2
Security Building	28 A	3	20	0	4	481	0	0	0	52	560
Human Resources Building	28 B	58	12	0	8	134	0	7	0	68	286
Health & Safety Building	53 A	82	163	0	42	3,133	0	54	11	356	3,831
In-Vivo Building	53 B	6	110	0	6	0	0	2	0	17	141
Administration Complex Total		201	901	0	134	13,478	0	133	4	935	15,786
Miscellaneous Complex											
10-Plex North Substation	16 H	0	5	0	0	0	0	0	0	0	5
10-Plex South Substation	16 J	0	5	0	0	0	0	0	0	0	5
Clearwell Pump House	18 G	1	4	0	0	0	0	1	0	3	9
Meteorologcal Tower	23	2	0	0	0	0	0	0	0	0	2
10-Plex Sewage Lift Station	25 J	0	0	0	0	0	0	0	0	0	0
Guard Post on West End of 2nd Street	26 D	0	0	0	0	0	0	0	0	2	2
Guard Post East of T-81	26 E	0	0	0	0	0	0	0	0	0	1
Guard Post South of Building 51	28 G	0	0	0	0	0	0	0	0	0	1
Utility Lines	G-004	0	986	23	0	0	0	0	23	0	1,033
Process Trailers	G-006	0	0	0	0	0	0	0	0	209	209
Non-Process Trailers	G-007	0	0	0	0	0	0	0	0	897	897
Pipe Bridges	G-008	554	0	0	0	26	0	0	0	0	581
Miscellaneous Complex Total		557.3	1,001.7	23.6	0.6	26.3	0.0	1.3	23.2	1,111.1	2,745
Below Grade Components		2,389	2,066	660	0	276,744	1,420	429	0	452	284,180
Operable Unit 3 Total		14,526	21,856	2,201	1,255	305,299	1,448	3,744	68	4,533	354,929

[1] The quantities of stockpiled coal vary seasonally. No significant quantities of coal are expected to remain after the Boiler Plant/Water Plant Complex is shut down.

DRAFT

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK.

D

R

A

APPENDIX D

SUPPORT DOCUMENTATION

F

T

DRAFT

THIS PAGE INTENTIONALLY LEFT BLANK

FERMCO OU2 - 7221

Department of Energy
Fernald Environmental Management Project
P.O. Box 398705
Cincinnati, Ohio 45239-8705
(513) 738-6357

JUN 30 1 51 PM '94

JUN 29 1994

DOE-1993-94

Mr. Thomas P. Schneider
Fernald Group Leader
Ohio Federal Facilities Office
Ohio Environmental Protection Agency
401 East Fifth Street
Dayton, Ohio 45402-2086

Dear Mr. Schneider:

REQUEST FOR APPROVAL OF MANAGEMENT PLAN FOR OPERABLE UNIT 2 INVESTIGATION DERIVED WASTE

In a meeting with you in Dayton on May 19, 1994, we discussed your agency's approval of the Management Plan for Investigation Derived waste (IDW). This is waste generated during the Operable Unit 2 (OU 2) Remedial Investigation Phase II sampling program. You indicated a willingness to approve the procedures for handling OU 2 IDW in the site's Management Plan. The procedures for OU 2 are enclosed and have been excerpted from the proposed site-wide IDW Management Plan which was previously submitted to your agency. We request your approval with the understanding that it is for the IDW from the OU 2 sampling program only, and that the proposed site-wide IDW Management Plan remains under review.

If you have any questions regarding this matter, please contact Rod Warner at (513) 648-3156.

Sincerely,

Jack R. Craig
Remedial Project Manager

Enclosure: As Stated

Recycled and Recyclable

EXCERPT FROM FEMP INVESTIGATION DERIVED WASTE MANAGEMENT PLAN

OU2 1993 Remedial Investigation: (220 drums)

Drill cuttings from investigations associated with Operable Unit 2 subunits will be disposed as described below:

South Field: cuttings will be placed in a near surface pit located in an identified low level contaminated area in the South Field.

Solid Waste Landfill: cuttings will be placed in a near surface pit located in the controlled area of the Solid Waste Landfill.

Active Flyash Pile: ash cuttings will be segregated to the extent possible and incorporated into the continued maintenance operation associated with Removal Action #10 (regrading and reapplication of the surface sealant). Soil cuttings or mixed soil/ash material will be placed in a near surface pit immediately exterior of the toe of the Active Flyash Pile.

Inactive Flyash Pile: ash cuttings will be segregated to the extent possible and placed in a near surface pit at the top of the pile, but below the soil cover. Soil or mixed soil/ash material will be placed in a separate near surface pit such that the soil cover is not fully penetrated.

Lime Sludge Ponds: lime sludge cuttings will be placed in the North Lime Sludge Pond. Soil or mixed soil/lime material will be placed in a near surface pit immediately exterior to the encircling dike.

Drummed decon water will be discharged to the General Sump of the FEMP Wastewater Treatment Facility.

Department of Energy
Fernald Environmental Management Project
P. O. Box 538705
Cincinnati, Ohio 45253-8705
(513) 648-3155

7221

FEB 2 4 1995

DOE-0582-95

Mr. James A. Saric, Remedial Project Manager
U. S. Environmental Protection Agency
Region V-5HRE-8J
77 W. Jackson Blvd.
Chicago, Illinois 60604-3590

Mr. Thomas P. Schneider, Project Manager
Ohio Federal Facilities Office
Ohio Environmental Protection Agency
401 East Fifth Street
Dayton, Ohio 45402-2086

Dear Mr. Saric and Mr. Schneider:

REQUEST FOR APPROVAL OF INTERIM MANAGEMENT PLAN FOR OPERABLE UNIT 5 INVESTIGATION DERIVED WASTE

Reference: Letter, Thomas A. Schneider (OEPA) to Jack Craig (DOE-FN), dated July 5, 1994.

The Department of Energy, Fernald Area Office (DOE-FN) is requesting approval from the Ohio Environmental Protection Agency (OEPA) and the U. S. Environmental Protection Agency (USEAP) for this proposed Interim Investigation-Derived Waste (IDW) Management Plan for Operable Unit 5 (OU5) soil/drill cuttings, which is intended to be in effect until the Sitewide Soil IDW Policy is approved. The objectives of this plan are consistent with the Interim IDW Management Plan that OEPA approved for Operable Unit 2 (OU2) on July 5, 1994 (Reference).

Currently there are numerous drums of IDW stored that were generated from earlier OU5 field investigations. These drums have been in the field since 1993, due to insufficient storage space and because there is no approved policy in place that adequately addresses management of OU5 IDW soil drill cuttings. Continued drum storage of existing or future OU5 IDW soil/drill cuttings is not considered appropriate in light of the National Contingency Plan's policy for Comprehensive Environmental Response, Compensation and Liability Act (CERCLA) sites to minimize IDW generated by CERCLA activities.

Recycled and Recyclable

Therefore, it is proposed that OU5 IDW soil/drill cuttings be managed as follows:

> *If the concentration of potential contaminants in IDW from a given depth of a sampling location exceeds the general concentration of existing ground surface contamination, or differs from the contaminants present at the ground surface, then the IDW will be managed on an Operable Unit 5 soil pile, as specified in Removal Action 17. If the concentration of potential contaminants in IDW collected from a given depth is generally equivalent to, or less than the concentrations of the same contaminants at the ground surface of a sampling location, then the IDW will be deposited in a shallow surface depression near the sampling location.*

Information contained in the Operable Unit 5 RI Report provides an adequate basis for compliance with this interim policy to determine the disposition of IDW located within the Operable Unit 5 area of concern. The interim IDW management strategy and RI information that is pertinent for future investigations will be referenced, as appropriate, in each corresponding work plan for agency review. The same approach and documentation will also be applied to the existing IDW that has been stored in approximately 200 drums since 1993. These drums are located on the Fernald property outside of the Production Area near the locations where the investigations took place.

DOE understands that this proposed interim Management Plan applies to soil/drill cuttings generated from Operable Unit 5 investigations, and that the proposed sitewide IDW Management Plan remains under review.

If you have any questions regarding this matter, please contact Rob Janke at (513) 648-3124 or Kathi Nickel at (513) 648-3166.

Sincerely,

Randy Allen

for Jack R. Craig
Fernald Remedial Action
Project Manager

FN:Nickel

cc:

K. H. Chaney, EM-423 QO
D. R. Koslowski, EM-42 QO
G. Jablonowski, USEPA-V AT-18J
J. Kwasniewski, OEPA-Columbus
P. Harris, OEPA-Dayton
M. Profitt, OEPA-Dayton
B. Cohan, GeoTrans
F. Bell, ATSDR
J. Michaels, PRC

bcc:

R. J. Janke, DOE-FN
D. J. Carr, FERMCO
E. M. Dupuis-Nouille, FERMCO
T. D. Hagen, FERMCO
M. A. Jewett, FERMCO
M. J. Strimbu, FERMCO
V. Zimmerman, FERMCO
AR Coordinator, FERMCO
OU5 Letter Log, FERMCO
R. L. Glenn, Parsons
J. W. Thiesing, FERMCO

Department of Energy
Fernald Environmental Management Project
P. O. Box 538705
Cincinnati, Ohio 45253-8705
(513) 648-3155

7221

MAR 2 3 1995

DOE-0711-95

Mr. James A. Saric, Remedial Project Manager
U. S. Environmental Protection Agency
Region V-5HRE-8J
77 W. Jackson Blvd
Chicago, Illinois 60604-3590

Mr. Tom Schneider, Project Manager
Southwest District Office
Ohio Environmental Protection Agency
401 East Fifth Street
Dayton, Ohio 45402-2086

Dear Mr. Saric and Mr. Schneider:

REQUEST FOR APPROVAL OF POLICY FOR MANAGEMENT OF AQUEOUS INVESTIGATION DERIVED WASTE

This letter requests your formal approval of the Fernald Environmental Management Project (FEMP) policy for management of aqueous Investigation Derived Waste (IDW). IDW to be managed under this policy includes purge water and development water from FEMP groundwater monitoring wells, as well as, wastewater generated by decontaminating sampling equipment. The inventory of backlog aqueous IDW currently in storage at the FEMP is also included. Unused sample fractions, extracts and other residues from laboratory analyses will be managed under a separate policy currently being developed; these materials are not addressed in this proposed policy.

The aqueous IDW policy previously presented for your review has been modified to take into account the treatment provided by the Advanced Wastewater Treatment (AWWT) facility, which began operation January 27, 1995. This modified proposal is based upon the fact that all IDW, regardless of its source, will be treated through the AWWT facility. The AWWT facility currently treats all FEMP stormwater and process wastewater, along with a portion of the South Plume groundwater. As illustrated in the attached schematic, the AWWT includes carbon filters upstream of the ion exchange beds. The carbon filters were included in the design to protect the ion exchange resin from possible damage caused by incidental Volatile Organic Compound (VOC) contamination. These carbon filters accomplish the same level of VOC removal provided by the Granular Activated Carbon (GAC) filters in the Plant 8 VOC system.

Recycled and Recyclable

Since all process wastewater and stormwater is now subjected to adequate VOC treatment, pretreatment based upon a threshold level of VOC contamination is no longer necessary, except for instances where VOC contamination is known to originate from listed waste. The Fire Training Facility and the Sewage Treatment Plant Sludge Drying Beds are potential sources of known listed hazardous constituents. Since these units are isolated from other potential sources of VOC contamination, VOCs encountered in perched water beneath these two units will be considered to potentially originate from listed waste. IDW from the vicinity of these two units which exhibits detectable levels of a "listed" VOC will be treated through the Plant 8 GAC system to remove the listed RCRA constituent to below the analytical detection limit before being sent to the AWWT via the General Sump.

All other aqueous IDW will be discharged to the wastewater treatment system at the location that most efficiently provides direct access to AWWT treatment. Purge water and well development water from wells in Operable Unit 2 (OU2) and Operable Unit 5 (OU5) will be collected in a truck-mounted tank, transported to the Stormwater Retention Basin (SWRB), and discharged directly to whichever of the two basins is being pumped to the AWWT at that time. Discharging purge water from these two areas to the SWRB avoids the need to transport the material through the production area and, as illustrated in the attached flow diagram, provides direct access to the AWWT. All other IDW streams will be discharged to the General Sump for subsequent treatment at the AWWT.

If you have any questions or comments, please contact Pete Yerace at (513)648-3161 or John Sattler at (513)648-3145.

Sincerely,

Johnny Reising

for Jack R. Craig
Fernald Remedial Action
Project Manager

FN:Yerace

REGULATORY PROGRAMS
REGULATORY TECHNICAL
SUPPORT DEPARTMENT

23 10 37 AM '95

cc:

K. H. Chaney, EM-423/QO
D. R. Kozlowski, EM-423/QO
G. Jablonowski, USEPA-V, HRE-8J
J. Kwasniewski, OEPA-Columbus
P. Harris, OEPA-Dayton
G. E. Mitchell, OEPA-SWDO
P. E. Pardi, OEPA-SWDO
M. Proffitt, OEPA-Dayton
S. McClellan, PRC
R. Cohen, GeoTrans
F. Bell, ATSDR
R. Owen, ODOH
K. A. Nickel, DOE-FN
S. M. Beckman, FERMCO/MS65-2
T. Hagen, FERMCO/65-2
E. M. Dupuis-Nouille, FERMCO/MS52-5
R. D. George, FERMCO/52-2
J. Thiesing, FERMCO
M. Yates, FERMCO/9
AR Coordinator, FERMCO

AWWT PROCESS FLOW DIAGRAM

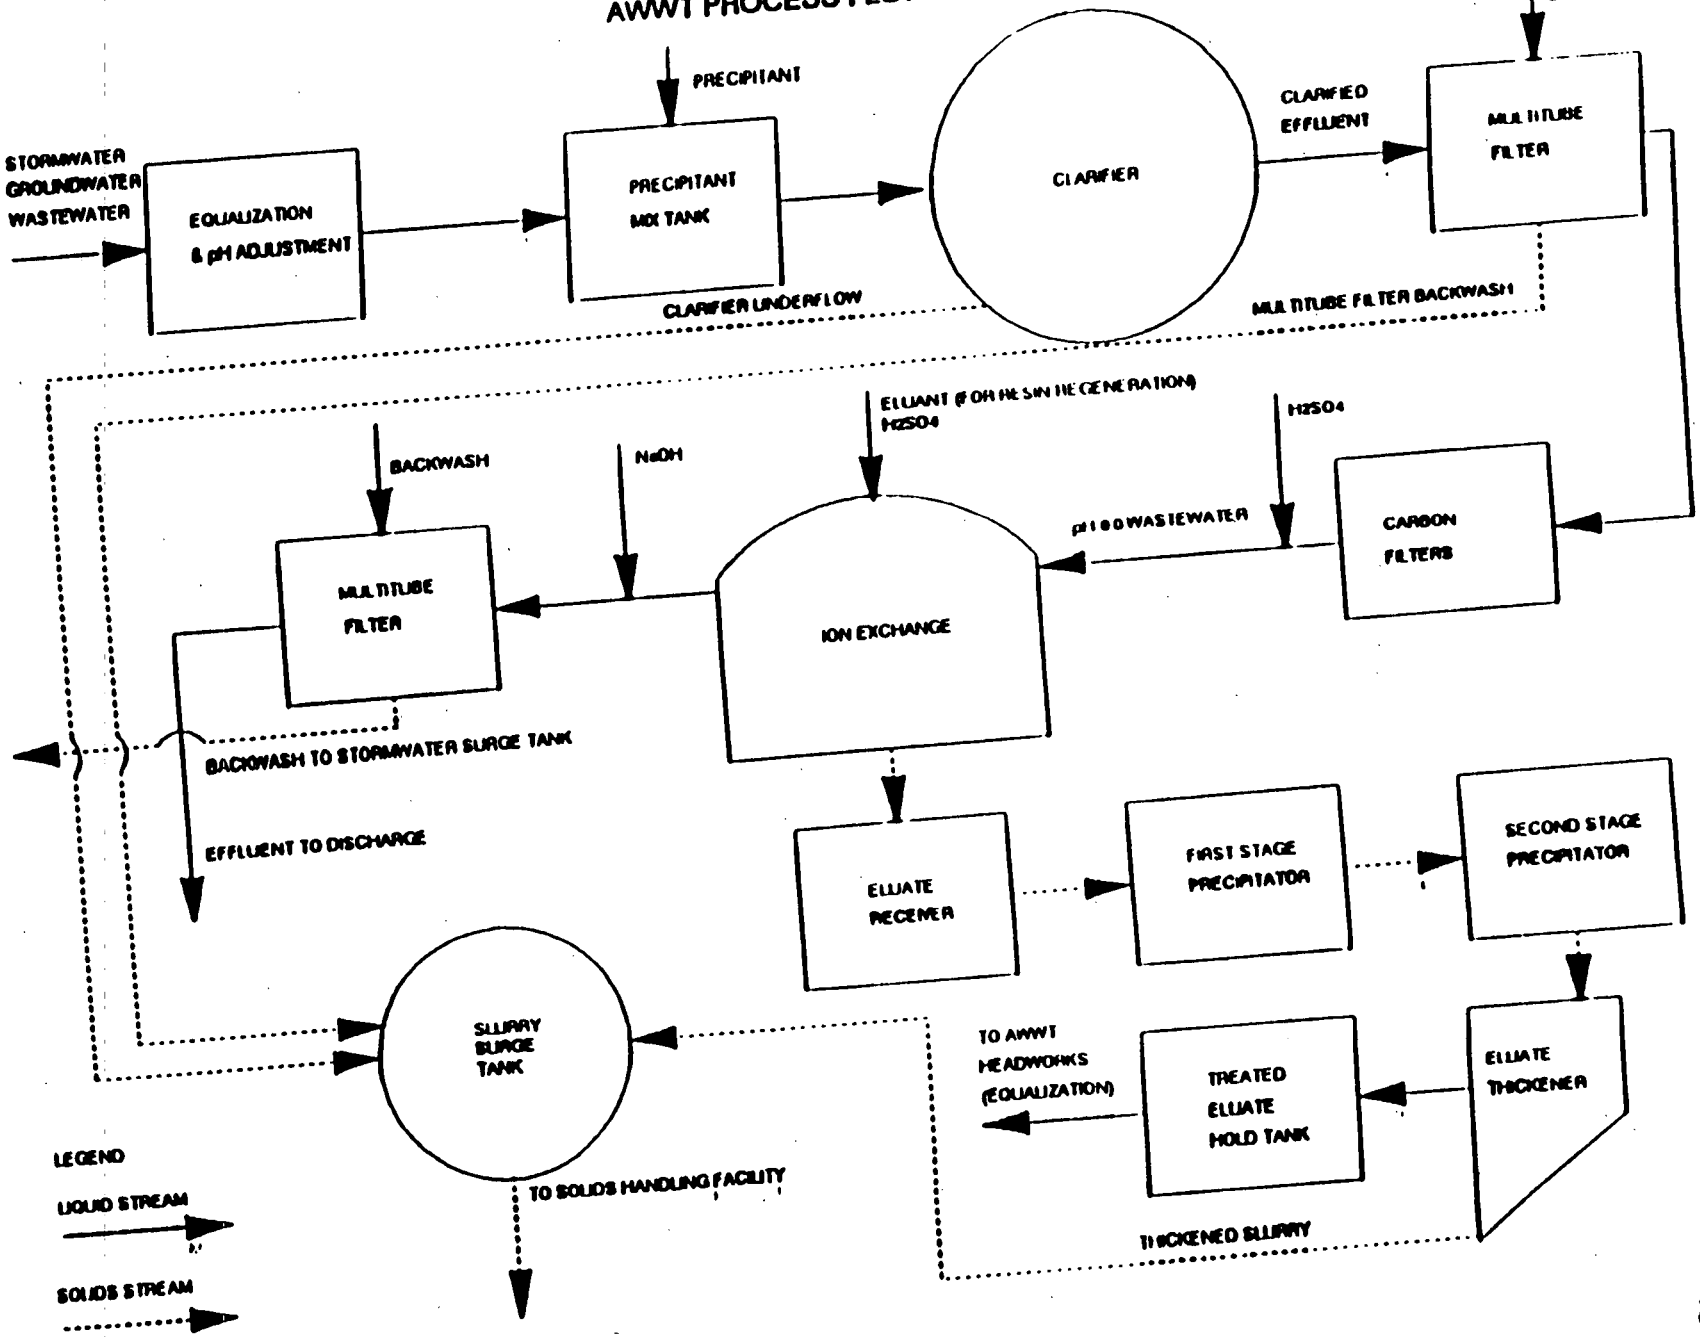

WASTEWATER FLOW DIAGRAM - AWWT OPERATIONAL

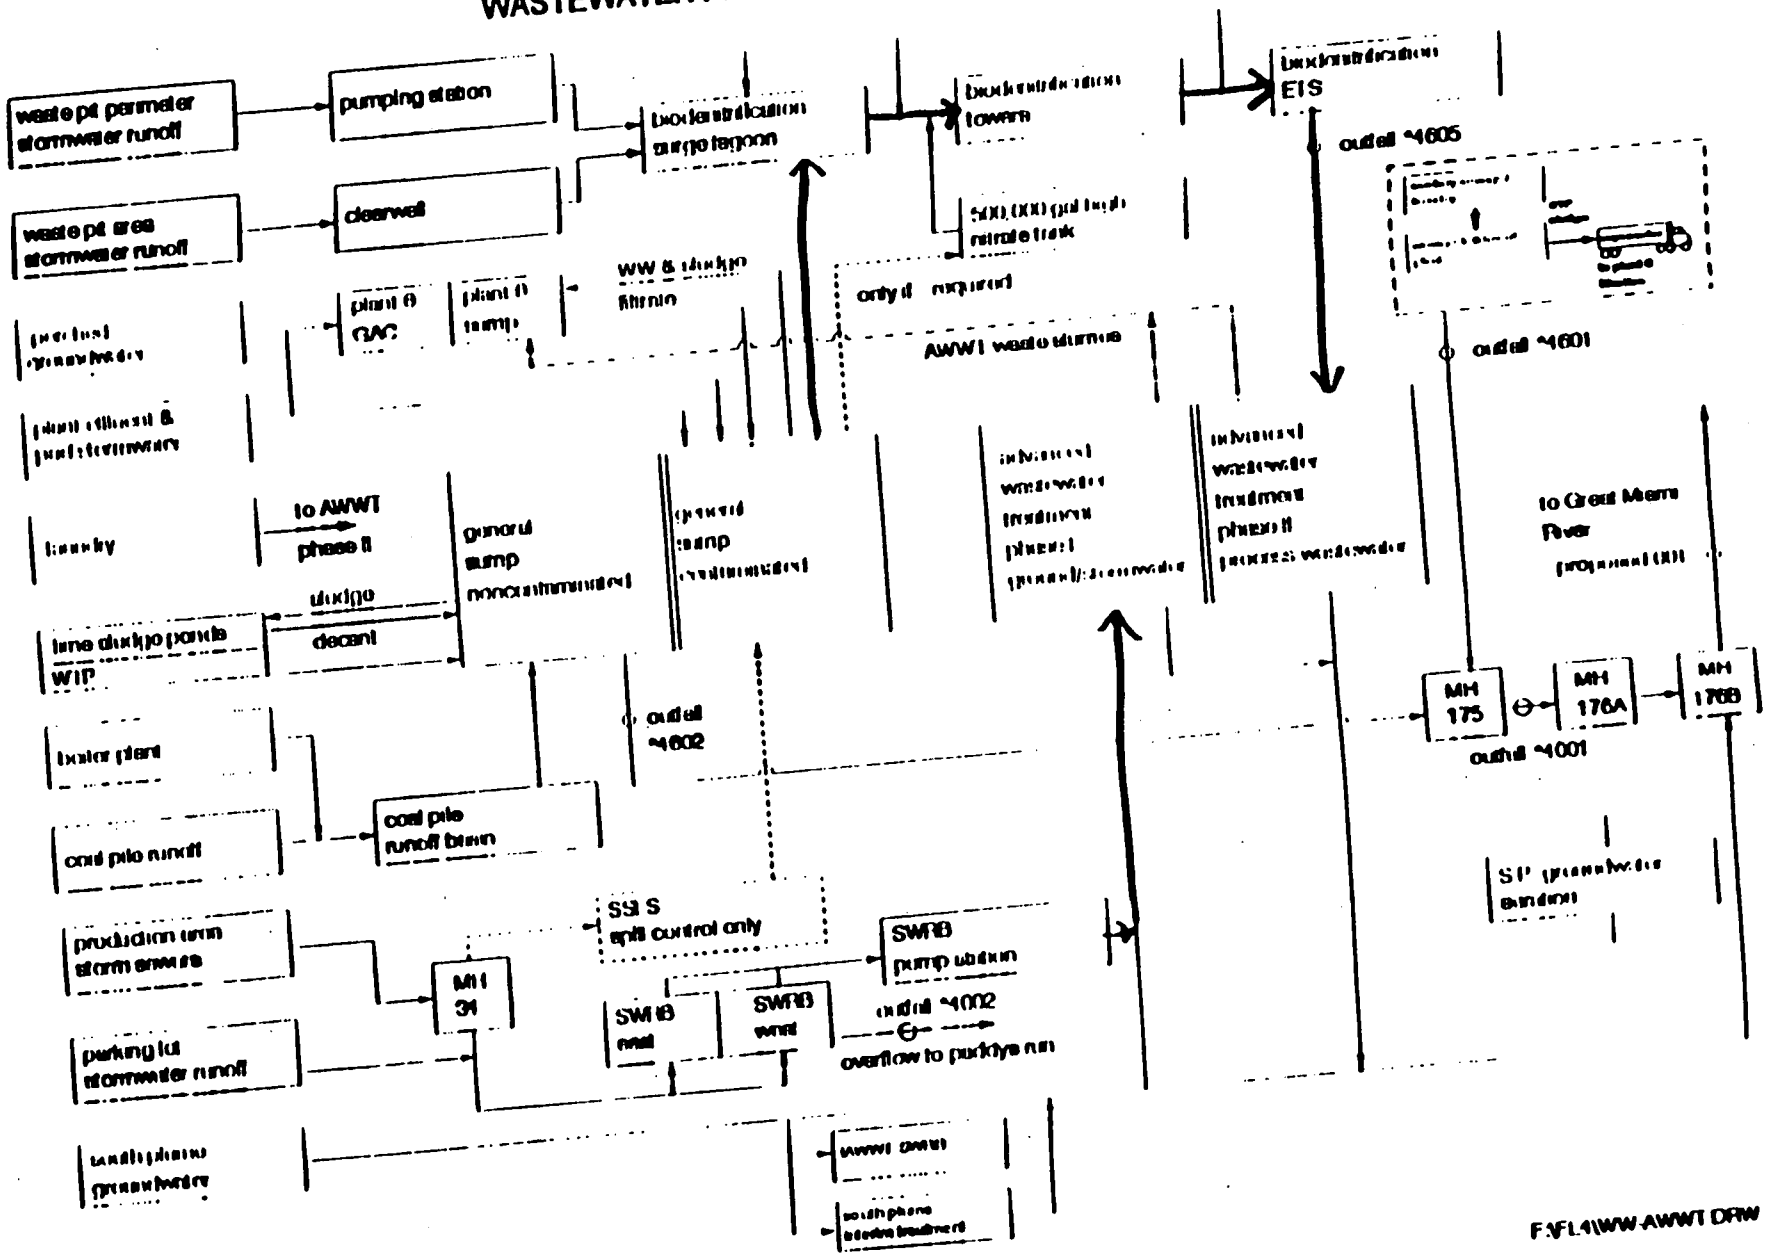

000095

UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 5
77 WEST JACKSON BOULEVARD
CHICAGO, IL 60604-3590

JAN 1 4 1994

REPLY TO THE ATTENTION OF

HRE-8J

Mr. Jack R. Craig
United States Department of Energy
Feed Materials Production Center
P.O. Box 398705
Cincinnati, Ohio 45239-8705

RE: Approval of Soil and Rubble Pile Cover

Dear Mr. Craig:

The United States Environmental Protection Agency (U.S. EPA) has completed its review of the United States Department of Energy's (U.S. DOE) Soil and Rubble Pile Cover Document. This document describes U.S. DOE's approach for sample collection, analysis, data evaluation, and recommendation for interim management of the soil and rubble pile north of 3rd Street. Although this pile is not a hazardous waste as defined by the Resource Conservation and Recovery Act, it is a solid waste. Also, the pile contains levels of radioactivity below the threshold established in Removal Action 17.

U.S. EPA concurs with U.S. DOE's proposal to remove visible rubble, and grade and seed the pile as an interim action, until final action is determined in the Operable Unit 5 Record of Decision. However, as discussed in previous meetings between the agencies, the pile material is <u>not</u> to be used as backfill.

Please contact me at (312) 886-0992 if you have any questions.

Sincerely,

James A. Saric
Remedial Project Manager

cc: Graham Mitchell, OEPA-SWDO
Pat Whitfield, U.S. DOE-HDQ
Jim Thiesing, FERMCO
Paul Clay, FERMCO

Printed on Recycled

OhioEPA
State of Ohio Environmental Protection Agency

Southwest District Office
40 South Main Street
Dayton, Ohio 45402-2086
(513) 285-6357
FAX (513) 285-6404

Post-it™ brand fax transmittal memo 7671 | # of pages ▸ 1

To Johnny Reising	From Tom Schneider
Co. DOE FEMP	Co. OEPA/DFO
Dept.	Phone # 285-6038
Fax # 648-3076	Fax #

7221

ge V. Voinovich
Governor

July 28, 1994

RE: DOE FEMP
MSL #531-0297
RA 17 PROPOSED CHANGES-
COMMENT

J. Ferrell
copy: T Clark
D Daley
K Kolthoff

Mr. Jack Craig
Project Manager
U.S. DOE FEMP
P.O. Box 398705
Cincinnati, OH 45329-8705

Dear Mr. Craig:

This letter provides Ohio EPA's concerns regarding "Proposed Changes to the Removal Action 17 Improved Storage of Soil and Debris" submitted to the agency on May 31, 1994. Ohio EPA is concerned that the proposed relocation of the CSF and subsequent delay may already be outdated. DOE needs to provide a justification for the relocation in light of recent finding of OU5 which suggest that the usefulness of soil washing is very limited. Additionally, it would seem appropriate if the CSF will actually be a staging facility for disposal that it should be located based upon accessibility to the disposal cell.

It was Ohio EPA's understanding that the CSF would provide interim storage for debris and soils generated by other removal actions and the OU3 Interim Remedial Action. The delay in construction of this facility questions its usefulness for this purpose. At this point it may be more appropriate for the agencies and DOE to discuss design of facilities which will act as staging areas for OU3 and OU5 remedial actions. Regardless of what the facility is called interim storage or staging, a discussion of the objectives of this facility should occur prior to any additional design activities.

Ohio EPA concurs with DOE's position regarding the TSS covers for the decon pad and scrap metal pad. Ohio EPA is available to discuss this issue with DOE and USEPA. If you should have any questions, please contact me.

Sincerely,

Thomas A. Schneider

Thomas A. Schneider
Fernald Project Manager
Office of Federal Facilities Oversight

Jim, I am scheduling a meeting with Hauser to discuss this. Will let you know about meeting where lot. J. Fer

UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 5
77 WEST JACKSON BOULEVARD
CHICAGO, IL 60604-3590

REPLY TO THE ATTENTION OF:

AUG 0 4 1994

HRE-8J

Mr. Jack R. Craig
United States Department of Energy
Feed Materials Production Center
P.O. Box 398705
Cincinnati, Ohio 45239-8705

RE: Proposed Changes to Removal Action 17

Dear Mr. Craig:

The United States Environmental Protection Agency (U.S. EPA) has completed its review of the Proposed Changes to Removal Action 17 Improved Storage and Debris. U.S. EPA has concerns with some of the proposed changes.

The relocation of the Central Storage Facility (CSF) and subsequent delay in the construction completion schedule may not be necessary. Recent findings have questioned the applicability of soil washing at the Fernald Environmental Management Project. It may be more appropriate to discuss which facilities will serve as staging areas for the Operable Unit 3 and 5 remedial actions.

U.S. EPA does concur with U.S. DOE's proposal to not erect the Tension Support Structure (TSS) for the scrap metal pad, and using separate procurement procedures to construct the TSS cover for the decontamination facility pad.

Please contact me at (312) 886-0992 if you have any questions.

Sincerely,

James A. Saric
Remedial Project Manager
Technical Enforcement Section #1
RCRA Enforcement Branch

cc: Tom Schneider, OEPA-SWDO
Pat Whitfield, U.S. DOE-HDQ
Don Ofte, FERMCO
Jim Thiesing, FERMCO
Paul Clay, FERMCO

Printed on Recyc

7221

UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 5
77 WEST JACKSON BOULEVARD
CHICAGO, IL 60604-3590

Hoover
TRC
KRK
JG

REPLY TO THE ATTENTION OF

GOVE LANG
RODNEY WHITAKER

JAN 0 4 1995

HRE-8J

Mr. Jack R. Craig
United States Department of Energy
Feed Materials Production Center
P.O. Box 398705
Cincinnati, Ohio 45239-8705

RE: Proposed Actions to Removal Action 17

Dear Mr. Craig:

The United States Environmental Protection Agency (U.S. EPA) has completed its review of the Proposed Actions to Removal Action (RA) 17 Improved Storage and Debris. U.S. EPA concurs with the proposed scope revisions and milestone changes to RA 17.

The United States Department of Energy must manage soil and debris consistently with RA 17 to assure no mixing of stockpile material with different designations occurs. Likewise, all controlled soil and debris stockpiles with engineered run-on and runoff controls or tarpaulin covers must be properly maintained.

Please contact me at (312) 886-0992 if you have any questions.

Sincerely,

James A. Saric
Remedial Project Manager
Technical Enforcement Section #1
RCRA Enforcement Branch

cc: Tom Schneider, OEPA-SWDO
Jack Baublitz, U.S. DOE-HDQ
Don Ofte, FERMCO
Jim Thiesing, FERMCO
Paul Clay, FERMCO

RECEIVED
JAN

Printed on Recycled Paper

DRAFT

APPENDIX E

REMEDIATION LEVELS

AND

WASTE ACCEPTANCE CRITERIA

TABLE E-1 OPERABLE UNIT 1 REMEDIATION LEVELS IN SURFACE SOILS

CONSTITUENT OF CONCERN	REMEDIATION LEVELS
RADIONUCLIDES:	
Cs-137 + 1 progeny	1.8 pCi/g
Th-230	902 pCi/g
U-235	9.3 pCi/g
U-238 + 2 progeny	56 pCi/g
CHEMICAL:	
Beryllium	2.1 mg/kg
Uranium	190[a] mg/kg

[a] 0.5 times the PRG to protect for multiple chemicals.

Source - Operable Unit 1 Record of Decision (DOE 1995)

DRAFT

TABLE E-2 OPERABLE UNIT 1 PIT SUBSURFACE SOIL REMEDIAL LEVELS[a] BASED ON GROUNDWATER MODELING

CONSTITUENT OF CONCERN	WASTE PIT 1	WASTE PIT 2	WASTE PIT 3	WASTE PIT 4	WASTE PIT 5	WASTE PIT 6	BURN PIT	CLEARWELL
RADIONUCLIDES:								
Tc-99	NR	5.5 pCi/g	0.75 pCi/g	0.26 pCi/g	1.4 pCi/g	7.3 pCi/g	14 pCi/g	9.9 pCi/g
U-238 +2d	13,000 pCi/g	NR	NR	11,000 pCi/g	NR	NR	NR	NR
CHEMICAL:								
PCBs[b]	0.78 pCi/g	NR	NR	NR	NR	NR	NR	NR

[a] Where calculated remedial levels are lower than background, the COC will be cleaned to establish background levels.
[b] PCBs (polychlorinated biphenyls) include all Aroclor congeners.
NR No Remediation Required

SOURCE - Operable Unit 1 Record of Decision (DOE 1995).

DRAFT

7221

000102

000103

TABLE E-3 OPERABLE UNIT 2 PRIMARY SOIL CLEANUP LEVELS[a] FOR THE SELECTED ALTERNATIVE

CONTAMINANT OF CONCERN	ALL SUBUNITS	SOLID WASTE LANDFILL	LIME SLUDGE POND	INACTIVE FLYASH PILE (WASTE/SOIL OVER THE GREAT MIAMI AQUIFER)	INACTIVE FLYASH PILE (WASTE/SOIL LOCATED OVER >16 FEET NATURAL SOIL)	SOUTH FIELD (WASTE/SOIL LOCATED OVER THE GREAT MIAMI AQUIFER)	SOUTH FIELD (WASTE/SOIL LOCATED OVER >16 FEET NATURAL SOIL)	ACTIVE FLYASH PILE
RADIONUCLIDES:								
Radium-226	1.8 pCi/g	NR	NR	NR	NR	NR	NR	NR
Radium-228	2.0 pCi/g	NR	NR	NR	NR	NR	NR	NR
Thorium-228	1.8 pCi/g	NR	NR	NR	NR	NR	NR	NR
Thorium-230	NR	NR	NR	NR	NR	6.97[c] pCi/g	6.97[c] pCi/g	NR
Thorium-232	1.5 pCi/g	NR	NR	NR	NR	NR	NR	NR
Uranium-234	NR	62.9[c] pCi/g	196[c] pCi/g	8.68[c] pCi/g	4.24[c] pCi/g	8.68[c] pCi/g	4.24[c] pCi/g	8.64[c] pCi/g
Uranium-235/236	NR	63.1[c] pCi/g	195[c] pCi/g	7.79[c] pCi/g	3.35[c] pCi/g	7.79[c] pCi/g	3.35[c] pCi/g	7.75[c] pCi/g
Uranium-238	NR	12.9[b] pCi/g	45.3[b] pCi/g	6.12[c] pCi/g	3.22[c] pCi/g	6.12[c] pCi/g	3.22[c] pCi/g	6.12[c] pCi/g
Uranium-Total	NR	38.6 mg/kg	136 mg/kg	24.8[c] mg/kg	24.8[c] mg/kg	24.8[c] mg/kg	24.8[c] mg/kg	28[c] mg/kg
CHEMICAL:								
Arsenic	NR	NR	NR	16.9 mg/kg	16.9 mg/kg	NR	NR	16.9 mg/kg
Lead	NR	NR	NR	NR	NR	400[d] mg/kg	NR	NR

[a] The cleanup level is the lowest value of the 10^{-6} ILCR, 0.2 Hazard Index, or ARAR standard.
[b] This value determined by calculating the uranium-238 concentration in uranium-total.
[c] Cleanup level due to off-property resident farmer receptor.
[d] The lead cleanup level applies to the Firing Range only, not the entire South Field area.
NR No Remediation Required

SOURCE - Table 2-23, Operable Unit 2 FS Report.

DRAFT

TABLE E-4 OPERABLE UNIT 2 SECONDARY SOIL CLEANUP LEVELS[a] FOR THE SELECTED ALTERNATIVE

CONSTITUENT OF CONCERN	SOUTH FIELD (WASTE/SOIL LOCATED OVER THE GREAT MIAMI AQUIFER)	SOUTH FIELD (WASTE/SOIL LOCATED OVER >16 FEET NATURAL SOIL)	ACTIVE FLYASH PILE
Aroclor-1260	25[b] mg/kg	25[b] mg/kg	NR
Benzo(a)anthracene	0.455 mg/kg	0.455 mg/kg	NR
Benzo(a)pyrene	0.777 mg/kg	0.777 mg/kg	NR
Benzo(b)fluoranthene	0.513[b] mg/kg	0.513[b] mg/kg	NR
Benzo(k)fluoranthene	0.603 mg/kg	0.603 mg/kg	NR
Dibenzo(a,h)anthracene	0.157[b] mg/kg	0.157[b] mg/kg	NR
Dieldrin	0.00957 mg/kg	0.00957 mg/kg	NR
Indeno(1,2,3-cd)pyrene	0.496[b] mg/kg	0.496[b] mg/kg	NR
Neptunium-237	NR	NR	4.99 pCi/g
Phenanthrene	0.19 mg/kg	0.19 mg/kg	NR
Technetium-99	71 pCi/g	71 pCi/g	NR
Thorium-230	6.97[b] pCi/g	6.97[b] pCi/g	NR

[a] The cleanup level is the lowest value of the 10^{-6} ILCR, 0.2 Hazard Index, or ARAR standard.
[b] Cleanup level due to off-property resident farmer receptor.
NR No Remediation Required

SOURCE - Table 2-23, Operable Unit 2 FS Report.

DRAFT

TABLE E-5 OPERABLE UNIT 4 PRELIMINARY REMEDIATION LEVELS[a] IN SOILS

CONSTITUENT OF CONCERN	PROPOSED REMEDIATION LEVEL
Pb-210 +2 progeny	78 pCi/g
Ra-226 +5 progeny	2 pCi/g
Ra-228 +1 progeny	2 pCi/g
Sr-90 +1 progeny	NR
Tc-99	NR
Th-228	2 pCi/g
U-238 +2 progeny	60 pCi/g

[a] Sum of background and PRG.
NR No Remediation Required

SOURCE - Operable Unit 4 Record of Decision

DRAFT

TABLE E-6 OPERABLE UNIT 5 FINAL REMEDIATION LEVELS FOR SOIL

Constituent	On-Property Final Remediation Levels	Off-Property Final Remediation Levels
Radionuclides (pCi/g)		
Cesium-137+1d	1.4×10^{0}	8.2×10^{-1}
Neptunium-237+1d	3.2×10^{0}	4.9×10^{-1}
Lead-210+2d	3.8×10^{1}	2.2×10^{0}
Plutonium-238	7.8×10^{1}	9.3×10^{0}
Plutonium-239/240	7.7×10^{1}	9.0×10^{0}
Radium-226+8d	1.7×10^{0}	1.5×10^{0}
Radium-228+1d	1.8×10^{0}	1.4×10^{0}
Strontium-90+1d	1.4×10^{1}	6.1×10^{-1}
Technetium-99	3.0×10^{1}	1.0×10^{0}
Thorium-228+7d	1.7×10^{0}	1.5×10^{0}
Thorium-230	2.8×10^{2}	8.0×10^{1}
Thorium-232+10d	1.5×10^{0}	1.4×10^{0}
Uranium, total (K_d=325 L/kg[a]) (ppm)	8.2×10^{1}	5.0×10^{1}
Uranium, total (K_d=15 L/kg[a]) (ppm)	2.0×10^{1}	NA
Chemicals (mg/kg)		
Acetone	4.3×10^{4}	4.3×10^{-1}
Antimony	9.6×10^{1}	6.1×10^{-1}
Aroclor-1254	1.3×10^{-1}	4.0×10^{-2}
Aroclor-1260	1.3×10^{-1}	4.0×10^{-2}
Arsenic	1.2×10^{1}	9.6×10^{0}
Barium	6.8×10^{4}	1.2×10^{2}
Benzene	8.5×10^{2}	4.3×10^{-1}
Benzo(a)anthracene	2.0×10^{1}	1.6×10^{-1}
Benzo(a)pyrene	2.0×10^{0}	9.0×10^{-2}
Benzo(b)fluoranthene	2.0×10^{1}	1.6×10^{-1}
Benzo(k)fluoranthene	2.0×10^{2}	9.0×10^{-2}
Beryllium	1.5×10^{0}	6.2×10^{-1}
Bis(2-chloroisopropyl)ether	4.2×10^{2}	2.0×10^{-1}
Bis(2-ethylhexyl)phthalate	8.2×10^{2}	2.6×10^{1}
Boron	7.4×10^{3}	4.0×10^{0}
Bromodichloromethane	4.0×10^{0}	1.8×10^{-1}
Bromoform	3.1×10^{1}	1.6×10^{0}
Bromomethane	8.2×10^{3}	2.4×10^{-2}
Cadmium	8.2×10^{1}	9.1×10^{-1}
Carbazole	1.2×10^{1}	3.1×10^{0}
Carbon disulfide	5.0×10^{3}	6.2×10^{0}
Carbon tetrachloride	2.1×10^{0}	9.1×10^{-2}
Chlordane	1.9×10^{-1}	3.8×10^{-2}
Chlorobenzene	3.4×10^{2}	1.9×10^{0}
Chloroform	4.5×10^{1}	5.0×10^{-1}
Chromium VI	3.0×10^{2}	1.1×10^{1}
Chrysene	2.0×10^{3}	1.6×10^{1}
Cobalt	7.4×10^{2}	2.6×10^{1}

DRAFT

TABLE E-6 OPERABLE UNIT 5 FINAL REMEDIATION LEVELS FOR SOIL (Cont'd)

Constituent	On-Property Final Remediation Levels	Off-Property Final Remediation Levels
Chemicals (Cont.) (mg/kg)		
Copper	2.2×10^{5}	2.0×10^{1}
Cyanide	1.2×10^{5}	8.0×10^{-1}
Dibenzo(a,h)anthracene	2.0×10^{0}	1.6×10^{-3}
3,3'-Dichlorobenzidine	5.5×10^{-1}	2.0×10^{-1}
1,2-Dichloroethane	1.6×10^{-1}	1.3×10^{-1}
1,1-Dichloroethene	4.1×10^{-1}	5.9×10^{-2}
Dieldrin	1.5×10^{-2}	8.8×10^{-3}
Di-n-octylphthalate	1.1×10^{3}	2.0×10^{-1}
Ethylbenzene	5.1×10^{3}	1.0×10^{-3}
Fluoride	7.8×10^{4}	8.5×10^{2}
Heptachlorodibenzofuran	8.8×10^{-4}	5.0×10^{-5}
Heptachlorodibenzo-p-dioxin	8.8×10^{-4}	5.0×10^{-5}
Indeno(1,2,3-cd)pyrene	2.0×10^{1}	1.6×10^{-2}
Lead	4.0×10^{2}	4.0×10^{2}
Manganese	4.6×10^{3}	1.4×10^{3}
Mercury	7.5×10^{0}	3.0×10^{-1}
Methyl-2-pentanone	2.5×10^{3}	9.4×10^{-1}
Methylene chloride	3.7×10^{1}	6.3×10^{-1}
4-Methylphenol	2.5×10^{2}	2.7×10^{-1}
Molybdenum	2.9×10^{3}	1.3×10^{1} [a]
Nickel	1.5×10^{4}	3.4×10^{1}
4-Nitroanaline	1.5×10^{2}	8.0×10^{-1}
N-nitrosodiphenylamine	5.1×10^{1}	1.3×10^{1}
N-nitrosodipropylamine	2.0×10^{-1}	2.0×10^{-1}
Octachlorodibenzofuran	8.8×10^{-3}	1.0×10^{-5}
Octachlorodibenzo-p-dioxin	8.8×10^{-3}	1.0×10^{-5}
Pentachlorophenol	2.3×10^{0}	9.7×10^{-1}
Selenium	5.4×10^{3}	2.5×10^{0}
Silver	2.9×10^{4}	1.0×10^{0}
Tetrachloroethene	3.6×10^{0}	1.0×10^{0}
Thallium	9.1×10^{1}	1.0×10^{0}
Toluene	1.0×10^{5}	2.7×10^{1}
Tributyl phosphate	2.5×10^{2}	2.9×10^{0}
1,1,2-Trichloroethane	4.3×10^{0}	1.9×10^{-1}
Trichloroethene	2.5×10^{1}	1.5×10^{0}
Vanadium	5.1×10^{3}	5.8×10^{1}
Vinyl chloride	1.3×10^{-1}	2.3×10^{-3}
Xylenes, total	9.2×10^{5}	4.0×10^{2}
Zinc	1.2×10^{5}	8.2×10^{1}

[a] K_1 = leaching coefficient

DRAFT

TABLE E-7 FINAL REMEDIATION LEVELS FOR SEDIMENT

Constituent	Final Remediation Levels
Radionuclides (pCi/g)	
Cesium-137(+1d)	7.0×10^{0}
Neptunium-237(+1d)	3.2×10^{1}
Lead-210(+2d)	3.9×10^{2}
Plutonium-238	1.2×10^{3}
Plutonium-239/240	1.1×10^{3}
Radium-226(+8d)	2.9×10^{0}
Radium-228(+1d)	4.8×10^{0}
Strontium-90(+1d)	7.1×10^{3}
Technetium-99	2.0×10^{5}
Thorium-228(+7d)	3.2×10^{0}
Thorium-230	1.8×10^{4}
Thorium-232(+10d)	1.6×10^{0}
Uranium, total (mg/kg)	2.1×10^{2}
Chemicals (mg/kg)	
Aroclor-1254	6.7×10^{-1}
Aroclor-1260	6.7×10^{-1}
Arsenic	9.4×10^{1}
Benzo(a)anthracene	1.9×10^{2}
Benzo(a)pyrene	1.9×10^{1}
Benzo(b)fluoranthene	1.9×10^{2}
Benzo(k)fluoranthene	1.9×10^{3}
Beryllium	3.3×10^{1}
Bis(2-ethylhexyl)phthalate	5.0×10^{3}
Bromoform	1.6×10^{2}
Cadmium	7.1×10^{1}
Carbazole	6.3×10^{1}
Chromium VI	3.0×10^{3}
Chrysene	1.9×10^{4}
Cobalt	3.6×10^{4}
Indeno(1,1,2-cd)-pyrene	1.9×10^{2}
Manganese	4.1×10^{2}
4-Methyl-2-pentanone	2.1×10^{3}
N-Nitrosodiphenylamine	2.6×10^{2}
Phenathrene	3.0×10^{-3}
Thallium	8.8×10^{1}

DRAFT

TABLE E-8 OPERABLE UNIT 5 ON-PROPERTY DISPOSAL FACILITY WASTE ACCEPTANCE CRITERIA

CONSTITUENT OF CONCERN	SOIL OU2	SOIL OU5	DEBRIS OU3
RADIONUCLIDES:			
Neptunium-237		3.12×10^{9} pCi/g	
Strontium-90		56.7×10^{9} pCi/g	
Technetium-99		29.1 pCi/g	105 g
U-238	346 pCi/g		
Total Uranium	1030 mg/kg	1030 mg/kg	
ORGANICS:			
1,2-Dichloroethane		*	
Carbazole		72.7×10^{3} mg/kg	
Bis(2-chlorisopropyl)ether		2.44×10^{-2} mg/kg	
Alpha-chlordane		2.89×10^{0} mg/kg	
Bromodichloromethane		9.03×10^{-1} mg/kg	
4-Nitroaniline		4.42×10^{-2} mg/kg	
Chloroethane		3.92×10^{3} mg/kg	
1,1,1-Trichloroethane[a]		*	
1,1-Dichloroethane[a]		*	
Carbon tetrachloride[a]		*	
Chloroform[a]		*	
Methylene chloride[a]		*	
Chloromethane[a]		*	
Vinyl chloride[a]		1.51×10^{0} mg/kg	
Tetrachloroethene[a]		128 mg/kg	
Trichloroethene[a]		128 mg/kg	
1,1-Dichloroehtene[a]		114 mg/kg	
1,2-Dichloroethene[a]		114 mg/kg	
Acetone[a]		*	
Benzene[a]		*	
Endrin[a]		*	
Ethylbenzene[a]		*	

DRAFT

TABLE E-8 OPERABLE UNIT 5 ON-PROPERTY DISPOSAL FACILITY WASTE ACCEPTANCE CRITERIA (Cont'd)

	SOIL		DEBRIS
CONSTITUENT OF CONCERN	**OU2**	**OU5**	**OU3**
Heptachlor[a]		*	
Heptachlor epoxide[a]		*	
Hexachlorobutadiene[a]		*	
Methoxychlor[a]		*	
Methyl ethyl ketone[a]		*	
Methyl isobutyl ketone[a]		*	
Toluene[a]		*	
Toxaphene[a]		106 x 10^3 mg/kg	
Xylenes[a]		*	
INORGANICS:			
Boron		1.04 x 10^3 mg/kg	
Mercury[a]		56.6 x 10^3 mg/kg	
Chromium VI[a]		*	
Barium[a]		*	
Lead[a]		*	
Silver[a]		*	

[a] RCRA-based constituent of concern.

* Denotes compounds that will not exceed designated Great Miami Aquifer action level within 1000-year performance period, regardless of starting concentration in the disposal facility.

SOURCE - Operable Unit 2 Record of Decision
Operable Unit 5 Feasibility Study
Onperable Unit 3 Draft Feasibility Study

DRAFT

D R A F T

THIS PAGE INTENTIONALLY LEFT BLANK.
