5·402.12

755

Department of Energy

Ohio Field Office
Fernald Area Office
P. O. Box 538705
Cincinnati, Ohio 45253-8705
(513) 648-3155

MAY 21 1997

DOE-0956-97

Mr. James A. Saric, Remedial Project Director
U.S. Environmental Protection Agency
Region V-SRF-5J
77 West Jackson Boulevard
Chicago, Illinois 60604-3590

Mr. Tom Schneider, Project Manager
Ohio Environmental Protection Agency
401 East 5th Street
Dayton, Ohio 45402-2911

Dear Mr. Saric and Mr. Schneider:

TRANSMITTAL OF THE FINAL VERSION OF THE RESTORATION AREA VERIFICATION SAMPLING PROGRAM PROJECT SPECIFIC PLAN

Reference:
1) Letter to Johnny Reising, U.S. DOE-FEMP, from James Saric, U.S. EPA dated February 26, 1997, "Restoration Area Verification Plan."

2) Letter to Johnny Reising, U.S. DOE-FEMP, from Thomas Schneider, OEPA dated February 28, 1997, "Conditional Approval Restoration Area PSP."

Enclosed for your review is the subject Project Specific Plan (PSP). In response to the U.S. Environmental Protection Agency (U.S. EPA) comments (Reference 1) and Ohio Environmental Protection Agency (OEPA) comments (Reference 2), the Department of Energy (DOE) conducted additional modeling to support the selection of a revised groundwater Final Remediation Level (FRL) for lead. The results of the additional modeling were faxed to you on March 27, 1997, and discussed during the weekly Department of Energy, Fernald Environmental Management Project (DOE-FEMP)/U.S. EPA and OEPA call held on April 1, 1997. Based on the input received on the conference call, the DOE prepared a more detailed write-up of the lead modeling and a Remedial Design Fact Sheet documenting the changes to groundwater FRLs for fluoride and lead. The lead modeling write-up and the fact sheet were faxed to you on April 25, 1997. The U.S. EPA comments on the write-up and fact sheet were received on May 7, 1997. On May 8, 1997 a revised (based on the U.S. EPA comments) write-up and fact sheet were faxed to you. The revised write-up and fact sheet were discussed with you on May 13, 1997, via conference call.

Recycled and Recyclable

The minor revisions requested during the May 13, 1997, call have been completed and the lead modeling results write-up and fact sheet are presented in the final PSP as Appendices B and C respectively.

As discussed on the May 13, 1997, conference call, in order to document the changes to the lead and fluoride groundwater FRLs, the fact sheet and a revised groundwater FRL table will be submitted to the FEMP Post-Decision File and to all holders of the Operable Unit 5 (OU5) Record of Decision (ROD). In accordance with the OEPA request on the May 13, 1997, conference call this distribution will not be made until the fact sheet has been discussed with interested public stakeholders at the May 27, 1997, OU5 roundtable.

With regards to the status of the work defined within the PSP, please note that the geoprobe work has been completed with the exception of a final location recently requested by the OEPA. Work on this final location began on Wednesday May 14, 1997. The quarterly sampling defined in the PSP has been initiated and is scheduled to be completed near the end of this year.

If you have any questions, please contact Robert Janke at (513) 648-3124, or Kathleen Nickel at (513) 648-3166.

Sincerely,

Johnny Reising

Johnny W. Reising
Fernald Remedial Action
Project Manager

FEMP:R.J. Janke

Enclosure: As Stated

cc w/enc:

N. Hallein, EM-42/CLOV
G. Jablonowski, USEPA-V, 5HRE-8J
R. Beaumier, TPSS/DERR, OEPA-Columbus
M. Rochotte, OEPA-Columbus
T. Schneider, OEPA-Dayton (total of 3 copies of enc.)
F. Bell, ATSDR
D. S. Ward, GeoTrans
R. Vandegrift, ODOH
R. Geiger, PRC
D. Carr, FDF/9
T. Hagen, FDF/65-2
J. Harmon, FDF/90
AR Coordinator/78

cc w/o enc:

C. Little, FDF/2
EDC, FDF/52-7

RESTORATION AREA VERIFICATION SAMPLING PROGRAM PROJECT SPECIFIC PLAN

FERNALD ENVIRONMENTAL MANAGEMENT PROJECT
FERNALD, OHIO

MAY 1997

U.S. DEPARTMENT OF ENERGY
FERNALD AREA OFFICE

2505-PSP-0003
REV. 0
FINAL

4

RESTORATION AREA VERIFICATION SAMPLING PROGRAM PROJECT SPECIFIC PLAN

FERNALD ENVIRONMENTAL MANAGEMENT PROJECT
FERNALD, OHIO

MAY 1997

U.S. DEPARTMENT OF ENERGY
FERNALD AREA OFFICE

FINAL 5

TABLE OF CONTENTS

List of Tables ii
List of Figures ii

1.0 Introduction 1
- 1.1 FRL Exceedances Detected Outside of the Restoration Footprint 2
- 1.2 Uranium Plume Delineation in the Area of Monitoring Well 3069 7

2.0 Management and Organization 10

3.0 Sampling Program 12
- 3.1 FRL Exceedances Detected Outside of the Restoration Footprint 12
- 3.2 Uranium Plume Delineation in the Area of Monitoring Well 3069 12

4.0 Quality Assurance/Quality Control Requirements 16
- 4.1 Project Requirements for Surveillances 16
- 4.2 Field Changes to the Project Specific Plan 16
- 4.3 Quality Assurance Samples 16

5.0 Equipment Decontamination 17

6.0 Health & Safety 18

7.0 Disposition of Investigation-Derived Wastes 19

8.0 Data Management 20
- 8.1 Validation 20
- 8.2 Data Entry 20

9.0 References 21

Appendix A Evaluation of FRL Exceedances Which Occur Outside of the Restoration Footprint
Appendix B Modeling Information to Support the Selection of the Lead FRL
Appendix C Remedial Design Fact Sheet - Groundwater FRLs for Fluoride and Lead

LIST OF TABLES

Table		Page
3-1	Analytical Program Requirements	15

LIST OF FIGURES

Figure		Page
1-1	Areas of the Great Miami Aquifer Requiring Remediation and the Aquifer Restoration Footprint	3
1-2	FRL Exceedance Locations to be Monitored	6
1-3	Location Map for Plume Delineation Activity	8
1-4	Total Uranium in Groundwater Cross Section A-A'	9

1.0 INTRODUCTION

The intent of the Restoration Area Verification Sampling Plan PSP can be summarized as follows:

- To evaluate all existing non-uranium groundwater data gathered outside of the uranium-based restoration footprint, and determine which sporadic FRL exceedances can be dismissed now, as non-FEMP related and/or not of concern. (Note that this analysis was accomplished as part of the development of the PSP, and is furnished in the PSP as Appendix A.) The intent of this evaluation is to satisfy a key data limitation noted in the Operable Unit 5 RI/FS regarding the sporadic and isolated detections above background. These isolated detections were not formally dismissed during the RI/FS process. Now that final FRLs are available with the issuance of the OU5 ROD, it is an appropriate and necessary step of the design process to assess these occurrences with respect to the FRLs.

- From the above evaluation, to determine which of the sporadic FRL exceedances require additional sampling before a final decision can be made regarding whether the exceedances drive a need to expand the restoration footprint beyond that based on uranium. (This determination was also conducted during the development of the PSP.) The results indicated that five constituents (antimony, manganese, cadmium, zinc, and lead) would require follow-up sampling before a final restoration footprint determination can be made.

- In parallel with the evaluation for the non-uranium constituents, to further define the vertical and lateral extent of uranium contamination above the FRL in the vicinity of Monitoring Well 3069, which was identified as a necessary follow-up activity through the UI's DMEPP sampling program.

The need to evaluate FRL exceedances outside of the aquifer restoration footprint has been reported in the OU5 FS Report (DOE 1995a) and the Draft Integrated Environmental Monitoring Plan (IEMP, DOE 1996a). The need to further delineate the 20 μg/L uranium plume in the area of Monitoring Well 3069 to support remedial design of the aquifer remedy is identified in the South Plume Removal Action, Design Monitoring Evaluation Program Plan, System Evaluation Report, for January 1, 1996 - June 30, 1996, (DOE 1996c). Restoration area verification was identified as part of the remedial design for aquifer restoration in the Operable Unit 5 Remedial Design Work Plan (DOE 1996b).

1.1 FRL EXCEEDANCES DETECTED OUTSIDE OF THE RESTORATION FOOTPRINT

The aquifer restoration footprint, shown in Figure 1-1, is the modeled non-retarded hydraulic capture zone which is predicted to result from the aquifer restoration under the 10-year restoration scenario presented in the Baseline Remedial Strategy Report for Aquifer Restoration (Remedial Design, Task 1). The size and dimension of the aquifer restoration footprint is dependent upon the amount and rate of pumping and/or injection which will be conducted to capture the 20 μg/L total uranium plume.

As noted in the Remedial Design Work Plan an evaluation of all existing non-uranium groundwater data for final remediation level (FRL) exceedances located outside of the restoration footprint was a necessary part of the remedial design for the aquifer restoration. The evaluation was conducted to determine if the non-uranium exceedances are attributable to the FEMP, are one time occurrences, are persistent and of such magnitude that they require a modification of the uranium based groundwater remedy or require additional monitoring to determine what additional action, if any, should be taken.

The establishment of FRLs provided a benchmark for the evaluation of all existing groundwater data. An evaluation of the groundwater data with respect to the ROD established FRLs was initiated in support of the 1995 RCRA Annual Report and the IEMP. The evaluation was completed in support of the preparation of this Project Specific Plan (PSP). As explained below, the results of this evaluation indicate that the majority of the FRL exceedances detected outside of the restoration footprint were either one time occurrences or are not attributable to the FEMP due to the upgradient position of the monitoring locations. The evaluation recommends additional monitoring for three constituents at three separate locations. It is proposed that this monitoring effort be incorporated into the IEMP.

The study area for the data evaluation found in Appendix A is the area outside of the aquifer restoration hydraulic capture zone but north of the Administrative Boundary for Aquifer Restoration, established in the Operable Unit 5 FS (Figure 1-1). Groundwater contamination attributed to the Paddys Run Road Site (PRRS), exists south of the Administrative Boundary. In the Operable Unit 5 Proposed Plan (DOE 1995b) it was acknowledged that DOE's role and involvement in OEPA's ongoing assessment and/or clean up of the PRRS plume, if any, would be defined separately as part of the PRRS response obligations and in accordance with the Paddys Run Road Site Project schedule.

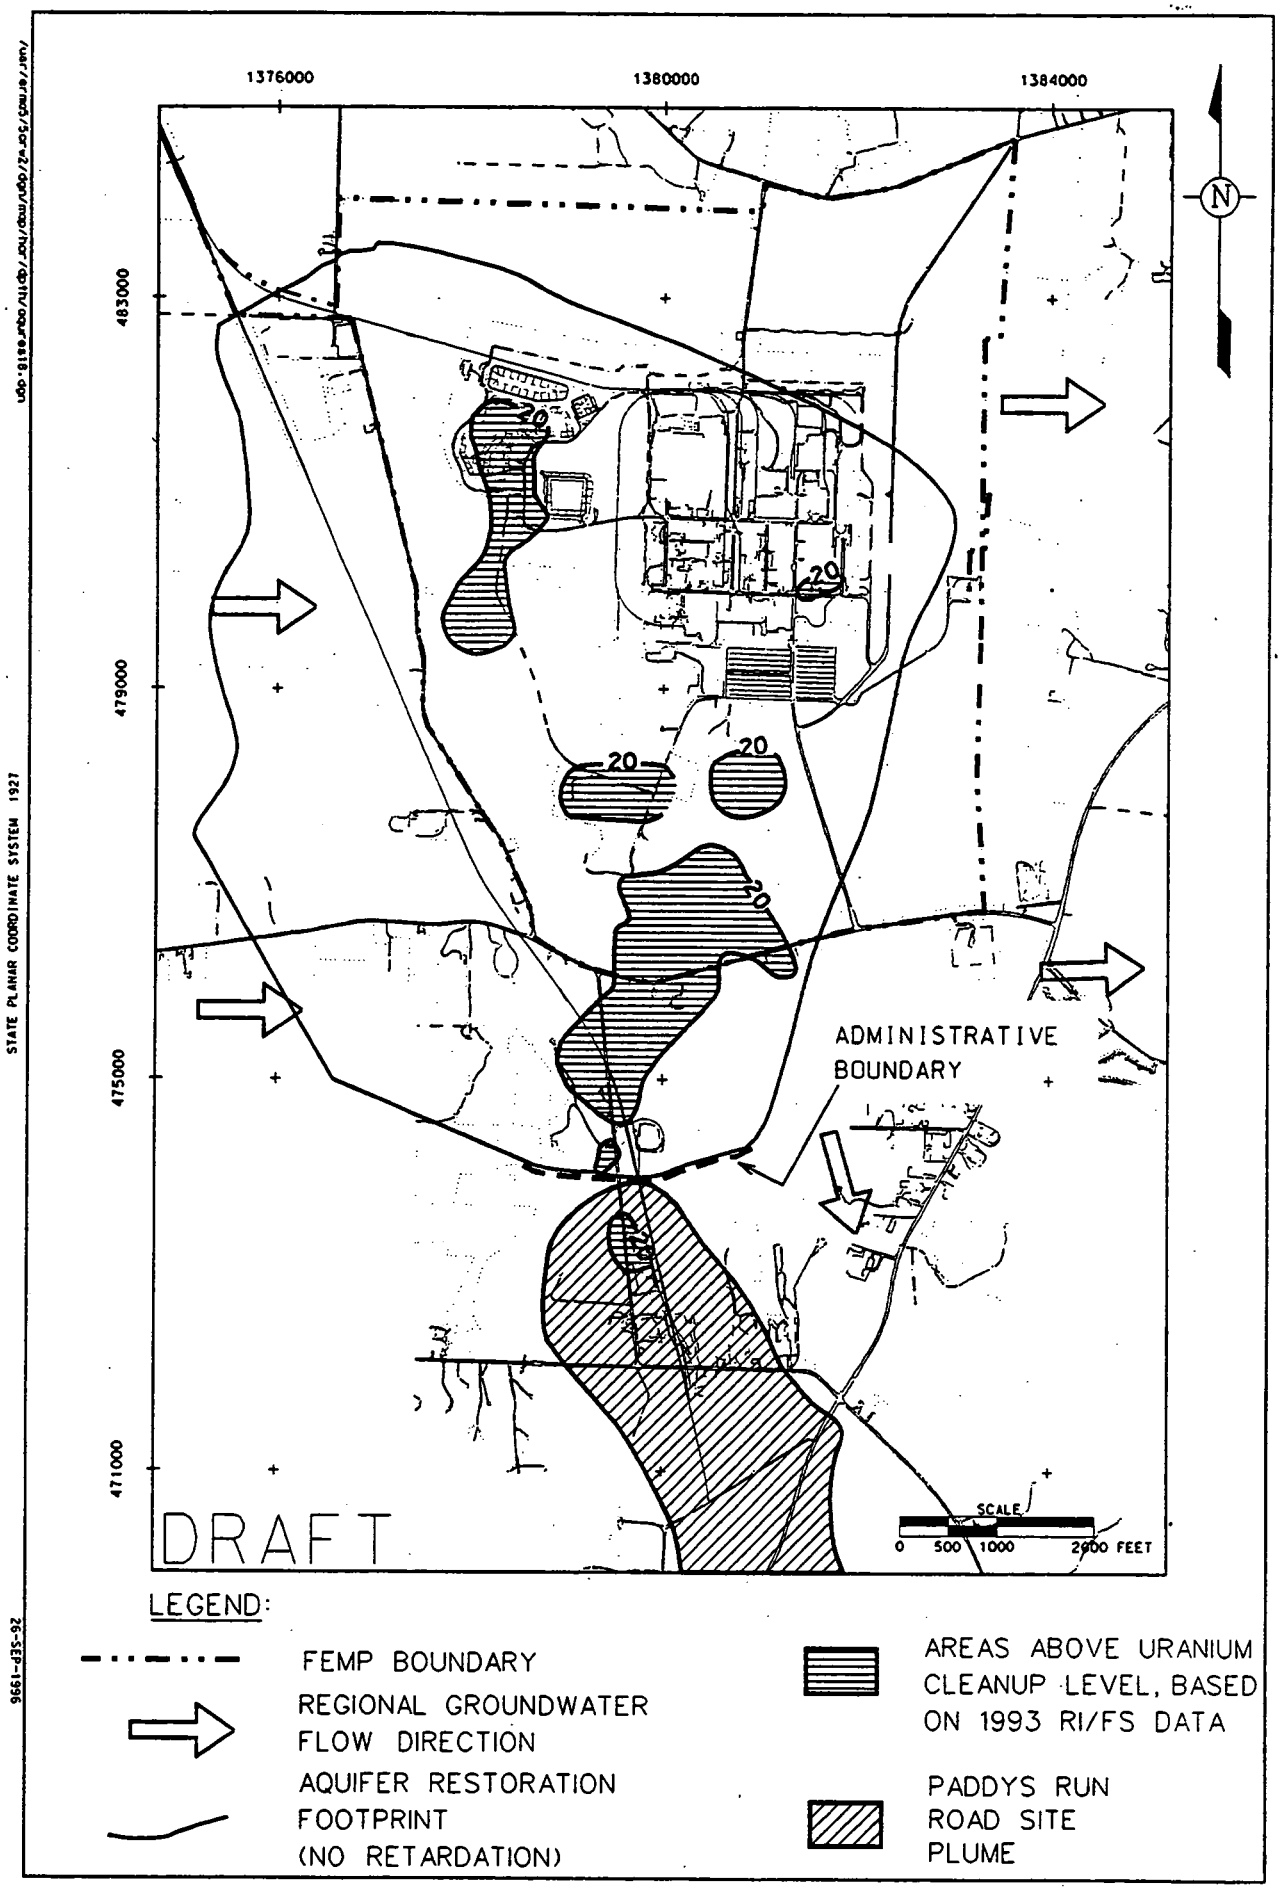

FIGURE 1-1. AREAS OF THE GREAT MIAMI AQUIFER REQUIRING REMEDIATION AND AQUIFER RESTORATION FOOTPRINT

The evaluation found in Appendix A concludes that the uranium based restoration area does not require modification at this time due to FRL exceedances identified in this evaluation. Of the 50 FRL constituents listed in the OU5 ROD, 14 have had at least 1 FRL exceedance outside the restoration footprint and north of the Administrative Boundary. The fourteen constituents are manganese, fluoride, nitrate, cadmium, lead, zinc, antimony, arsenic, mercury, nickel, trichloroethene, silver, thorium-228, and thorium-232. Of these fourteen constituents;

- Mercury, nickel, trichloroethene, silver, thorium-228, and thorium-232 can be dismissed from further monitoring outside the restoration footprint because the FRL exceedances were a one time occurrence with subsequent data indicating concentrations below the FRL.

- Fluoride can be dismissed from further monitoring outside the restoration footprint because the exceedances were identified using an FRL based on a background value of 0.89 mg/L. The MCL for fluoride in the OU5 ROD has been changed from .089 mg/L (95th percentile of background) to 4 mg/L (Safe Drinking Water Act Maximum Contaminant Level). When fluoride detects are compared against the MCL, no FRL exceedances result. Appendix A provides additional justification for changing the fluoride FRL.

- Nitrate can be dismissed from further monitoring outside of the restoration footprint. FRL exceedances for nitrate have been recorded at six location outside of the restoration footprint. Five of the locations are upgradient of the FEMP. The sixth location is an agricultural area downgradient of the FEMP. It is believed that this exceedance is due to fertilizer or some other agricultural activity and is not FEMP related. Additional information can be found in Appendix A.

- Arsenic can be dismissed from further monitoring outside of the restoration footprint. FRL exceedances for arsenic have been recorded at 10 locations outside of the restoration footprint. At six of the locations the last two sampling events have been below the FRL. The remaining four locations are upgradient of FEMP source areas. Additional information can be found in Appendix A.

- Many of the lead exceedances can be dismissed from further monitoring outside of the restoration footprint because they were identified using an FRL based on a background value of 0.002 mg/L. The FRL for lead in the OU5 ROD has been changed from a background based value of 0.002 mg/L to a value based on the Safe Drinking Water Act (SDWA) action level (0.015 mg/L). Using the SDWA action level does not eliminate all of the FRL exceedances for lead, but it does eliminate a majority of them. Appendices A and B provide additional information regarding the change of the groundwater lead FRL.

- Exceedances for antimony, manganese, cadmium, zinc and lead, at several locations outside of the aquifer restoration footprint, are not one time occurrences and due to their location relative to the FEMP could be attributable to the FEMP. Therefore they cannot be dismissed from further monitoring at this time.

The RCRA property boundary monitoring program currently monitors the majority of the locations where potentially FEMP related and persistent FRL exceedances are found outside of the aquifer restoration footprint. Only three of the identified exceedance locations are currently not being monitored by the RCRA Property Boundary Program; Well 3423 for antimony, Well 2436 for manganese, and Well 3091 for zinc. Figure 1-2 identifies the locations where monitoring for FRL exceedances outside the aquifer restoration footprint is recommended. It is proposed that quarterly sampling at these locations for the noted FRL constituents be completed as part of the IEMP groundwater sampling. The quarterly sampling would continue for a period of one year at which time data would be evaluated to determine additional actions at these locations.

The decision process for determining the final restoration footprint (and necessary follow-up actions, as appropriate) will follow these steps:

- Collect four quarter's worth of focused data for the parameters with FRL exceedances at the eight specified locations
- Complete geoprobe activity to refine the depth and lateral extent of uranium contamination triggered by findings in the vicinity of Well 3069
- Prepare a summary report including recommendations regarding the need for modification of the footprint beyond that dictated by uranium. The report will be submitted 90 days following compilation of the fourth quarter's data, in accordance with the final RD Work Plan.
- Finalize report following input from EPA and OEPA
- Proceed with any design modifications/additions to affected restoration modules, if necessary
- Incorporate any monitoring based actions arising from this process into the IEMP scope.

The sampling discussed above, to support the Restoration Area Verification Sampling PSP, is a focused effort targeted solely at confirming/refining the restoration area footprint for design purposes. Outside of this effort, the ongoing routine sampling that will be conducted through the IEMP will be utilized for the following broader purposes: to track remedy performance; confirm the success of hydraulic containment; and to continue to fulfill regulatory-driven groundwater monitoring obligations at the property boundary.

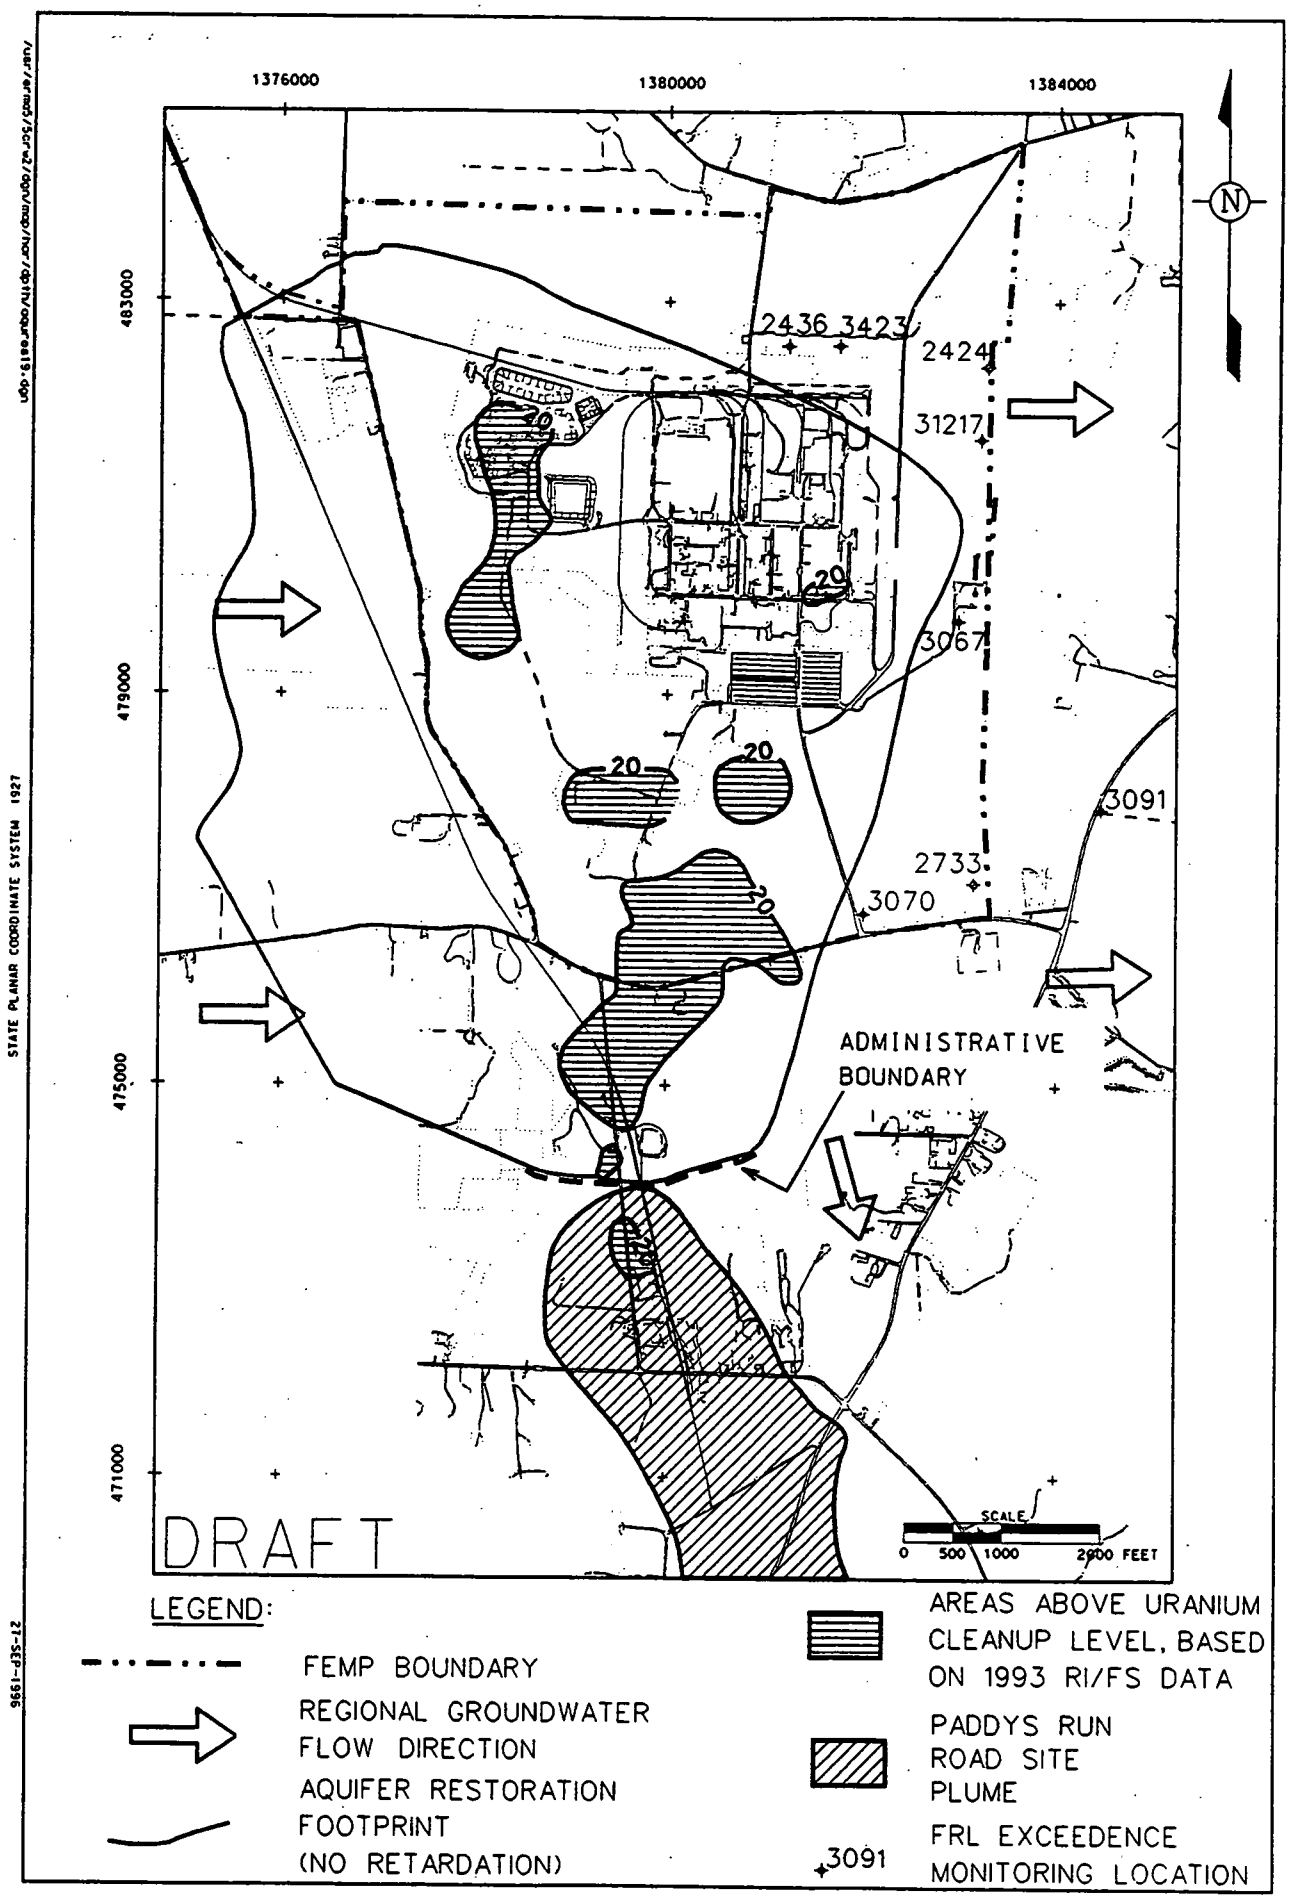

FIGURE 1-2. FRL EXCEEDANCE LOCATIONS TO BE MONITORED

13

1.2 URANIUM PLUME DELINEATION IN THE AREA OF MONITORING WELL 3069

In the area of monitoring Well 3069, the total uranium plume appears to bifurcate near the water table, and yet is present at relatively high concentration at depth. A recent interpretation for the behavior of the plume in this area, as reported in the South Plume Removal Action, Design Monitoring Evaluation Program Plan, System Evaluation Report, for January 1, 1996 to June 30, 1996, (DOE, 1996c) is that recharge from a nearby drainage ditch is causing the uranium plume to dilute near the water table and appears to be pushing higher uranium concentrations deeper into the aquifer. Figures 1-3 and 1-4 illustrate the situation being described. At Well 2434 uranium concentrations are below 20 μg/L. However, at Monitoring Well 3069, which is adjacent to monitoring Well 2434 but completed at a deeper level, uranium concentrations as high as 223 μg/L, with an average concentration of 156 μg/L during the first half of 1996, have been recorded since the 1993 Remedial Investigation sampling which indicated a concentration of 20 μg/L at Monitoring Well 3069. The area of identified recharge is the ditch labeled "Southeast Drainage Ditch" on the figures. To further substantiate the recharge theory, water chemistry of the surface water will be determined and compared with water chemistry of the aquifer as part of the Injection Demonstration Project.

The 20 μg/L total uranium plume may not be accurately defined by the 2000 and 3000 series monitoring well network in this area, and therefore additional sampling to determine the vertical and lateral extent of the > 20 μg/L uranium plume is needed. As discussed in Section 3, six locations have been selected for sampling, Figure 1-3. Collection of additional uranium data is needed to support the restoration design, which is in progress. The sampling program is presented in Section 3.2. Based on the findings at the initial six locations more sampling locations may be required. Additional sampling locations, if required, will follow the same sampling protocol as noted for the initial six locations in Section 3.2.

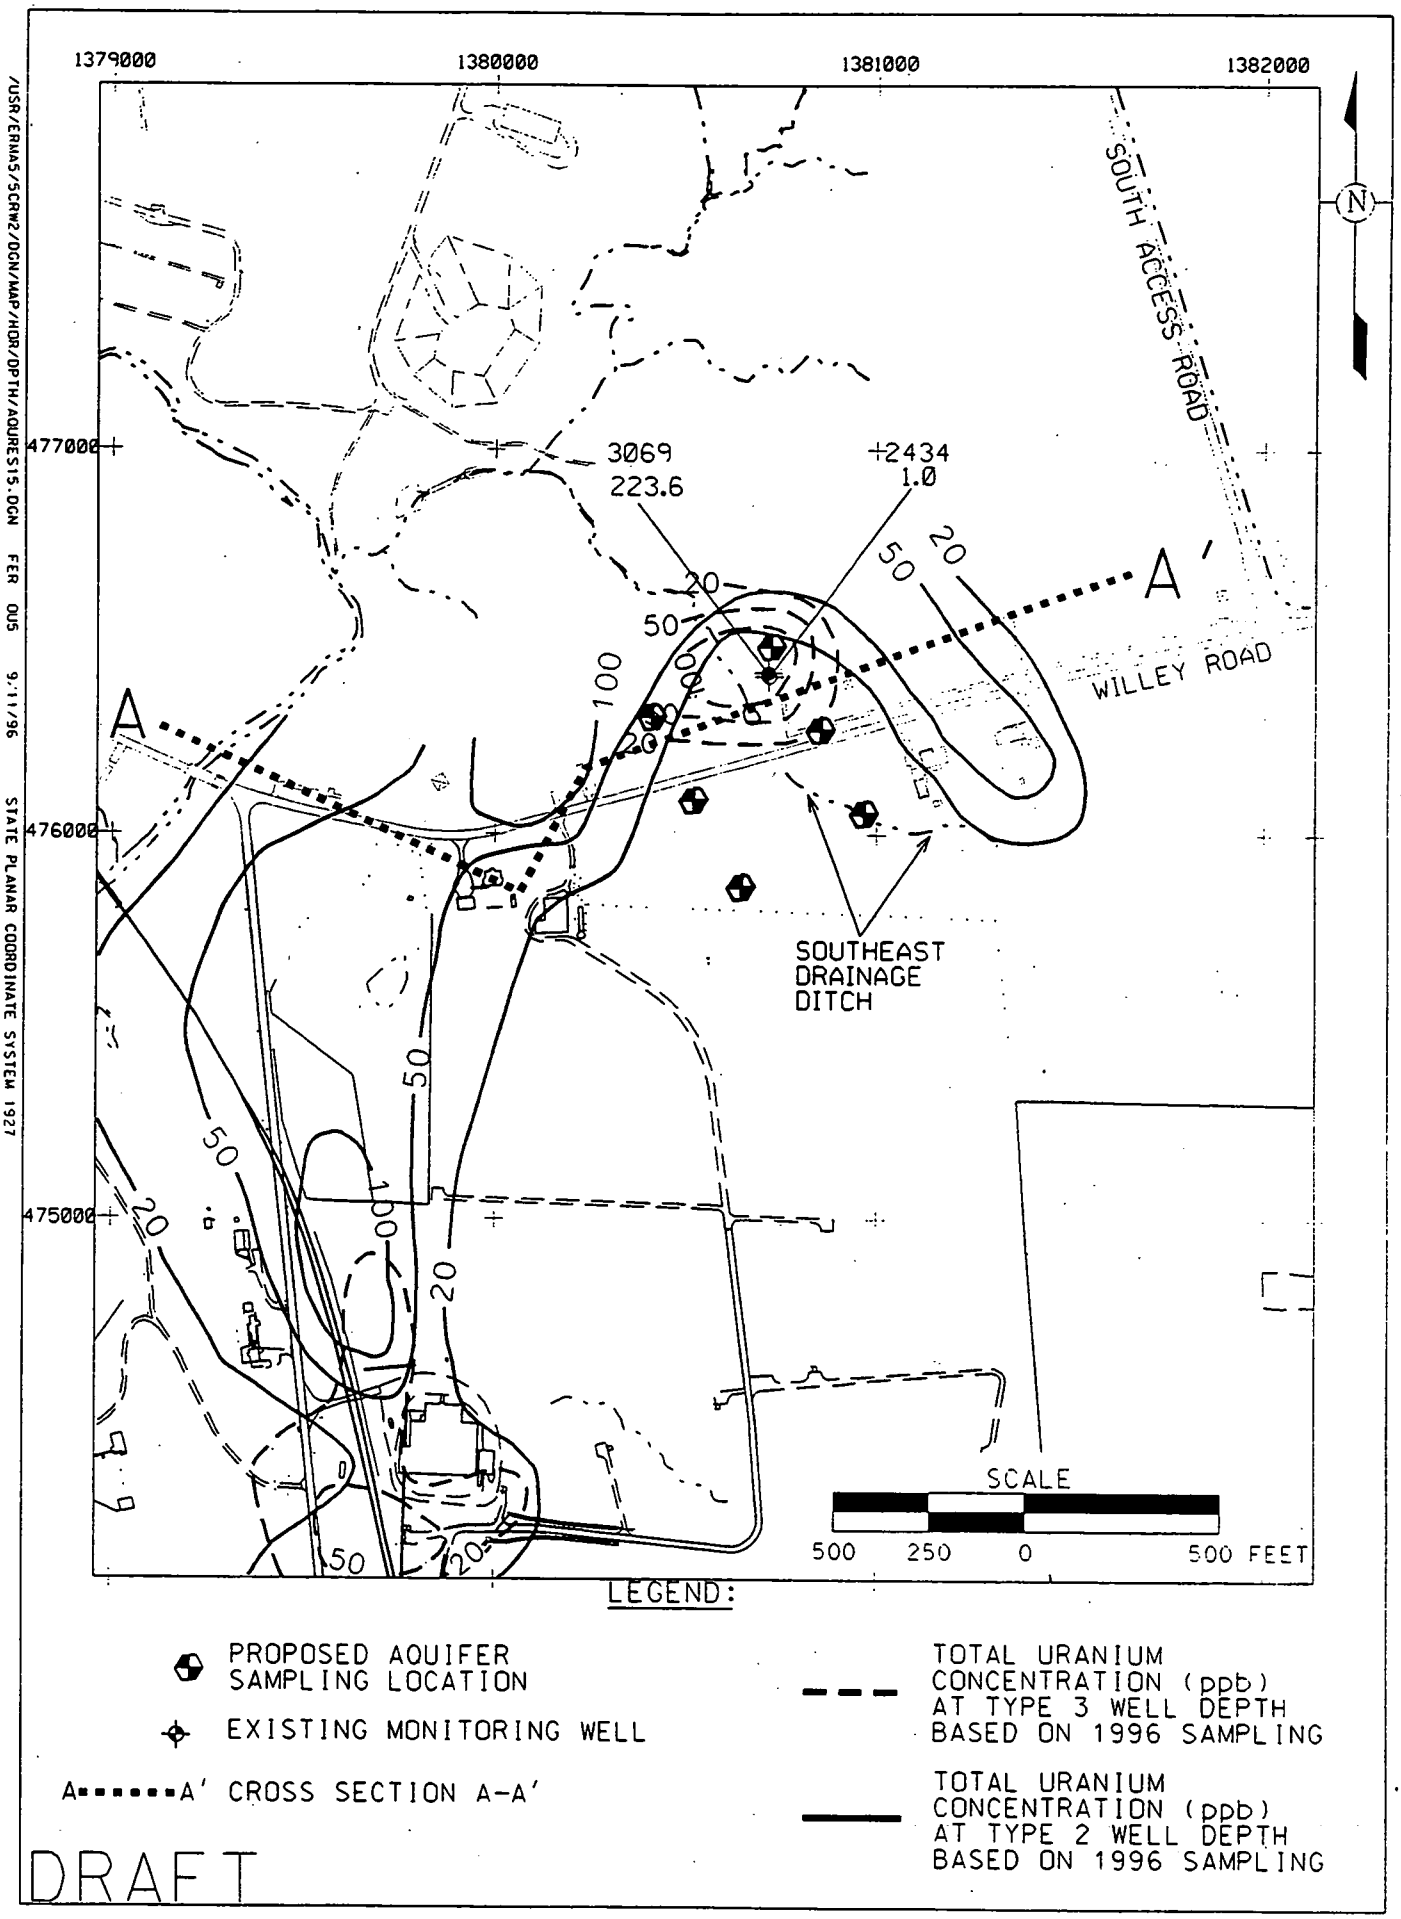

FIGURE 1-3. LOCATION MAP FOR PLUME DELINEATION ACTIVITY

15

/usr/armo5/5crw2/dgn/map/hor/dpth/psdsec01.dgn

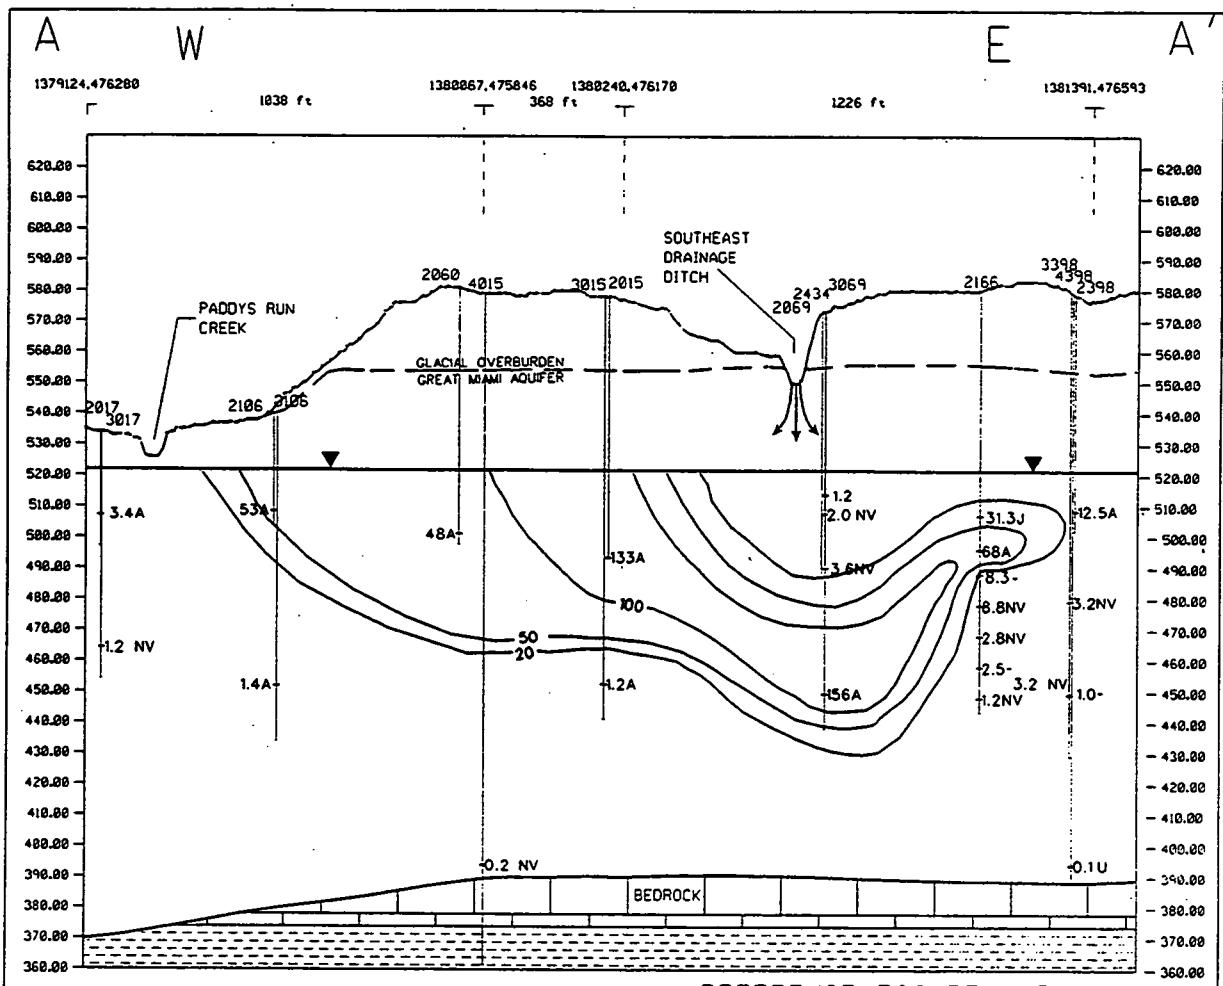

REFERENCE FIGURE 1-3. FOR CROSS-SECTION LOCATION

LEGEND:

+ 77.1 — TOTAL URANIUM IN GROUNDWATER (ug/L)

—20— TOTAL URANIUM ISOPLETH FOR GROUNDWATER (ug/L)

— — — GLACIAL OVERBURDEN/ GREAT MIAMI AQUIFER BOUNDARY

1771 — MONITORING WELL/ BORING NUMBER

▼ — WATER ELEVATION

REPRESENTS INFILTRATION OF "CLEAN" SURFACE WATER

DATA QUALIFIERS:

NV = NONVALIDATED

\- = VALIDTED, NOT QUALIFIED

J = VALIDATED, ESTIMATED

A = AVERAGE OF 1996 1st. AND 2nd. QUARTER DATA

NOTE:
URANIUM VALUES ARE FROM FIGURE 4-104 OF THE OU5 RI REPORT UNLESS QUALIFIED WITH AN "A". THE WATER ELEVATION SHOWN IS ESTIMATED.

DRAFT

SCALE

500 250 0 500 FEET

STATE PLANAR COORDINATE SYSTEM 1927

27-SEP-1996

FIGURE 1-4. TOTAL URANIUM IN GROUNDWATER CROSS-SECTION A-A'

2.0 MANAGEMENT AND ORGANIZATION

This section defines the roles and responsibilities of key management and technical personnel associated with the completion of the work defined in this PSP. Sampling activities defined in this PSP will be performed by Fluor Daniel Fernald. Descriptions of some of the key technical responsibilities of project personnel or organizations are provided below.

The DOE Operable Unit 5 Team Leader is responsible for:

- Providing direction and oversight to the completion of PSP activities
- Acting as the point of contact within DOE and for the regulators and stakeholders for all communications concerning work carried out under this PSP.

The Fluor Daniel Fernald Aquifer Restoration Project Director is responsible for:

- Providing overall project management and technical guidance to the Fluor Daniel Fernald team
- Ensuring the necessary resources are allocated to the project for the efficient and safe completion of PSP activities
- Overseeing and auditing PSP activities to ensure that the work is being performed efficiently and in accordance with all regulatory requirements and commitments, DOE Orders, site policies and procedures, and safe working practices.

The Fluor Daniel Fernald Project Manager is responsible for:

- The safe and prompt completion of work outlined in the PSP
- Oversight and programmatic direction of sampling activities
- Providing a technical lead for the collection and interpretation of sampling data
- Establishing and maintaining the scope, schedule, and cost baseline
- Reporting to the DOE Aquifer Restoration Project Team Leader and Fluor Daniel Fernald Aquifer Restoration Project Manager on the status of PSP activities and on the identification of any problems encountered in the accomplishment of the PSP
- Obtaining the necessary funding to complete the sampling and data analysis activities

The Fluor Daniel Fernald Technical Lead is responsible for:

- Reporting to the Fluor Daniel Fernald Project Manager on the progress of PSP activities
- Interpreting and reporting the sampling results

3.0 SAMPLING PROGRAM

Analytical Program Requirements are summarized in Table 3-1. All monitoring wells will be purged and sampled using procedures specified in SCQ Section 6.2. All analyses will be conducted by the appropriate FEMP or contracted laboratory using procedures which meet the standards for these analytical support levels as established in the SCQ. Sample collection procedures and guidance sections of the SCQ are used to conduct groundwater monitoring:

Standard Operating Procedures

ADM-02	Field Project Prerequisites
EM-EQT-06	Geoprobe Operation (Draft)
EM-GWM-FO-201	Groundwater Sampling Activities
EM-GWM-202	Groundwater Sample Shipment

Sitewide CERCLA Quality (SCQ) Assurance Project Plan

Section 5	Field Activities
Section 6	Sampling Requirements
Section 7	Sample Custody
Section 9	Analytical Procedures
Appendix I	Field Calibration Requirements
Appendix J	Field Activity Methods
Appendix K	Sampling Methods

3.1 FRL EXCEEDANCES DETECTED OUTSIDE OF THE RESTORATION FOOTPRINT

The following scope of work will be added to the IEMP. Quarterly groundwater samples will be collected from Monitoring Wells 3423, 2436, and 3091 and sampled for antimony, manganese, and zinc respectively, at ASL Level B (see Table 3-1). Detection limits used will be the limits that are identified in the Operable Unit 5 FS Report as being the lowest achievable.

3.2 URANIUM PLUME DELINEATION IN THE AREA OF MONITORING WELL 3069

A Geoprobe™ screen point or mill-slotted well point sampler will be used to collect groundwater samples from the six locations shown in Figure 1-3. Collection of off property samples will be subject to the approval of the land owner. Sampling will take place at depth increments of 10 feet from the top of the water table to a depth of approximately 150 feet below the ground surface to obtain a complete vertical profile of the greater than 20 μg/L total uranium plume. The depths required to obtain this vertical profile are near the depth limits of the Geoprobe tool. If sampling indicates that the deeper

sampling is required to profile the plume, then a different method for obtaining the sample may need to be used. Groundwater samples will be analyzed for total uranium at ASL Level B (see Table 3-1). One matrix spike duplicate and one rinsate sample shall be collected at each location.

It is estimated that the water table is located at a depth of approximately 60 feet below the ground surface in this area. It is expected that nine depth intervals can be sampled at each location (one every ten foot of depth) for a total of 54 sampling events.

Past experience with groundwater samples collected using the Geoprobe™ screen point sampler has indicated high sample turbidity (due to suspended solids) which requires excessive amounts of HNO_3 to preserve the sample. Dissolution of suspended solids by HNO_3 results in a sample that is not representative of groundwater in the aquifer. Analysis of samples of this type (where sediments have been dissolved) leads to biased results and could lead to inaccurate assessments of contaminant concentrations in the aquifer. A pre-filtering step described below will be used to alleviate this problem.

Groundwater samples collected using the Geoprobe™ screen point or mill-slotted well point sampler will be pre-filtered using a 11 micron filter to remove the majority of suspended solids. The pre-filtered sample will then be split into a filtered sample (0.45 micron filter) and an unfiltered total sample per Section 5.8.4 and 5.8.5 of procedure SC-GWM-FO-201. Duplicate filtered and unfiltered samples will also be prepared. The duplicate samples will be archived temporarily for re-analysis purposes if necessary. All samples will be filtered or poured into 250-ml containers preserved with HNO_3 (0.4 mL). Groundwater sample collection will be accomplished using a 3/8 inch O.D. polyethylene tubing equipped with a ball check valve. New tubing will be used for each sample collected.

During pre-probing and deployment of the sampling screen, it may be necessary to remove the tool screen from the hole which may result in partial hole collapse. The amount of time the probe hole is left open will be minimized to the extent practical. The glacial till in the planned investigation area contains no constituents of concern above FRLs.

The 1.0- to 1.5-inch diameter probe will be plugged with a bentonite slurry following groundwater sample collection. The bentonite will be mixed to SCQ density specifications (approximately 9.4 lbs. per gallon) and pumped through probe rods to the bottom of the bore hole as the probe rods are removed. For the purpose of this PSP, the aquifer material will be allowed to collapse naturally up to the water table. Plugging of the probed hole with bentonite slurry will begin 3 feet above the water table and continue to the ground surface. The volume of the bentonite slurry used in the plugging process will be monitored and recorded.

TABLE 3-1

ANALYTICAL PROGRAM REQUIREMENTS

Constituent	Sample Type	ASL	Holding Time	Preservation	Container[a]
Metals	Grab	B	6 months	HNO_3 to pH < 2	Plastic or glass
Total Uranium	Grab	B	6 months or 5x half-life, whichever is less	HNO_3 to pH < 2	Plastic or glass
Field Parameters[a]	Grab	A	NA[b]	NA[b]	NA[b]

[a]Field parameters include dissolved oxygen, pH, specific conductance, temperature and turbidity
[b]NA = Not applicable

4.0 QUALITY ASSURANCE/QUALITY CONTROL REQUIREMENTS

Groundwater Monitoring Sampling events follow Quality Assurance/Quality Control (QA/QC) protocol established in Section 4 and Appendix K of the SCQ.

4.1 PROJECT REQUIREMENTS FOR SURVEILLANCES

Self-assessment of work processes and operations shall be undertaken to assure quality of performance. Self-assessment shall be performed by the Project Manager, and shall encompass technical and procedure requirements. Such self-assessment may be conducted at any point in the project.

Independent assessment shall be performed by the FEMP QA organization by conducting surveillances. At a minimum, one surveillance shall be conducted, consisting of monitoring/observing ongoing project activity and work areas to verify conformance to specified requirements. Surveillances shall be planned and documented in accordance with Section 12.3 of the SCQ.

4.2 FIELD CHANGES TO THE PROJECT SPECIFIC PLAN

Prior to the implementation of field changes, the Project Manager shall be informed of the proposed field changes. Once approval has been obtained (verbal or written) from the Project Manager and QA representative for the field changes to the PSP, the field changes may be implemented. Field changes to the PSP shall be noted on a Variance Request form. QA must receive the completed Variance Request form, which includes the signatures of the Project Manager, and the QA/QC Representative, within one week of the granting of the verbal approval.

4.3 QUALITY ASSURANCE SAMPLES

Field quality assurance samples shall include one rinsate per geoprobe location, and one matrix spike duplicate for each analytical batch.

5.0 EQUIPMENT DECONTAMINATION

Sampling equipment shall be decontaminated prior to transport to the sample field site and after all sampling is completed to limit the introduction of contaminants from equipment to sampled media and to protect worker safety and health.

The decontamination of equipment that comes into contact with groundwater shall be a Level II Decontamination as referenced in Section K.11 of the SCQ and as described in Section 6.4.1 of the SCQ and Section 5.7.6 of SOP EM-GWM-FO-201, "Groundwater Sampling Activities." Probing equipment that will not be in contact with the groundwater shall be decontaminated at Level I per SCQ procedures.

6.0 HEALTH & SAFETY

EM Sampling Technicians shall conform to precautionary surveys performed by the personnel representing the Utility Engineer, Industrial Hygiene, and Radiological Control. Concurrence to applicable safety permits (indicated by the signature of each EM Sampling Technician assigned to this project) is expected by EM Sampling Technicians in the performance of their assigned duties.

The EM Field Supervisor or the Lead Sampling Technician will ensure that each EM Sampling Technician performing sampling related to this project has read the Programmatic Health and Safety Plan (PHSP) and the applicable surveys that protect worker safety and health. EM Sampling Technicians who do not sign these documents shall not participate in the execution of sampling activities related to the completion of assigned project responsibilities. A copy of applicable safety permits/surveys issued for worker safety and health shall be posted at each sample location and at the completion of the project, the completed forms shall be submitted for incorporation into the project files.

7.0 DISPOSITION OF INVESTIGATION-DERIVED WASTES

During completion of sampling activities, EM Sampling Technicians may generate contact wastes, purge water, and decontamination waste. Following completion of sampling, the EM Sampling Technicians shall place contact wastes into properly labeled bags and disposition in accordance with appropriate FEMP waste management policies. The EM Sampling Technicians shall decant decontamination solution into appropriate containers which will be ultimately transferred to Plant 8 for treatment.

8.0 DATA MANAGEMENT

This data management plan will be implemented so information collected during the investigation will be properly managed following completion of the field activities. As specified in Section 5.1 of the SCQ, sampling teams shall describe daily activities on the Field Activity Log (FAL) sufficient for the sampling team to reconstruct a particular situation without reliance on memory. Sample collection logs shall be completed according to instructions specified in Appendix B of the SCQ.

8.1 VALIDATION

To assure appropriate documentation was completed during field activities and that documentation was completed correctly, field documentation shall be validated.

Analytical data shall be validated upon receipt. Validation shall be performed to the highest ASL permitted by the data.

The Data Quality Group shall provide to the Project Manager and to Analytical Data Management (ADM) copies of the summary reports listing validation qualifiers applied along with copies of the validated data sheets. All original validation summary forms and validation reports shall be submitted to ADM for permanent storage.

8.2 DATA ENTRY

Analytical data shall be received from the contract laboratory by electronic data transfer in a compatible format with the FEMP database and in hard-copy format. Hard-copy documents are kept in permanent storage in the Project Files; the electronic database is permanently archived in a neutral ASCII file format.

9.0 REFERENCES

U.S. Dept. of Energy, 1996a, "Integrated Environmental Monitoring Plan, Draft," Fernald Environmental Management Project, U.S. Dept. of Energy, Fernald Field Office, Cincinnati, OH.

U.S. Dept. of Energy, 1996b, "Remedial Design Work Plan for Remedial Actions at Operable Unit 5," Fernald Environmental Management Project, U.S. Dept. of Energy, Fernald Field Office, Cincinnati, OH.

U.S. Dept. of Energy, 1996c, "South Plume Removal Action Design Monitoring Evaluation Program Plan, System Evaluation Report for January 1, 1996-June 30, 1996," Fernald Environmental Management Project, U.S. Dept. of Energy, Fernald Field Office, Cincinnati, OH.

U.S. Dept. of Energy, 1995a, "Feasibility Study Report for Operable Unit 5," Fernald Environmental Management Project, U.S. Dept. of Energy, Fernald Field Office, Cincinnati, OH.

U.S. Dept. of Energy, 1995b, "Proposed Plan for Operable Unit 5," Fernald Environmental Management Project, U.S. Dept. of Energy, Fernald Field Office, Cincinnati, OH.

APPENDIX A

EVALUATION OF FRL EXCEEDANCES WHICH OCCUR OUTSIDE OF THE RESTORATION FOOTPRINT

A.1 Introduction

Constituents (uranium and non-uranium) which will be used to assess the progress and success of the aquifer restoration have been assigned Final Remediation Levels (FRLs) in the Operable Unit 5 ROD and are referred to in this evaluation as FRL constituents. If an FRL constituent is detected in the Great Miami Aquifer at a concentration above its FRL, then it is referred to as an FRL exceedance.

Data evaluation in support of the Integrated Environmental Monitoring Plan (IEMP, DOE 1996a) indicated that fourteen FRL constituents have had at least one FRL exceedance at some location outside of the restoration footprint, and north of the PRRS Administrative Boundary, Figure A.1-1. The fourteen FRL exceedances, which are the scope of this evaluation, are: manganese, fluoride, nitrate, cadmium, lead, zinc, antimony, arsenic, mercury, nickel, trichloroethene, silver, thorium-228, and thorium-232. As explained in the IEMP, FRL exceedances located outside of the restoration footprint will not be addressed by the planned configuration of pumping and injection wells designed for the aquifer restoration. A decision needs to be made on whether or not the exceedances outside of the restoration footprint are attributable to the FEMP and need to be monitored and remediated.

The evaluation presented in this appendix reviews the Operable Unit 5 remedial investigation study groundwater data set, supplemented with groundwater data collected in 1994 and 1995 to further evaluate the nature of the 14 FRL exceedances located outside the restoration footprint.

During the preparation of this PSP it was discovered that FRLs for two constituents (fluoride and lead) were not selected in accordance with the approved FRL development protocol found in the Operable Unit 5 Feasibility Study. The Operable Unit 5 Feasibility Study (Section 2, page 2-54) outlined two Cases for potential groundwater FRLs. These two Cases are: Case 1 which "considered a target risk level of 10^{-6} ILCR and an HI of 0.2 to a resident farmer," and Case 2 which "employed the MCLs, proposed MCLs and nonzero MCLGs as target cleanup values. For those COCs with no MCLs, proposed MCLS, or nonzero MCLGs, Case 2 considered a target risk level of 10^{-5} and an HI of 0.2 to a resident farmer."

Case 2 was ultimately selected as part of the preferred alternative in the approved Operable Unit 5 Proposed Plan and was subsequently utilized to establish the groundwater FRLs found in the final Operable Unit 5 ROD. Figure A.1-2 (Process For Development of Groundwater FRLs) illustrates the

Case 2 FRL development process. In the OU5 FS process for the development of the fluoride FRL, the MCL for fluoride (4 mg/L) was inadvertently overlooked, and according to the approved Case 2 development process the MCL should have been selected as the FRL; (the current FRL was inadvertently established based on the 95th percentile background concentration of fluoride, which is 0.89 mg/L).

In light of the approved Case 2 FRL development process, the current background based FRL for lead (0.002 mg/L) is also not appropriate. There is no MCL for lead and currently there are no toxicity data from which to derive specific health-based cleanup levels for lead. The apparent reason for this lack of toxicity information is that the appropriate reference dose for lead is widely disputed among toxicologists. However, the 0.015 mg/L action level for lead was promulgated as a protective standard for all drinking water supplies nationwide. In the absence of additional toxicological data, it is reasonable to apply this standard as an appropriate lead cleanup level for the FEMP. DOE understands that U.S. EPA has adopted this approach for lead at a number of Superfund sites nationwide.

The SDWA action level for lead was documented in the Operable Unit 5 Feasibility Study and ROD ARAR tables, however, since it was not a true MCL it was overlooked in the development of the lead FRL for groundwater. In the absence of an MCL for lead DOE believes that the SDWA health based action level of 0.015 mg/L is an appropriate substitute for the MCL. Appendix B presents modeling results evaluated to support the selection of the SDWA action level as the Final Remediation Level (FRL) for lead in groundwater. The modeling was conducted using the most recent version (version 99D) of the EPA's IEUBK model for lead.

Based on the above information the evaluation lead and fluoride contained in this appendix (and summarized in Section 1.0) was completed utilizing the MCL for fluoride (4 mg/L) and the SDWA action level for lead (0.015 mg/L) rather than the using the inappropriate background-based FRLs.

EPA, OEPA and DOE have agreed to change the groundwater FRLs for fluoride and lead, currently found in the OU5 ROD as follows:

- The groundwater FRL for fluoride will change from 0.89 mg/L (95th percentile background concentration) to 4 mg/L (MCL), and

- The groundwater FRL for lead will change from 0.002 mg/L (95th percentile background concentration) to 0.015 mg/L (Safe Drinking Water Act Action Level).

A remedial design fact sheet pertaining to the changes in the groundwater FRL values for fluoride and lead is provided in Appendix C.

A.2 Background

The aquifer restoration footprint, shown in Figure A.2-1, is the modeled non-retarded hydraulic capture zone which is predicted to result from the aquifer restoration under the 10-year restoration scenario presented in the Baseline Remedial Strategy Report for Aquifer Restoration (Remedial Design, Task 1). The size and dimension of the aquifer restoration footprint is dependent upon the amount and rate of pumping and/or injection which will be conducted to capture the 20 μg/L total uranium plume.

In general, FRLs assigned for the cleanup are based on either a promulgated ARAR value, the 95th percentile background concentration, the lowest reasonable and achievable detection limit, or the risk based Preliminary Remediation Goal (PRG). A promulgated ARAR value takes precedence, unless background concentrations are higher than the ARAR value. If an ARAR does not exist for a constituent, then the FRL is usually based on the 95th percentile background concentration or the PRG, whichever is higher. A detailed discussion of FRL development is provided in Section 2 of the approved Operable Unit 5 FS Report.

A.3 Evaluation

As noted in the RD Work Plan, an evaluation of all existing non-uranium groundwater data for final remediation level (FRL) exceedances located outside of the restoration footprint was a necessary part of the remedial design for the aquifer restoration. The focus of this evaluation was to determine if the non-uranium exceedances are attributable to the FEMP, are one time occurrences, are persistent and of such magnitude that they require a modification of the uranium based groundwater remedy or require additional monitoring to determine what additional action, if any, should be taken.

As mentioned above, there are 14 constituents that have had an FRL exceedance outside of the aquifer restoration footprint and north of the Administrative Boundary for aquifer restoration. Concentration data were graphed at each of the exceedance locations to identify the persistence of the exceedance. To be conservative, the values plotted on the graphs represent the greatest reported concentration for each

date of filtered and unfiltered samples, as well as normal and duplicate samples. Any large discrepancy between concentrations of the same constituent on the same date were noted on the individual graphs.

If an exceedance was a one time occurrence and is no longer occurring, then there is no need to continue monitoring for the constituent or to remediate the location. If two or more sampling events following an exceedance indicate that concentrations are below the FRL, then the location will not be considered for further monitoring or remediation. The evaluation of each of the 14 constituents with FRL exceedances is described below.

Antimony

The FRL for antimony is 0.006 mg/L, which is an MCL under the Safe Drinking Water Act. FRL exceedances for antimony have been recorded at 5 locations (Monitoring Wells 2432, 3070, 2424, 3423, and 2066) outside of the restoration footprint, Figure A.3-1. The FRL exceedances range from 0.0245 mg/L to 0.116 mg/L. Figures A.3-2 through A.3-6 show the concentration versus sample date for the five different locations.

Data from Monitoring Wells 2432, 3070, and 2424 (Figures A.3-2 through A.3-4 respectively) indicate that the FRL exceedance was a one time event and subsequent sampling indicates that the concentration is below the FRL, therefore monitoring for FRL exceedances of antimony at these locations is not necessary. However, Monitoring Wells 2432, 3070, and 2424 will continue to be monitored for antimony as part of the IEMP RCRA Property Boundary Program.

Data from Monitoring Well 2066 (Figure A.3-5) indicates that the last sampling event measured an FRL exceedance. This well is upgradient of the FEMP and has been used as a background well for the FEMP. Because of its upgradient location, the antimony exceedance is not attributed to the FEMP; therefore, it is proposed that no additional monitoring for antimony take place at Monitoring Well 2066.

Data from Well 3423 (Figure A.3-6) indicates that the FRL exceedance for antimony was not a one time event. Given the location of this well the exceedance could be attributable to the FEMP and should be monitored. It is proposed that the task of sampling Monitoring Well 3423 for antimony be added to the IEMP.

Arsenic

The FRL for arsenic is 0.05, which is an MCL established by the Safe Drinking Water Act. FRL exceedances for arsenic have been recorded at 10 locations (Monitoring Wells 2026, 2036, 2056, 2105, 2679, 3063, 3066, 3092, 3679, and 3678) outside of the restoration footprint, Figure A.3-7. Figures A.3-8 through A.3-17 are graphs of the concentration versus sampling date for the 10 different locations.

At Wells 2026, 2036, 2056, 2105, 3063, and 3092 (Figures A.3-8 through A.3-13 respectively), the last two (or more) sampling events indicate that arsenic concentrations are below the FRL. With the exception of Monitoring Well 3092, all of the wells are upgradient of the FEMP. The remaining four wells (3066, 3679, 2679 and 3678) are all located upgradient (north) of the former production area and Waste Storage Area (Figure A.3-7). FRL exceedances for arsenic at wells 3066, 3679, 2679, and 3678 are not one time occurrences (Figures A.3-14 through A.3-17, respectively). FRL exceedances for arsenic at these locations are not attributable to former FEMP operations because these locations are upgradient of the FEMP and therefore will not be monitored or remediated. It is proposed that with the exception of those wells currently being sampled as part of the RCRA Property Boundary Program, no additional monitoring take place outside of the Aquifer Restoration Footprint for arsenic.

Cadmium

The FRL for cadmium is 0.014 mg/L and is based on background which ranges from 0.0022 mg/L to 0.014 mg/L (DOE 1994). FRL exceedances of cadmium have been recorded at four locations outside of the restoration footprint (Monitoring Wells 3898, 2733, 3067, and 2424), Figure A.3-18. The FRL exceedances range from 0.0155 mg/L to 0.0285 mg/L.

At Wells 2424, 2733, 3067, and 3898 (Figures A.3-19 through A.3-22 respectively) the FRL exceedances for cadmium were one time occurrences. It is proposed that with the exception of those wells currently being sampled as part of the RCRA Property Boundary Program, no additional monitoring take place outside of the Aquifer Restoration Footprint for cadmium.

Fluoride

The FRL for fluoride is recorded as 0.89 mg/L in the OU5 ROD (DOE 1996a) and is based on background which ranges from 0.1 mg/L to 1.9 mg/L (DOE 1994). The MCL for fluoride is 4 mg/L.

The MCL value for fluoride was inadvertently overlooked in the development of the fluoride FRL. The fluoride MCL should be used as the FRL since MCLs, when higher than background, take precedence over background in the FRL development process.

FRL exceedances of fluoride have been recorded at 16 locations outside of the restoration footprint, Figure A.3-23. The FRL exceedances range from 0.9 mg/L to 1.8 mg/L. When the MCL value is used as the FRL, there are no fluoride exceedances outside of the restoration footprint.

EPA, OEPA and DOE have agreed to change the groundwater FRL value for fluoride from 0.89 mg/L to 4 mg/L (see Appendix C). With this change, exceedances outside of the aquifer restoration footprint are no longer an issue.

It is proposed that with the exception of those wells currently being sampled as part of the RCRA Property Boundary Program, no additional monitoring take place outside of the Aquifer Restoration Footprint for fluoride.

Lead

The FRL for lead is recorded as 0.002 mg/L in the OU5 ROD (DOE 1996a) and is based on background which ranges from <0.001 mg/L to 0.002 mg/L (DOE 1994). The SDWA action level for lead is 0.015 mg/L. EPA, OEPA, and DOE have agreed to change the groundwater FRL value for lead from 0.002 mg/L to 0.015 mg/L (see Appendix C). Modeling results evaluated to support the selection of the SDWA action level as the Final Remediation Level (FRL) for lead in groundwater is provided in Appendix B. FRL exceedances of lead (based on 0.002 mg/L) have been recorded at 26 locations outside of the restoration footprint, Figure A.3-24. The FRL exceedances range from 0.0021 mg/L to 0.08 mg/L. Compared against the SDWA action level, exceedances have only been recorded at the five locations (Monitoring Wells 2056, 2121, 2122, 2733, and 3070) as shown in Figures A.3-25 to A.3-29. Three of these exceedances are located upgradient of the FEMP (Monitoring Wells 2056, 2121, and 2122). Two of the exceedances are located downgradient of the southern portion of the FEMP (Monitoring Wells 3070 and 2733).

The lead exceedances recorded at the upgradient locations (Monitoring Wells 2056, 2121, and 2122) are not attributable to the FEMP. The exceedances recorded in the downgradient locations 3070

and 2733 could be attributed to the FEMP and should be monitored. Both locations are currently being monitored as part of the RCRA Property Boundary Monitoring network.

Manganese

The FRL for manganese is 0.9 mg/L and is based on background which ranges from 0.0043 mg/L to 0.904 mg/L. FRL exceedances of manganese have been recorded at three locations outside of the restoration footprint (Monitoring Wells 2424, 2436, and 2733), Figure A.3-30. The FRL exceedances range from 0.931 mg/L to 1.13 mg/L. Figures A.3-31 through A.3-33 show the concentrations versus sample date for Wells 2733, 2424, and 2436 respectively.

The graph for Well 2733 (Figure A.3-31) indicates that the FRL exceedance for manganese was a one time occurrence. The graphs for Monitoring Wells 2424 and 2436 (Figures A.3-32 and A.3-33 respectively) indicate that the FRL exceedance for manganese was not a one time event and given their location the exceedances could be attributed to the FEMP. These two locations outside of the aquifer restoration footprint should be monitored for manganese. Both locations (Monitoring Wells 2424 and 2436) are currently being monitored as part of the RCRA Property Boundary Monitoring network.

Mercury

The FRL for mercury is 0.002 mg/L, which is an MCL established by the Safe Drinking Water Act. One location (Monitoring Well 2091) had a one time FRL exceedance which was outside of the restoration footprint (Figure A.3-34). Figure A.3-35 shows the concentration versus sample date for this location. As the graph illustrates, six sampling events subsequent to the one detection indicate that mercury levels at this location are below the FRL. It is proposed that no additional monitoring for mercury outside of the aquifer restoration footprint be conducted, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program.

Nickel

The FRL for nickel is 0.1 mg/L, which is an MCL established by the Safe Drinking Water Act. FRL exceedances for nickel have been recorded at two Monitoring wells (3092 and 2067) outside of the restoration footprint (Figure A.3-36). The FRL exceedances range from 0.218 mg/L to 0.26 mg/L. Figures A.3-37 and A.3-38 show the concentration versus sample date for the two different locations. These figures indicate that the FRL exceedance for nickel at both locations was a one time occurrence.

It is proposed that no additional monitoring for nickel outside of the aquifer restoration footprint be conducted, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program.

Nitrate

The FRL for nitrate is 11 mg/L and is based on background which ranges from 0.014 mg/L to 24.9 mg/L (DOE 1994). FRL exceedances of nitrate have been recorded at six locations outside of the restoration footprint, Figure A.3-39. The FRL exceedances range from 11.1 mg/L to 24.9 mg/L; within the range used to define background. Five of the six locations with FRL exceedances (Monitoring Wells 2036, 2123, 2098, 3099, and 2026) were used to define background in 1994. Concentration versus sample date plots for Monitoring Wells 2036, 2123, 2098, 3099, and 2026 are provided in Figures A.3-40 through A.3-44 respectively.

Well 2091 is the only location with an FRL exceedance outside of the restoration footprint that was not also used to define background in 1994. Figure A.3-45 is a concentration versus sample date plot for Well 2091. This well is located east of the FEMP near State Route 128 in an agricultural area. It is believed that this exceedance is due to fertilizer or other agricultural activities and is not FEMP related.

It is proposed that no additional monitoring for nitrate outside of the aquifer restoration footprint be conducted, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program. The nitrate exceedances located outside of the aquifer restoration footprint are judged to either be within the range of values used to define background, or not attributable to former production at the FEMP due to their location relative to known agricultural areas.

Silver

The FRL for silver is 0.005 mg/L, which is a proposed MCL under the Safe Drinking Water Act. One location outside of the restoration footprint, Monitoring Well 2036 which is located upgradient of the FEMP, had a one time FRL exceedance, Figure A.3-46. Figure A.3-47 shows the concentration versus sample date for this location. It is proposed that no additional monitoring for silver outside of the aquifer restoration footprint be conducted, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program.

Trichloroethene

The FRL for Trichloroethene is 0.005 mg/L, which is an MCL established by the Safe Drinking Water Act. One location (Monitoring Well 3051) had a one time FRL exceedance which was outside of the restoration footprint (Figure A.3-48). Figure A.3-49 shows the concentration versus sample date for this location.

Well 3051 was plugged and abandoned and replaced by Monitoring Well 31217. Figure A.3-50 is the concentration versus sample date graph for trichloroethene data collected at Well 31217. The data indicates that no exceedances of trichloroethene have been detected in this well. It is proposed that no additional monitoring for trichloroethene outside of the aquifer restoration footprint be required, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program.

Thorium-228 and Thorium-232

Both thorium-228 and thorium-232 have been detected outside of the restoration footprint at concentrations above their FRL (Figure A.3-51). The FRL for thorium-228 and thorium 232 is 4 pCi/L and 1.2 pCi/L, respectively. These exceedances occurred at only one location (Monitoring Well 2092) north of the Administrative Boundary for aquifer restoration. Figures A.3-52 and A.3-53 show the concentration versus sample date for thorium-228 and thorium-232, respectively. These figures indicate that the detections were one time occurrences which took place on 04/24/90. Subsequent sampling events indicate that the concentrations are below the FRL. It is proposed that no additional monitoring for thorium-228 or thorium-232 outside of the aquifer restoration footprint be conducted, above and beyond what is already being conducted as part of the RCRA Property Boundary Monitoring Program.

Zinc

The FRL for zinc is 0.021 mg/L and is based on background which ranges from 0.0087 mg/L to 0.021 mg/L (DOE 1994). FRL exceedances of zinc have been recorded at 12 locations outside of the restoration footprint, Figure A.3-54. The FRL exceedances range from 0.0238 mg/L to 0.124 mg/L.

Figures A.3-55 through A.3-66 show the concentration versus sample data for the twelve locations. FRL exceedances for zinc at Monitoring Wells 2426, 2431, 3733, and 2432 (Figures A.3-55

through A.3-58 respectively) were one time occurrences. The last two or more sampling events at each location indicate that concentrations are below the FRL. It is proposed that no additional monitoring for zinc be conducted at these four locations.

FRL exceedances at Monitoring Wells 2051, 3431, 3066, and 2733, were not one time occurrences, but the last two or more sampling events at each well indicated that no FRL exceedance was present (Figures A.3-59 through A.3-62). It is proposed that no additional monitoring for zinc be conducted at these four locations.

FRL exceedances at Monitoring Wells 2066, 2424, 3091, and 3051, were not one time occurrences Figures A.3-63 through A.3-66 respectively. Monitoring Well 2066 is located upgradient of the FEMP former Production Area and the Waste Storage Area. Therefore, zinc exceedances at this location are not attributable to the FEMP. It is proposed that no additional monitoring for zinc be conducted at Monitoring Well 2066. As mentioned earlier, Monitoring Well 3051 has been plugged and abandoned and replaced with Monitoring Well 31217. It is proposed that groundwater monitoring for zinc be conducted at Monitoring Wells 2424, 3091, and 31217. All three of these wells are currently being monitored as part of the RCRA Property Boundary Monitoring Program.

A.4 Conclusions

Of the 50 FRL constituents listed in the OU5 ROD, 14 have had at least 1 FRL exceedance outside the restoration footprint and north of the Administrative Boundary. The fourteen constituents are manganese, fluoride, nitrate, cadmium, lead, zinc, antimony, arsenic, mercury, nickel, trichloroethene, silver, thorium-228, and thorium-232. Of these fourteen constituents;

- Mercury, nickel, trichloroethene, silver, thorium-228, and thorium-232 can be dismissed from further monitoring outside the restoration footprint because the FRL exceedances were a one time occurrence with subsequent data indicating concentrations below the FRL.
- Fluoride can be dismissed from further monitoring outside the restoration footprint because the exceedances were identified using an FRL based on a background value of 0.89 mg/L. The MCL for fluoride is 4 mg/L. EPA, OEPA and DOE have agreed to change the groundwater FRL value for fluoride from 0.89 mg/L to 4 mg/L (see Appendix C). When fluoride detects are compared against the MCL, no FRL exceedances result.

- Nitrate can be dismissed from further monitoring outside the restoration footprint because the FRL exceedances are either within the range used to define background and/or not attributable to the FEMP.

- Arsenic can be dismissed from further monitoring outside the restoration footprint because the FRL exceedances are not attributable to the FEMP.

- Many of the lead exceedances can be dismissed from further monitoring outside of the restoration footprint because they were identified using an FRL based on a background value of 0.002 mg/L. The SDWA action level for lead is 0.015 mg/L. The SDWA action level has been selected to guide the restoration (see Appendix C). It is proposed that the decision to monitor and remediate outside of the restoration footprint (as well as to monitor the restoration within the footprint) for lead be based on the SDWA action level. Using the SDWA action level does not eliminate all of the FRL exceedances for lead, but it does eliminate a majority of them.

- Exceedances for antimony, manganese, cadmium, zinc and lead, at several locations outside of the aquifer restoration footprint, are not one time occurrences and due to their location relative to the FEMP could be attributable to the FEMP. Therefore they cannot be dismissed from further monitoring at this time.

The RCRA property boundary monitoring program currently monitors the majority of the locations where potentially FEMP related and persistent FRL exceedances are found outside of the aquifer restoration footprint. Only three of the identified exceedance locations are currently not being monitored by the RCRA Property Boundary Program; Monitoring Well 3423 for antimony, Monitoring Well 2436 for manganese, and Monitoring Well 3091 for zinc. It is proposed that quarterly sampling at these locations for the noted FRL constituents be added to the scope of the IEMP. The quarterly sampling will continue for a period of one year at which time data will be evaluated to determine the need for additional actions at these locations.

A.5 References

U.S. Dept. of Energy, 1996a, "Integrated Environmental Monitoring Plan, Draft," Fernald Environmental Management Project, DOE, Fernald Field Office, Cincinnati, OH.

U.S. Dept. of Energy, 1996b, "Record of Decision for Remedial Actions at Operable Unit 5, Final," Fernald Environmental Management Project, DOE, Fernald Field Office, Cincinnati, OH.

U.S. Dept of Energy, 1994. "Characterization of Background Water Quality for Stream and Groundwater, Final," Fernald Environmental Management Project, DOE, Fernald Field Office, Cincinnati, OH.

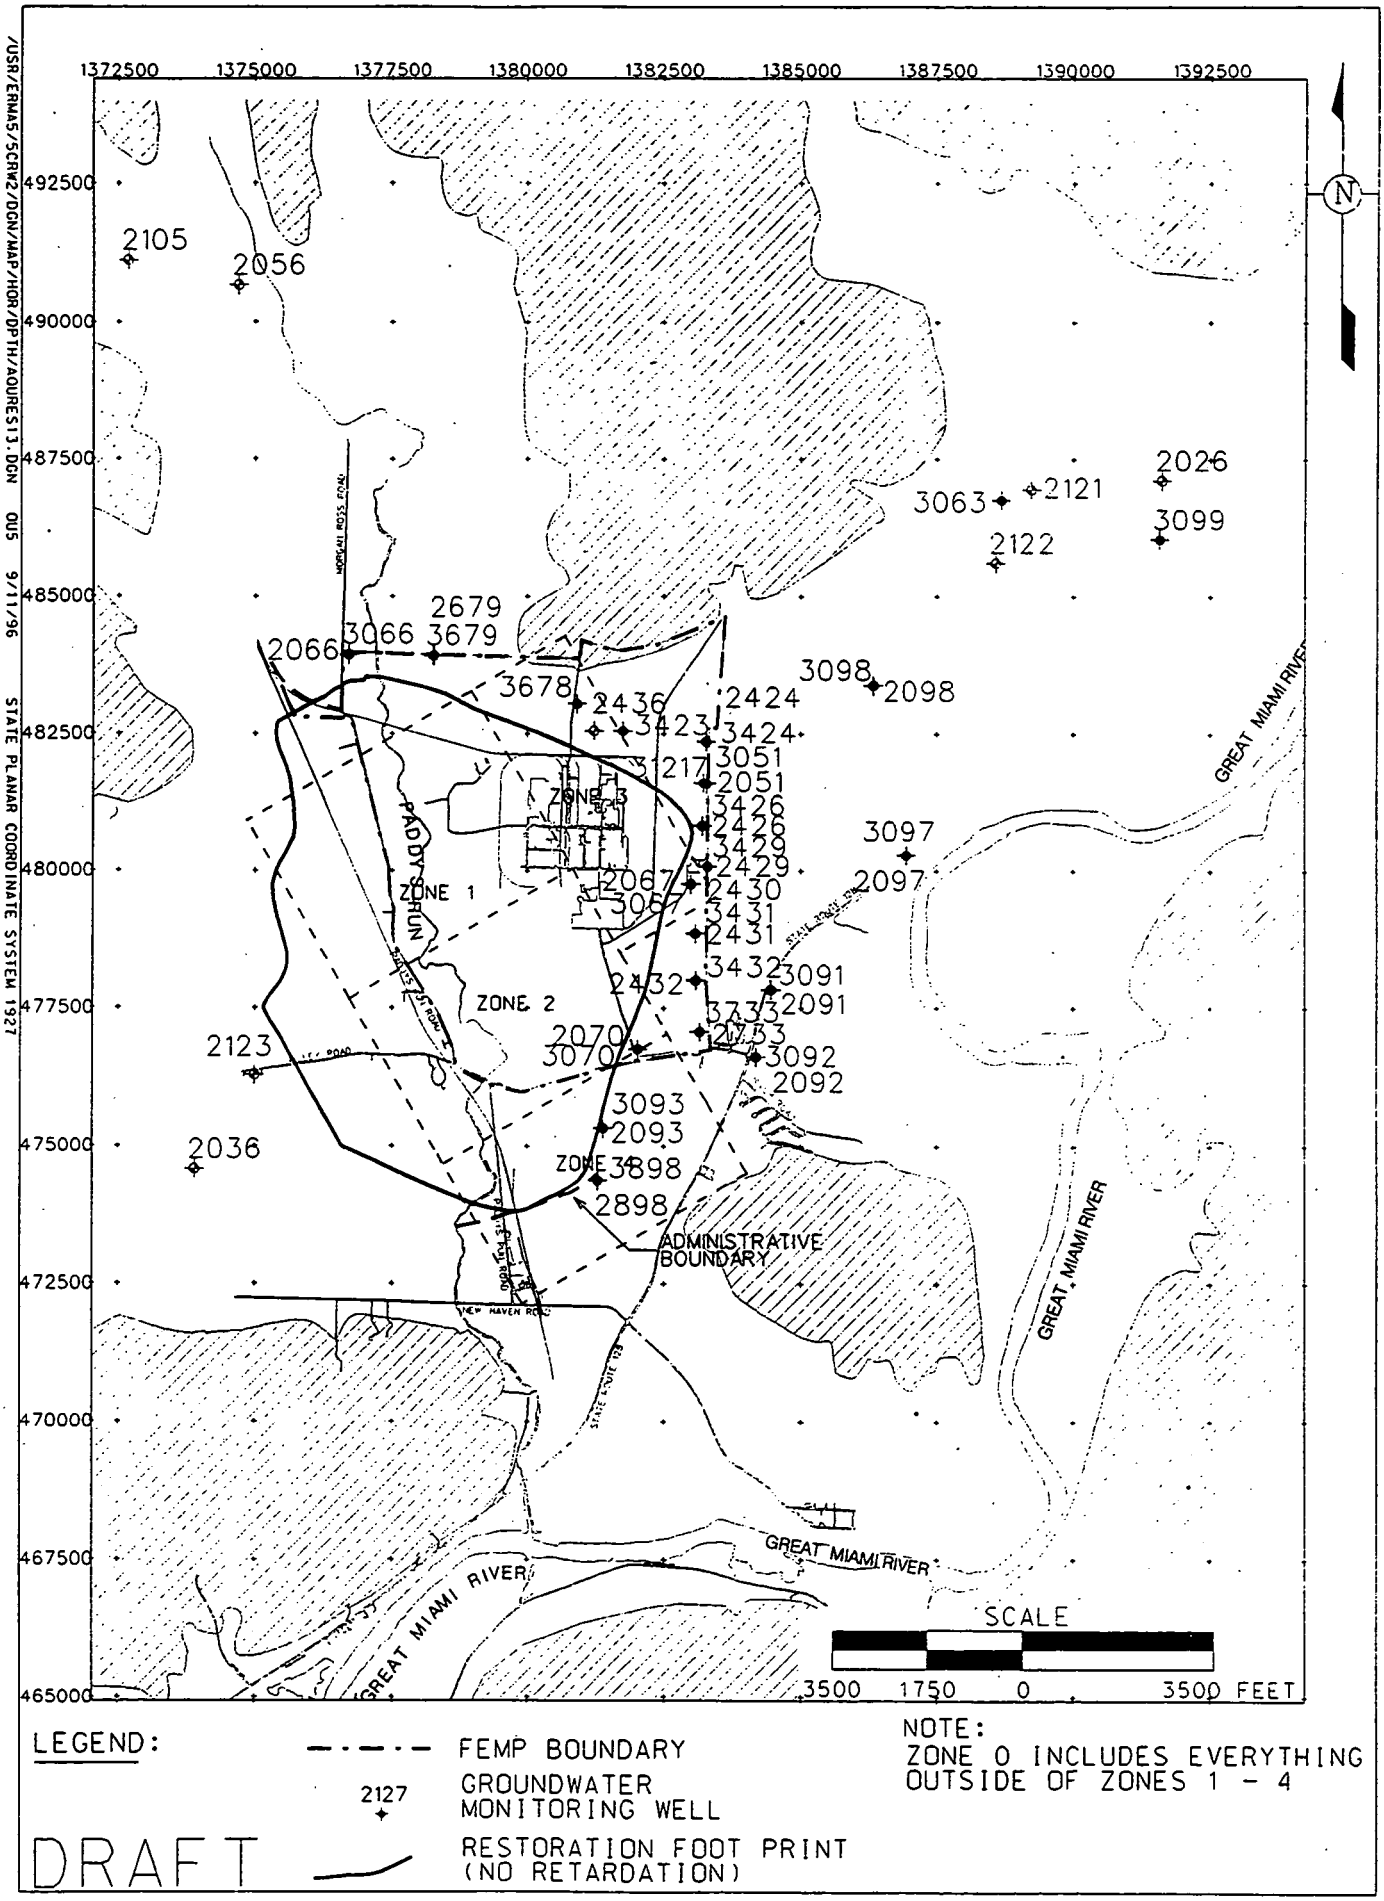

FIGURE A.1-1. MONITORING WELLS WITH FRL EXCEEDENCES LOCATED OUTSIDE THE RESTORATION FOOTPRINT AND NORTH OF THE ADMINISTRATIVE BOUNDARY

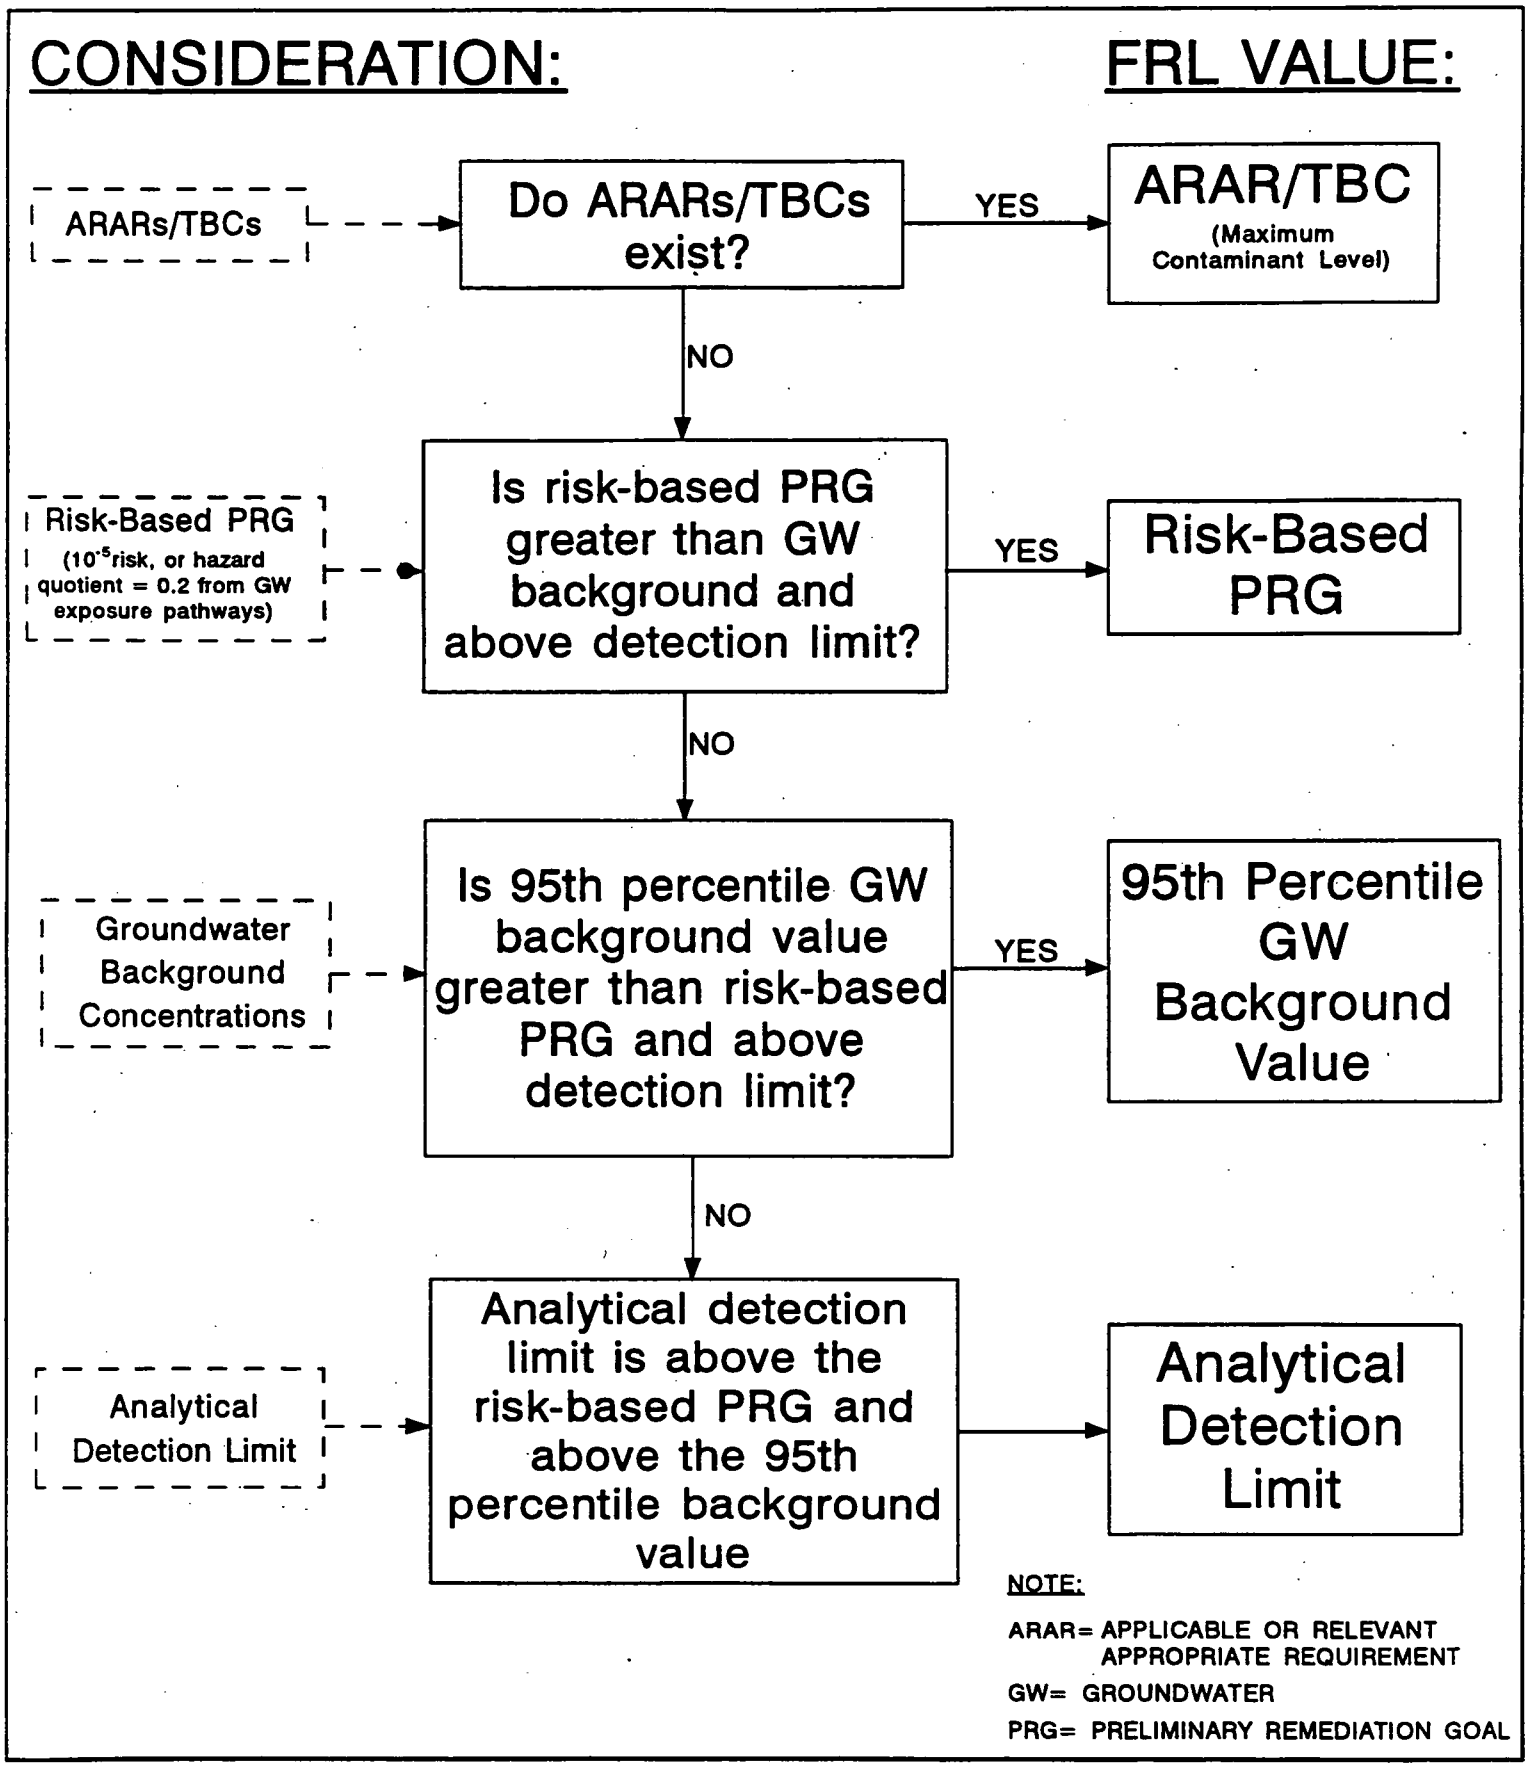

FIGURE A.1-2. PROCESS FOR DEVELOPMENT OF GROUNDWATER FRLs.

(ARAR/10^{-5} Case Contained in the OU5 Proposed Plan and Ultimately Selected in the OU5 ROD [Ref. OU5 FS p. 2-54])

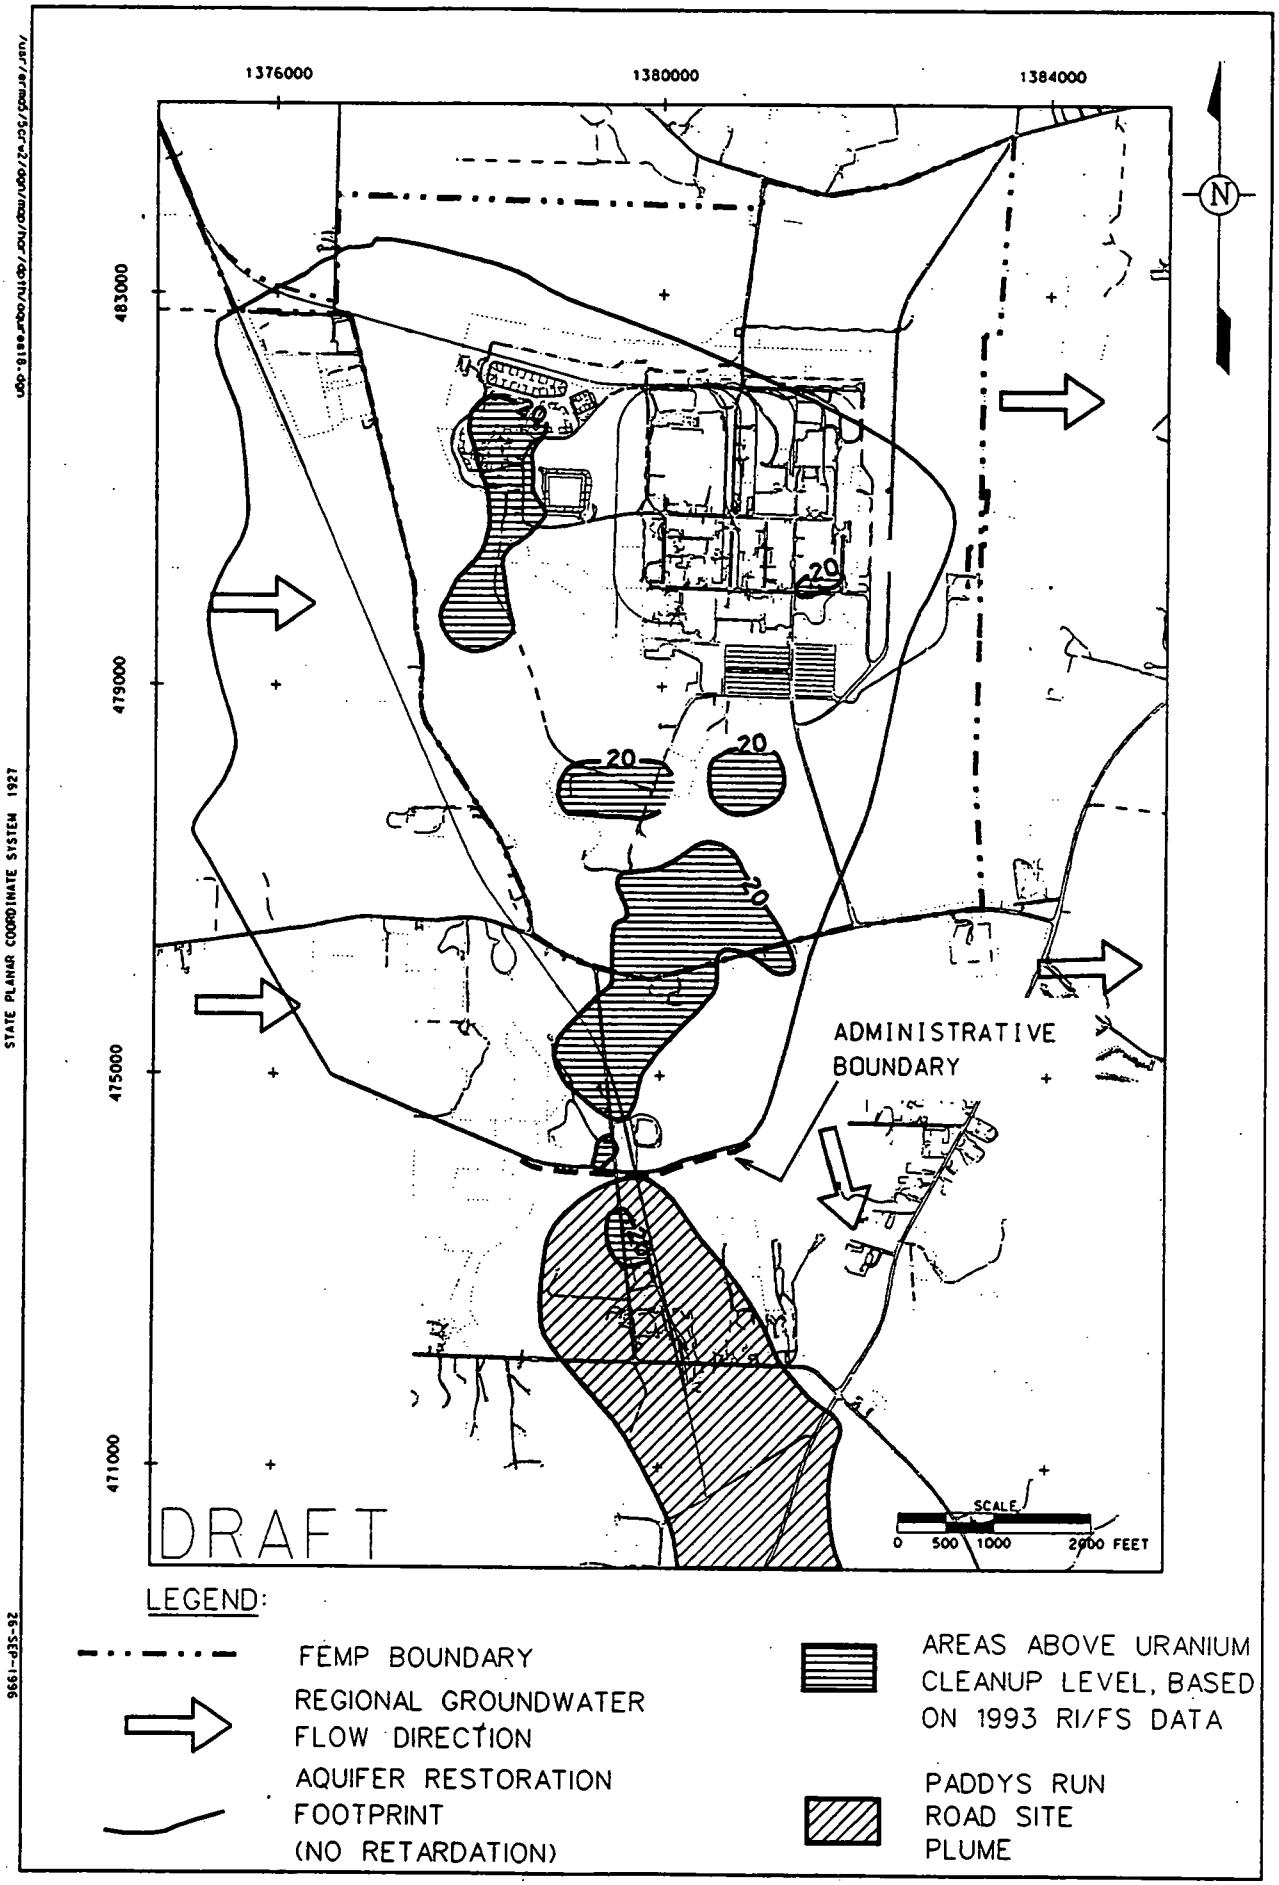

FIGURE A.2-1. AREAS OF THE GREAT MIAMI AQUIFER REQUIRING REMEDIATION AND AQUIFER RESTORATION FOOTPRINT

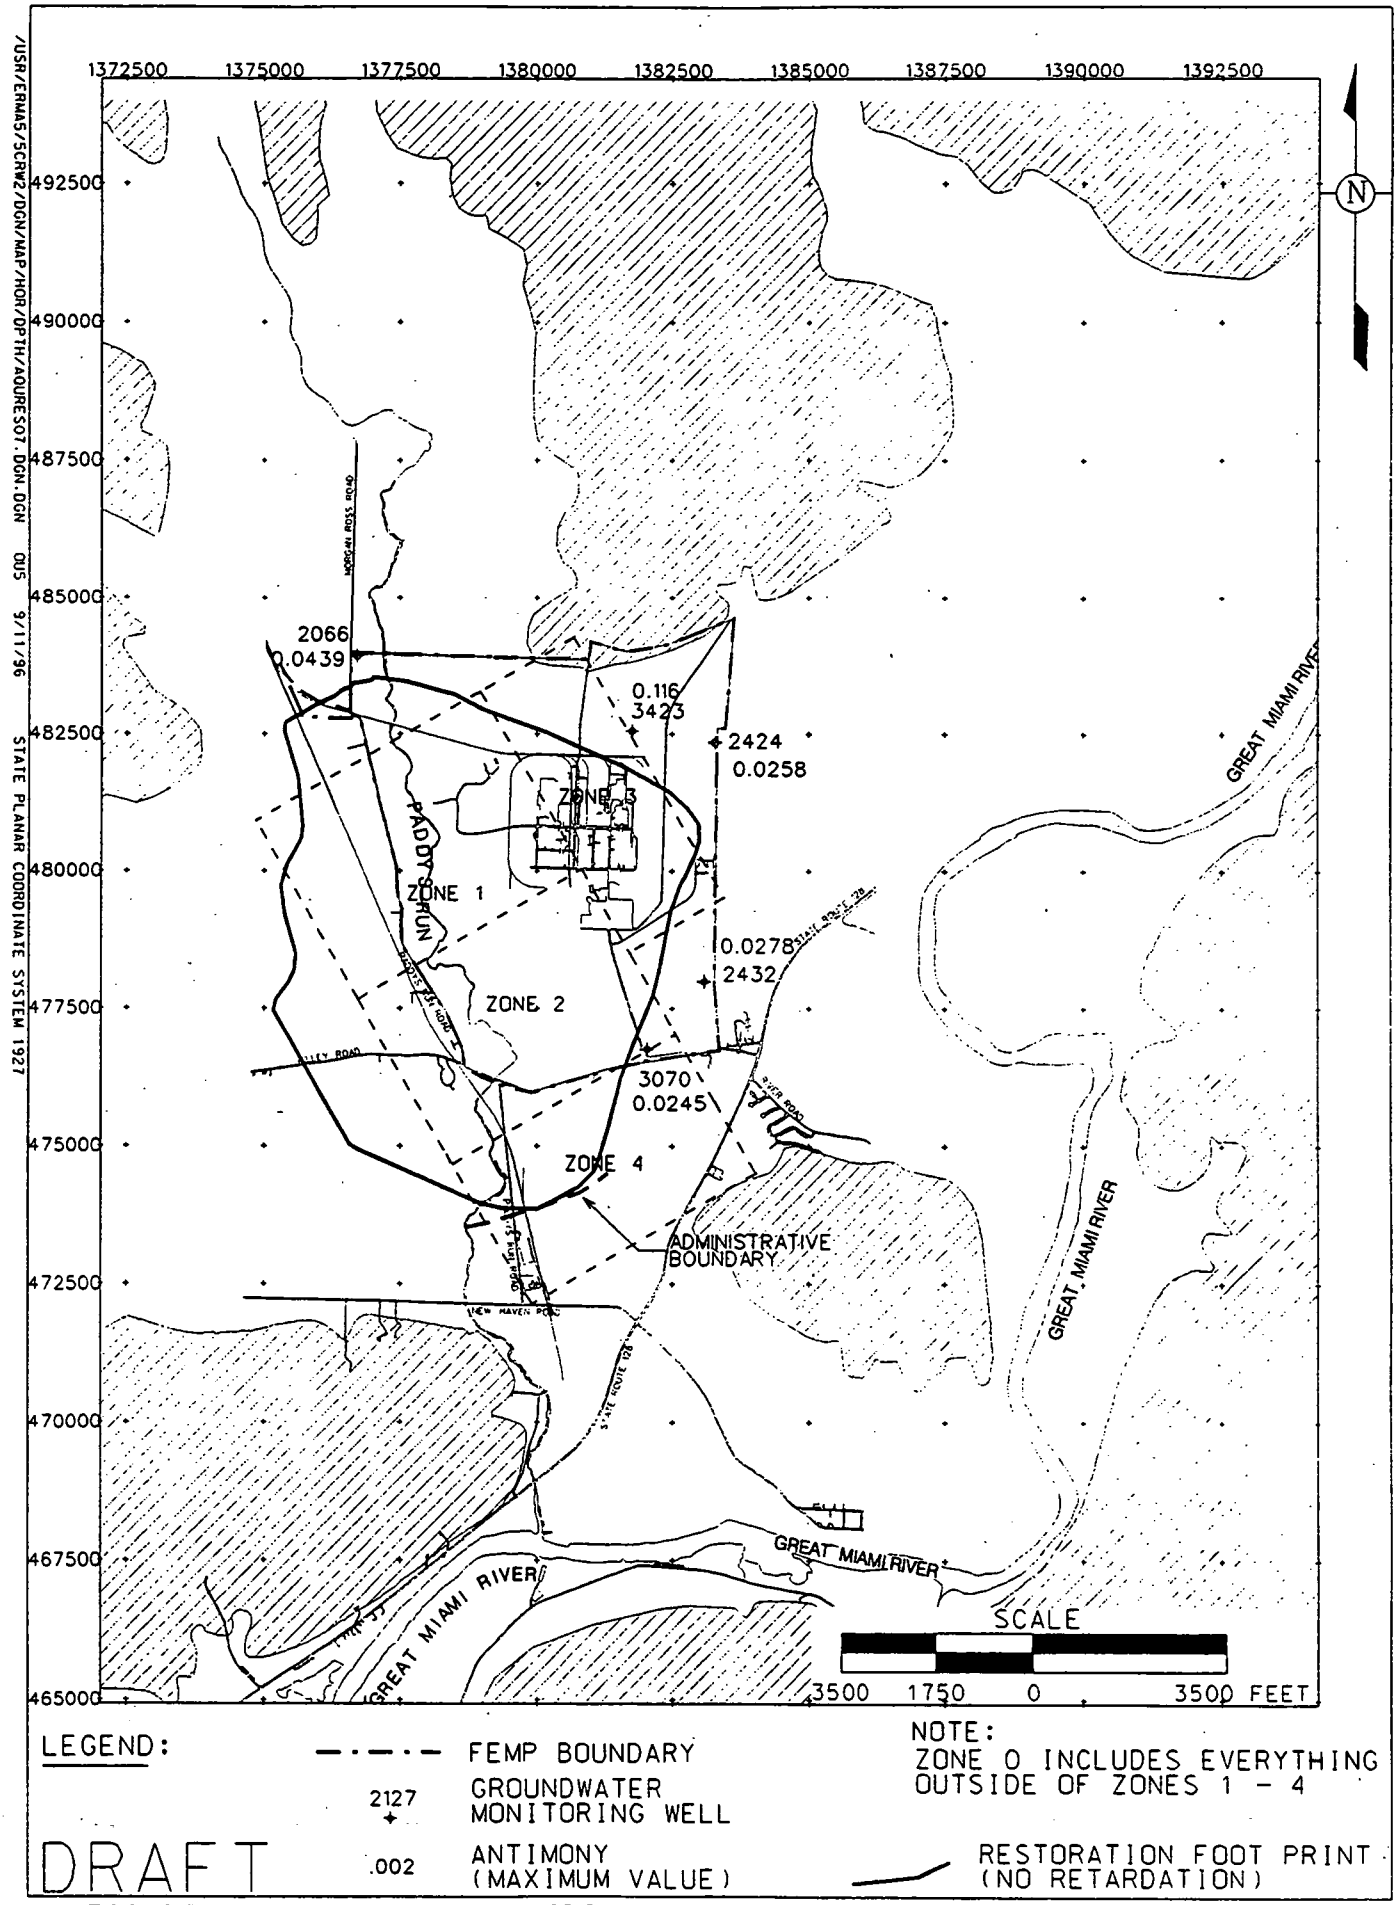

FIGURE A.3-1. FRL EXCEEDENCES FOR ANTIMONY LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

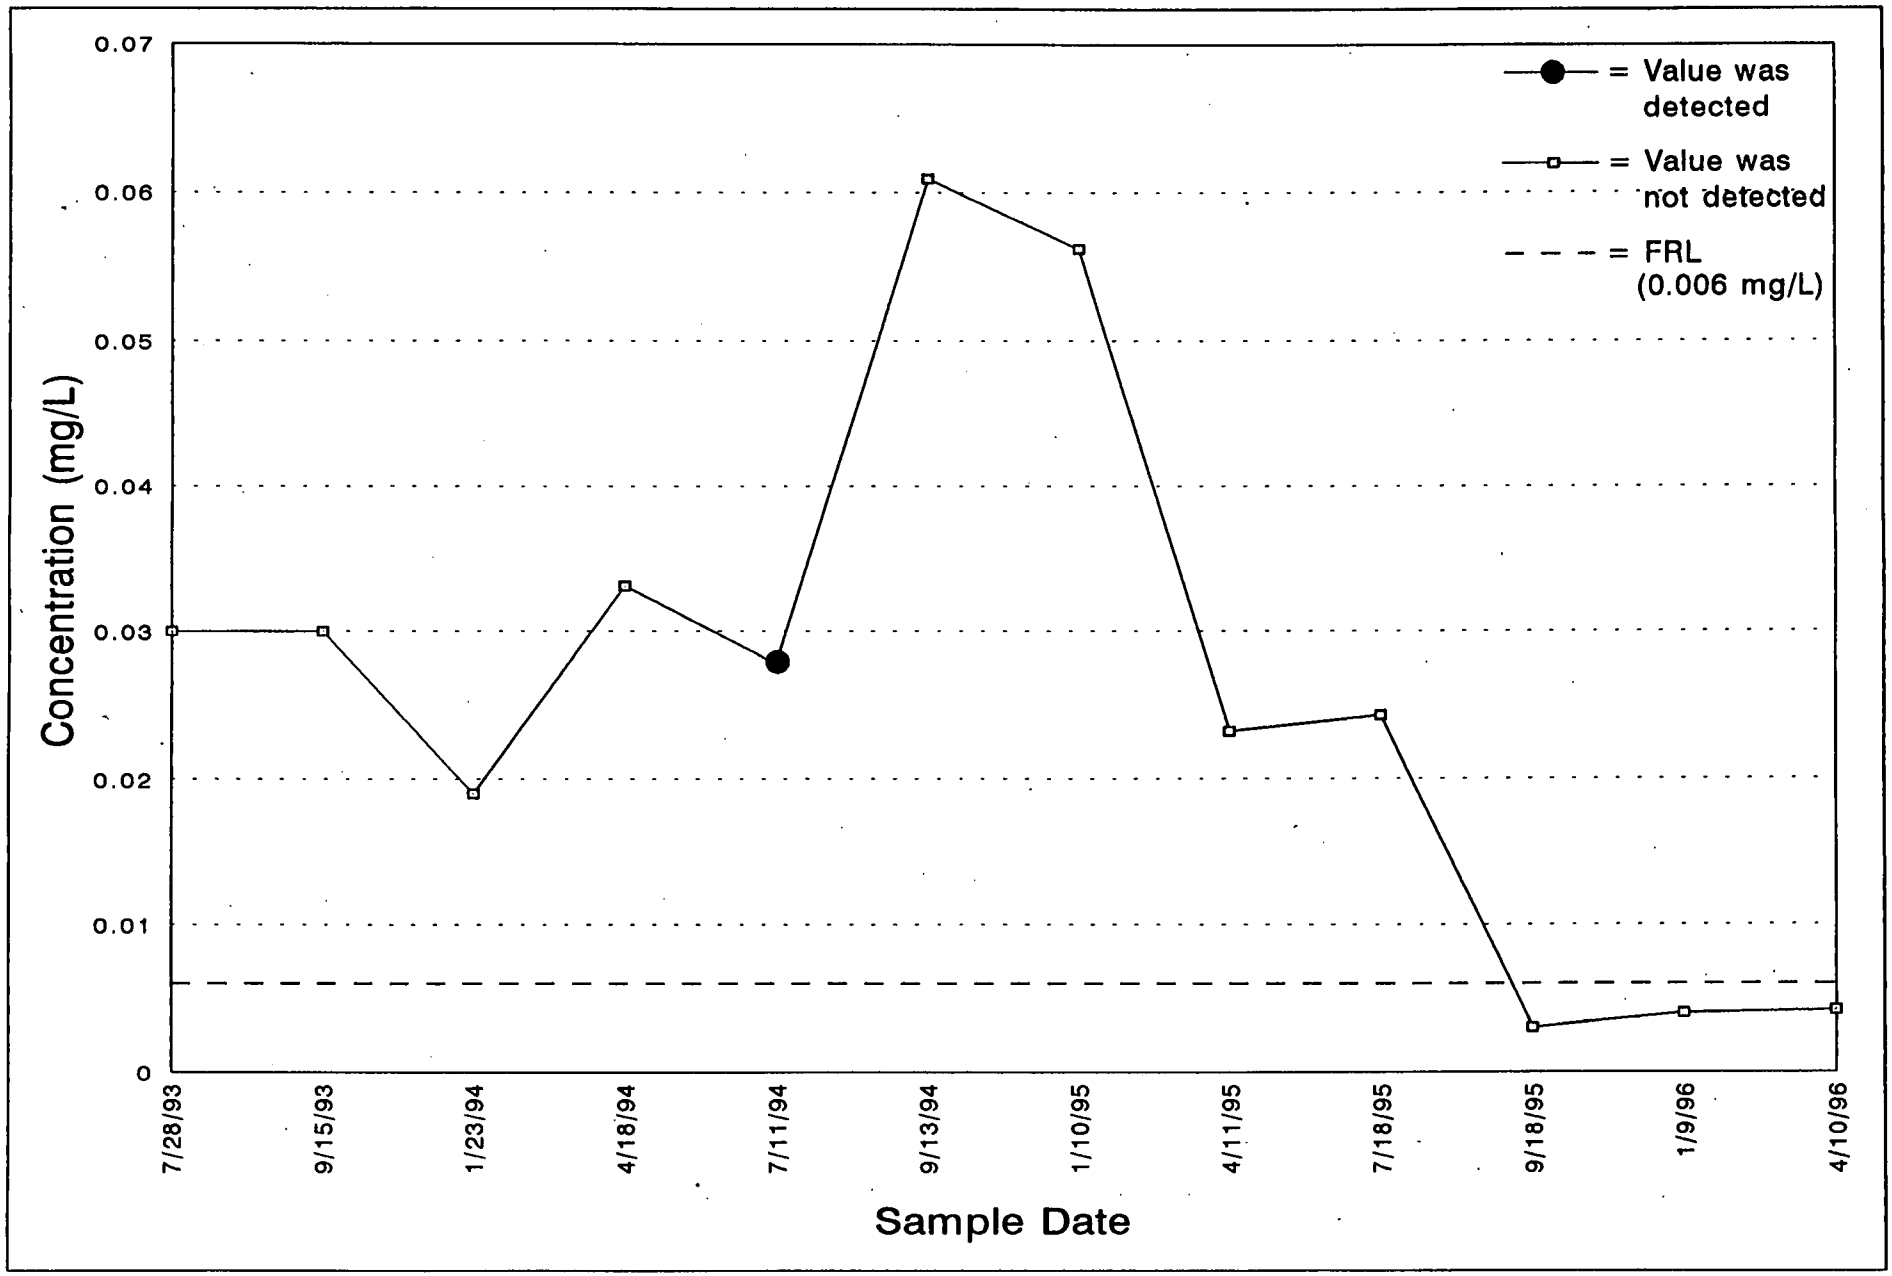

FIGURE A.3-2. ANTIMONY CONCENTRATION VS. TIME, WELL 2432

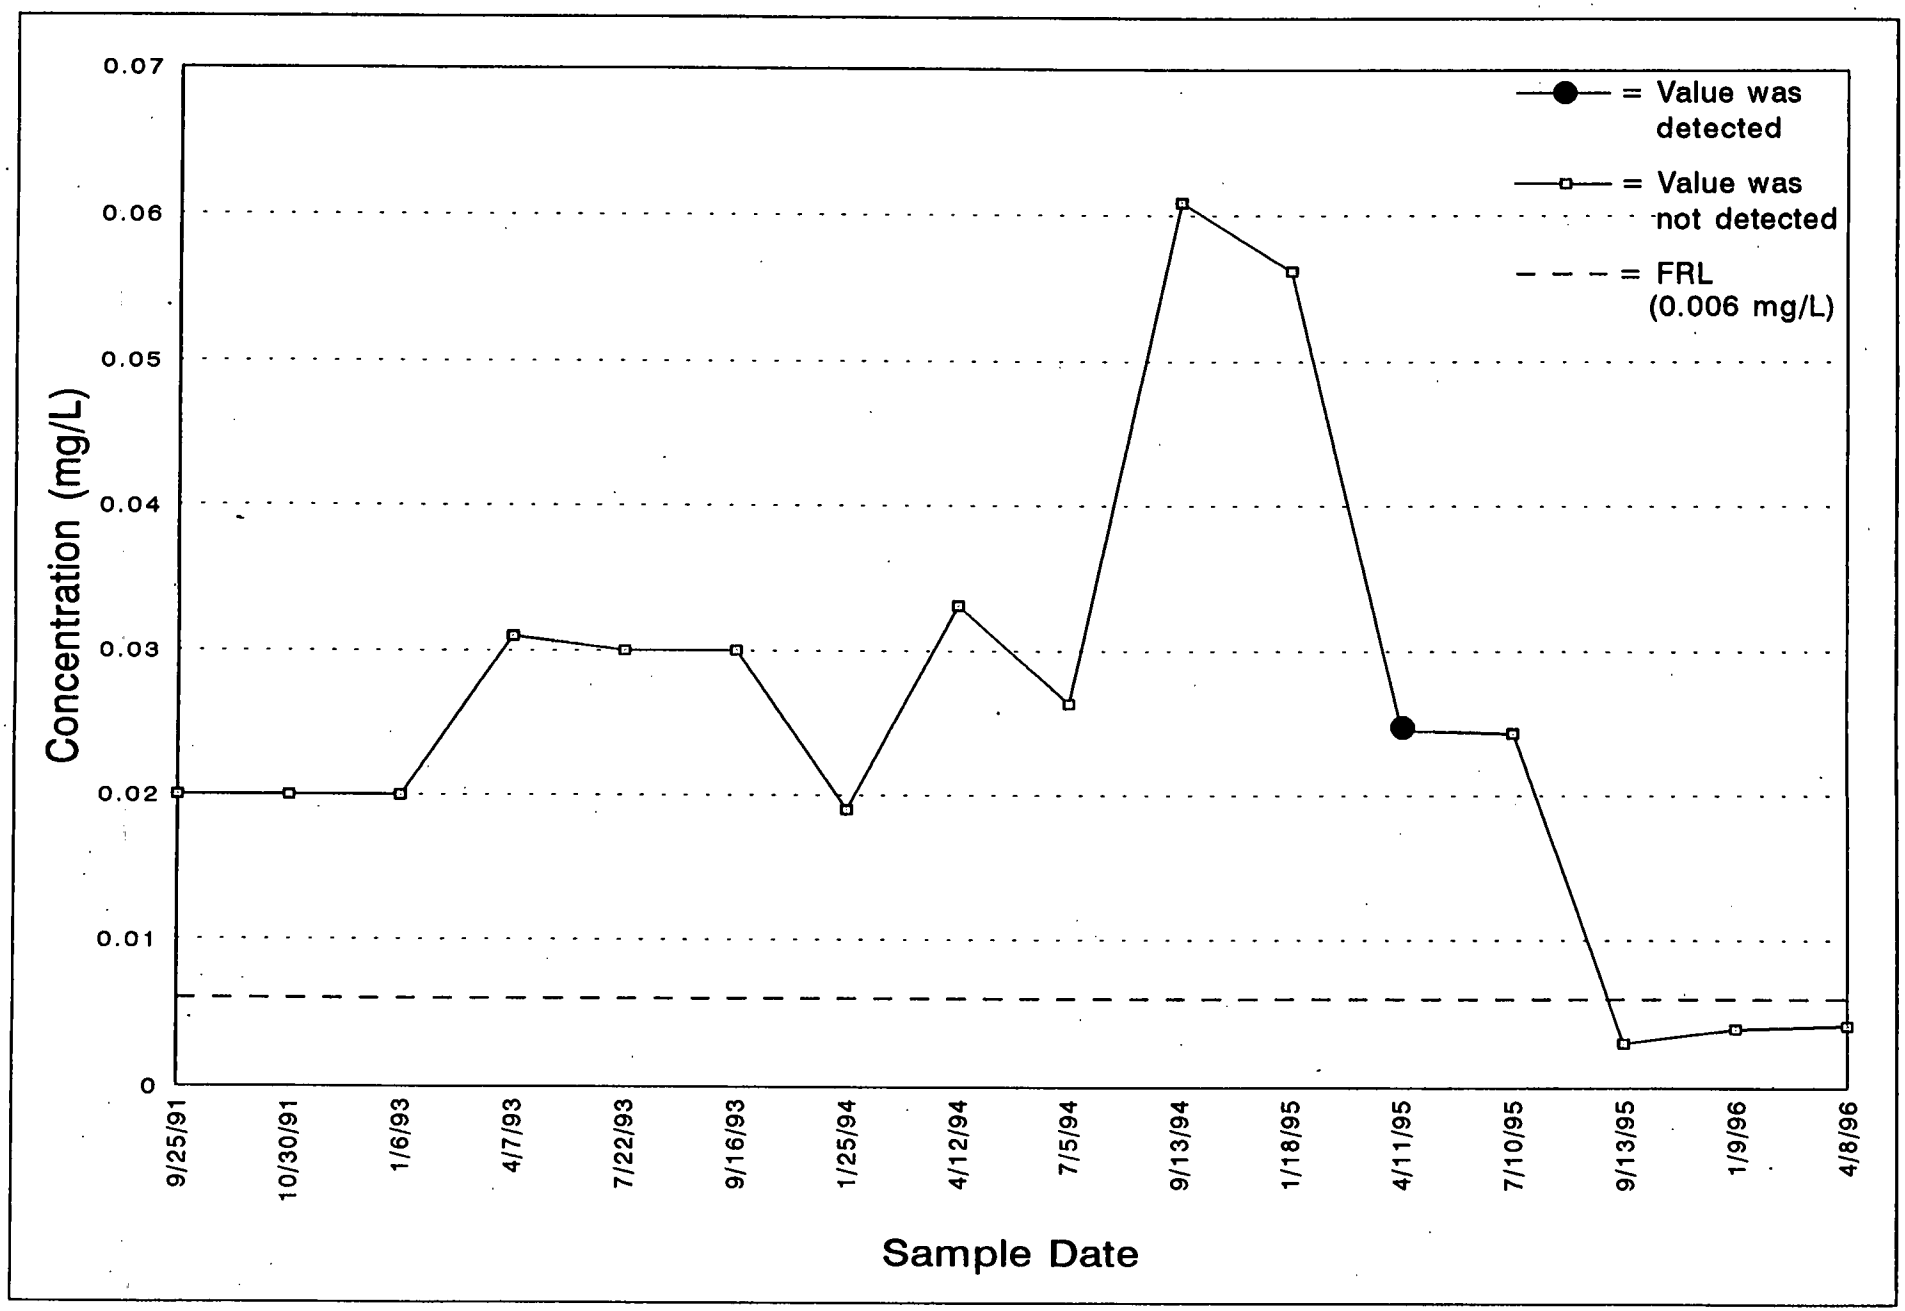

FIGURE A.3-3. ANTIMONY CONCENTRATION VS. TIME, WELL 3070

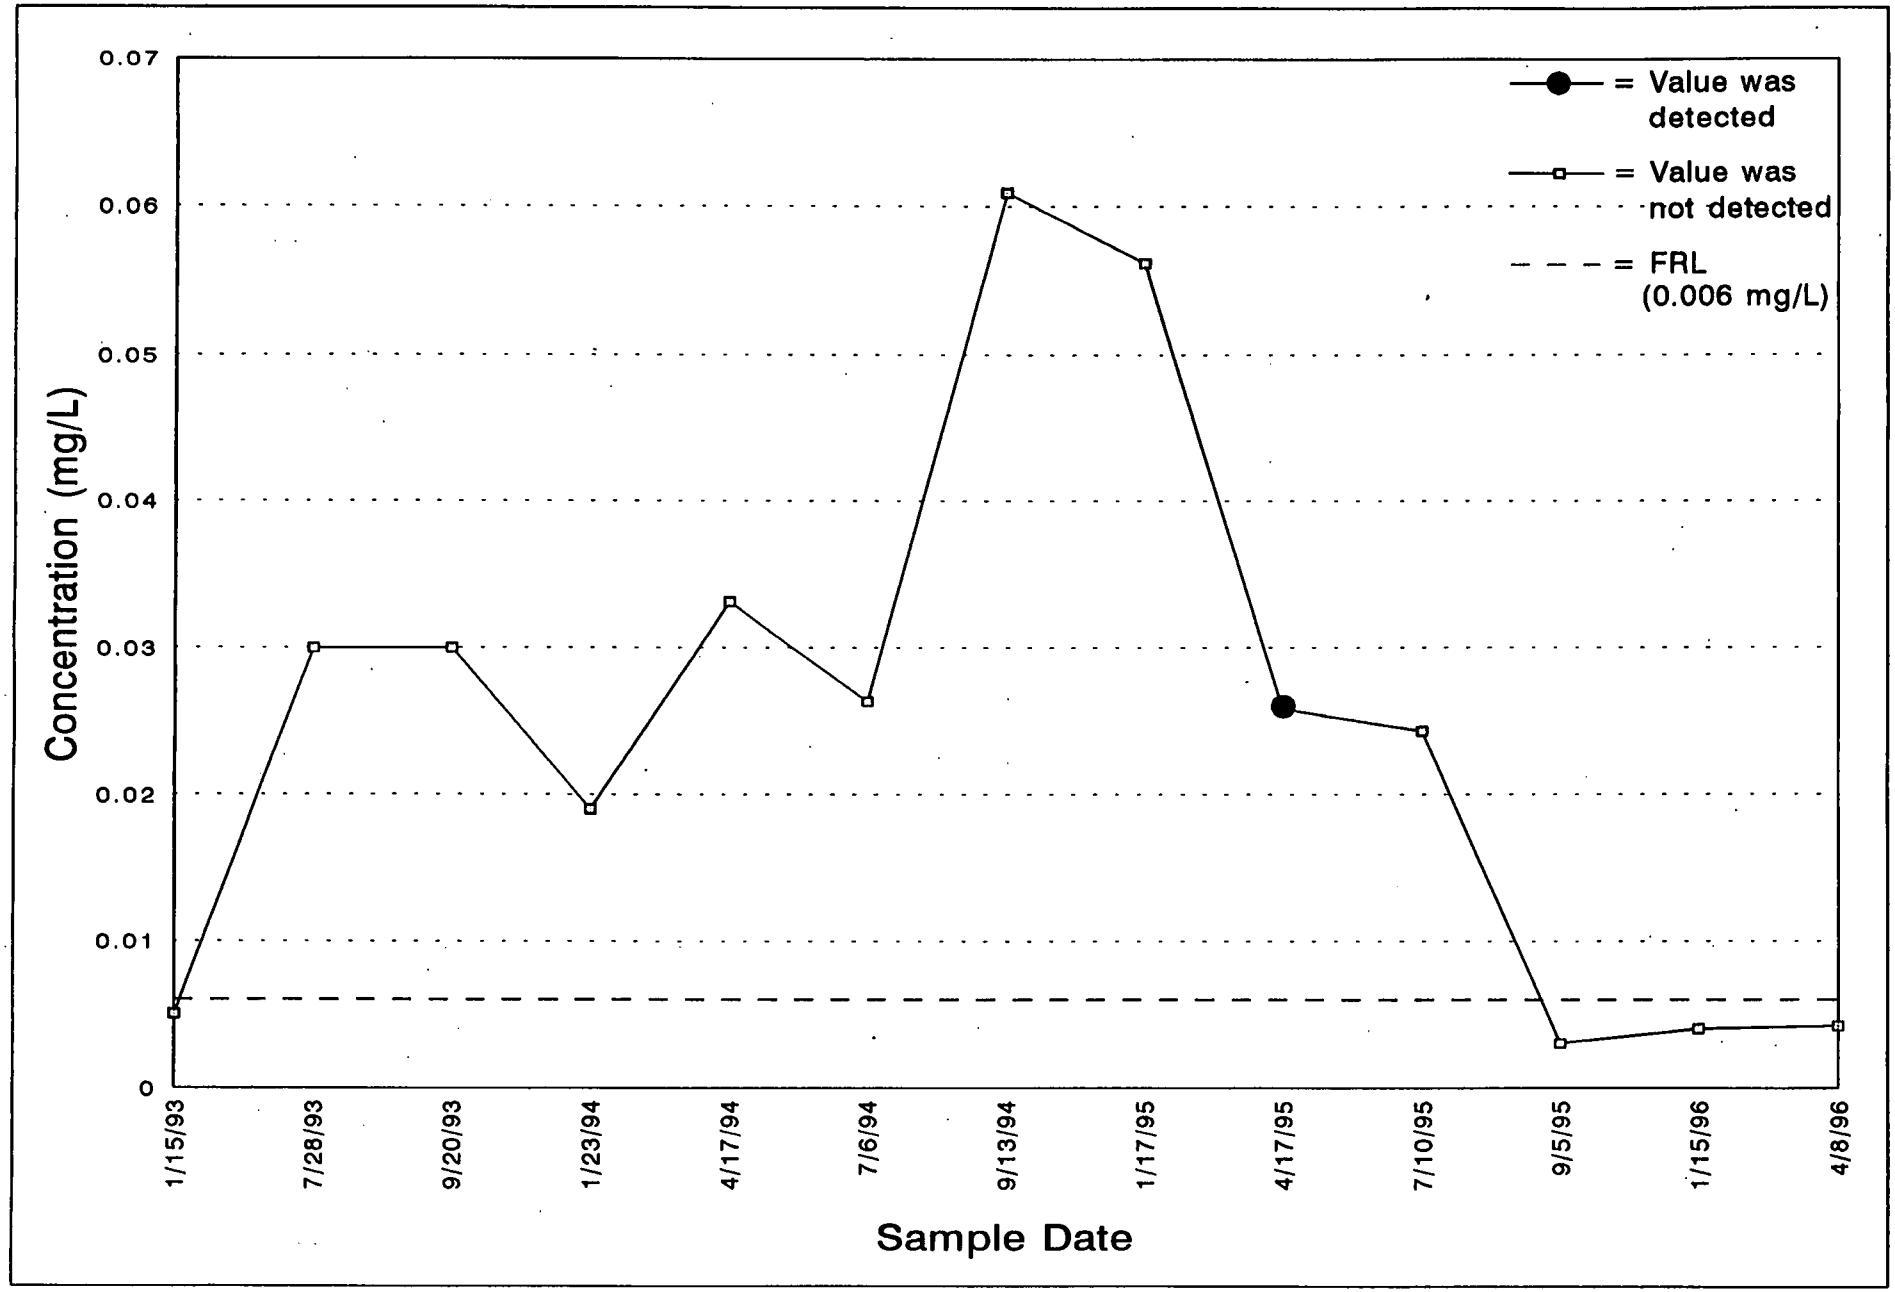

FIGURE A.3-4. ANTIMONY CONCENTRATION VS. TIME, WELL 2424

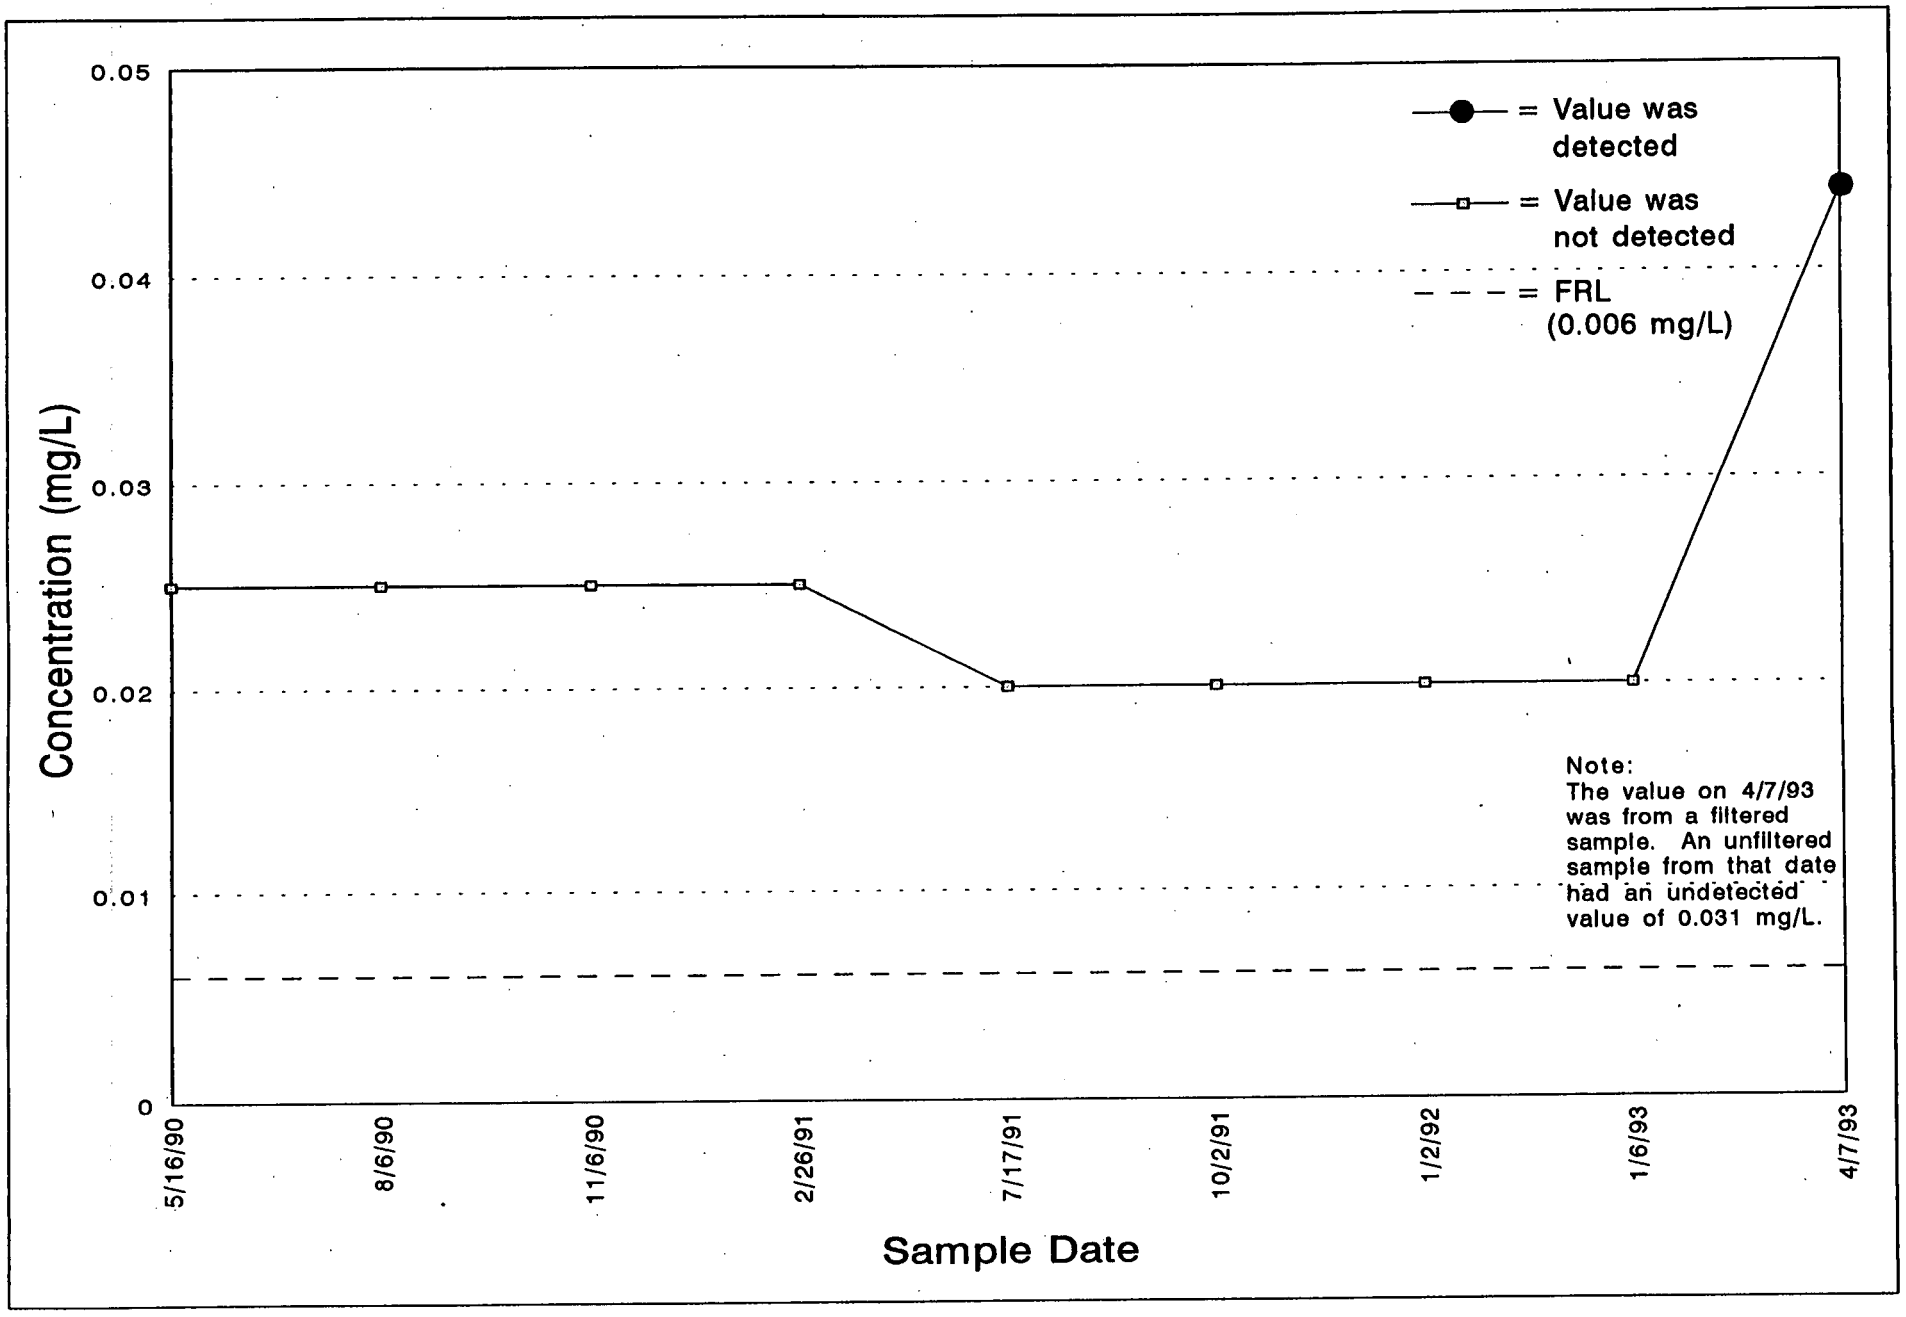

FIGURE A.3-5. ANTIMONY CONCENTRATION VS. TIME, WELL 2066

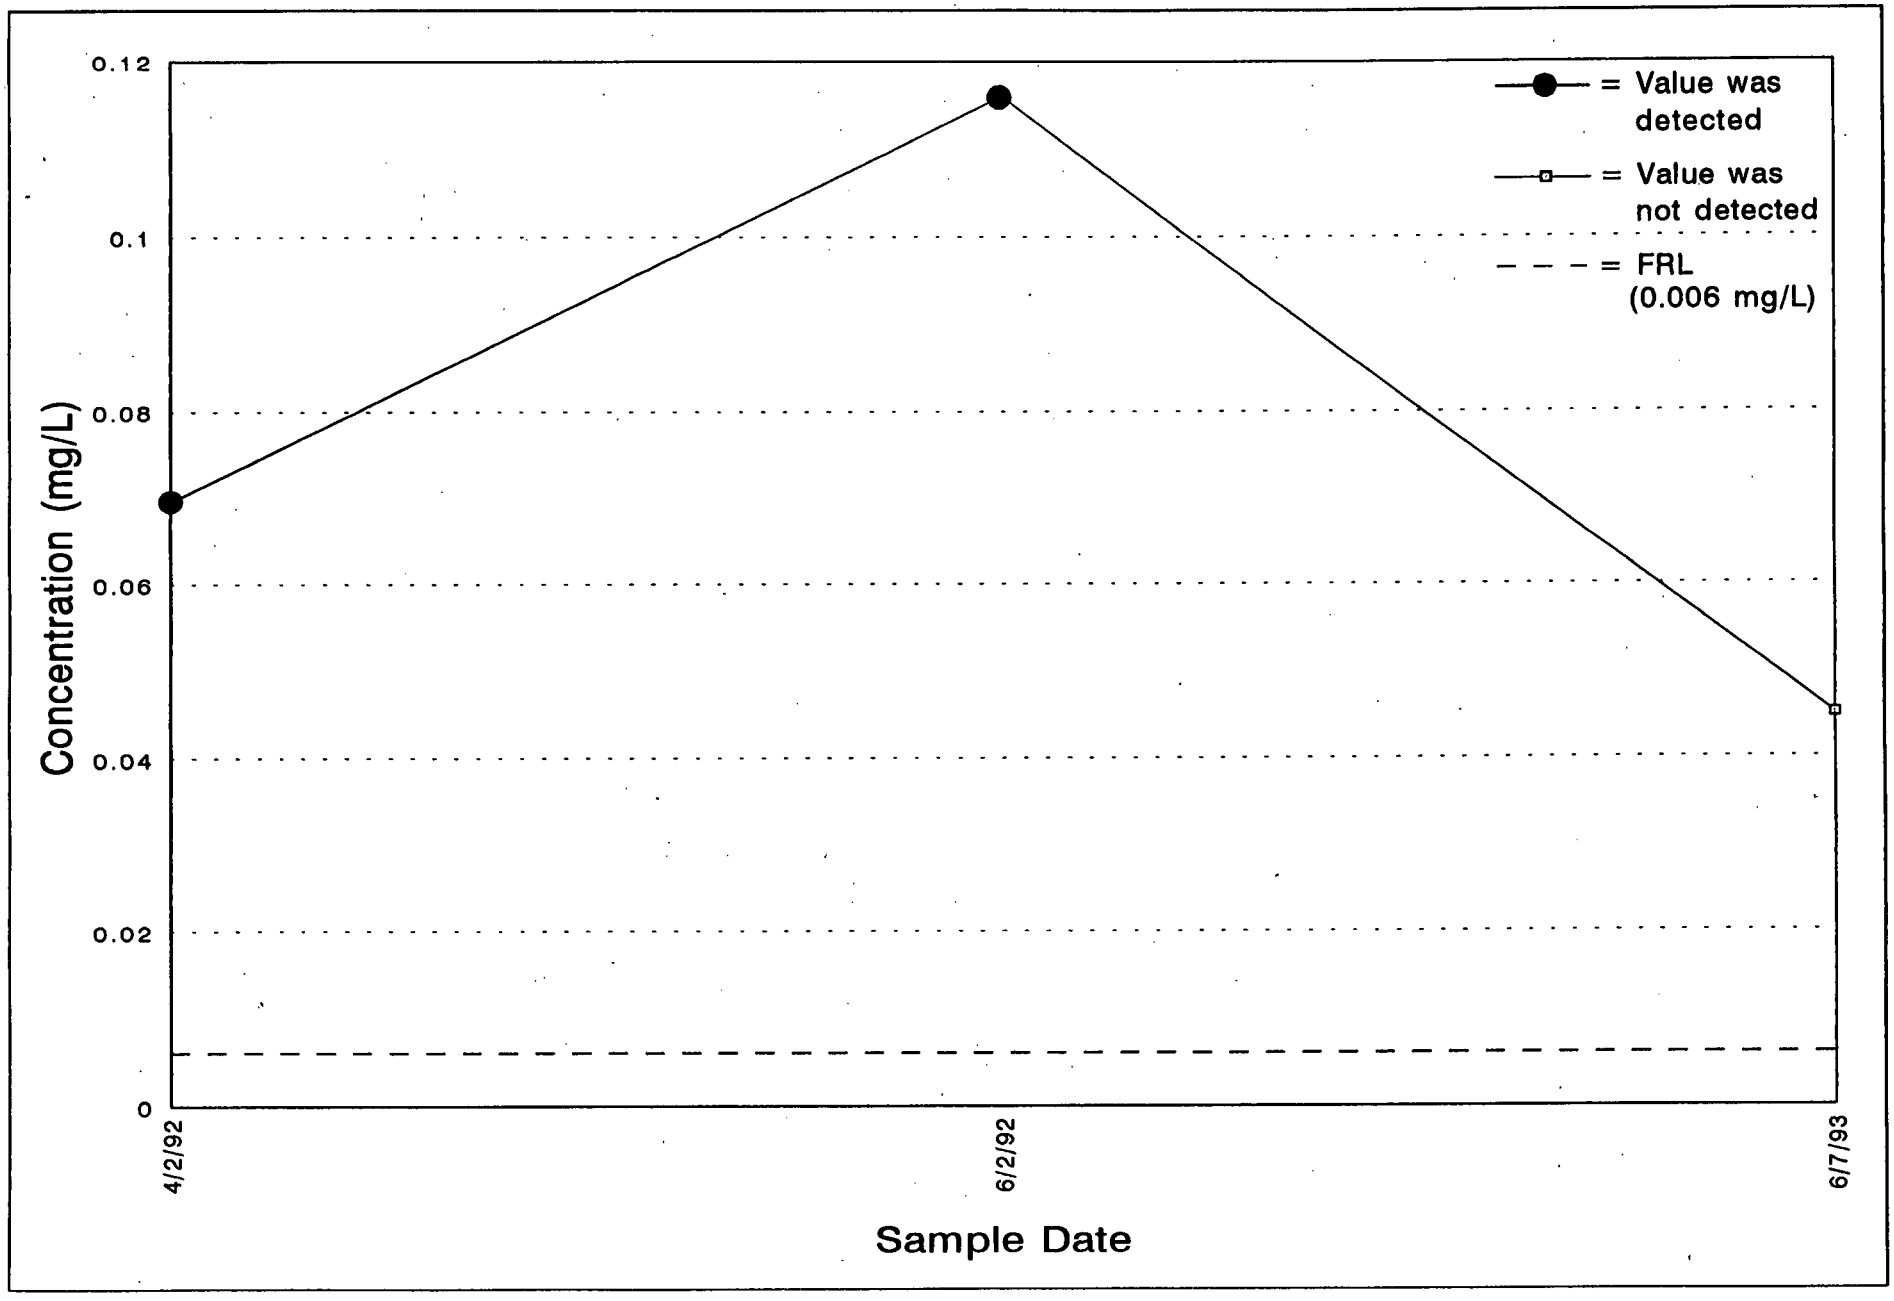

FIGURE A.3-6. ANTIMONY CONCENTRATION VS. TIME, WELL 3423

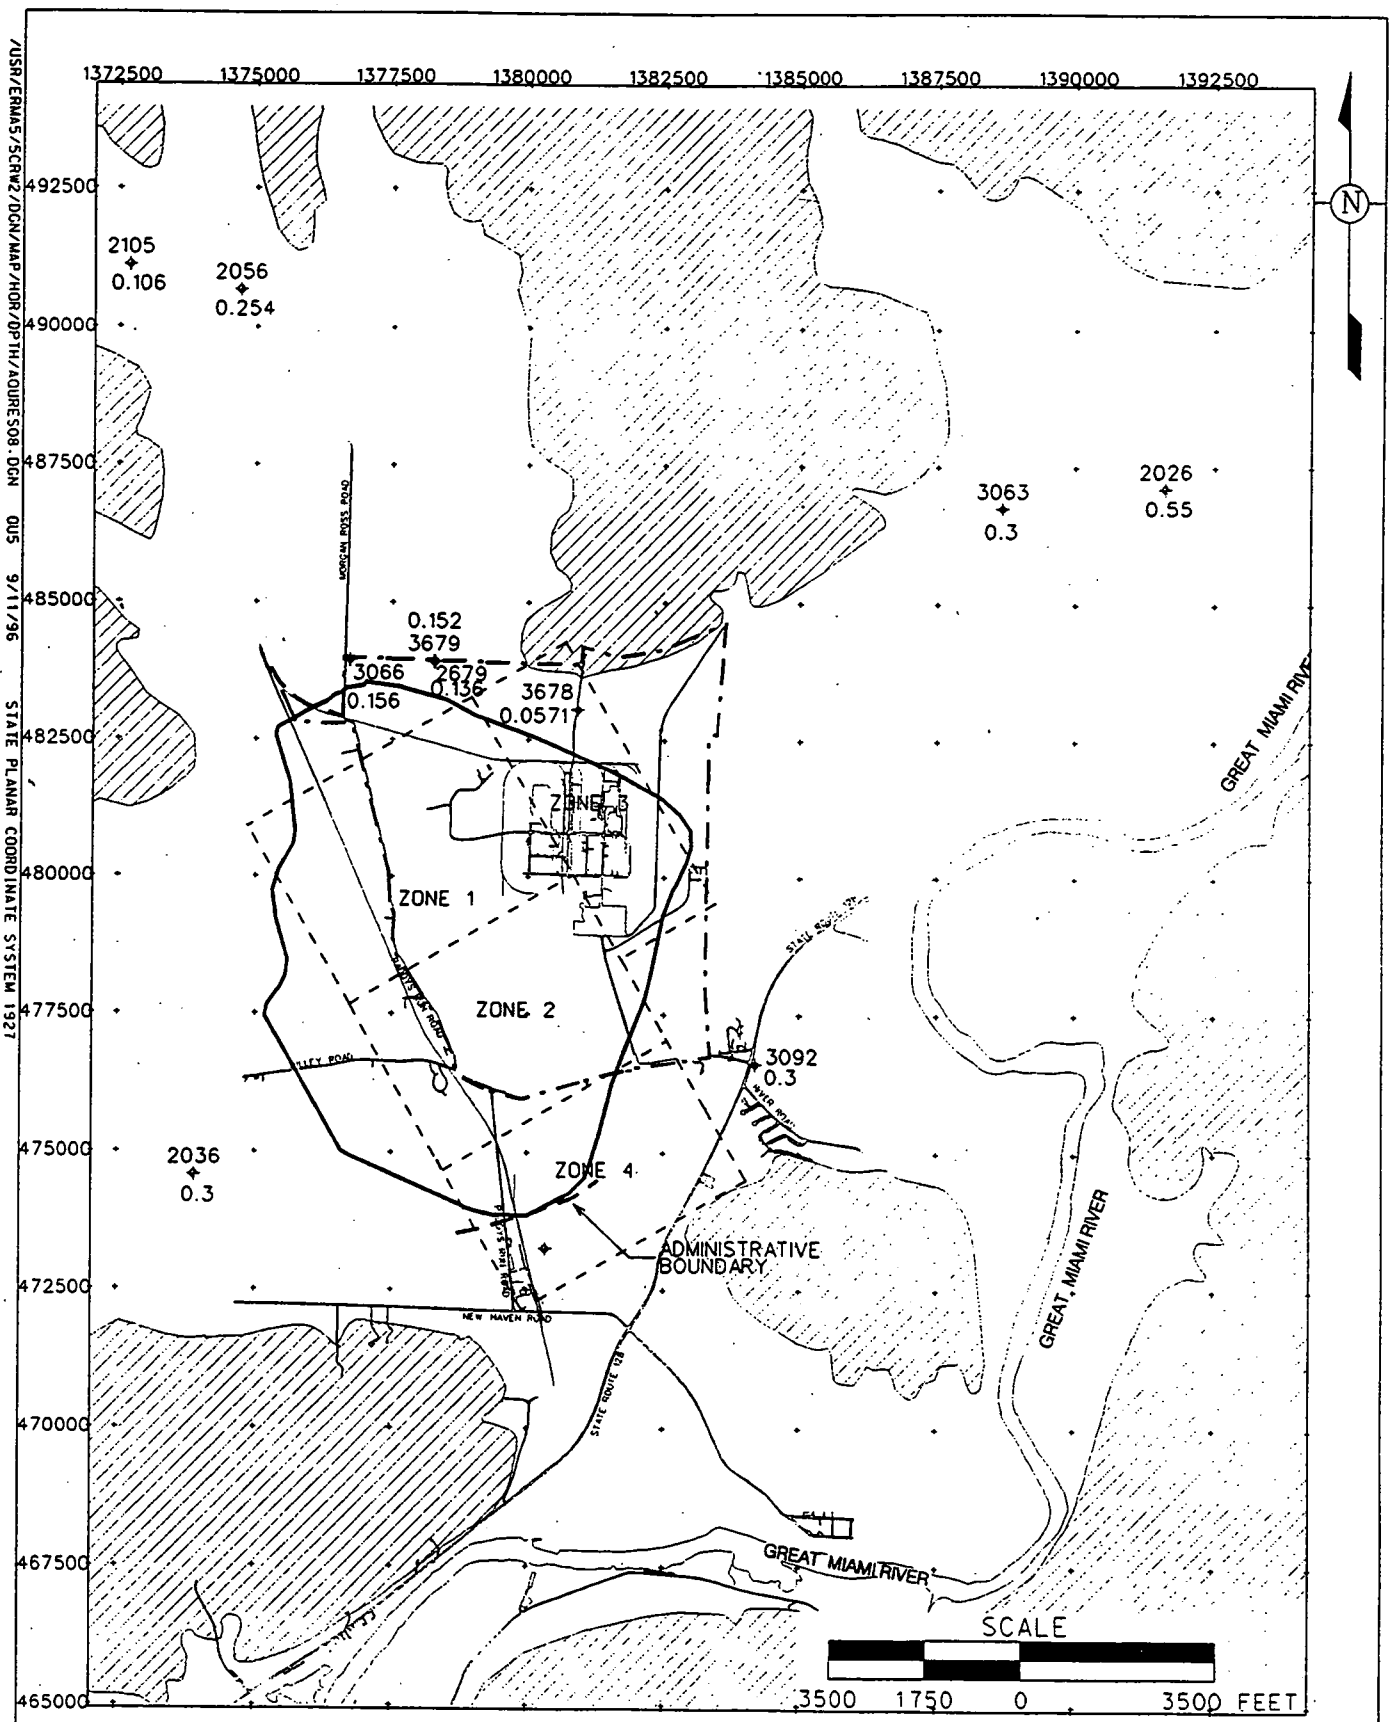

LEGEND:

FEMP BOUNDARY

2127 GROUNDWATER MONITORING WELL

0.3 ARSENIC (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-7. FRL EXCEEDENCES FOR ARSENIC LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

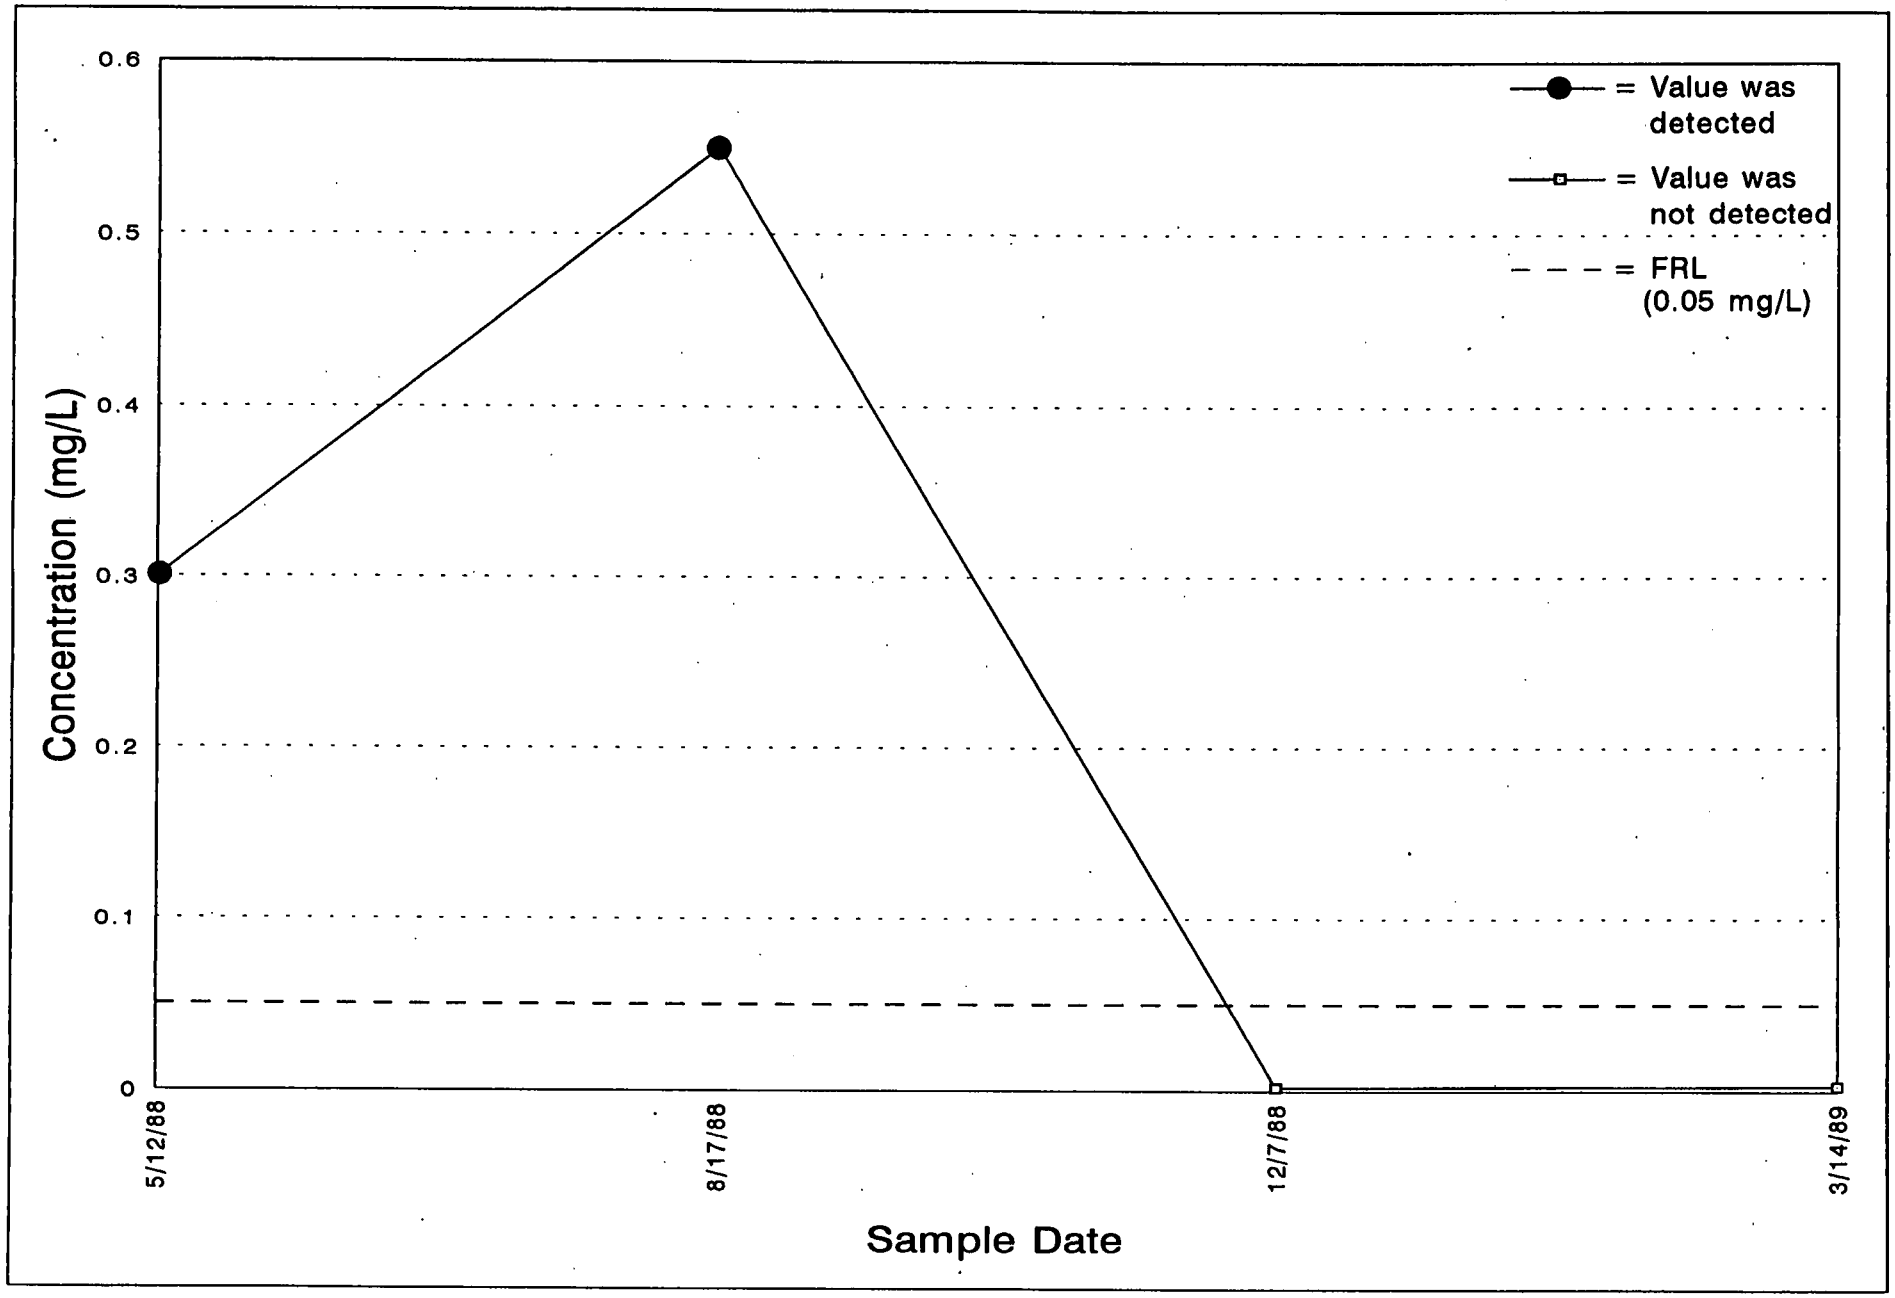

FIGURE A.3-8. ARSENIC CONCENTRATION VS. TIME, WELL 2026

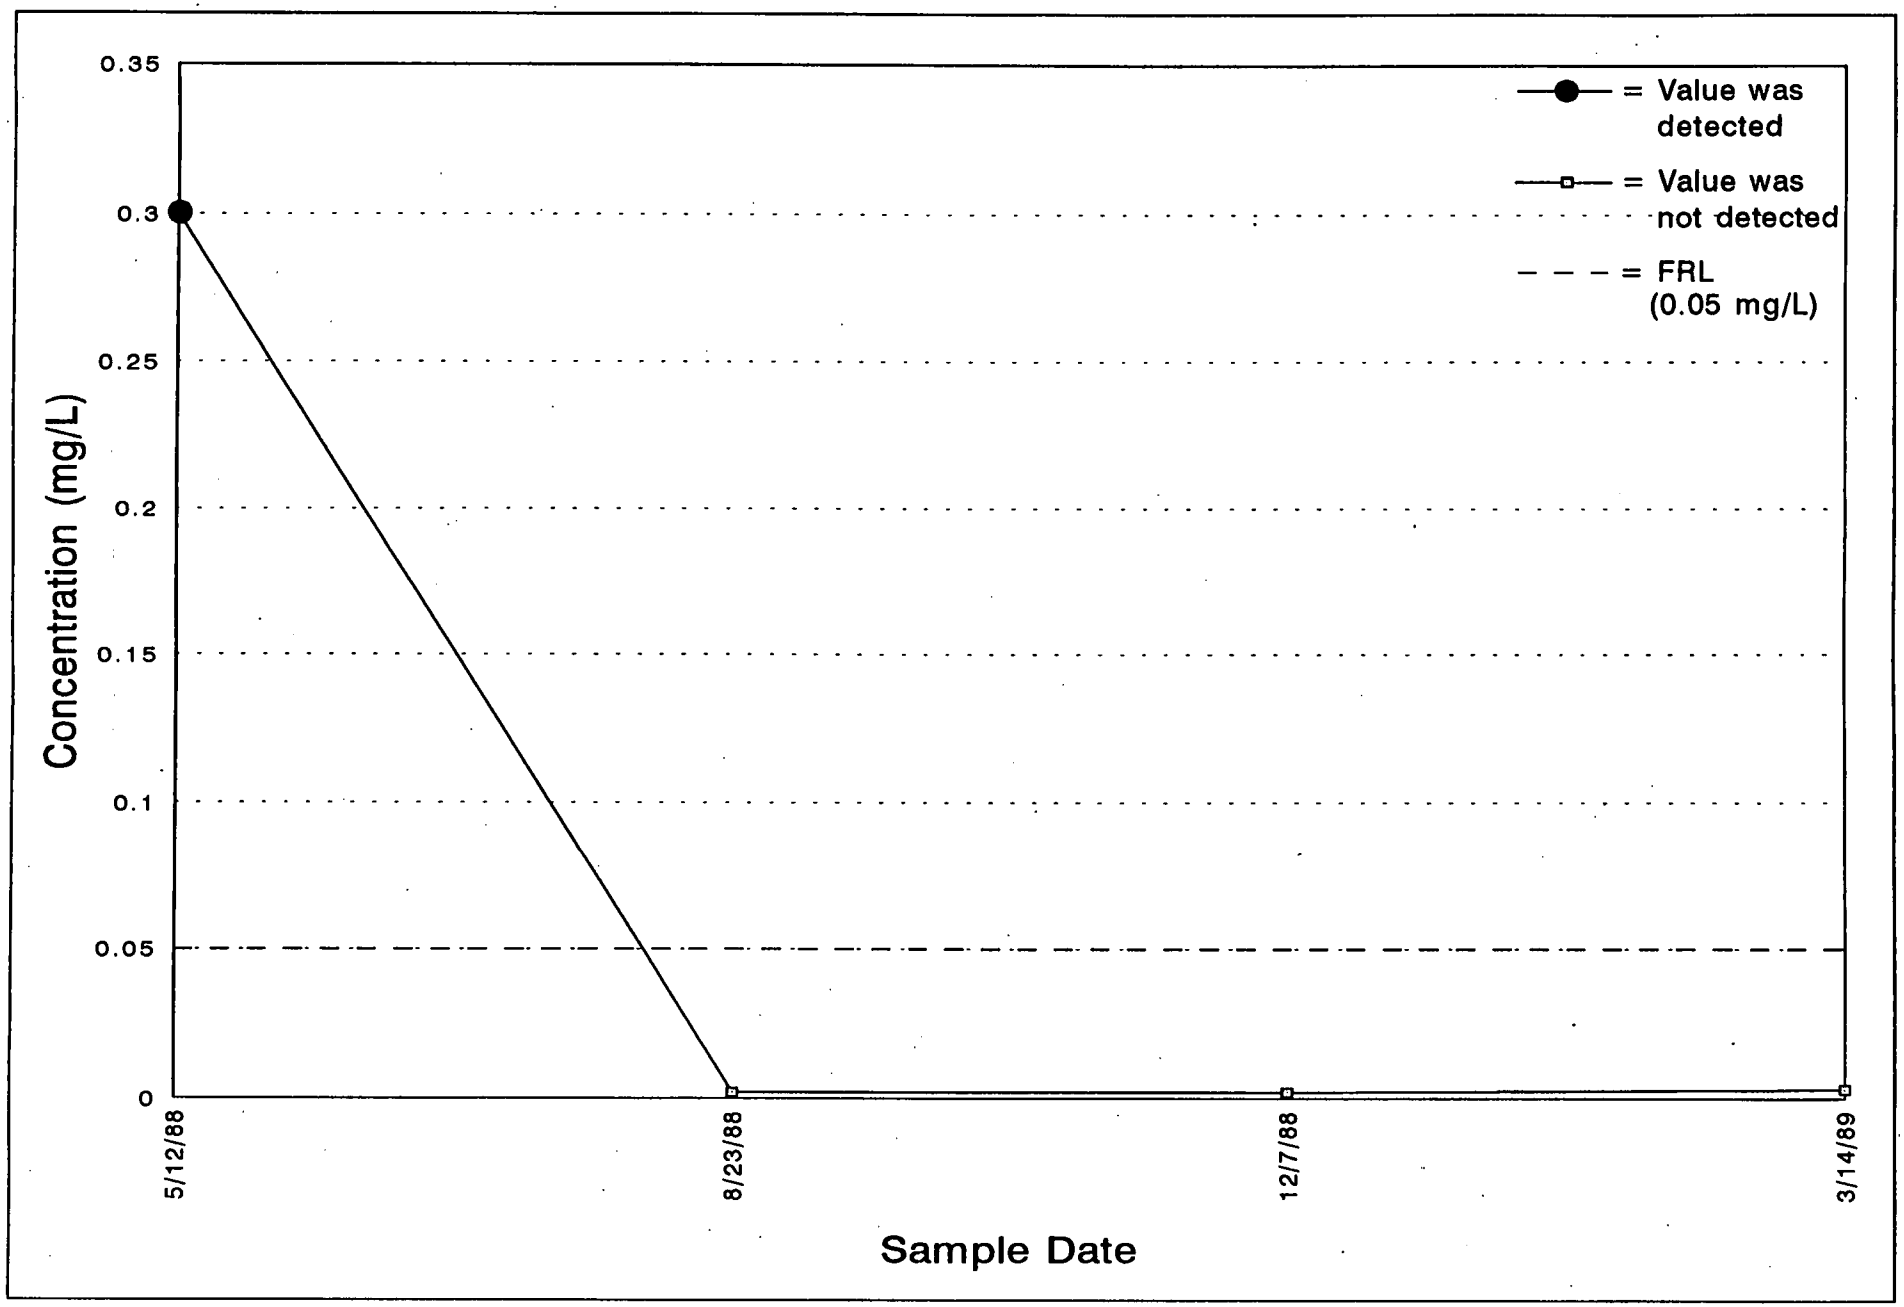

FIGURE A.3-9. ARSENIC CONCENTRATION VS. TIME, WELL 2036

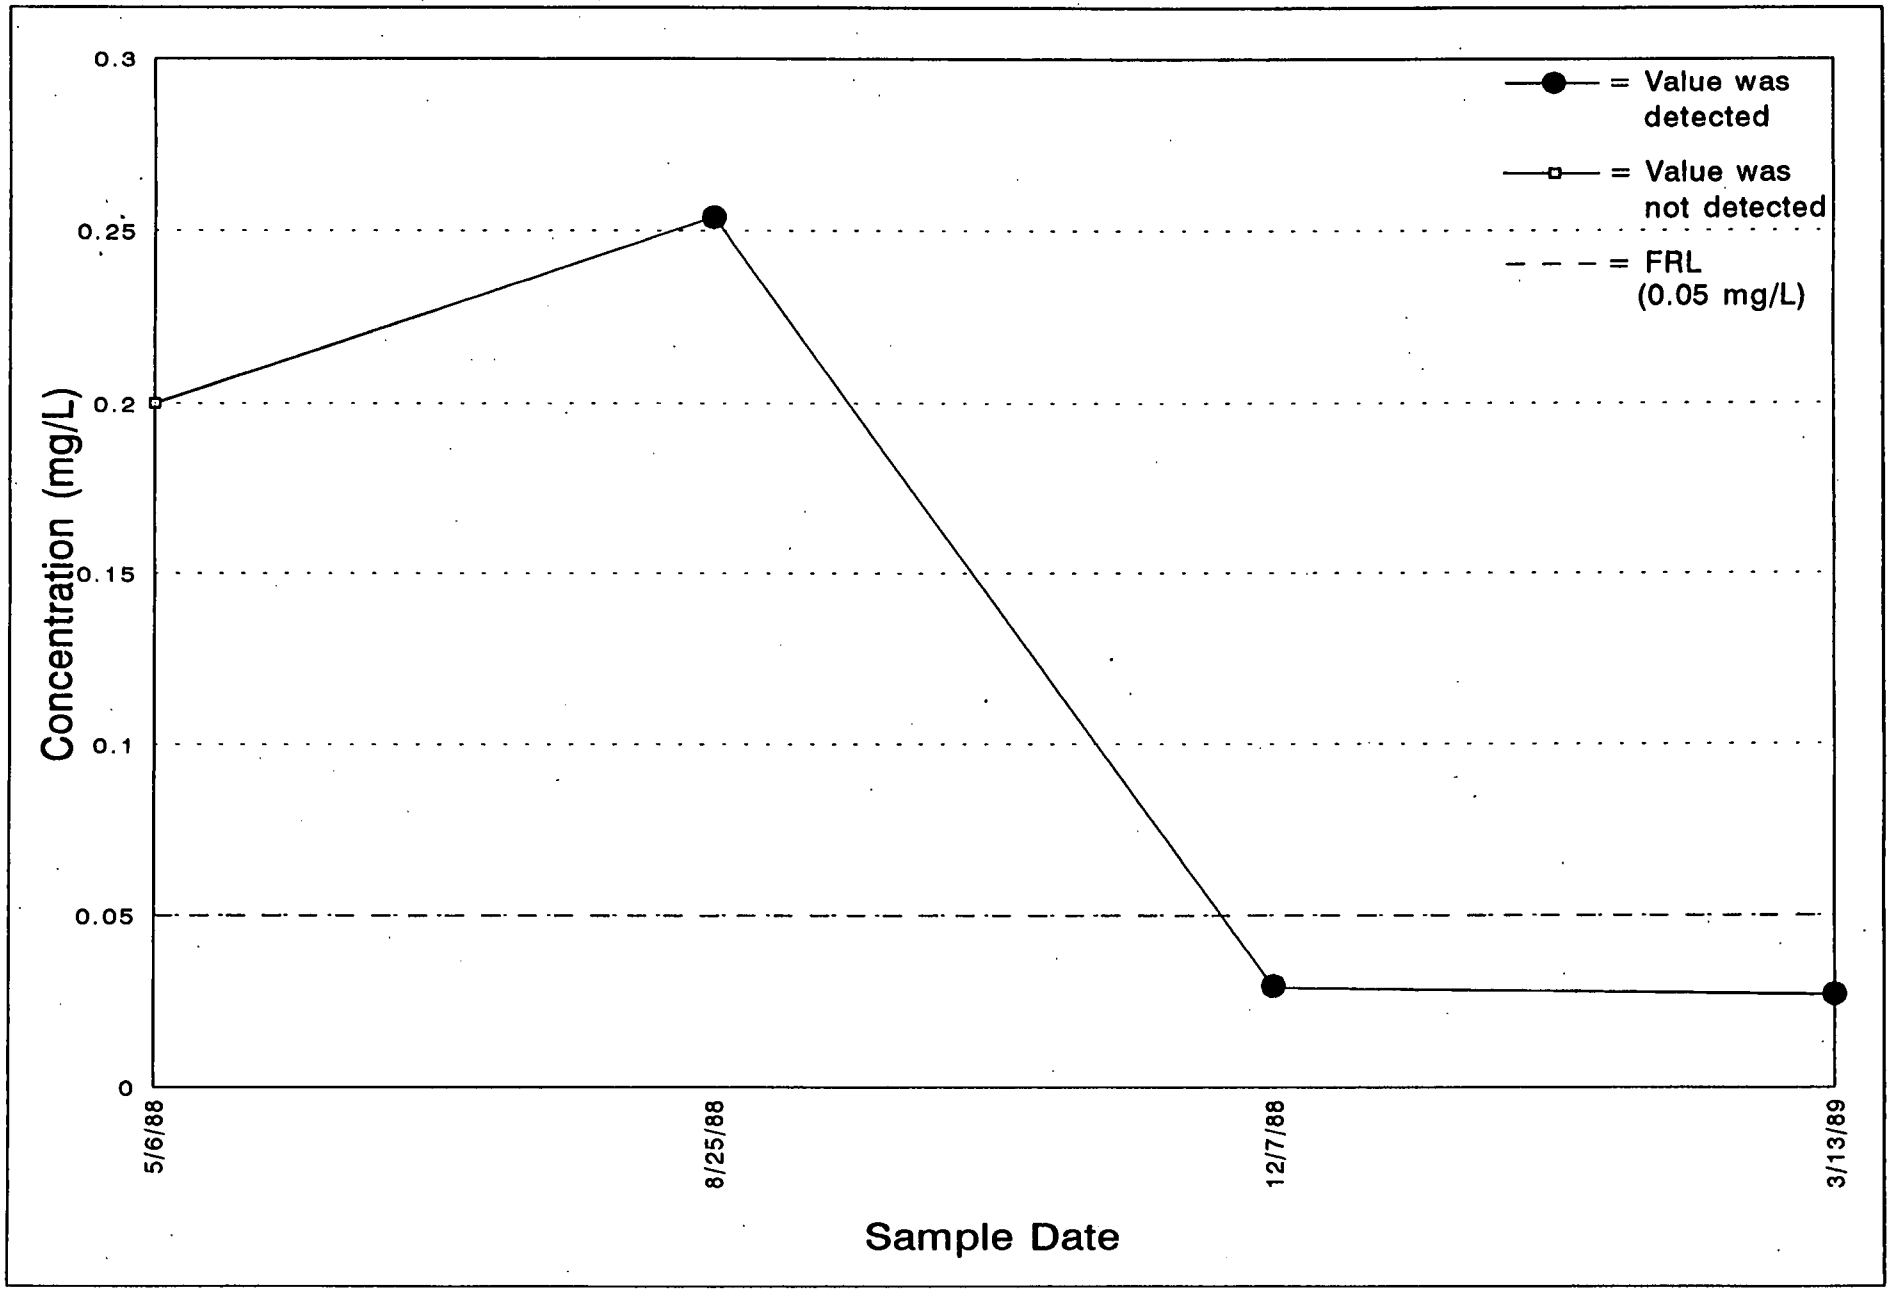

FIGURE A.3-10. ARSENIC CONCENTRATION VS. TIME, WELL 2056

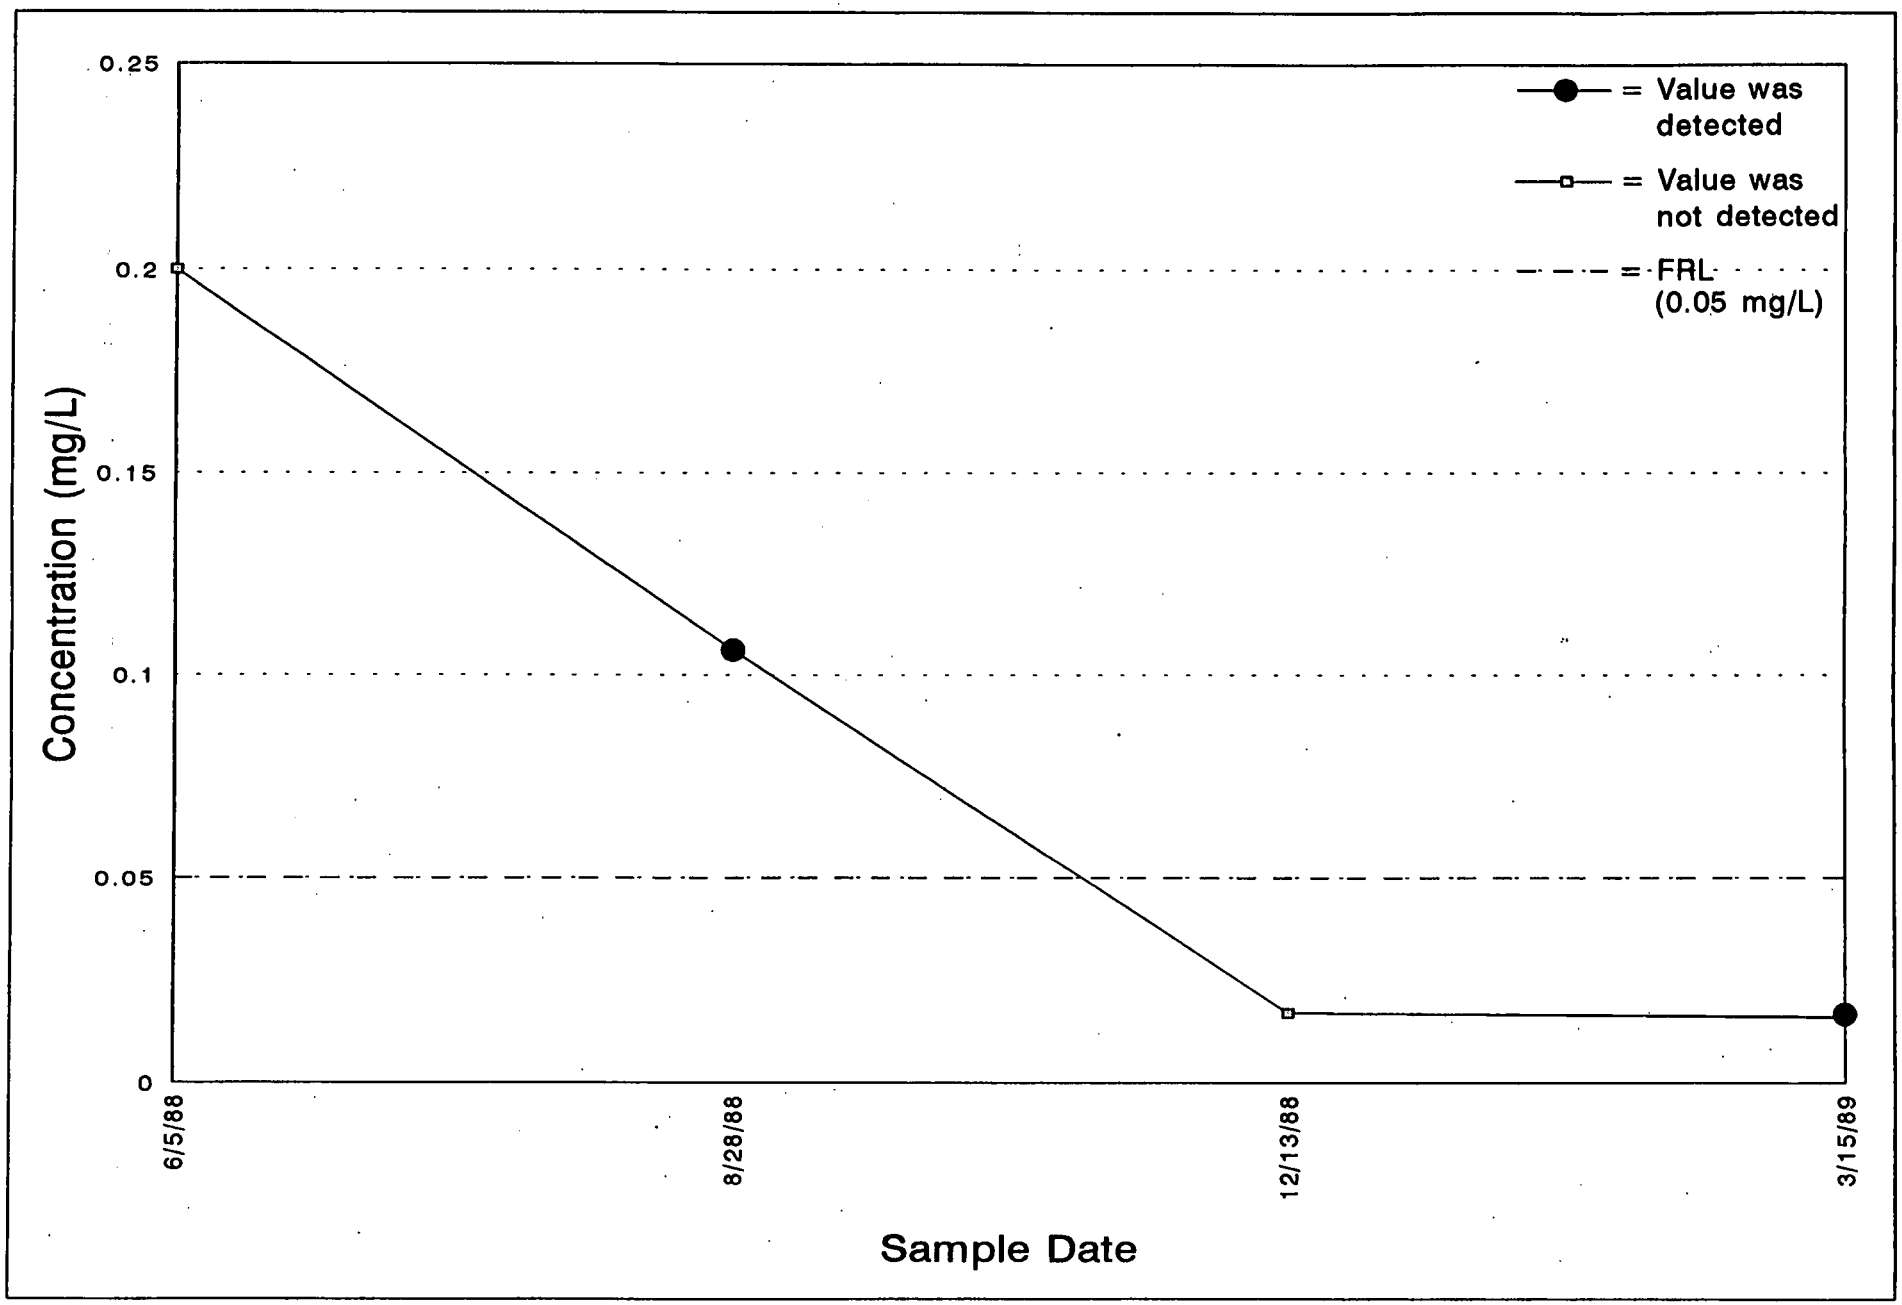

FIGURE A.3-11. ARSENIC CONCENTRATION VS. TIME, WELL 2105

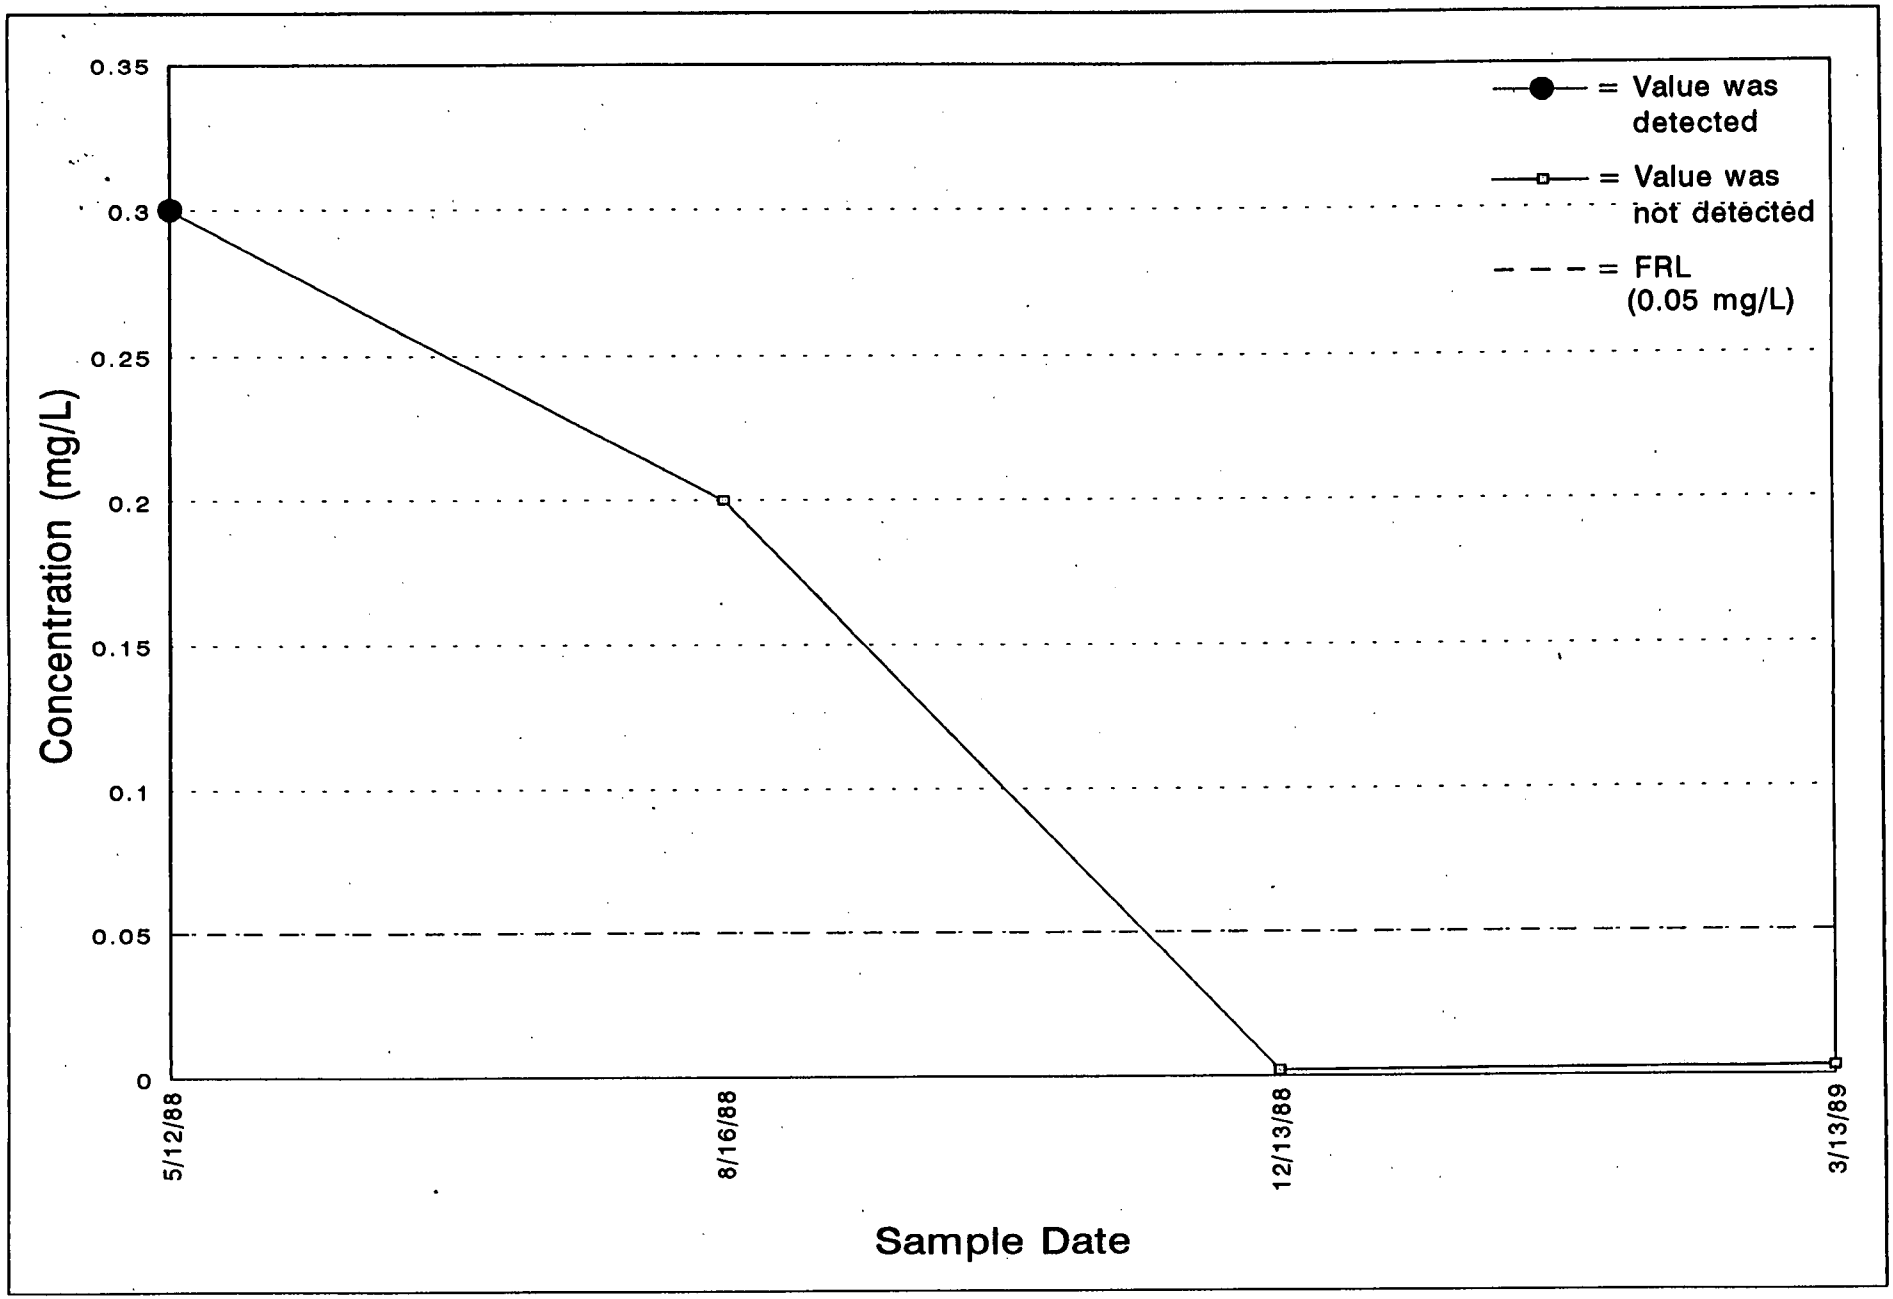

FIGURE A.3-12. ARSENIC CONCENTRATION VS. TIME, WELL 3063

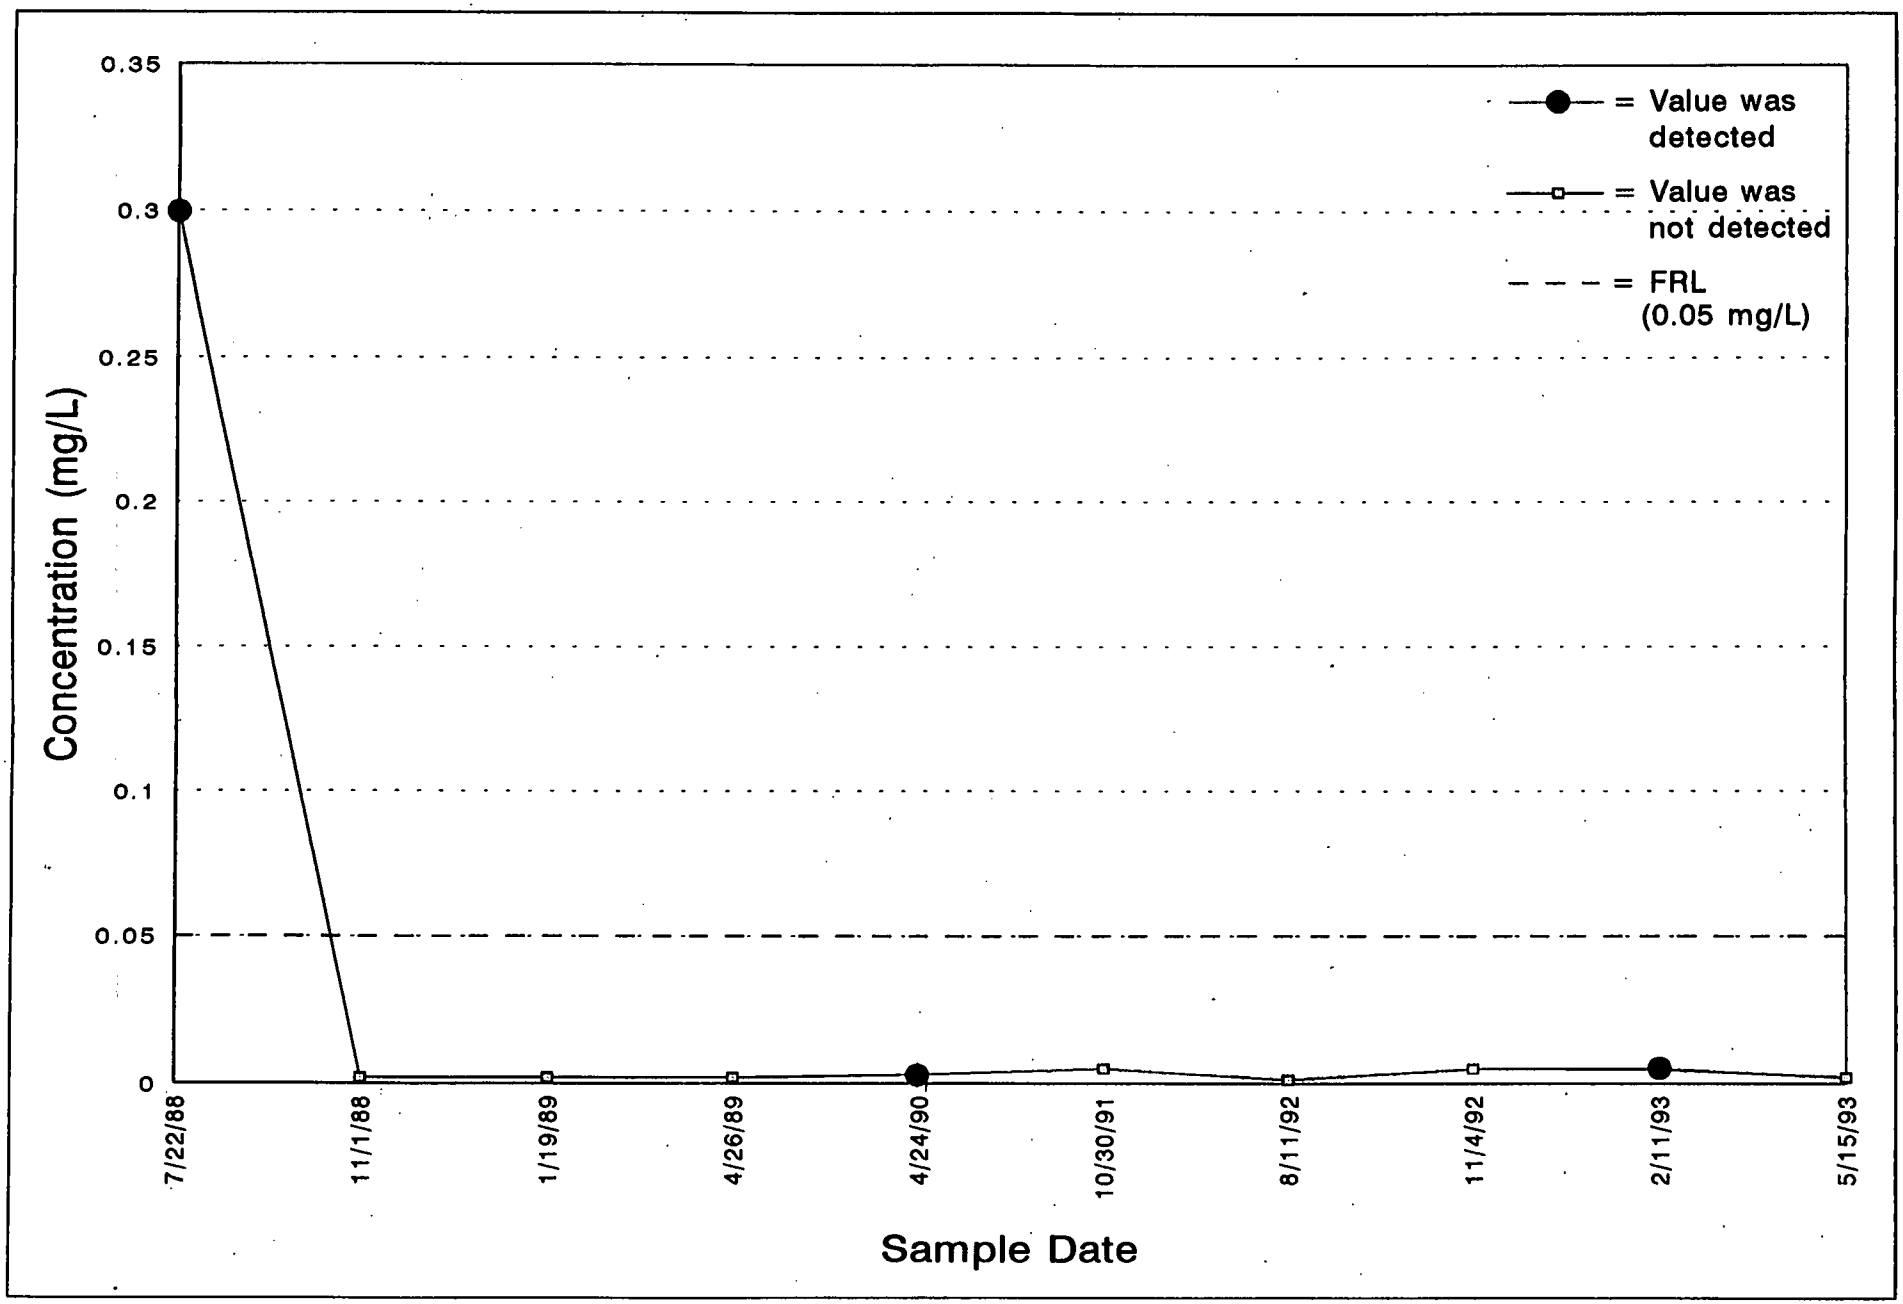

FIGURE A.3-13. ARSENIC CONCENTRATION VS. TIME, WELL 3092

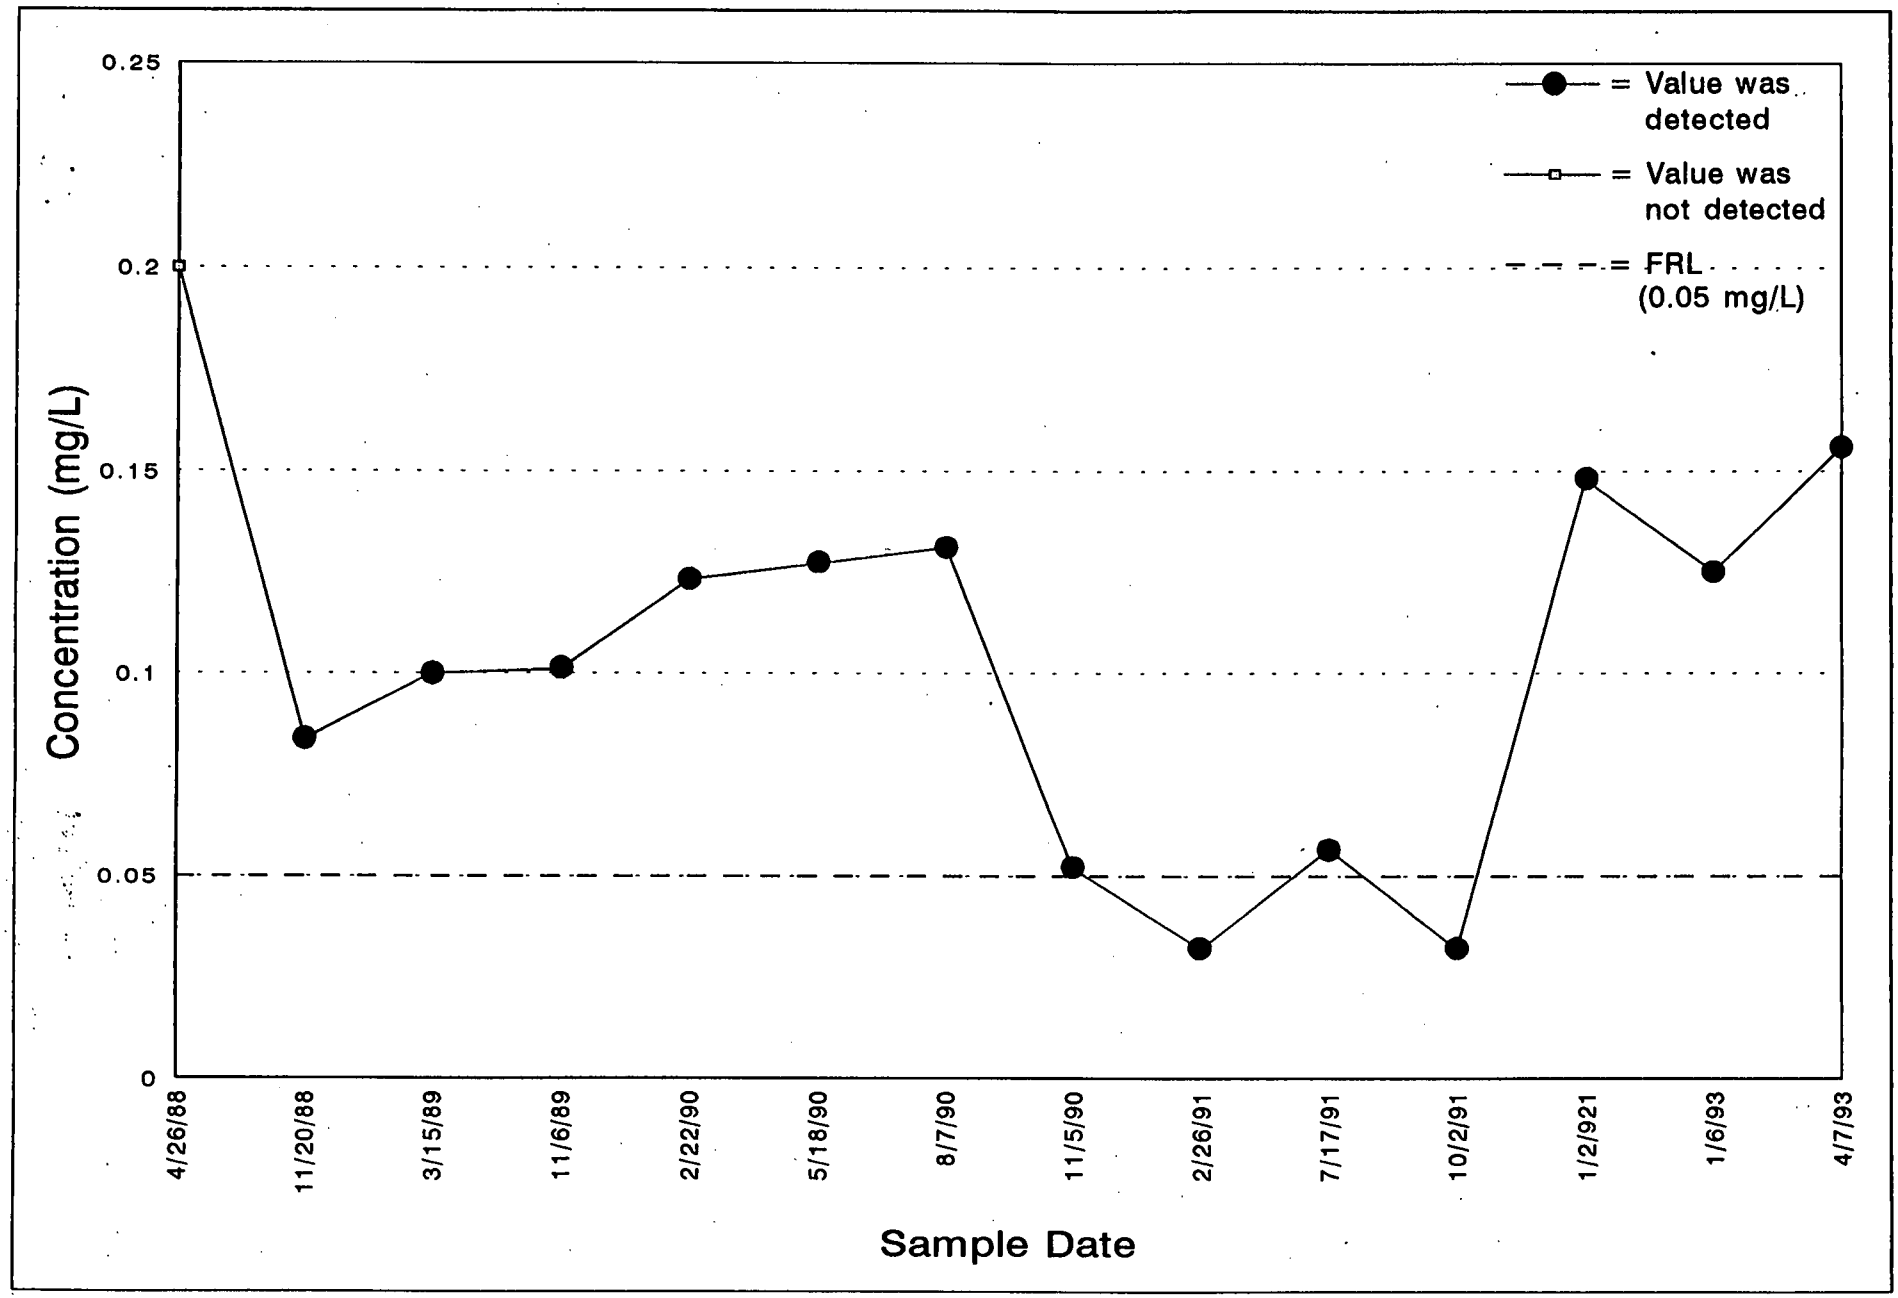

FIGURE A.3-14. ARSENIC CONCENTRATION VS. TIME, WELL 3066

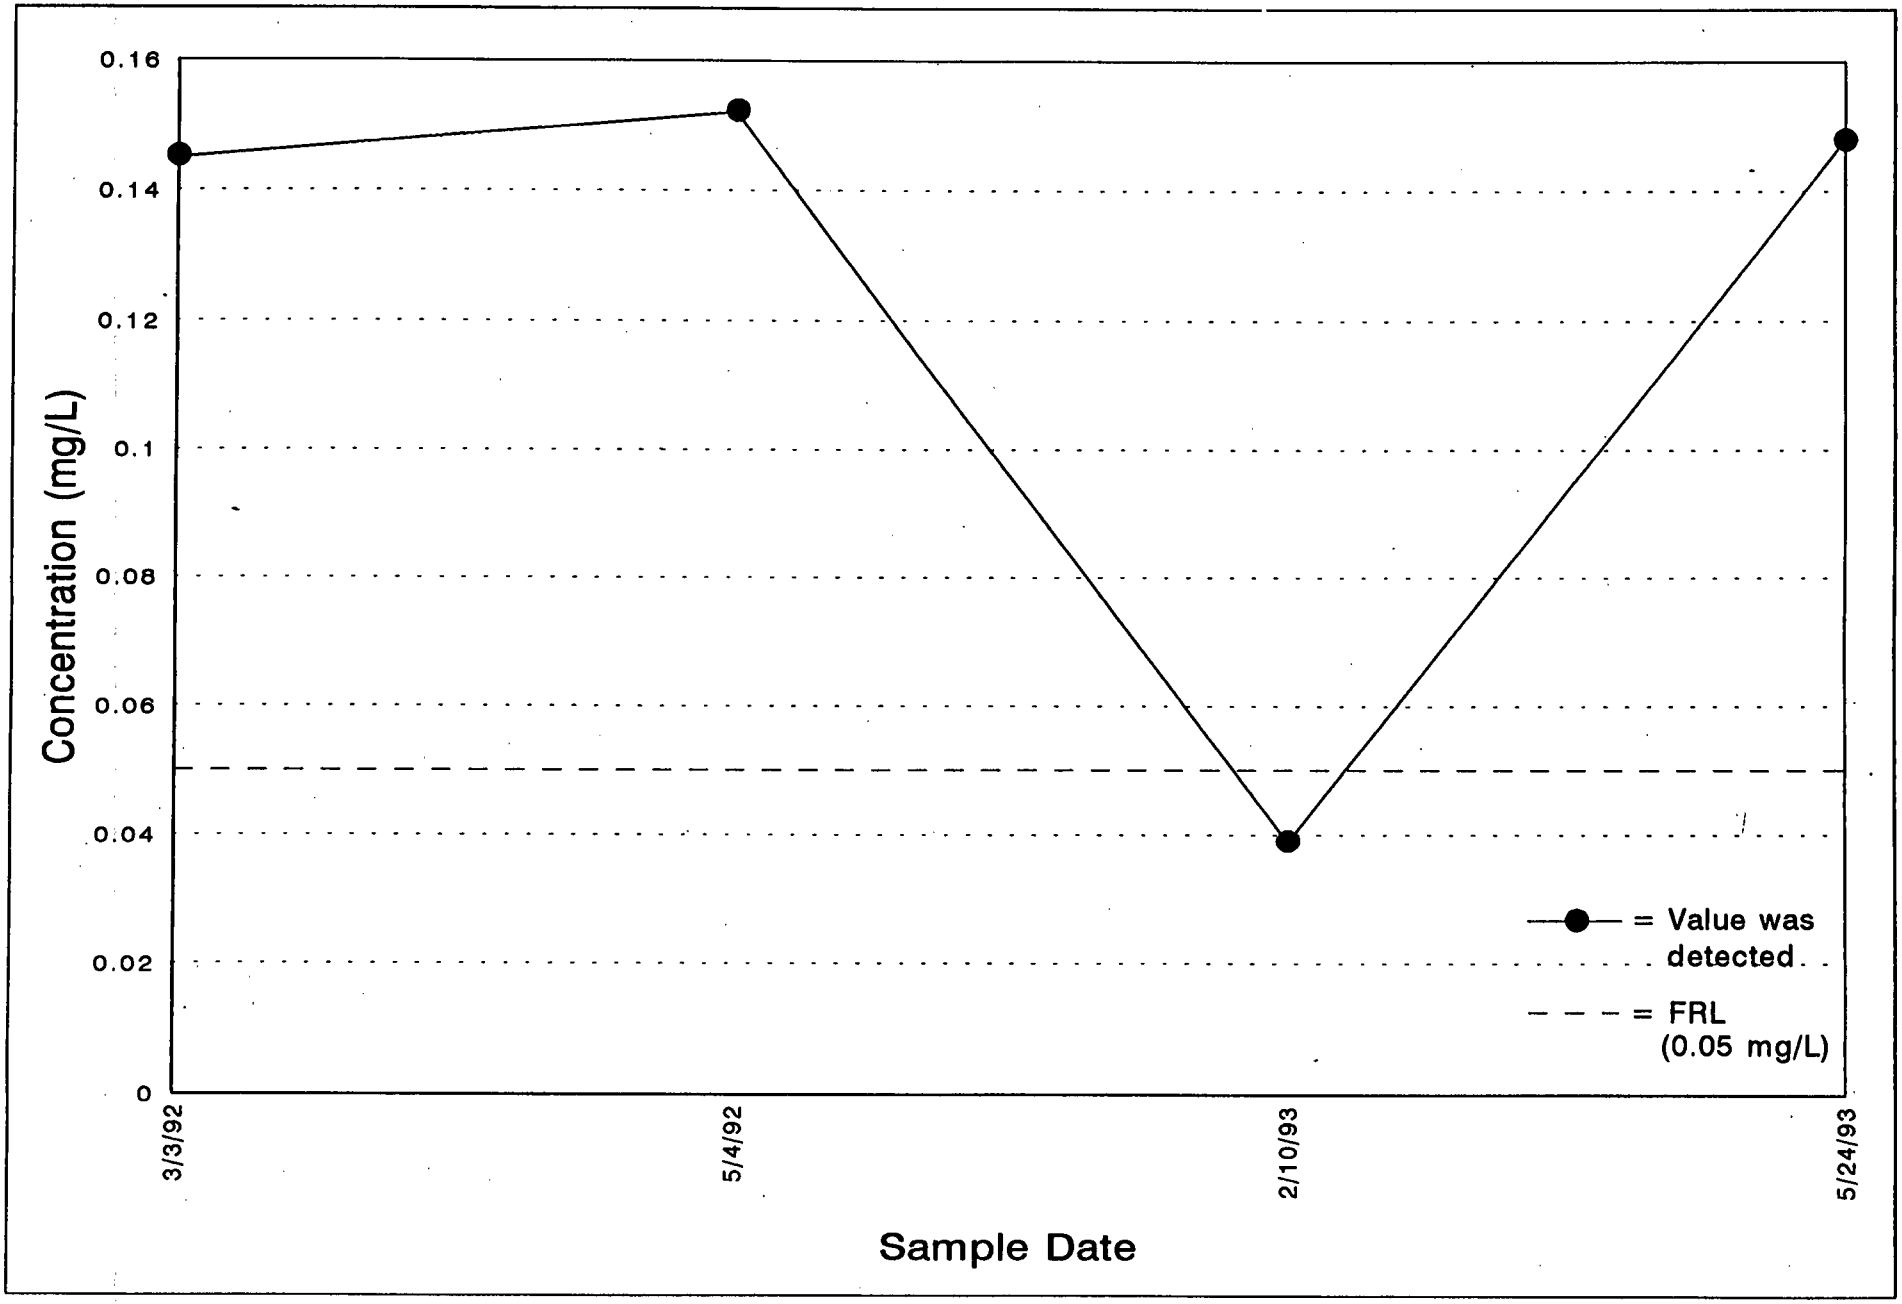

FIGURE A.3-15. ARSENIC CONCENTRATION VS. TIME, WELL 3679

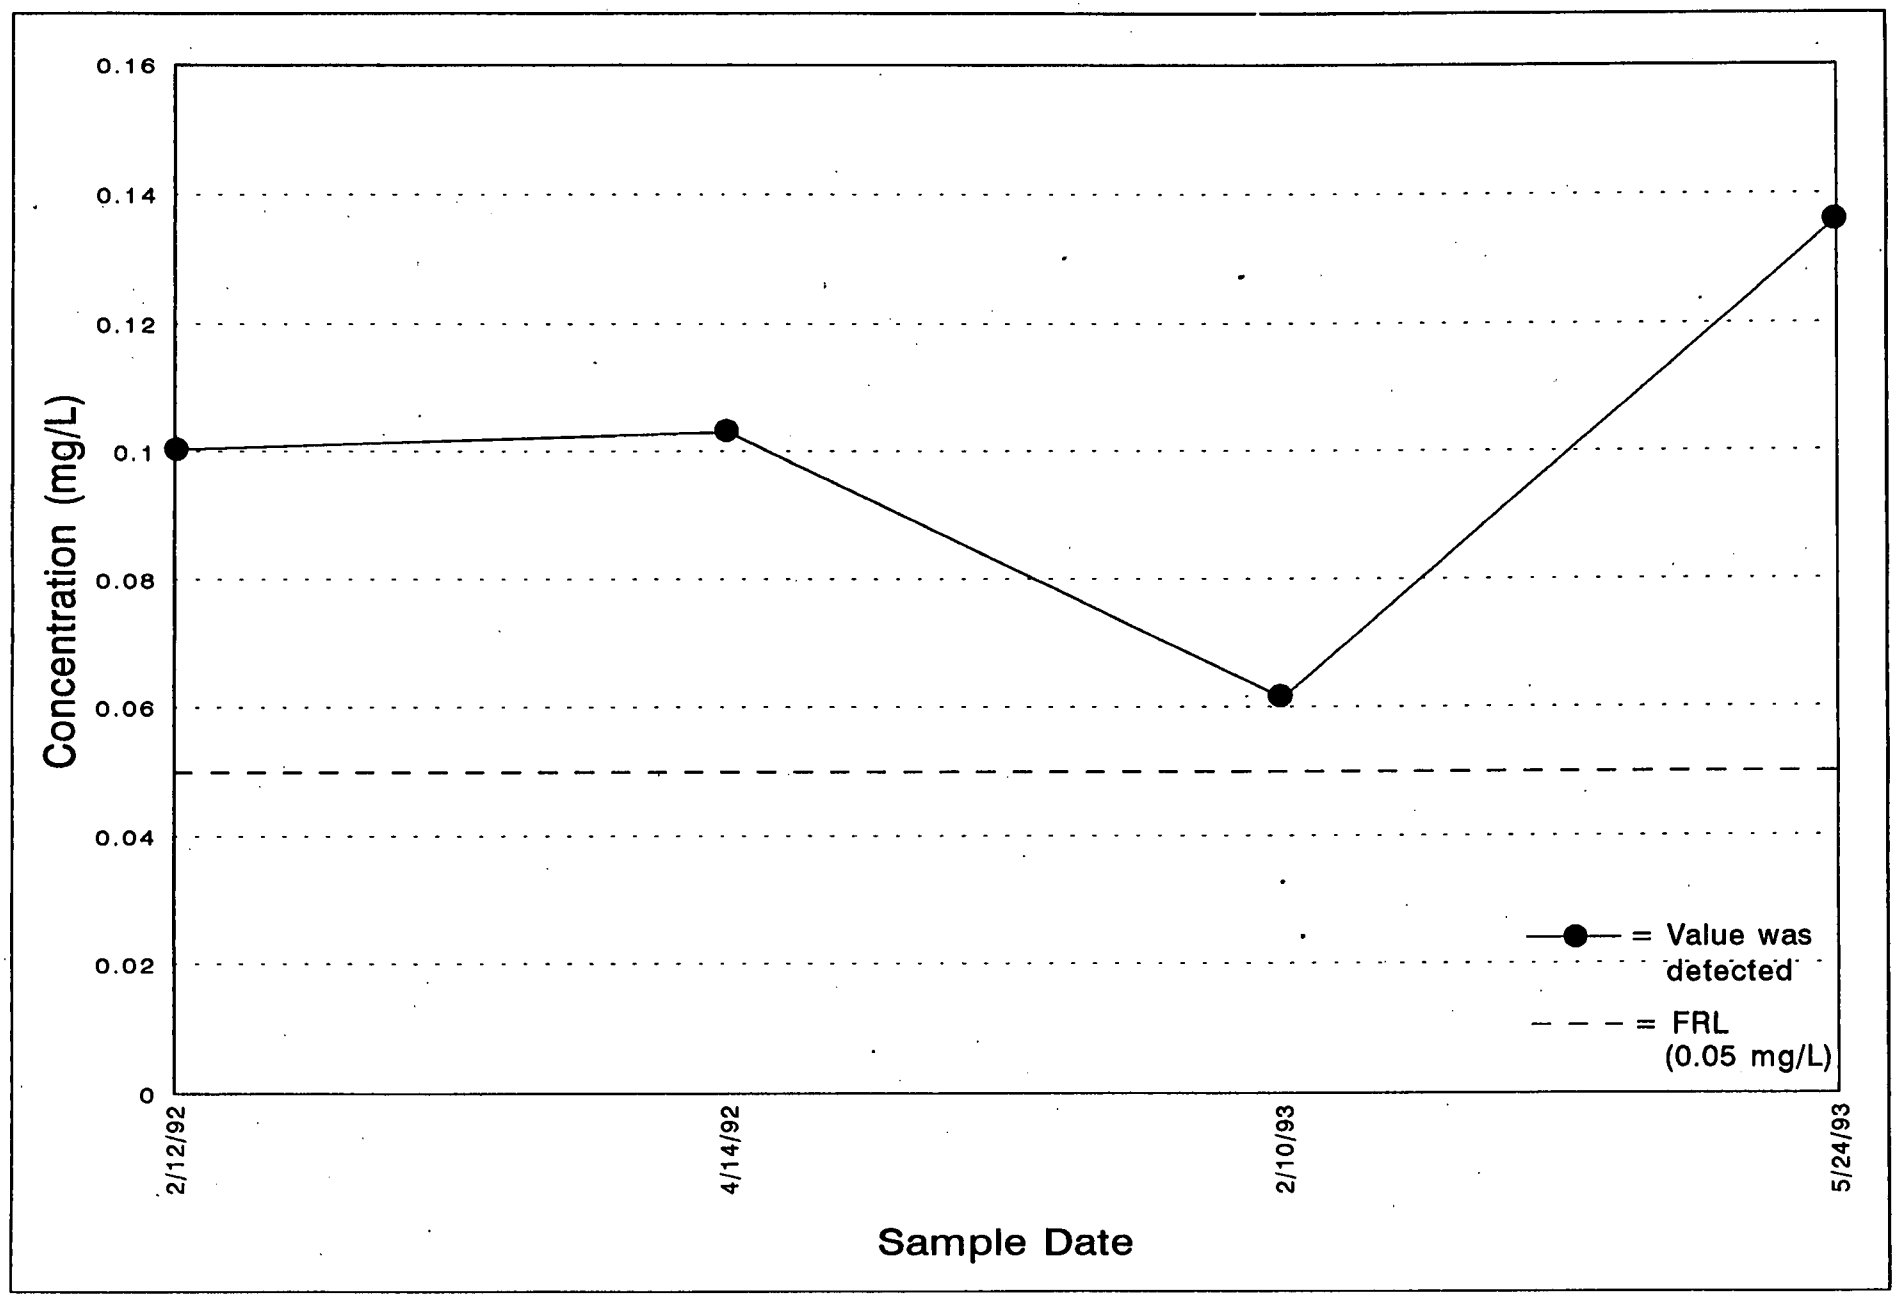

FIGURE A.3-16. ARSENIC CONCENTRATION VS. TIME, WELL 2679

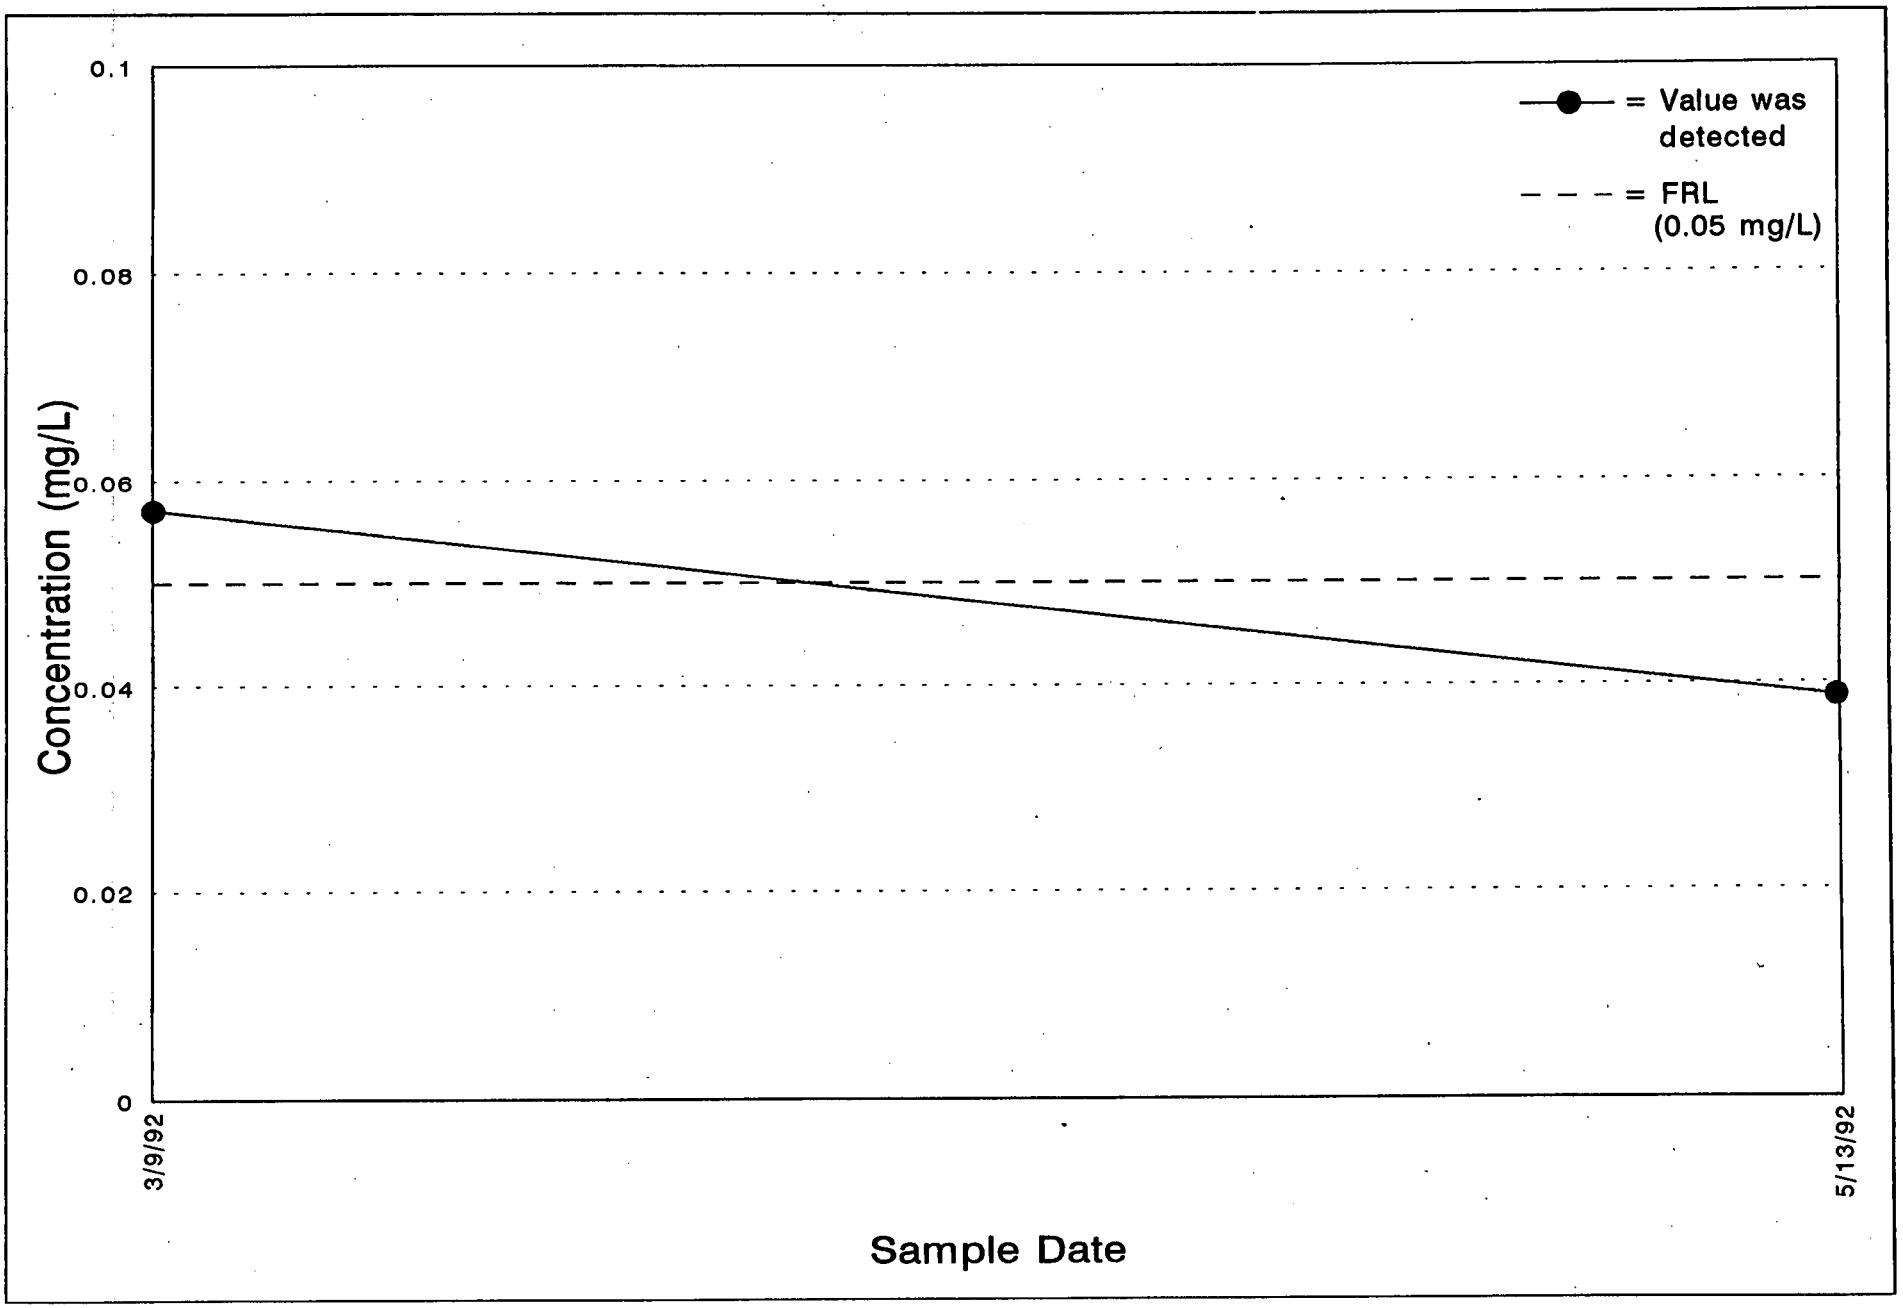

FIGURE A.3-17. ARSENIC CONCENTRATION VS. TIME, WELL 3678

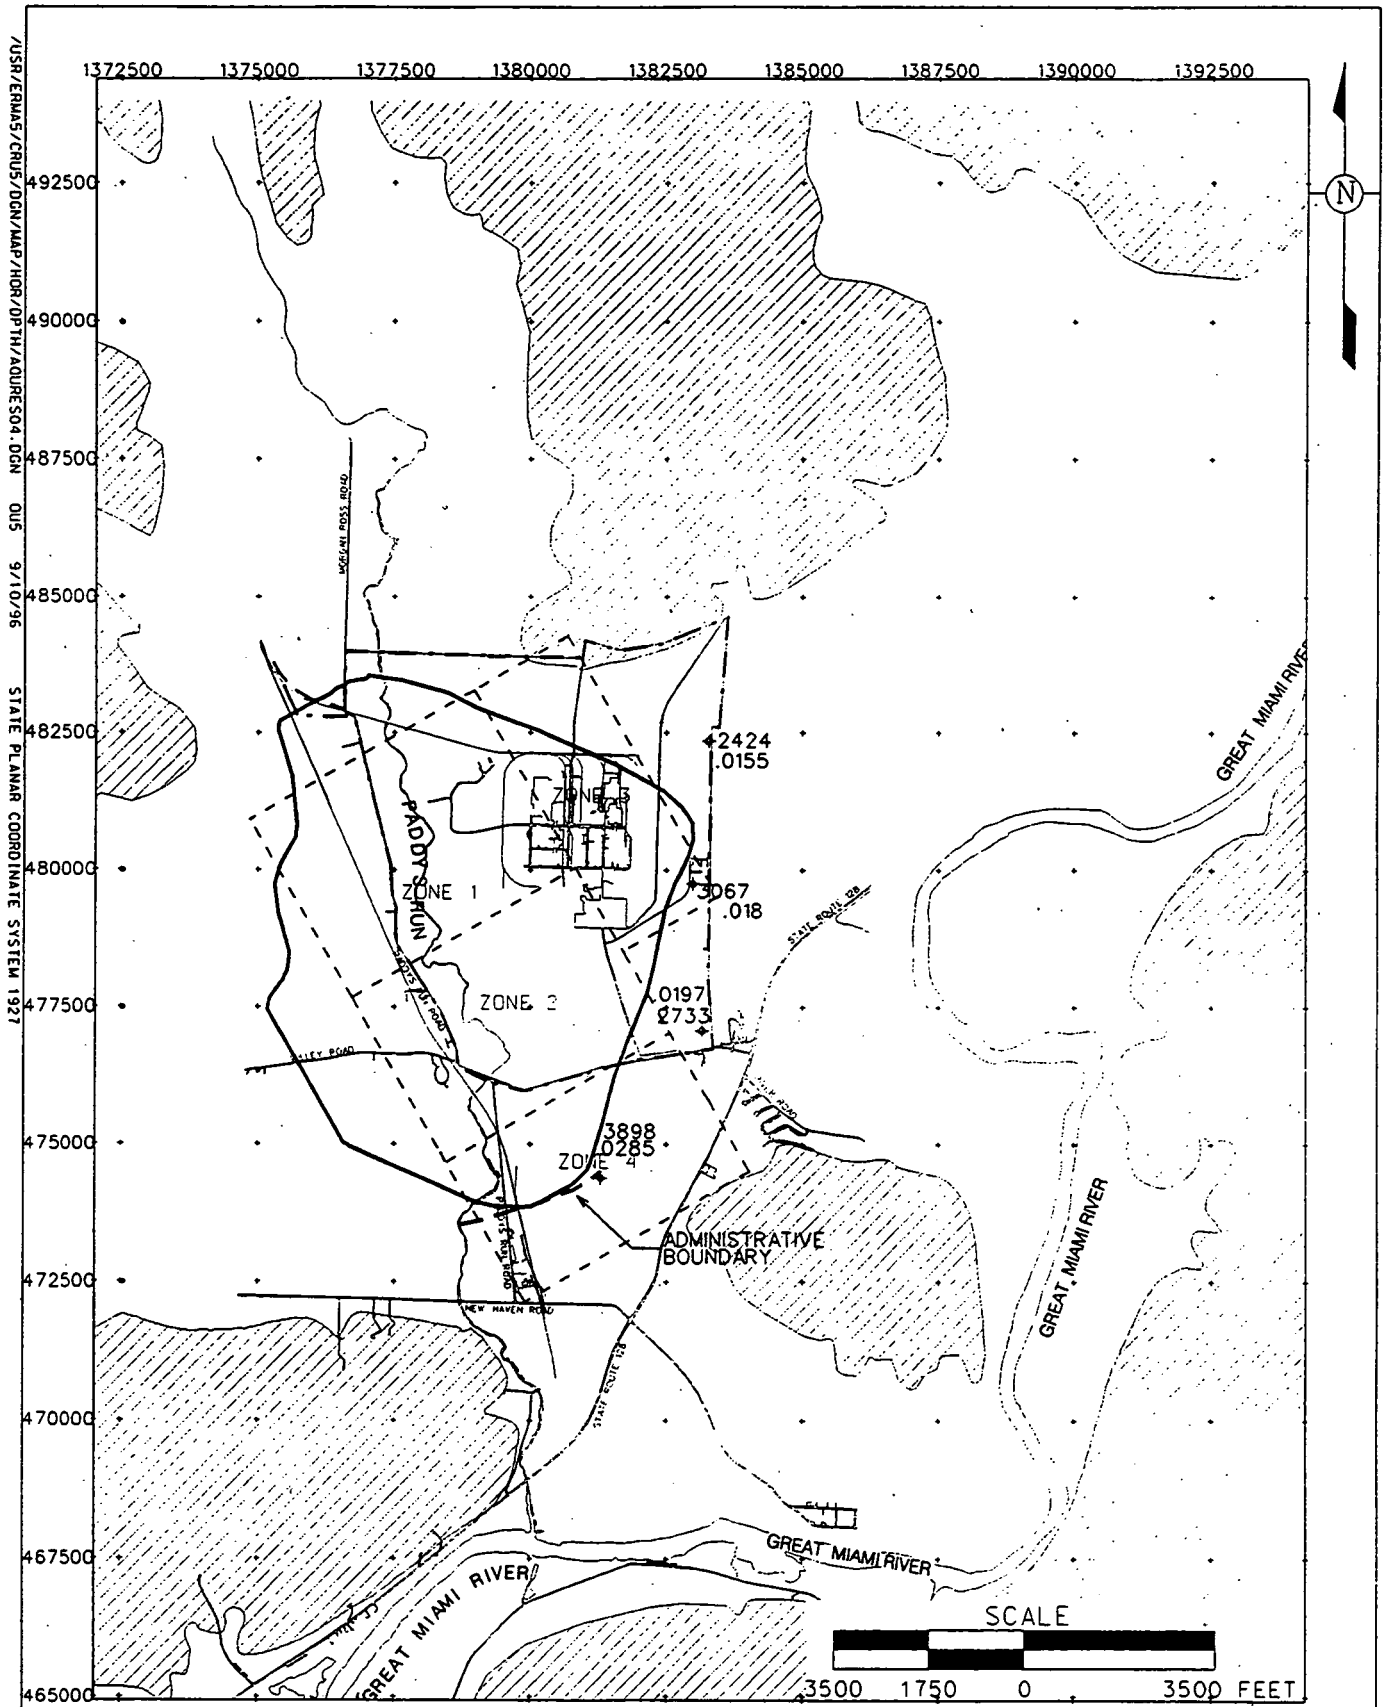

LEGEND:

— · — · — FEMP BOUNDARY

2127 ✦ GROUNDWATER MONITORING WELL

12.8 CADMIUM (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-18. FRL EXCEEDENCES FOR CADMIUM LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

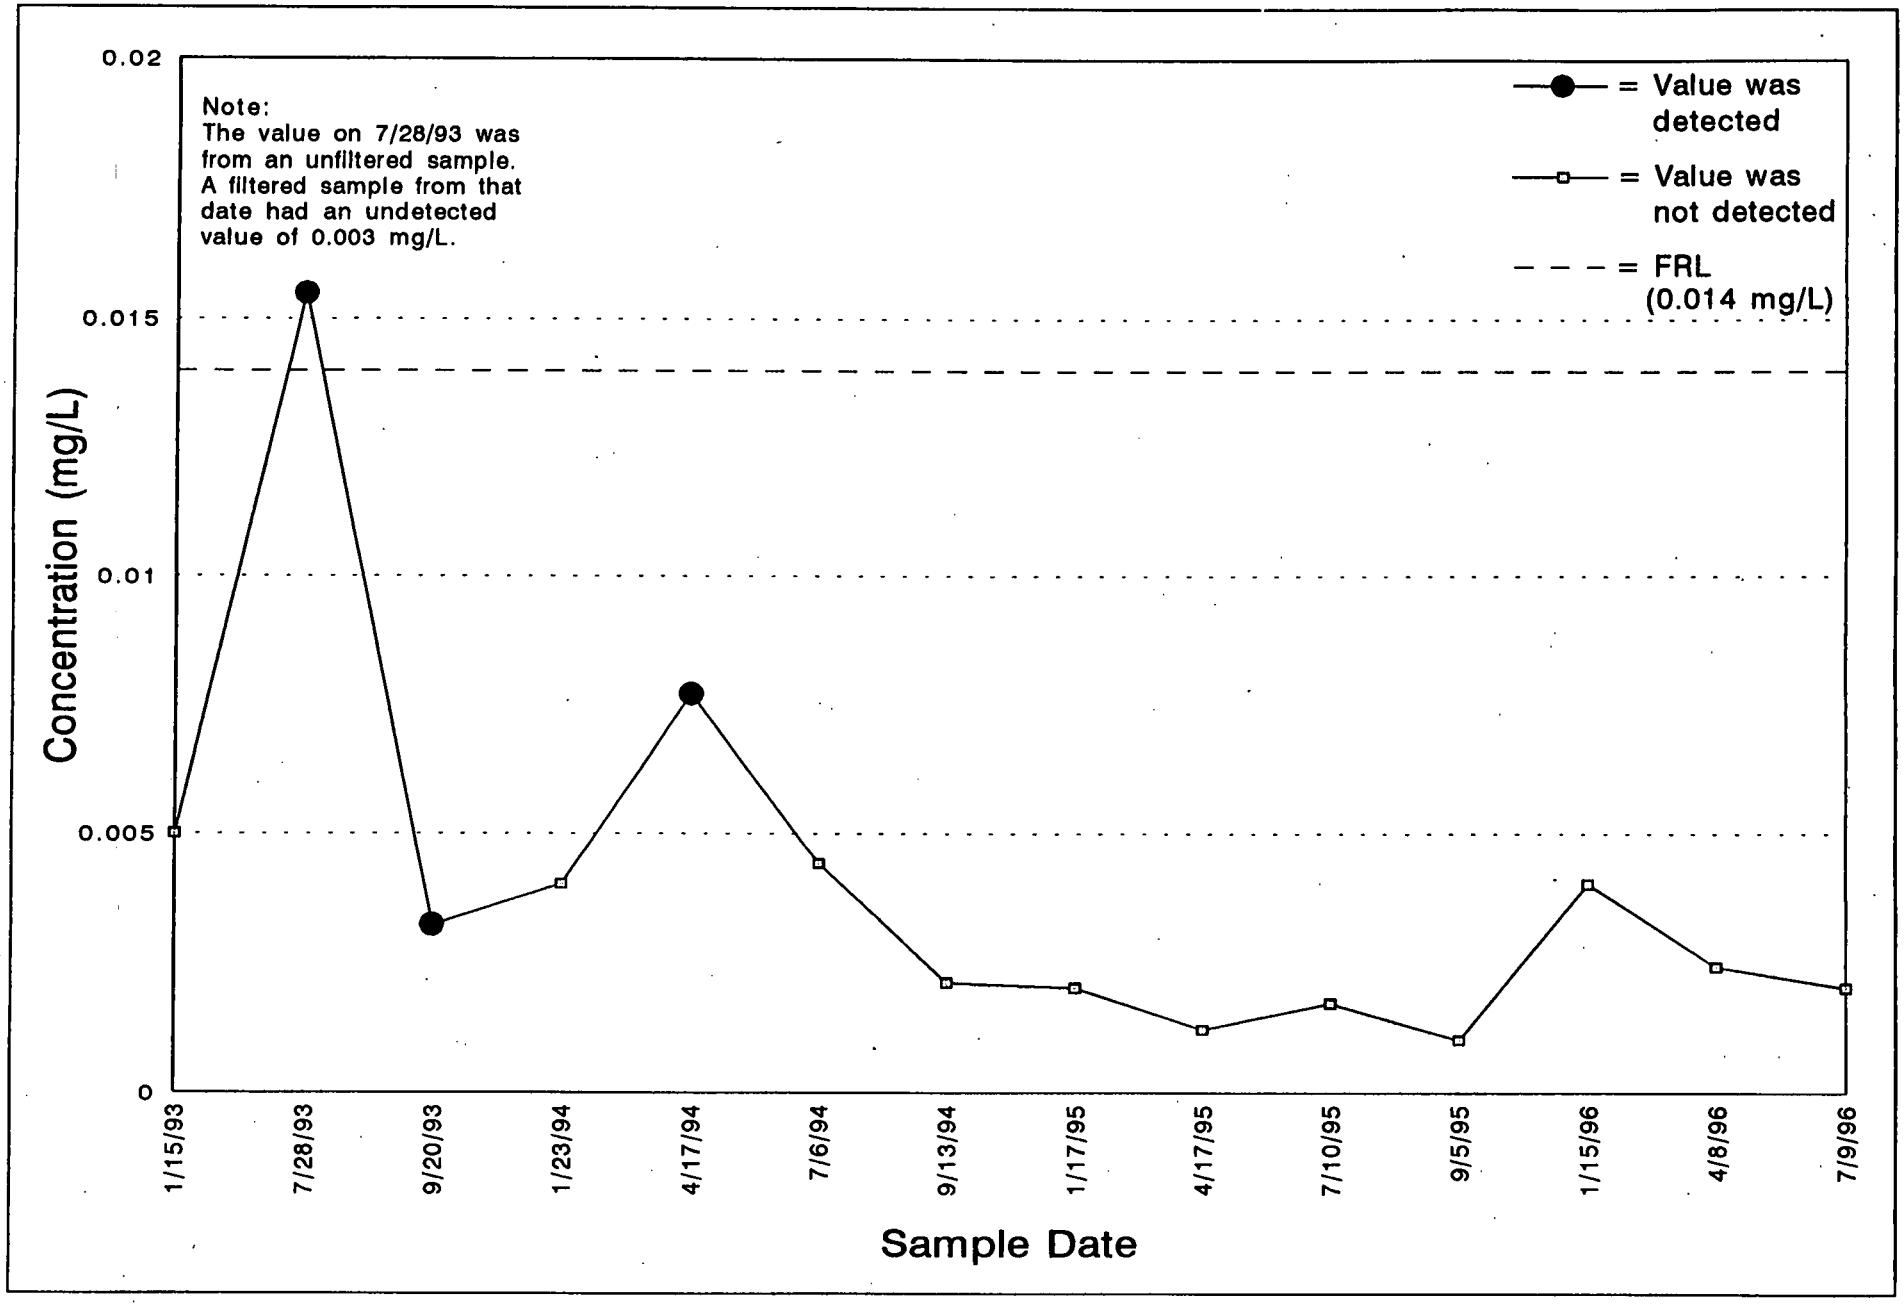

FIGURE A.3-19. CADMIUM CONCENTRATION VS. TIME, WELL 2424

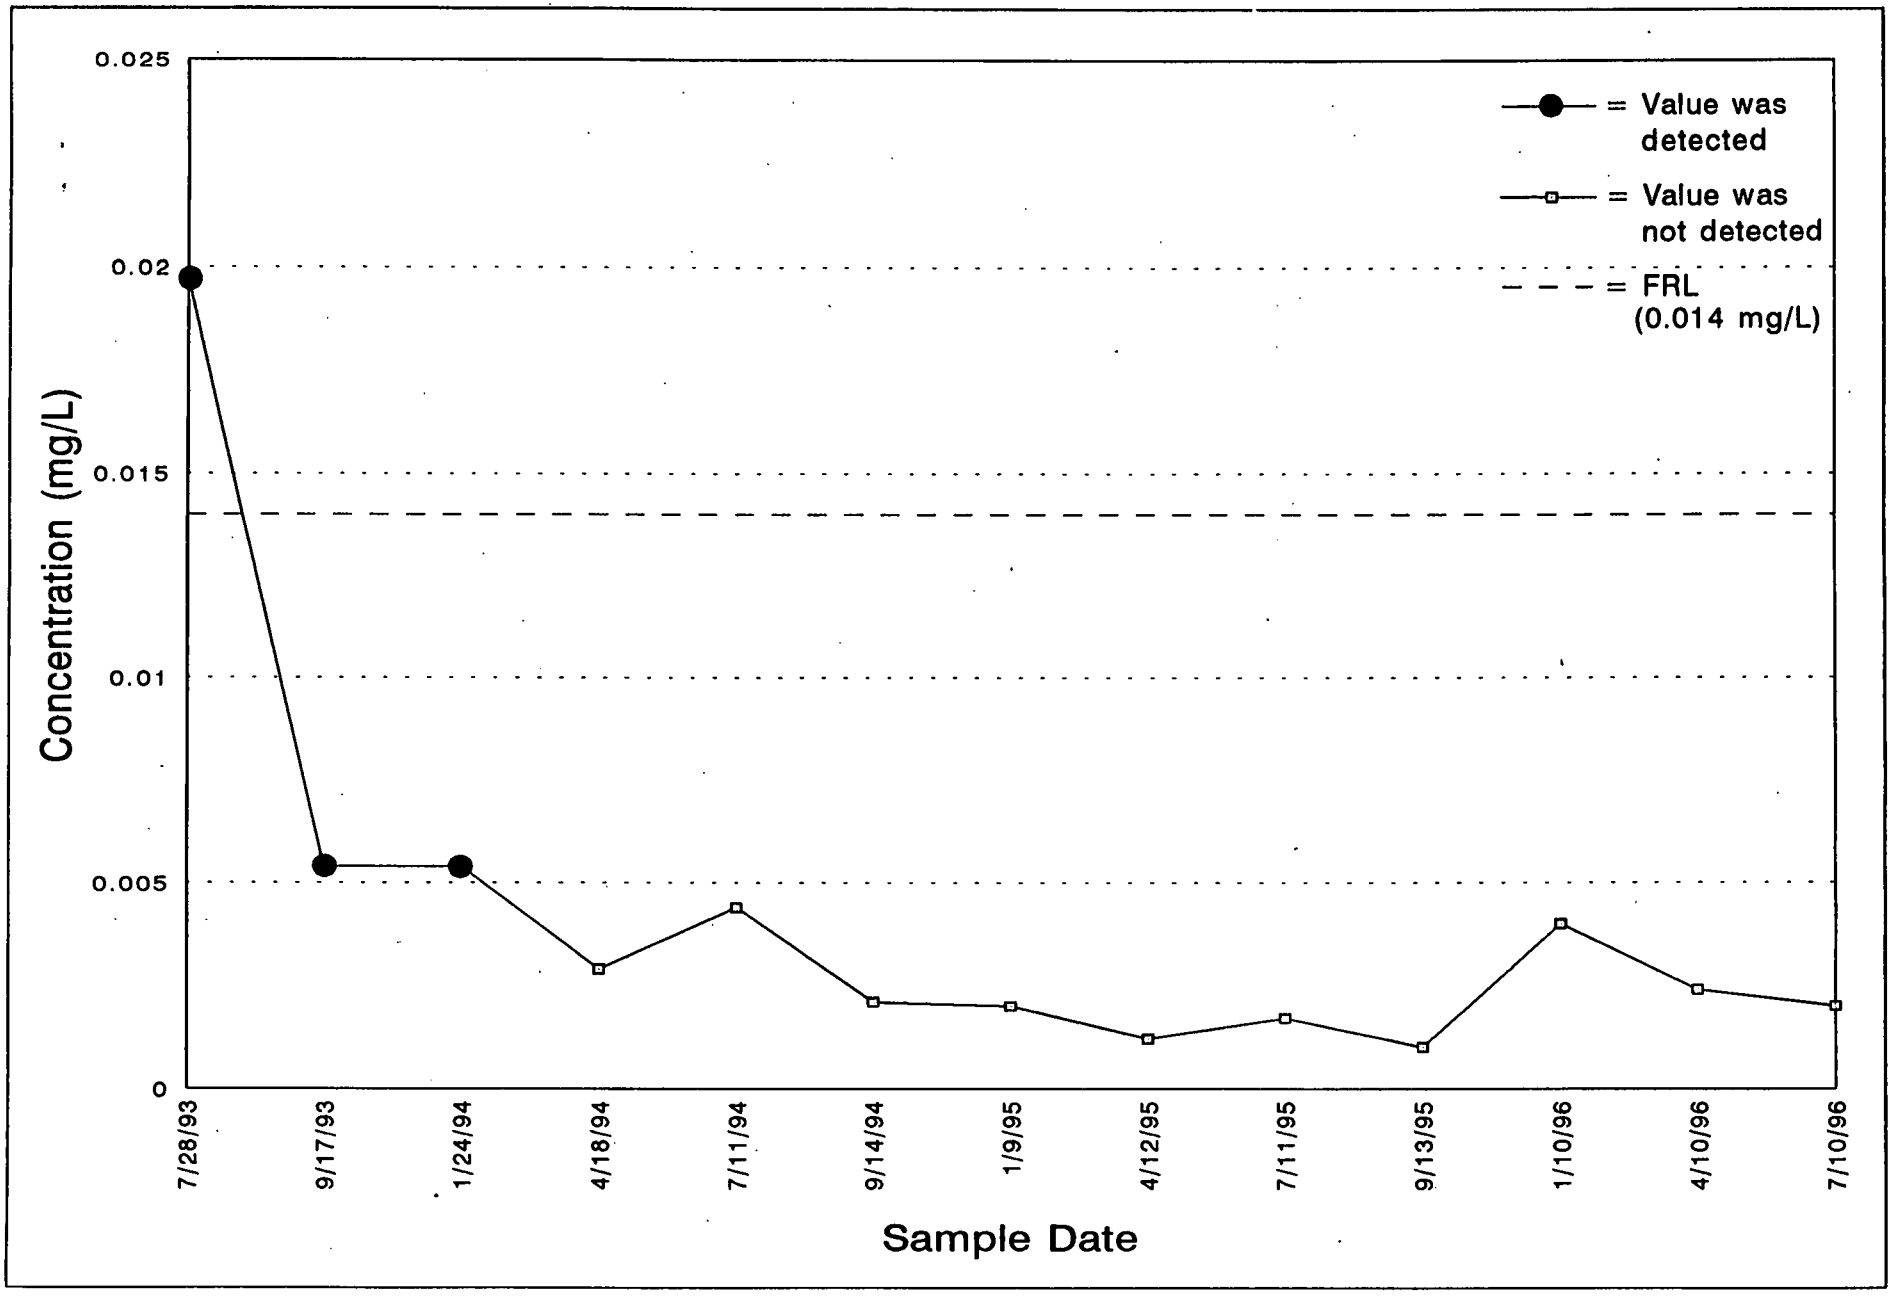

FIGURE A.3-20. CADMIUM CONCENTRATION VS. TIME, WELL 2733

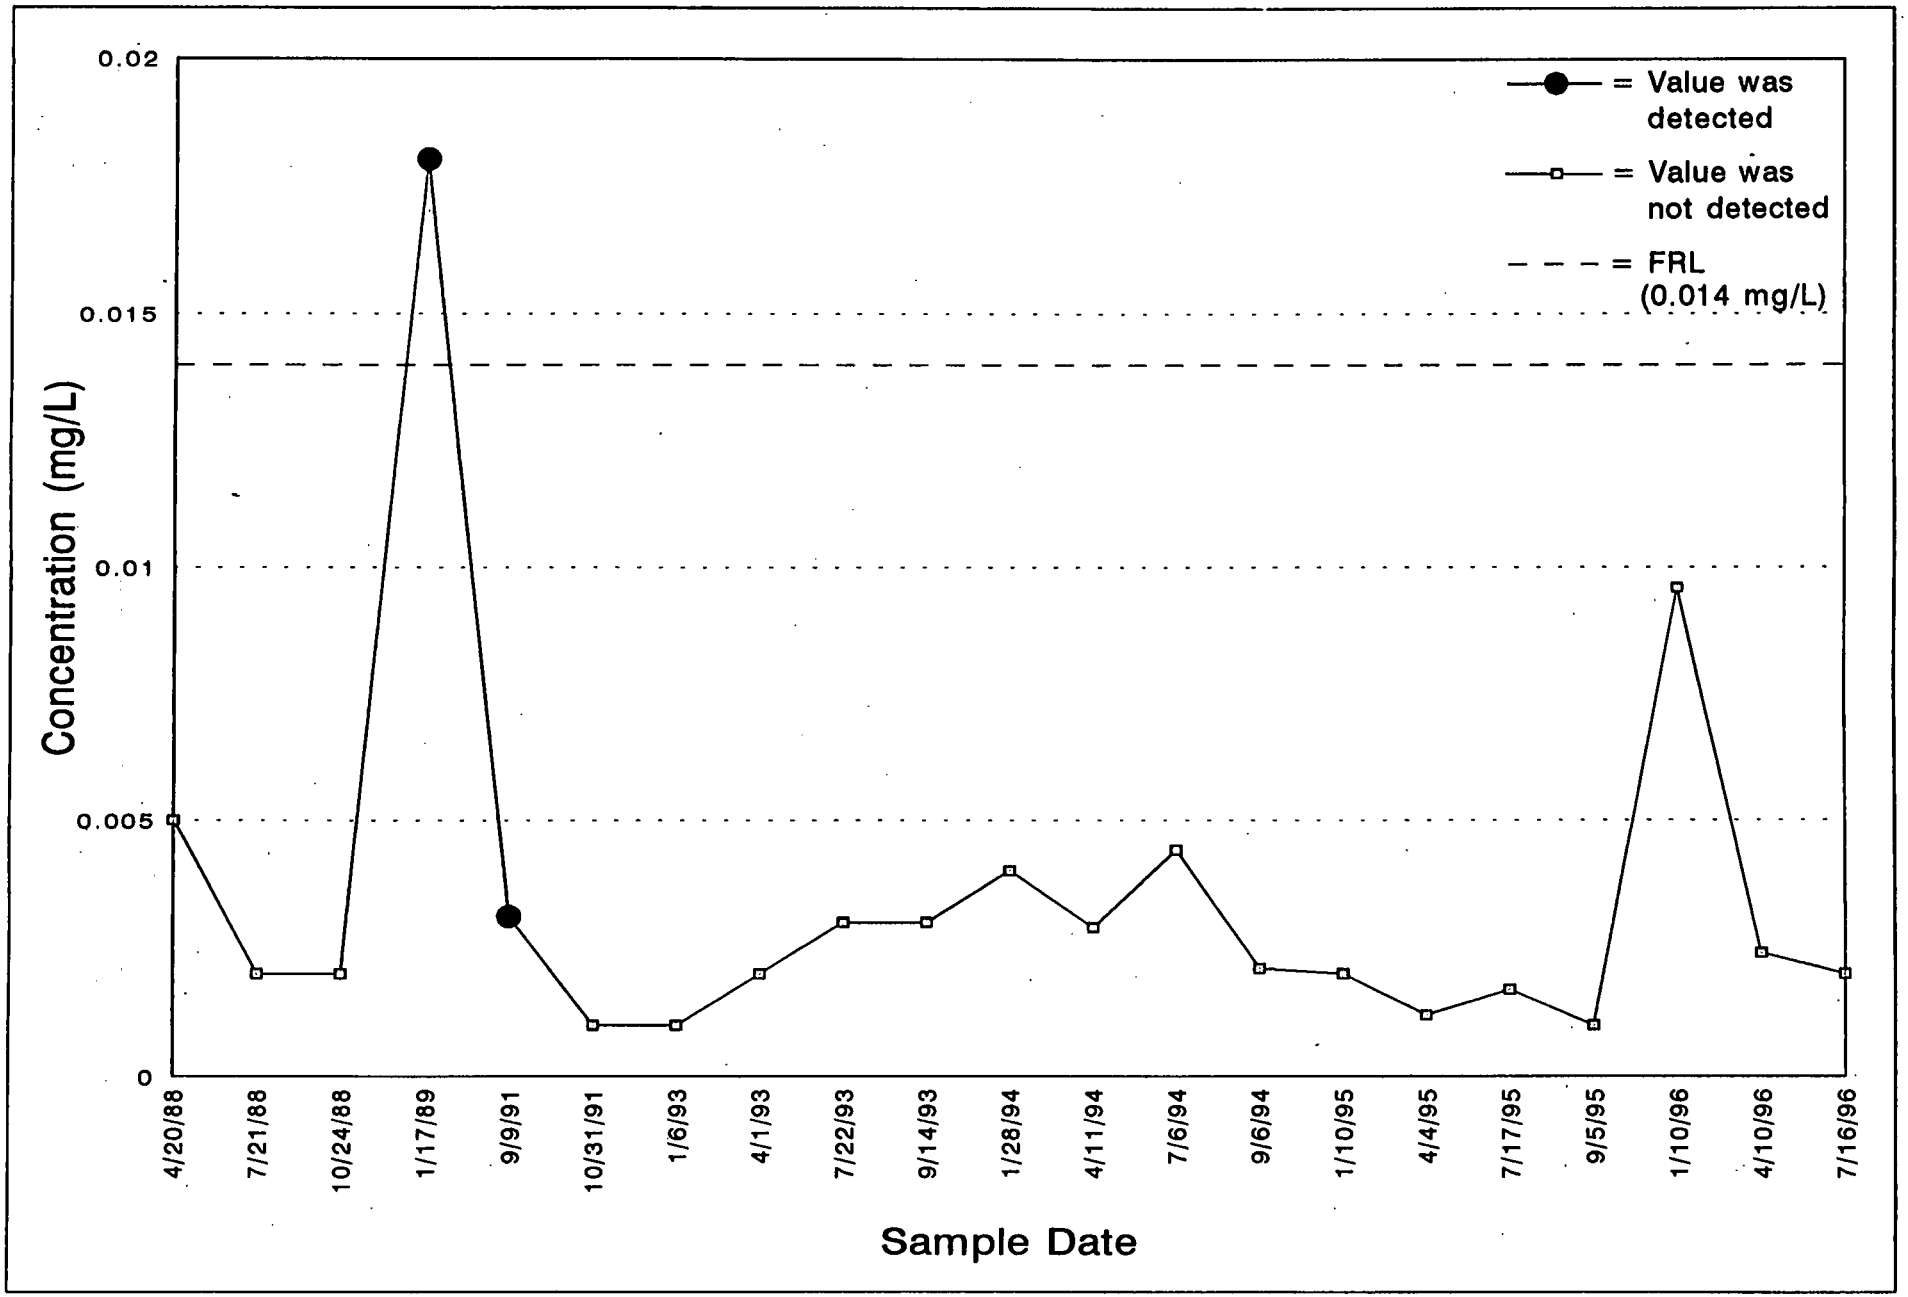

FIGURE A.3-21. CADMIUM CONCENTRATION VS. TIME, WELL 3067

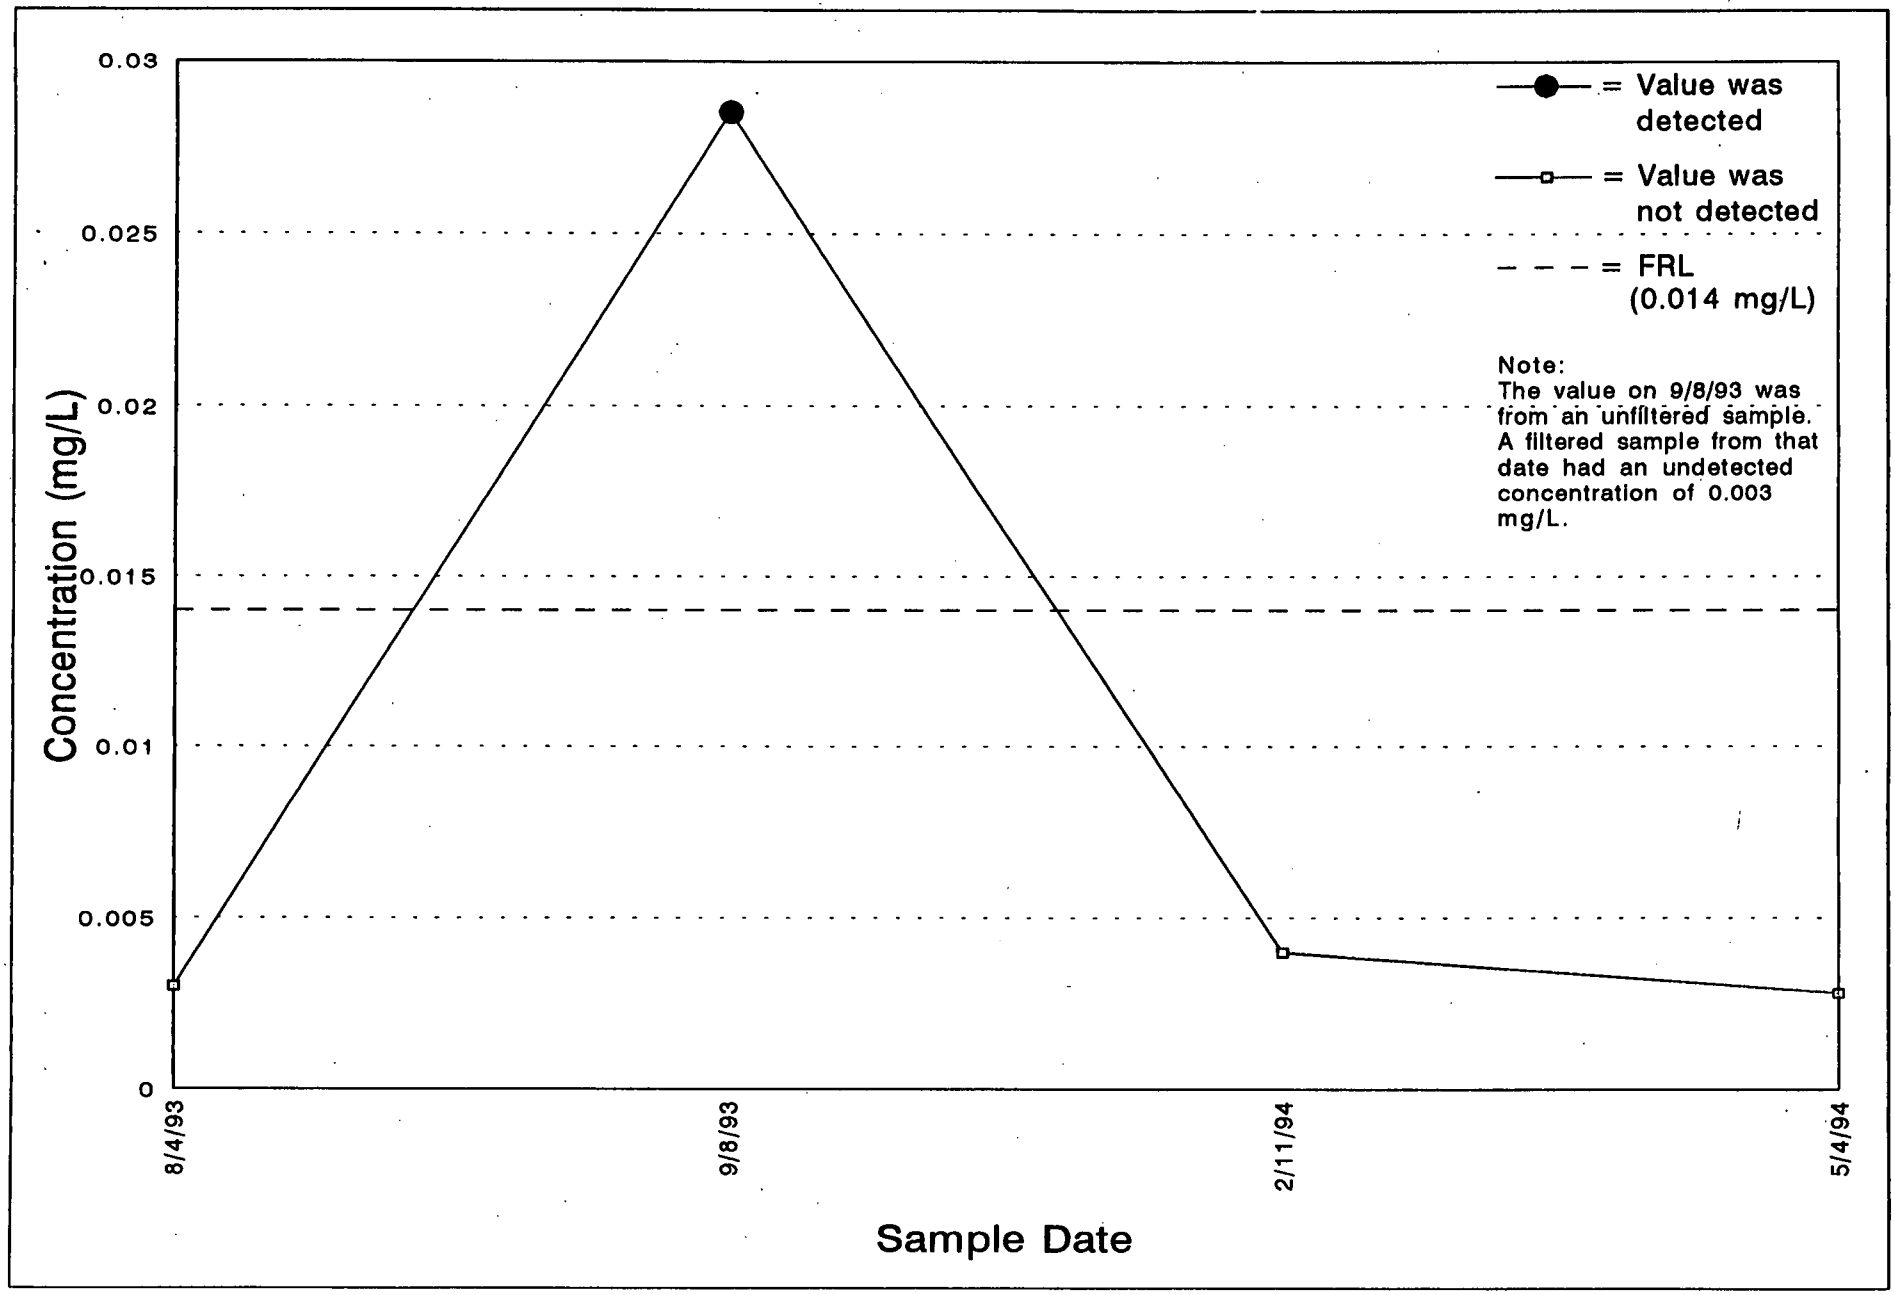

FIGURE A.3-22. CADMIUM CONCENTRATION VS. TIME, WELL 3898

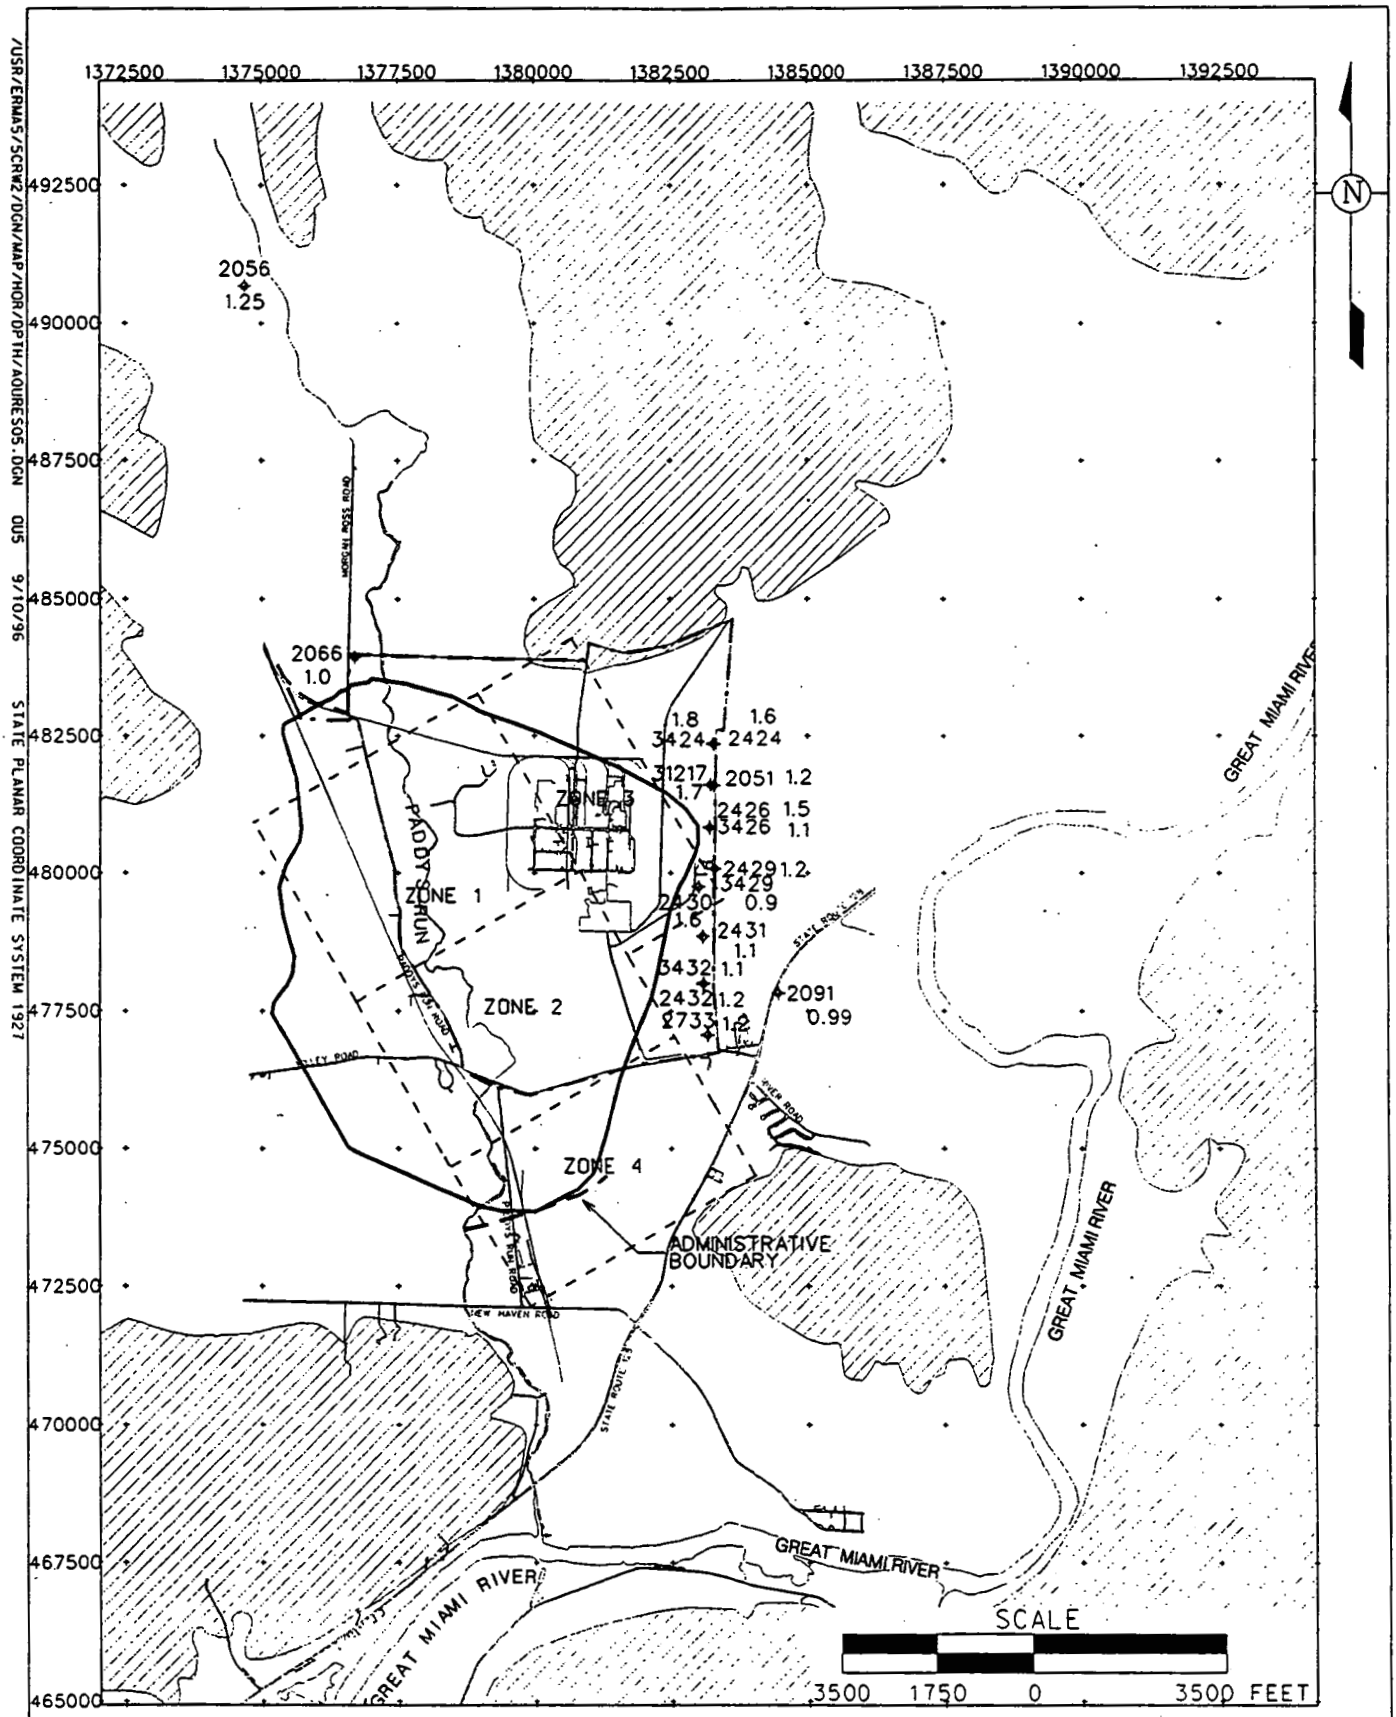

LEGEND:

FEMP BOUNDARY

2127 GROUNDWATER MONITORING WELL

1.8 FLUORIDE (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-23. FRL EXCEEDENCES FOR FLUORIDE LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

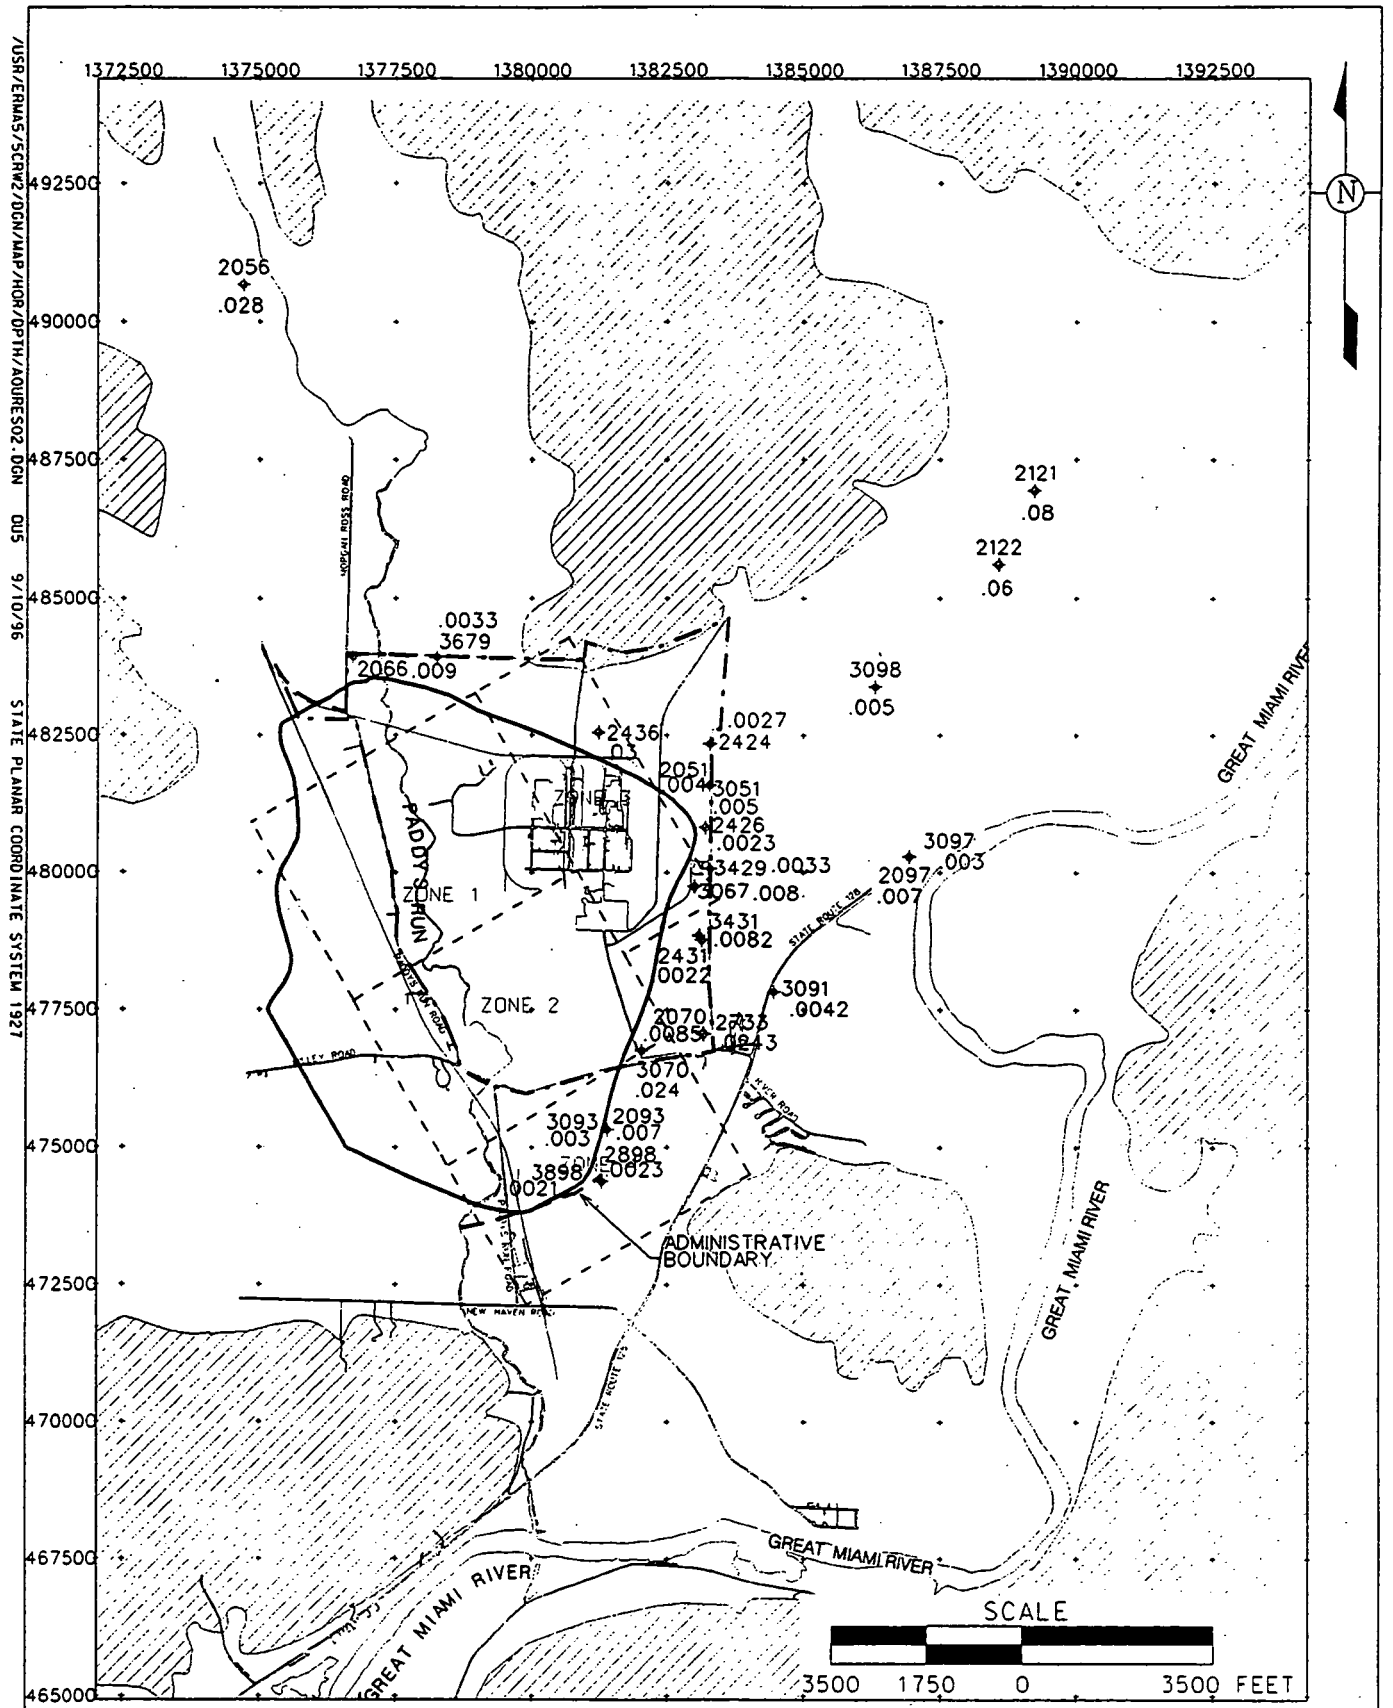

LEGEND:

— · — · — FEMP BOUNDARY

2127 ✦ GROUNDWATER MONITORING WELL

12.8 LEAD (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-24. FRL EXCEEDENCES FOR LEAD LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

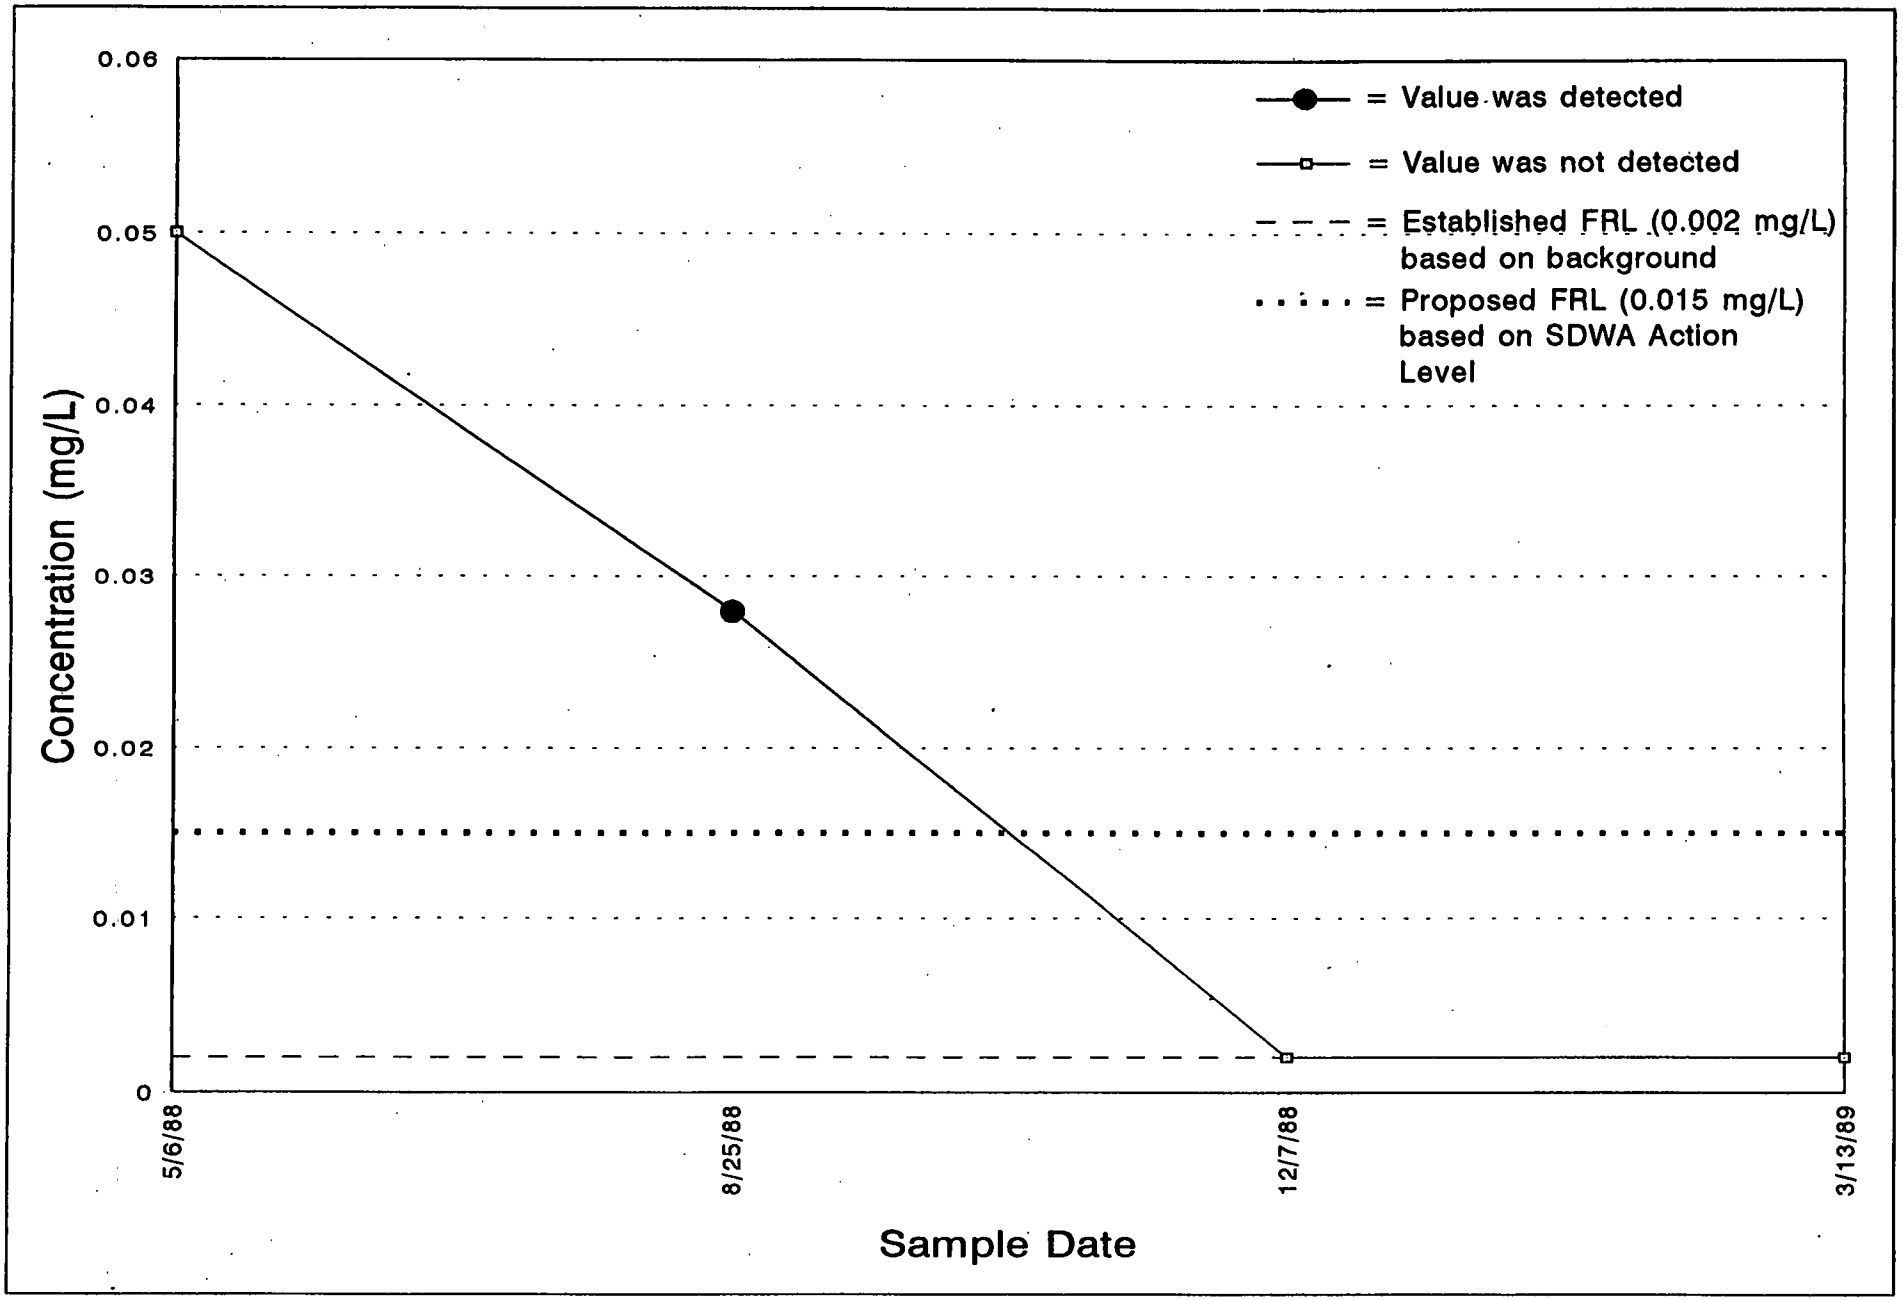

FIGURE A.3-25. LEAD CONCENTRATION VS. TIME, WELL 2056

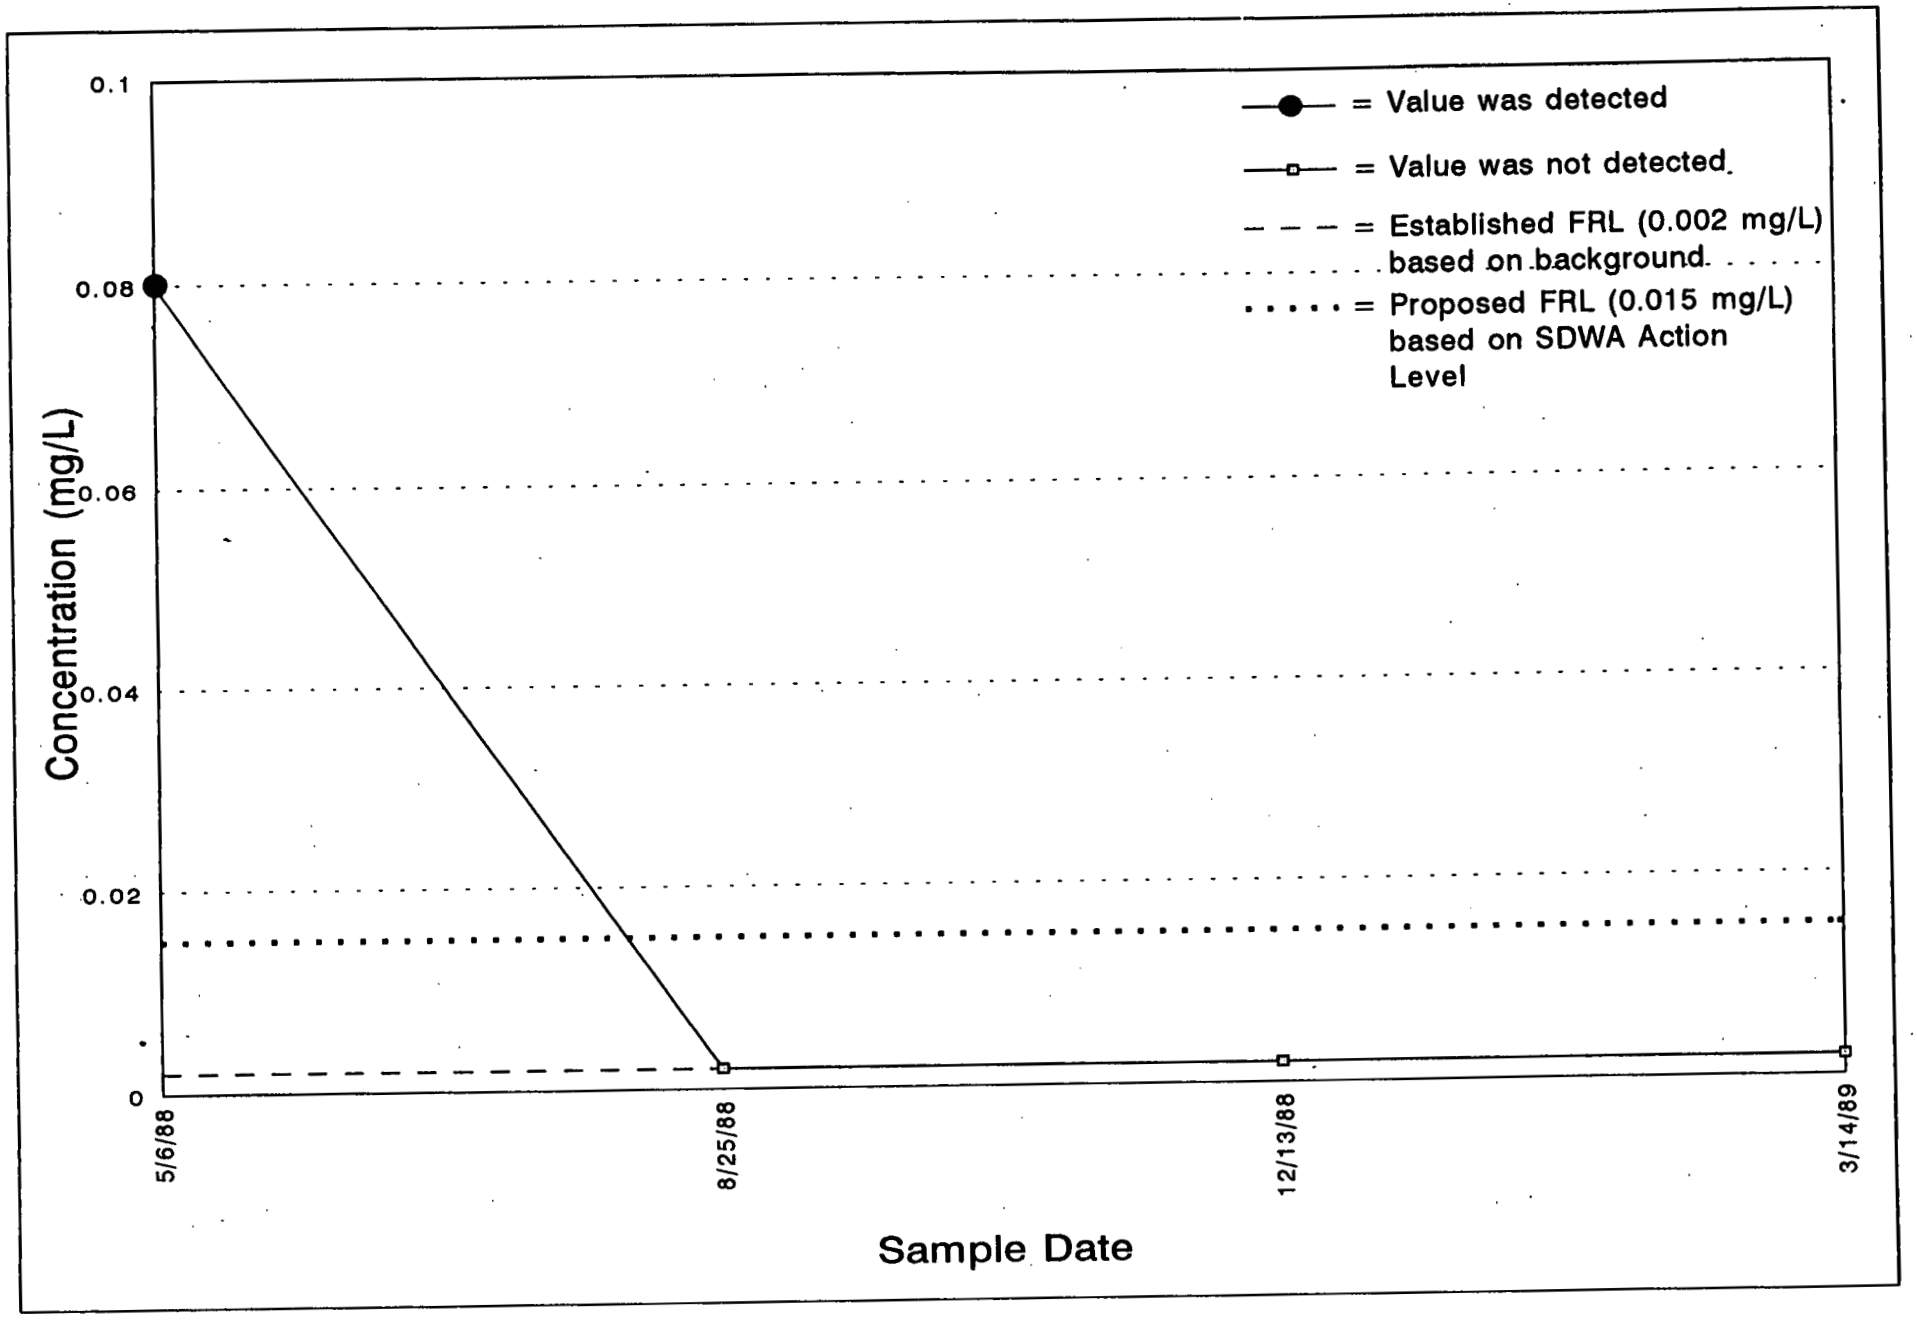

FIGURE A.3-26. LEAD CONCENTRATION VS. TIME, WELL 2121

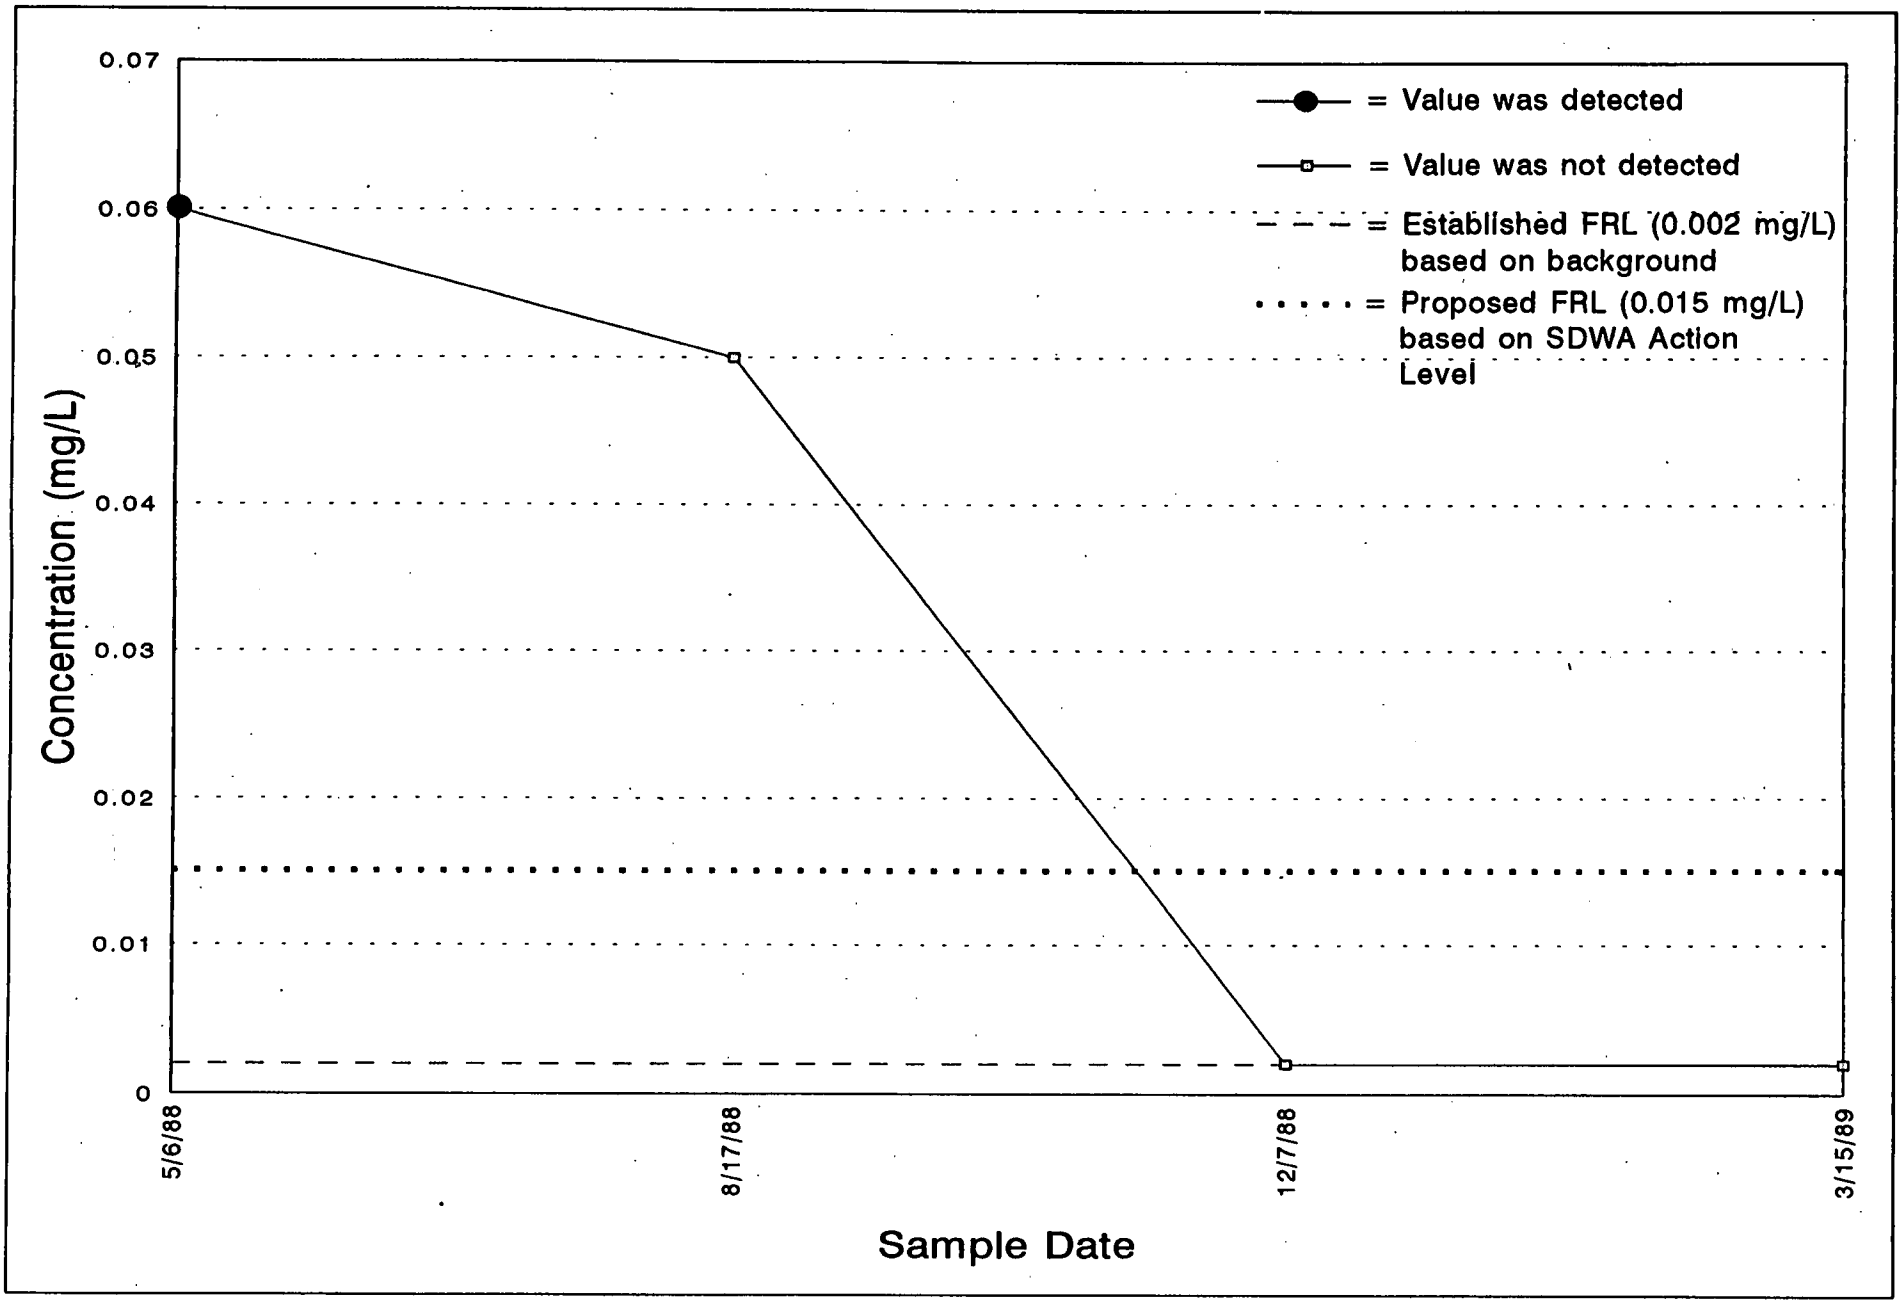

FIGURE A.3-27. LEAD CONCENTRATION VS. TIME, WELL 2122

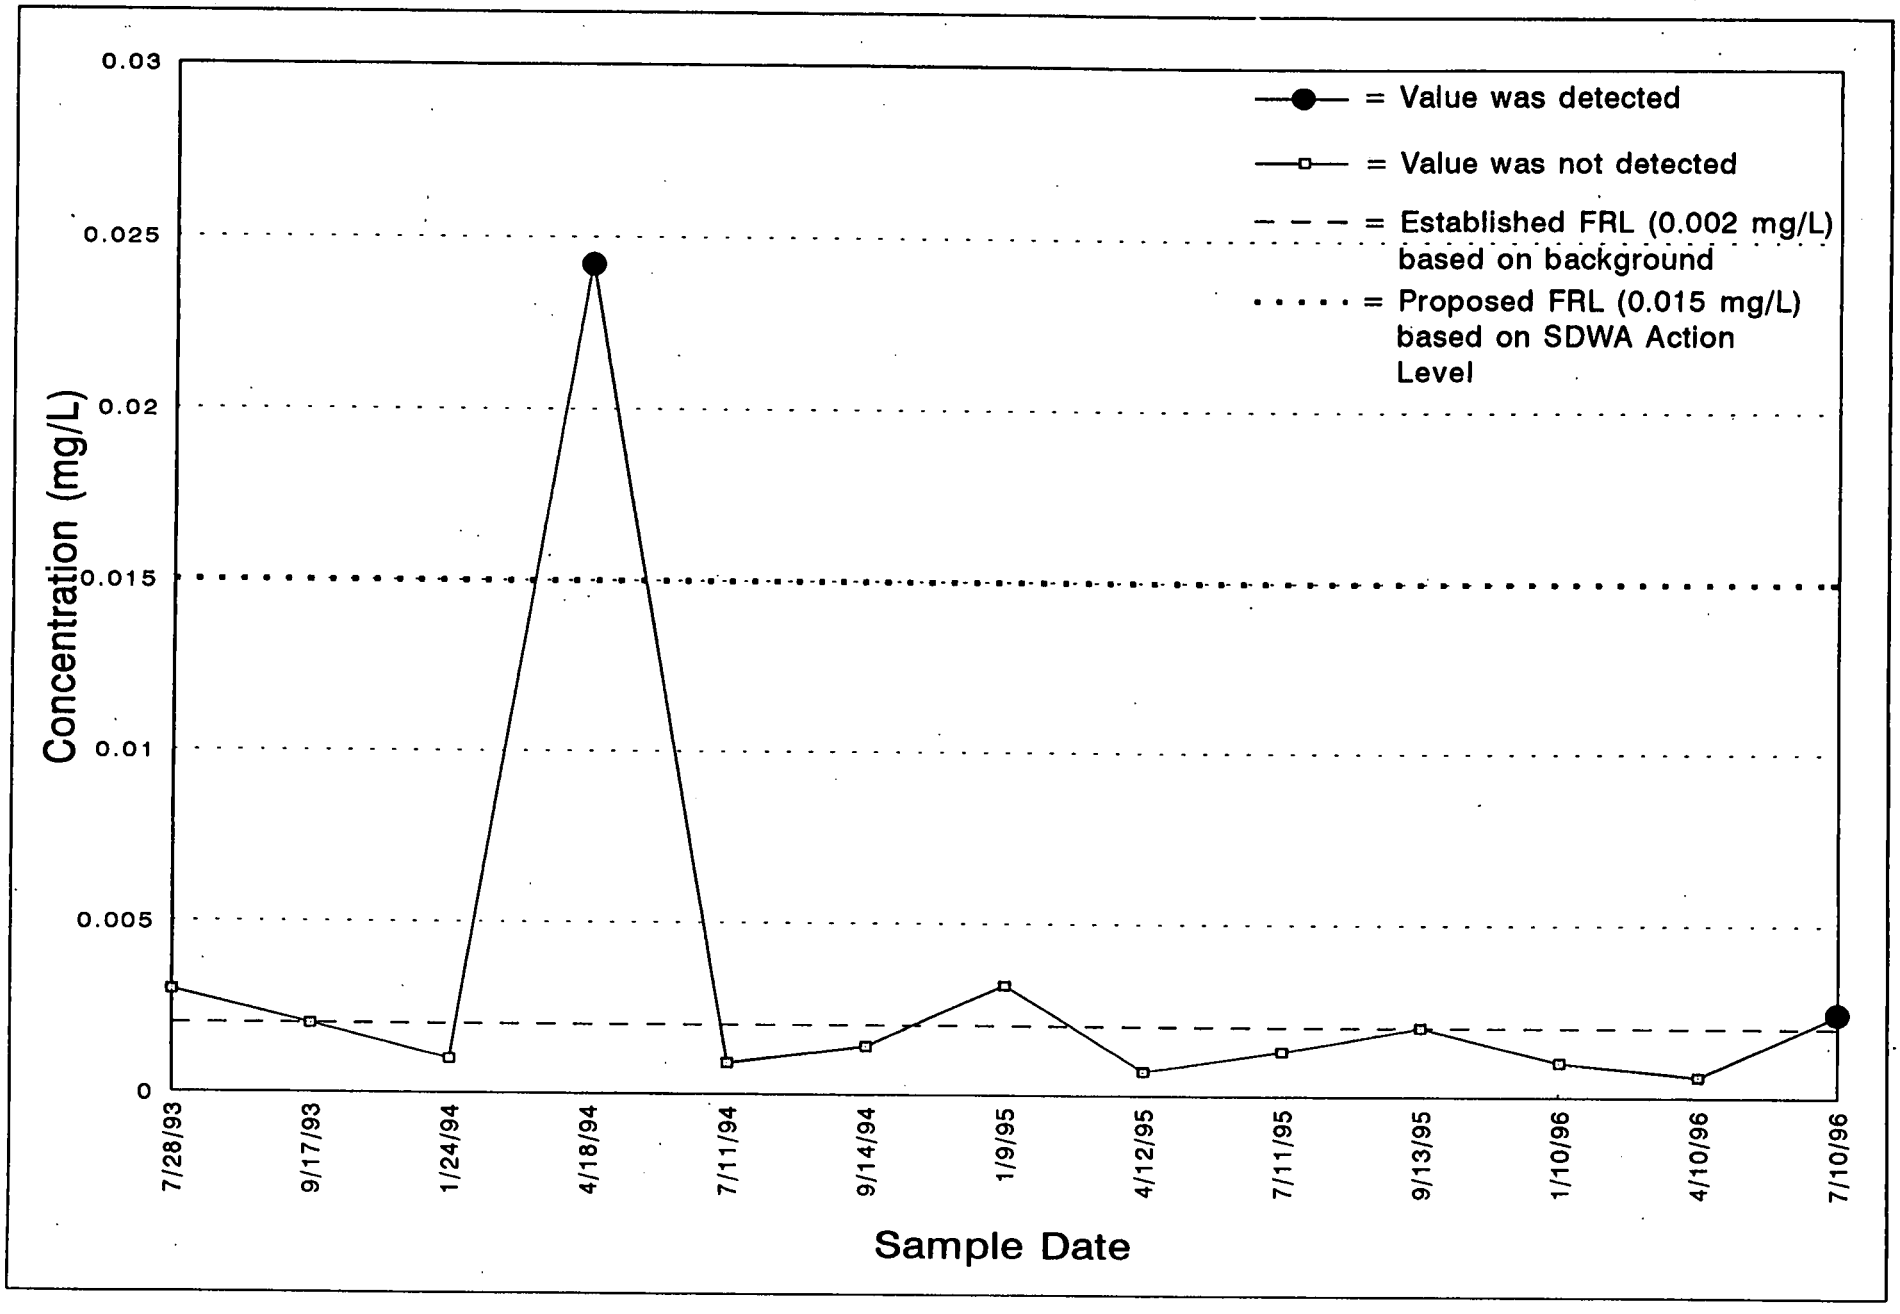

FIGURE A.3-28. LEAD CONCENTRATION VS. TIME, WELL 2733

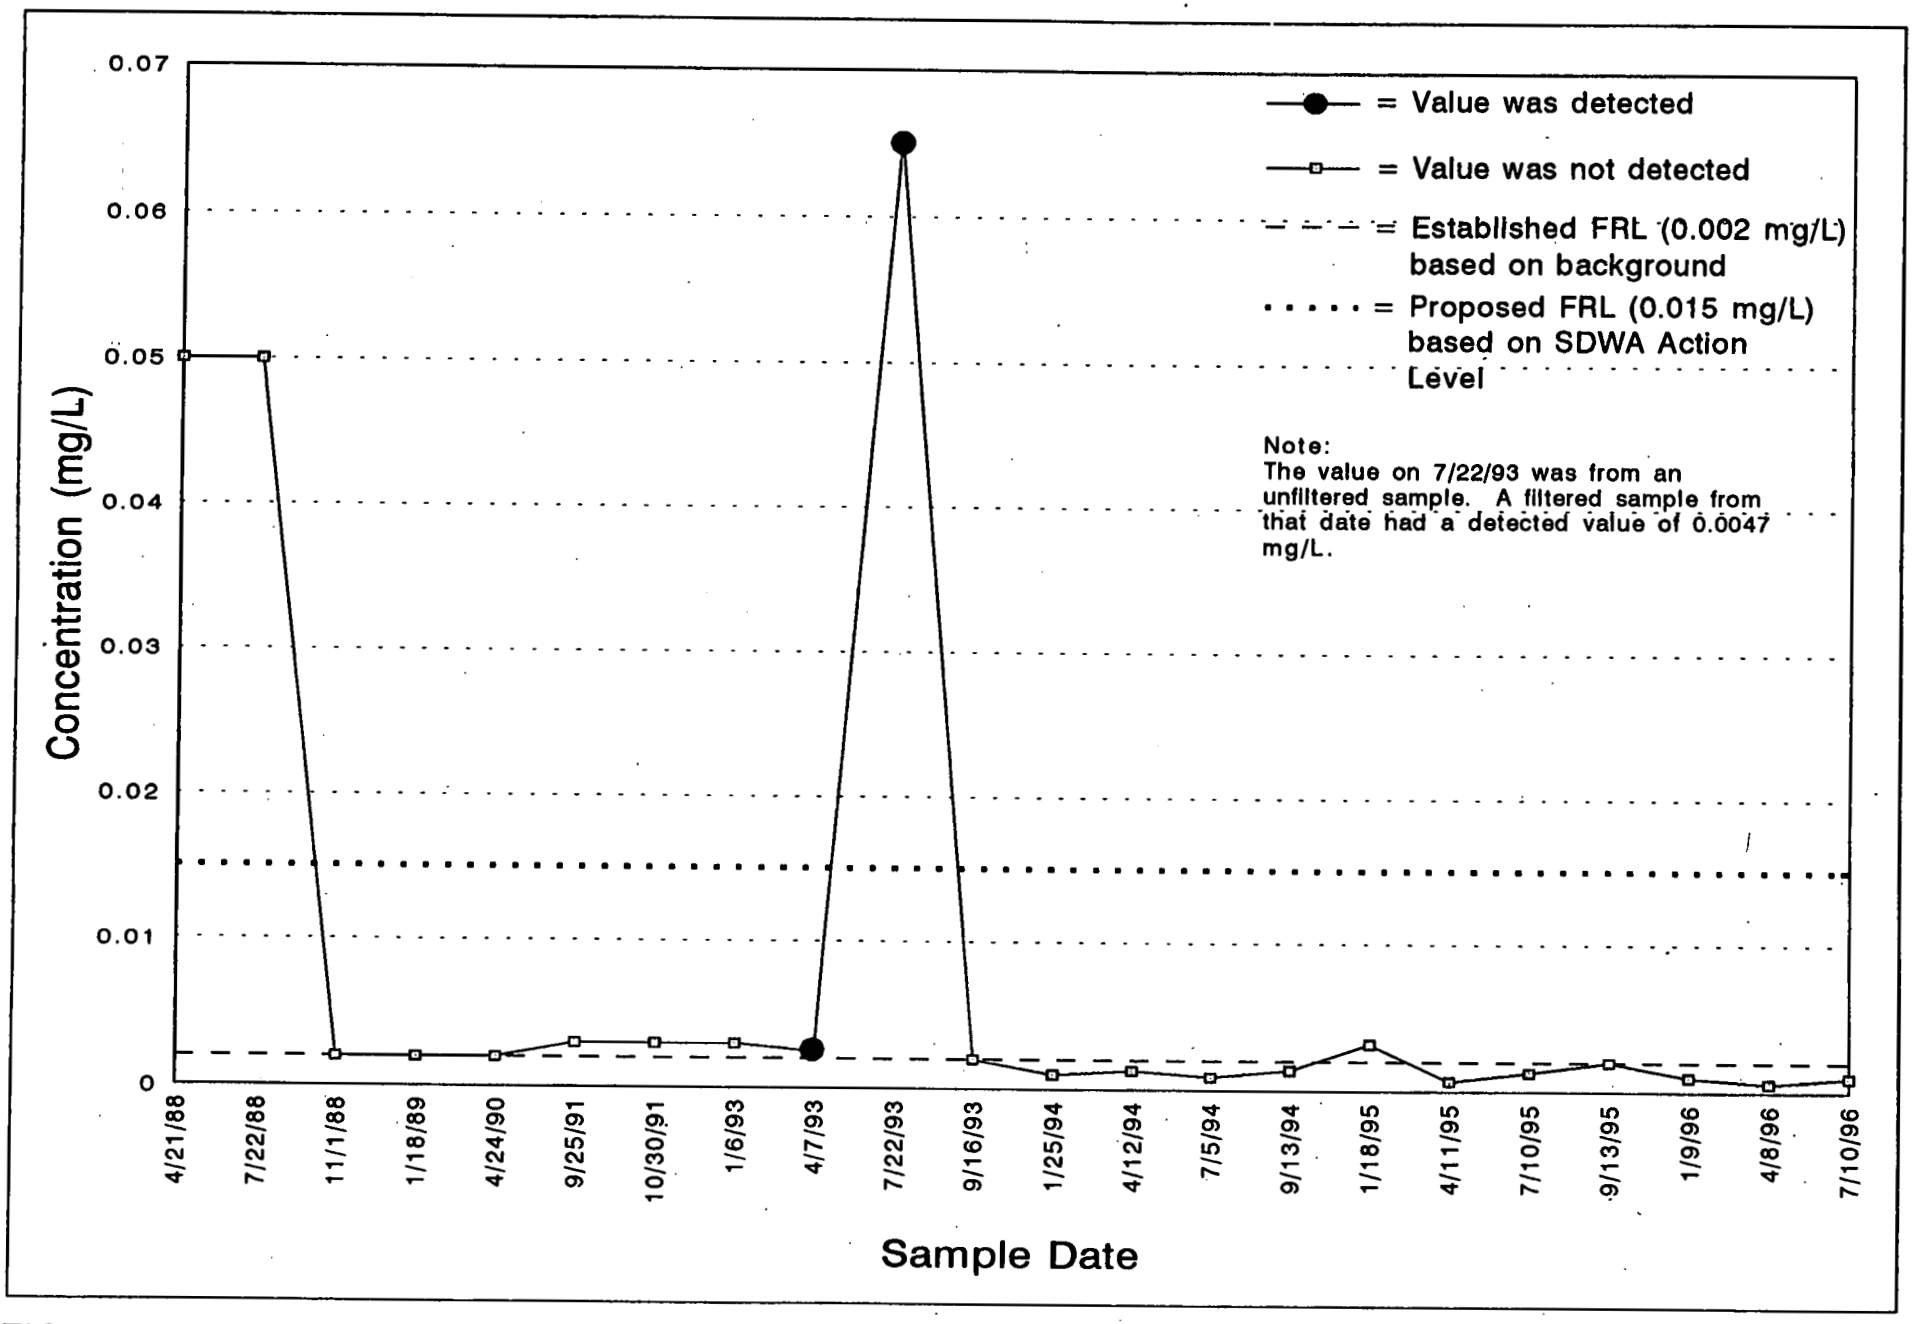

FIGURE A.3-29. LEAD CONCENTRATION VS. TIME, WELL 3070

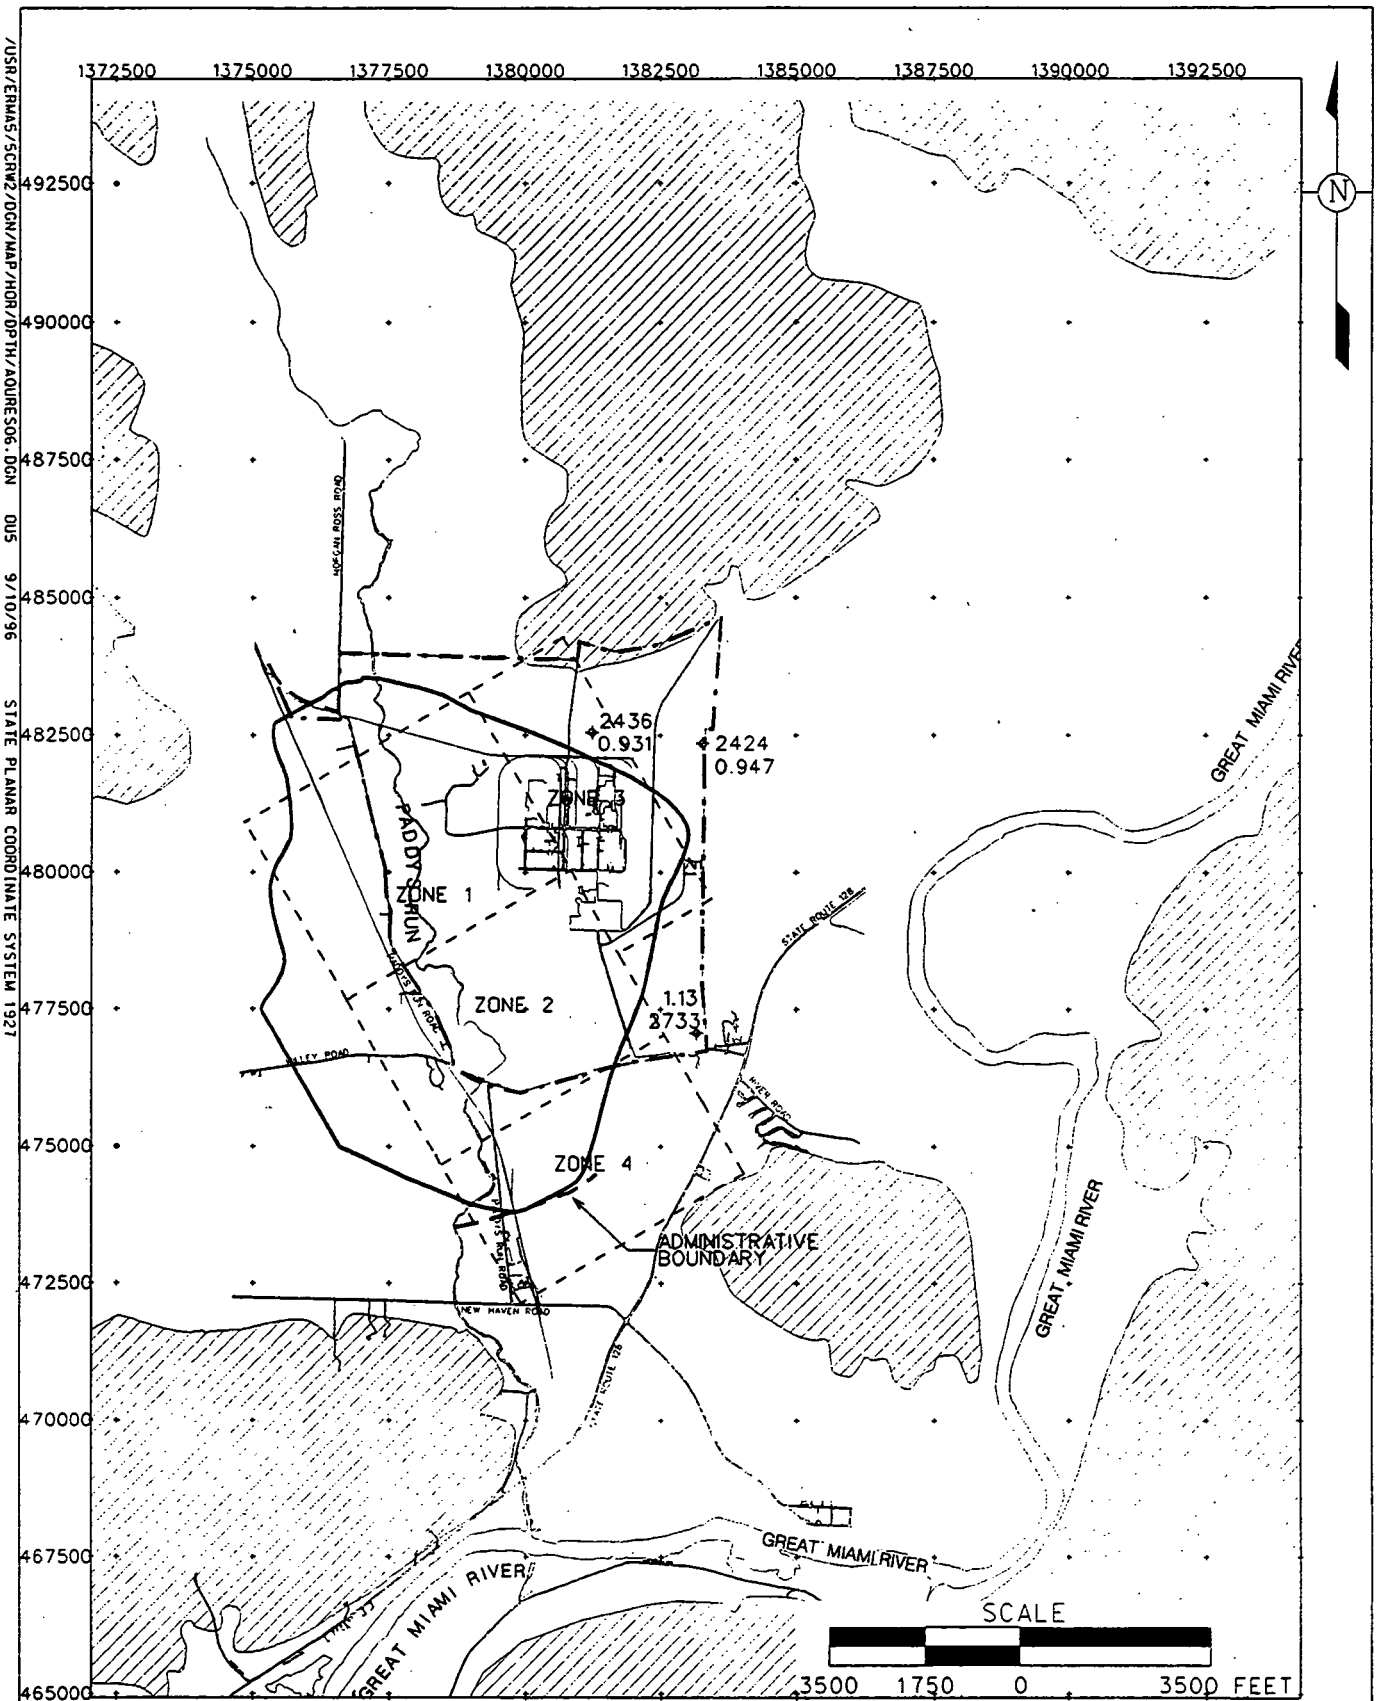

LEGEND:

FEMP BOUNDARY

2127 GROUNDWATER MONITORING WELL

1.8 MANGANESE (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-30. FRL EXCEEDENCES FOR MANGANESE LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

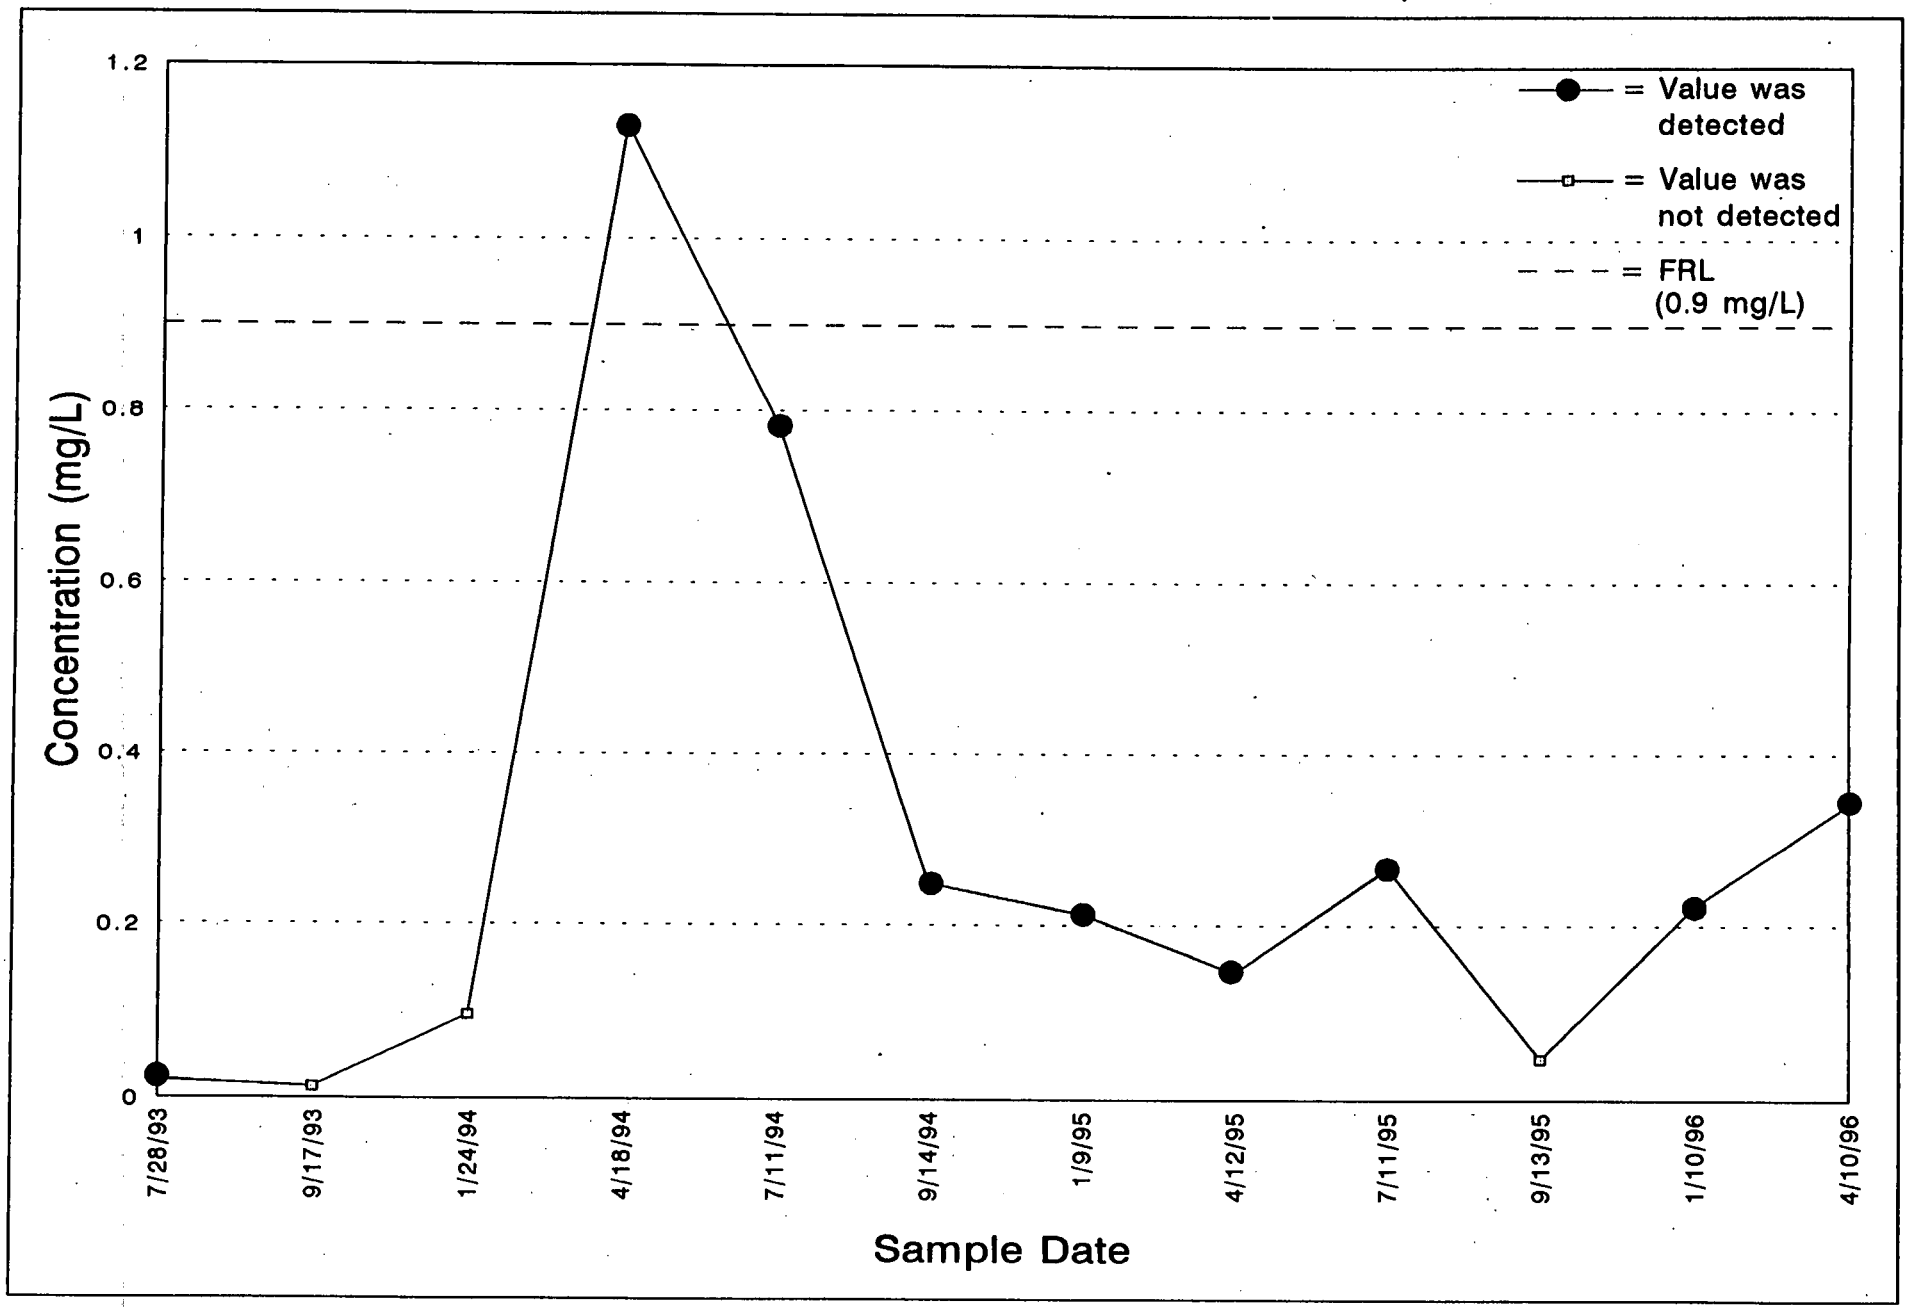

FIGURE A.3-31. MANGANESE CONCENTRATION VS. TIME, WELL 2733

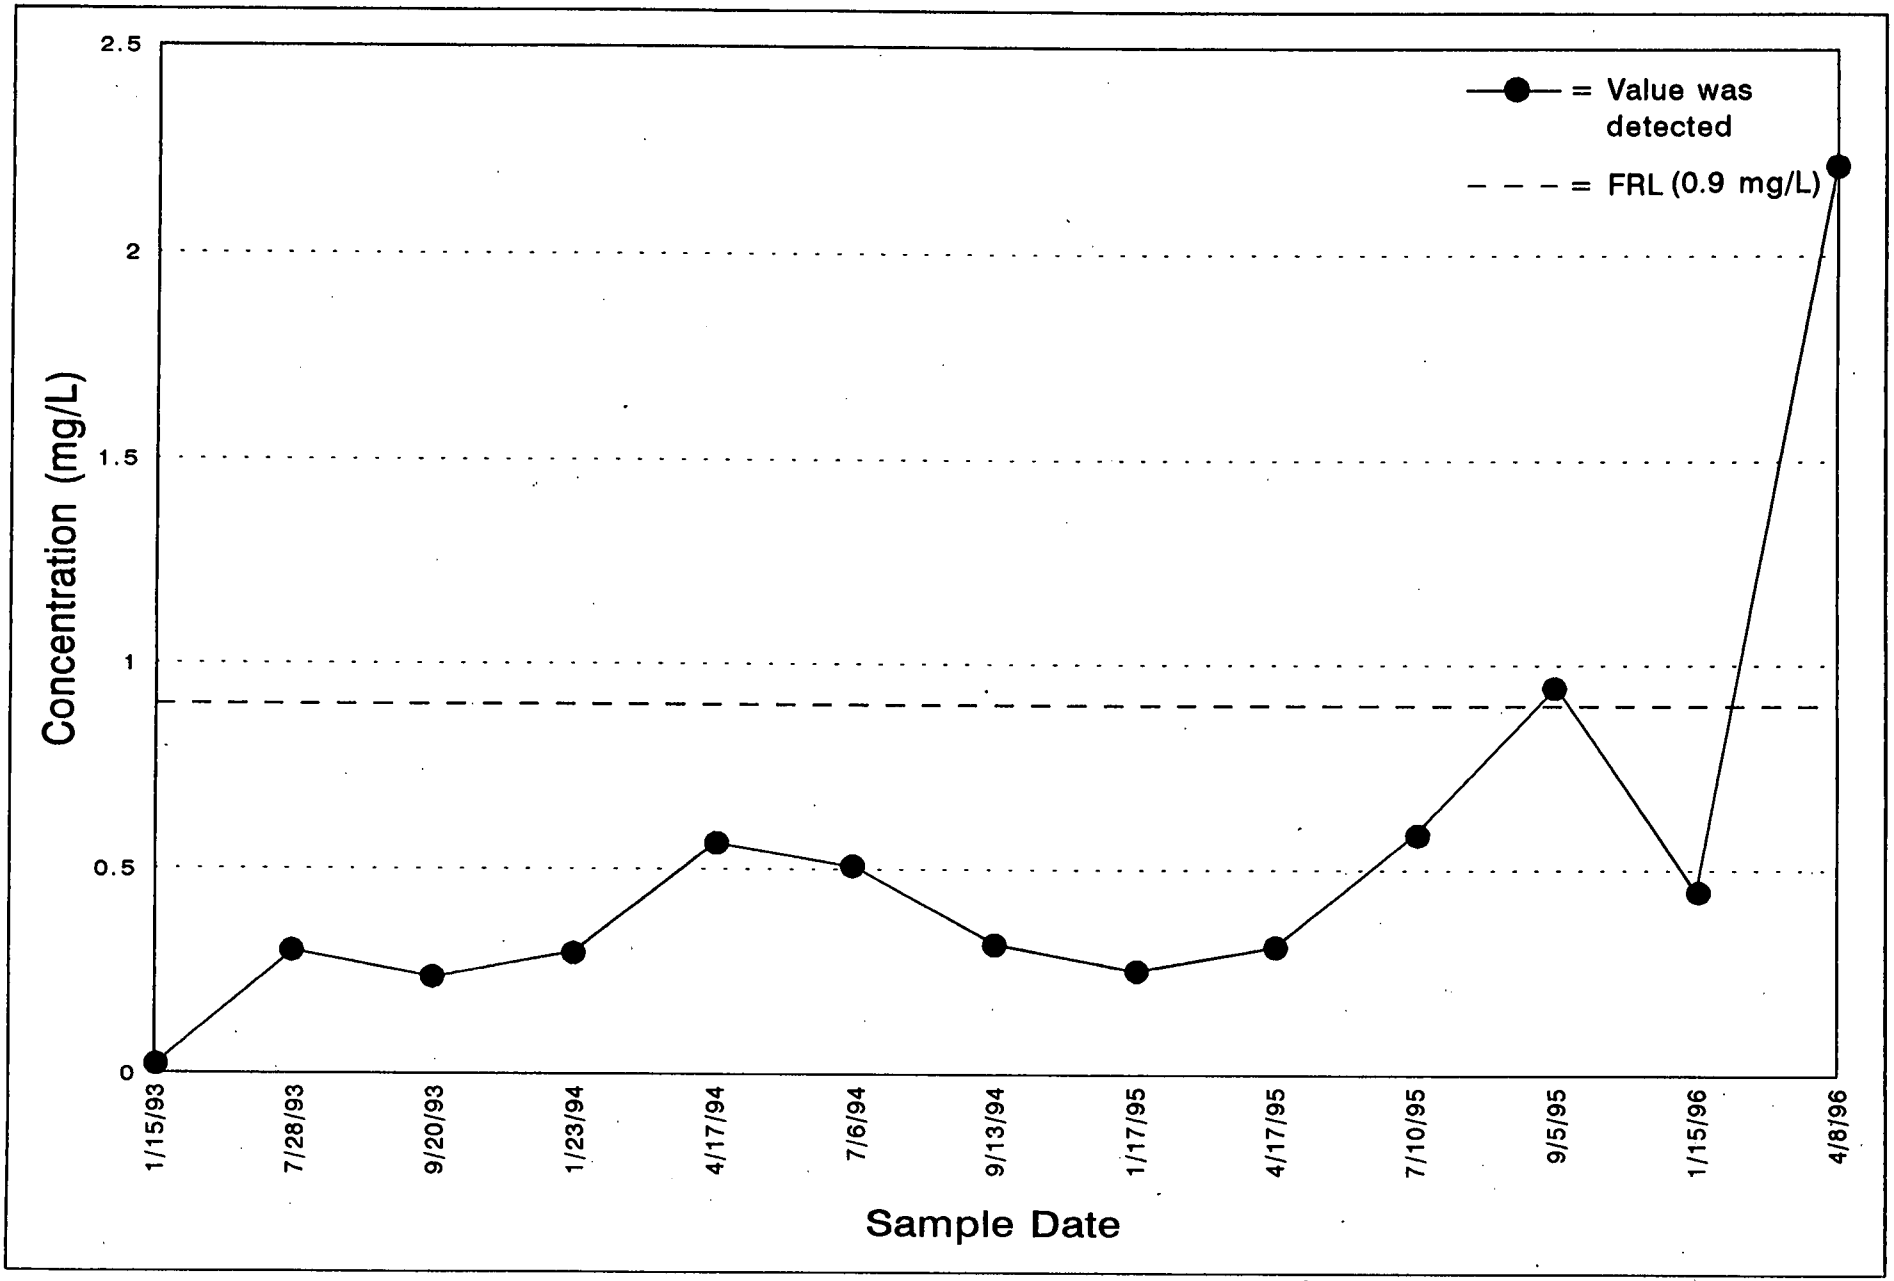

FIGURE A.3-32. MANGANESE CONCENTRATION VS. TIME, WELL 2424

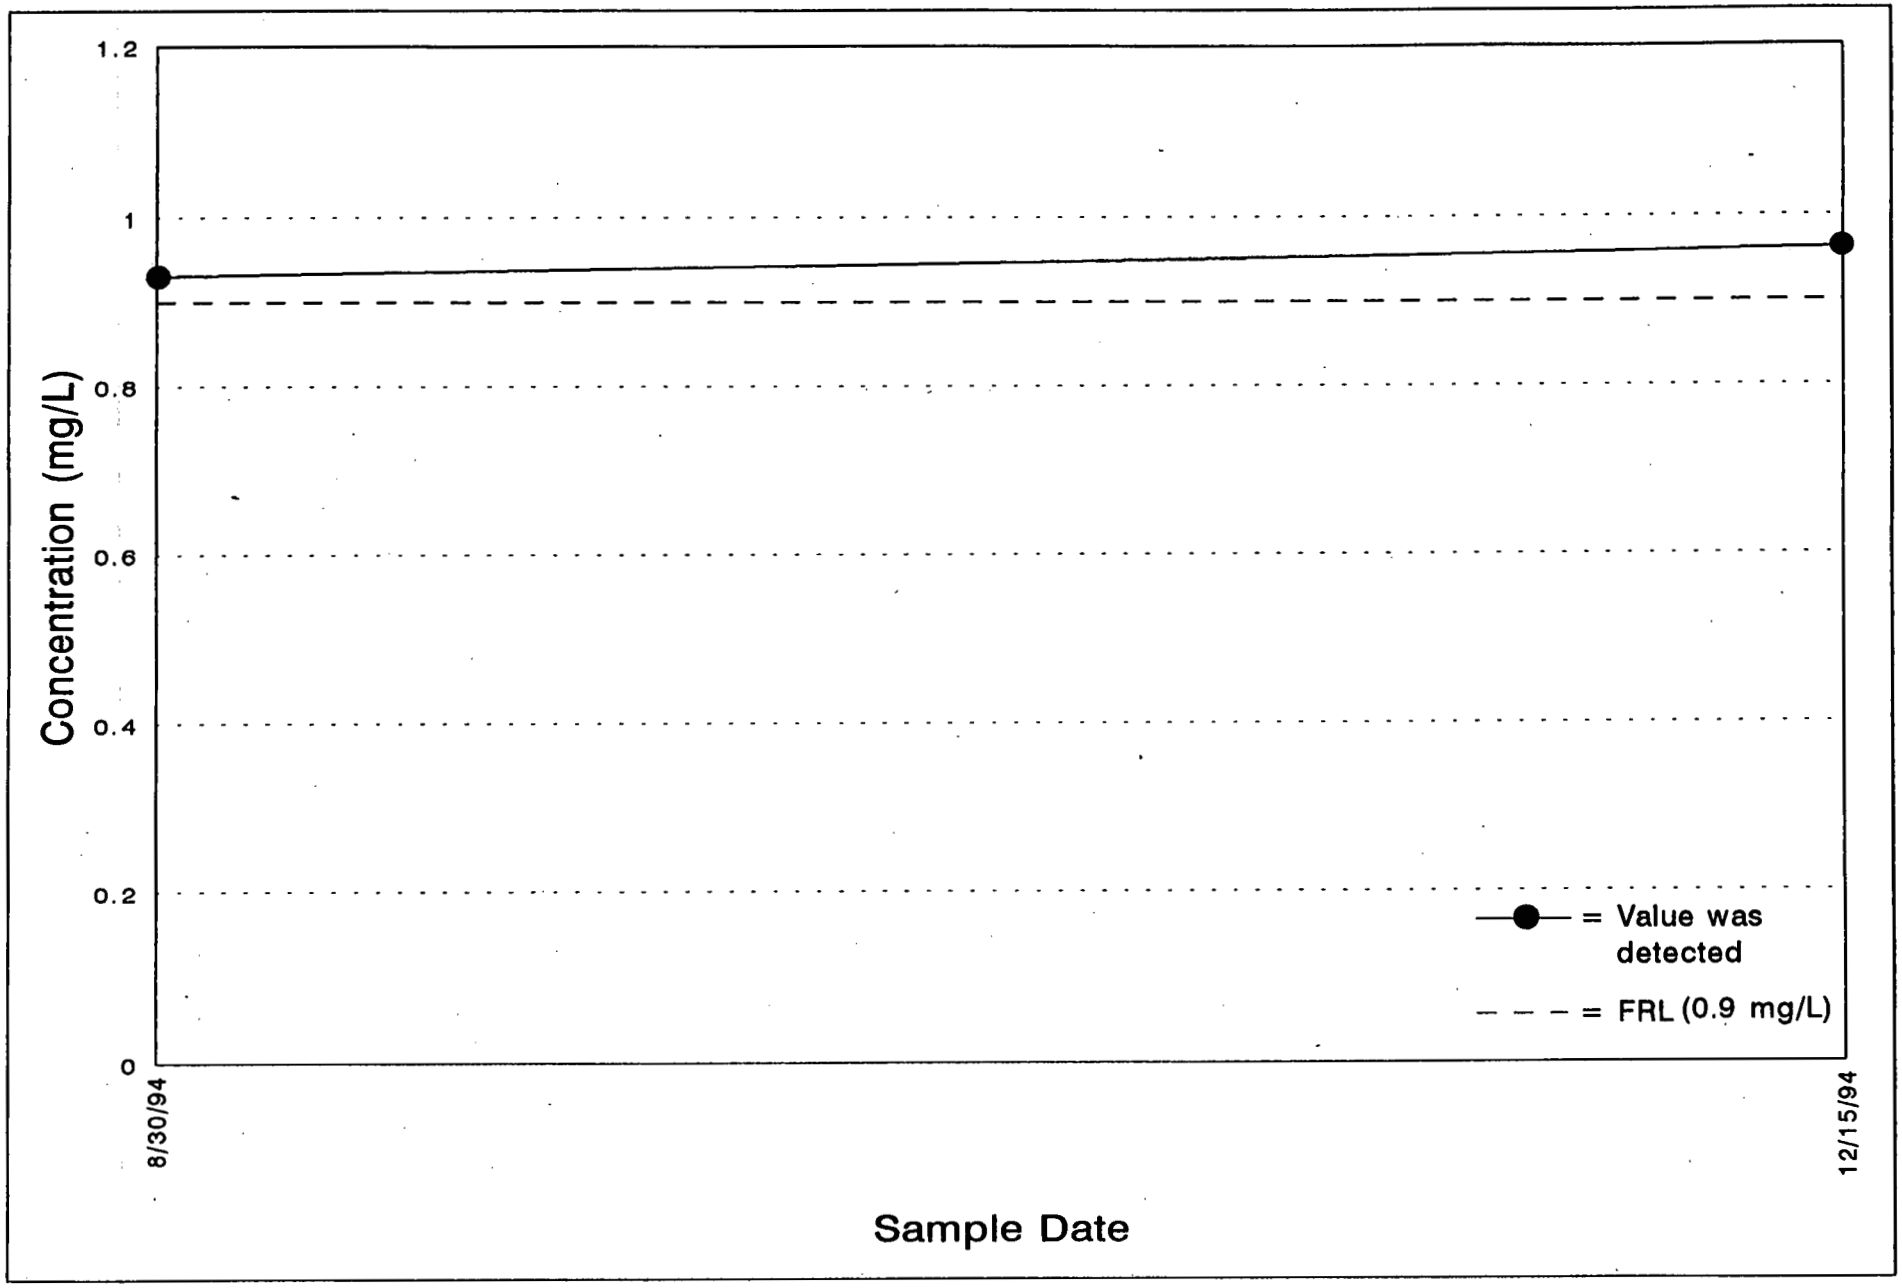

FIGURE A.3-33. MANGANESE CONCENTRATION VS. TIME, WELL 2436

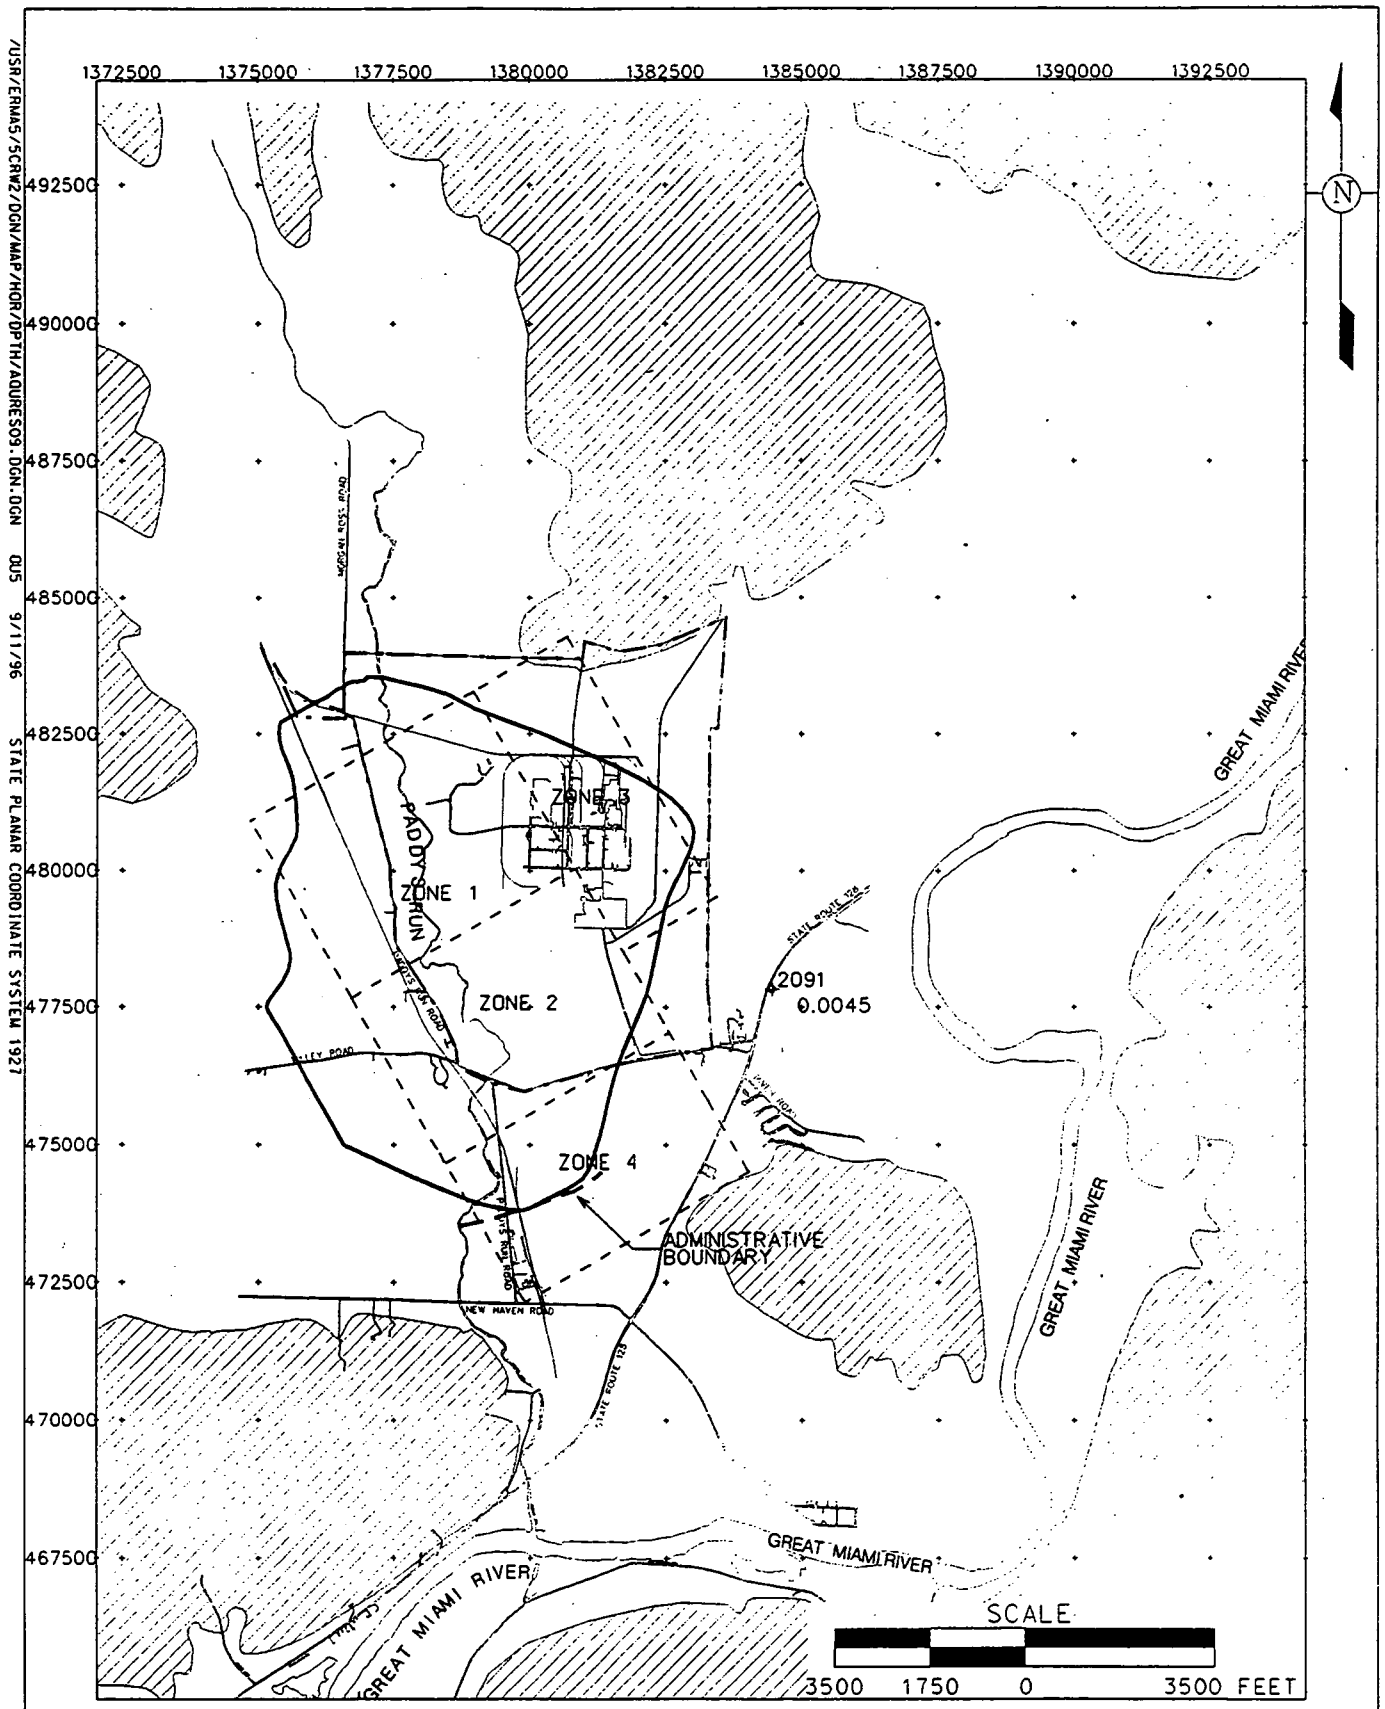

LEGEND:

- FEMP BOUNDARY
- 2127 GROUNDWATER MONITORING WELL
- .004 MERCURY (MAXIMUM VALUE)
- RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-34. FRL EXCEEDENCES FOR MERCURY LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

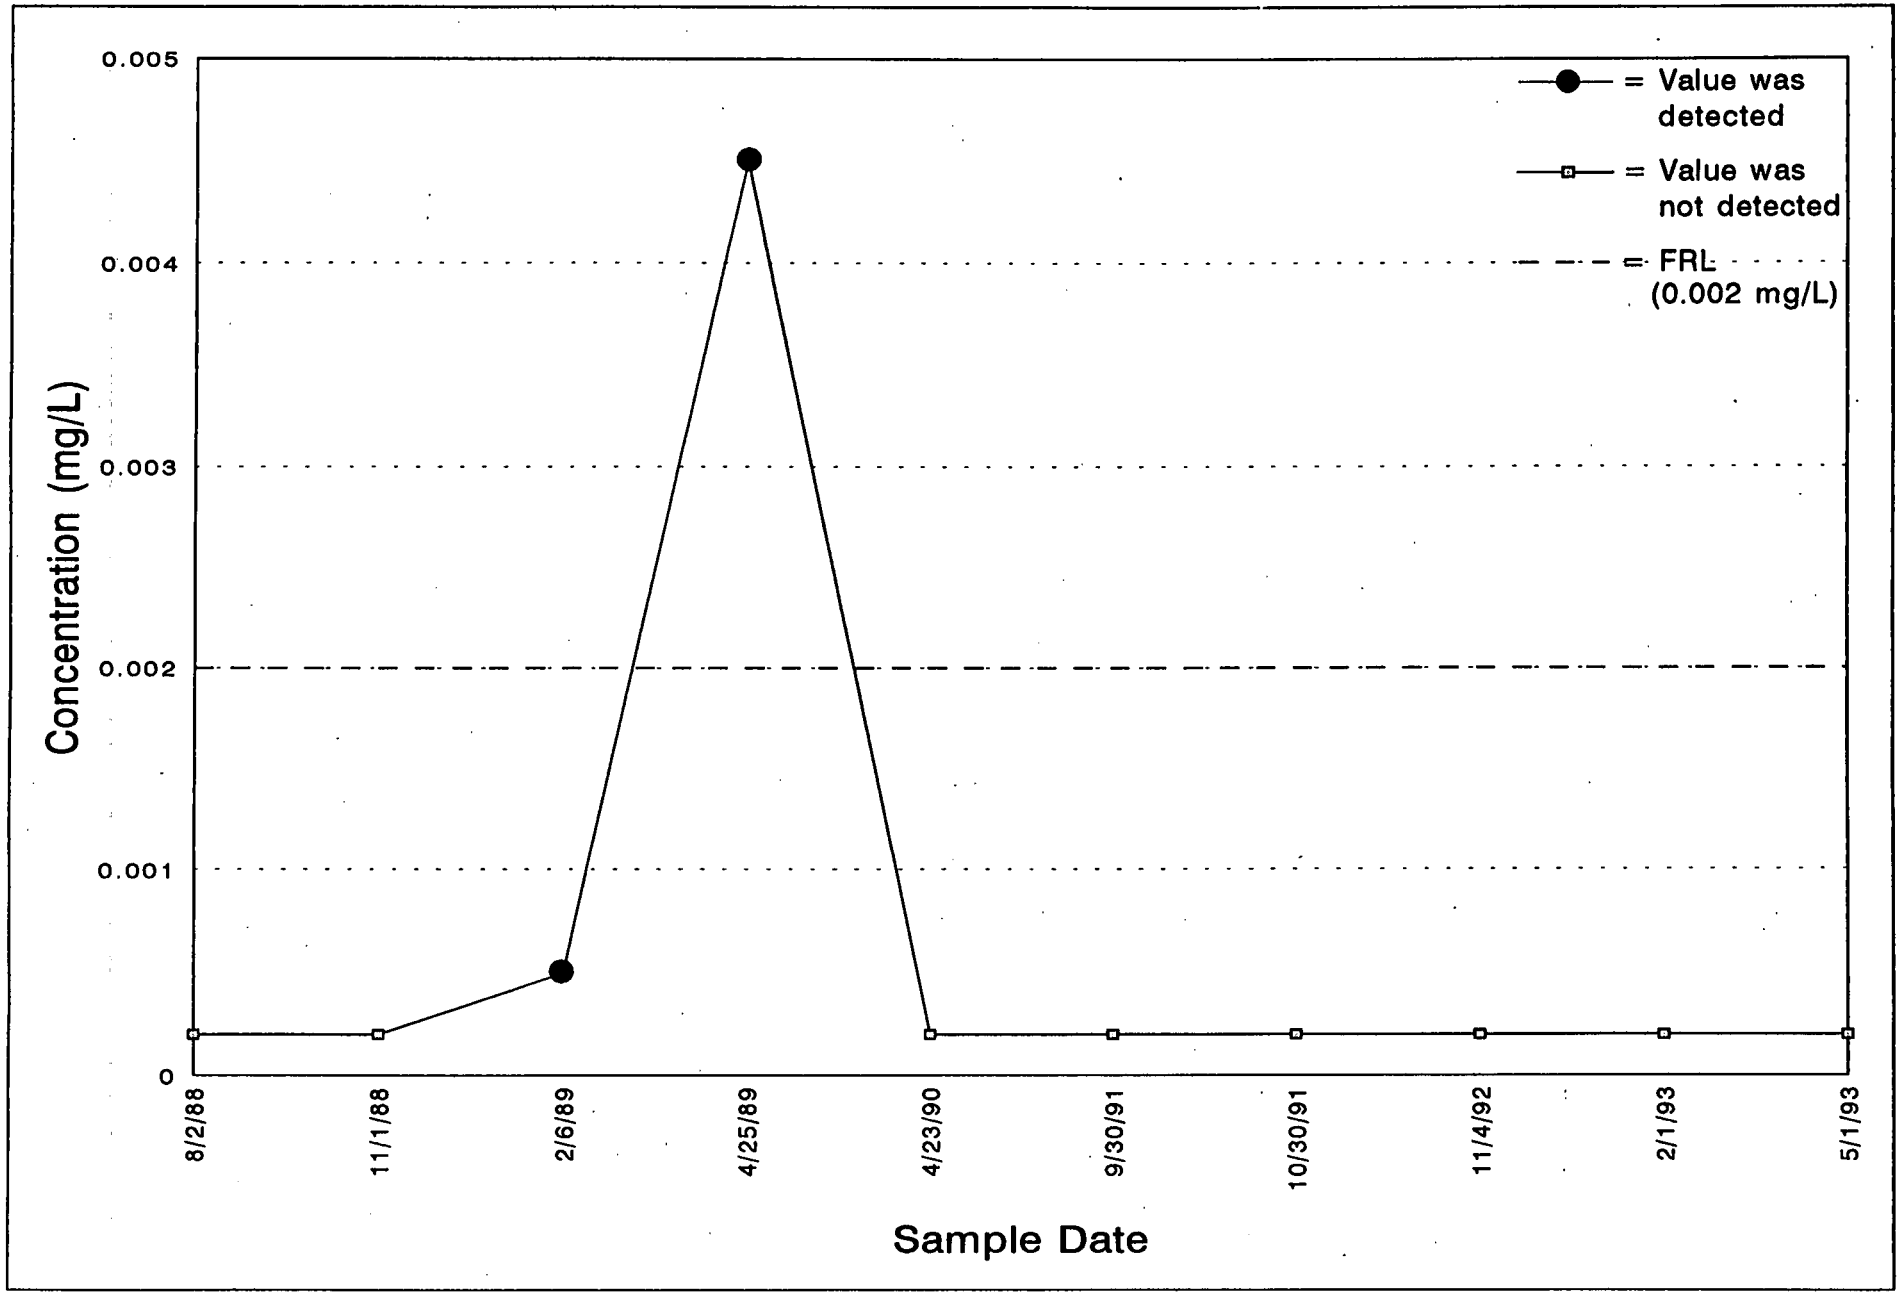

FIGURE A.3-35. MERCURY CONCENTRATION VS. TIME, WELL 2091

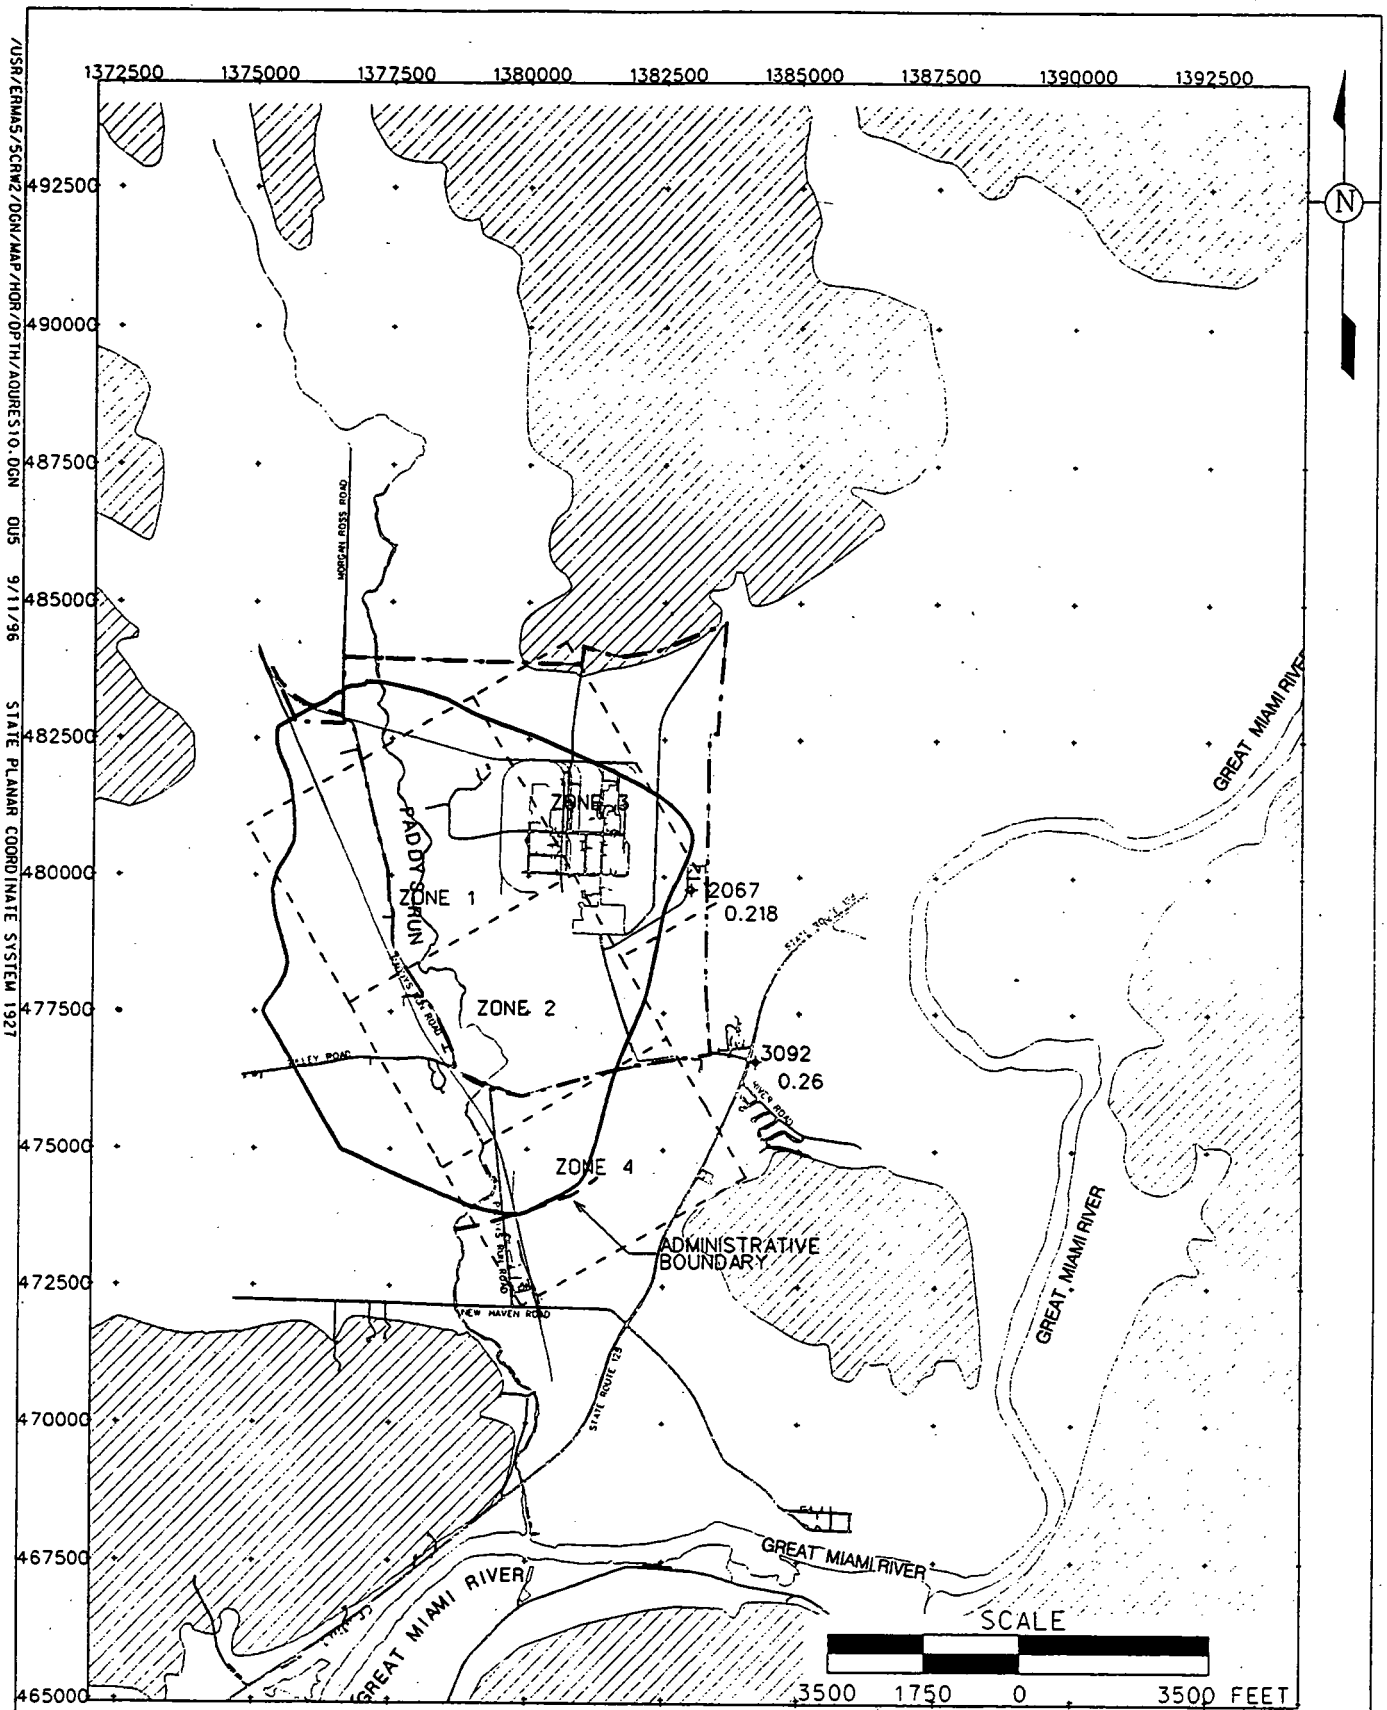

LEGEND:

— · — · — FEMP BOUNDARY

2127 ✦ GROUNDWATER MONITORING WELL

0.26 NICKEL (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-36. FRL EXCEEDENCES FOR NICKEL LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

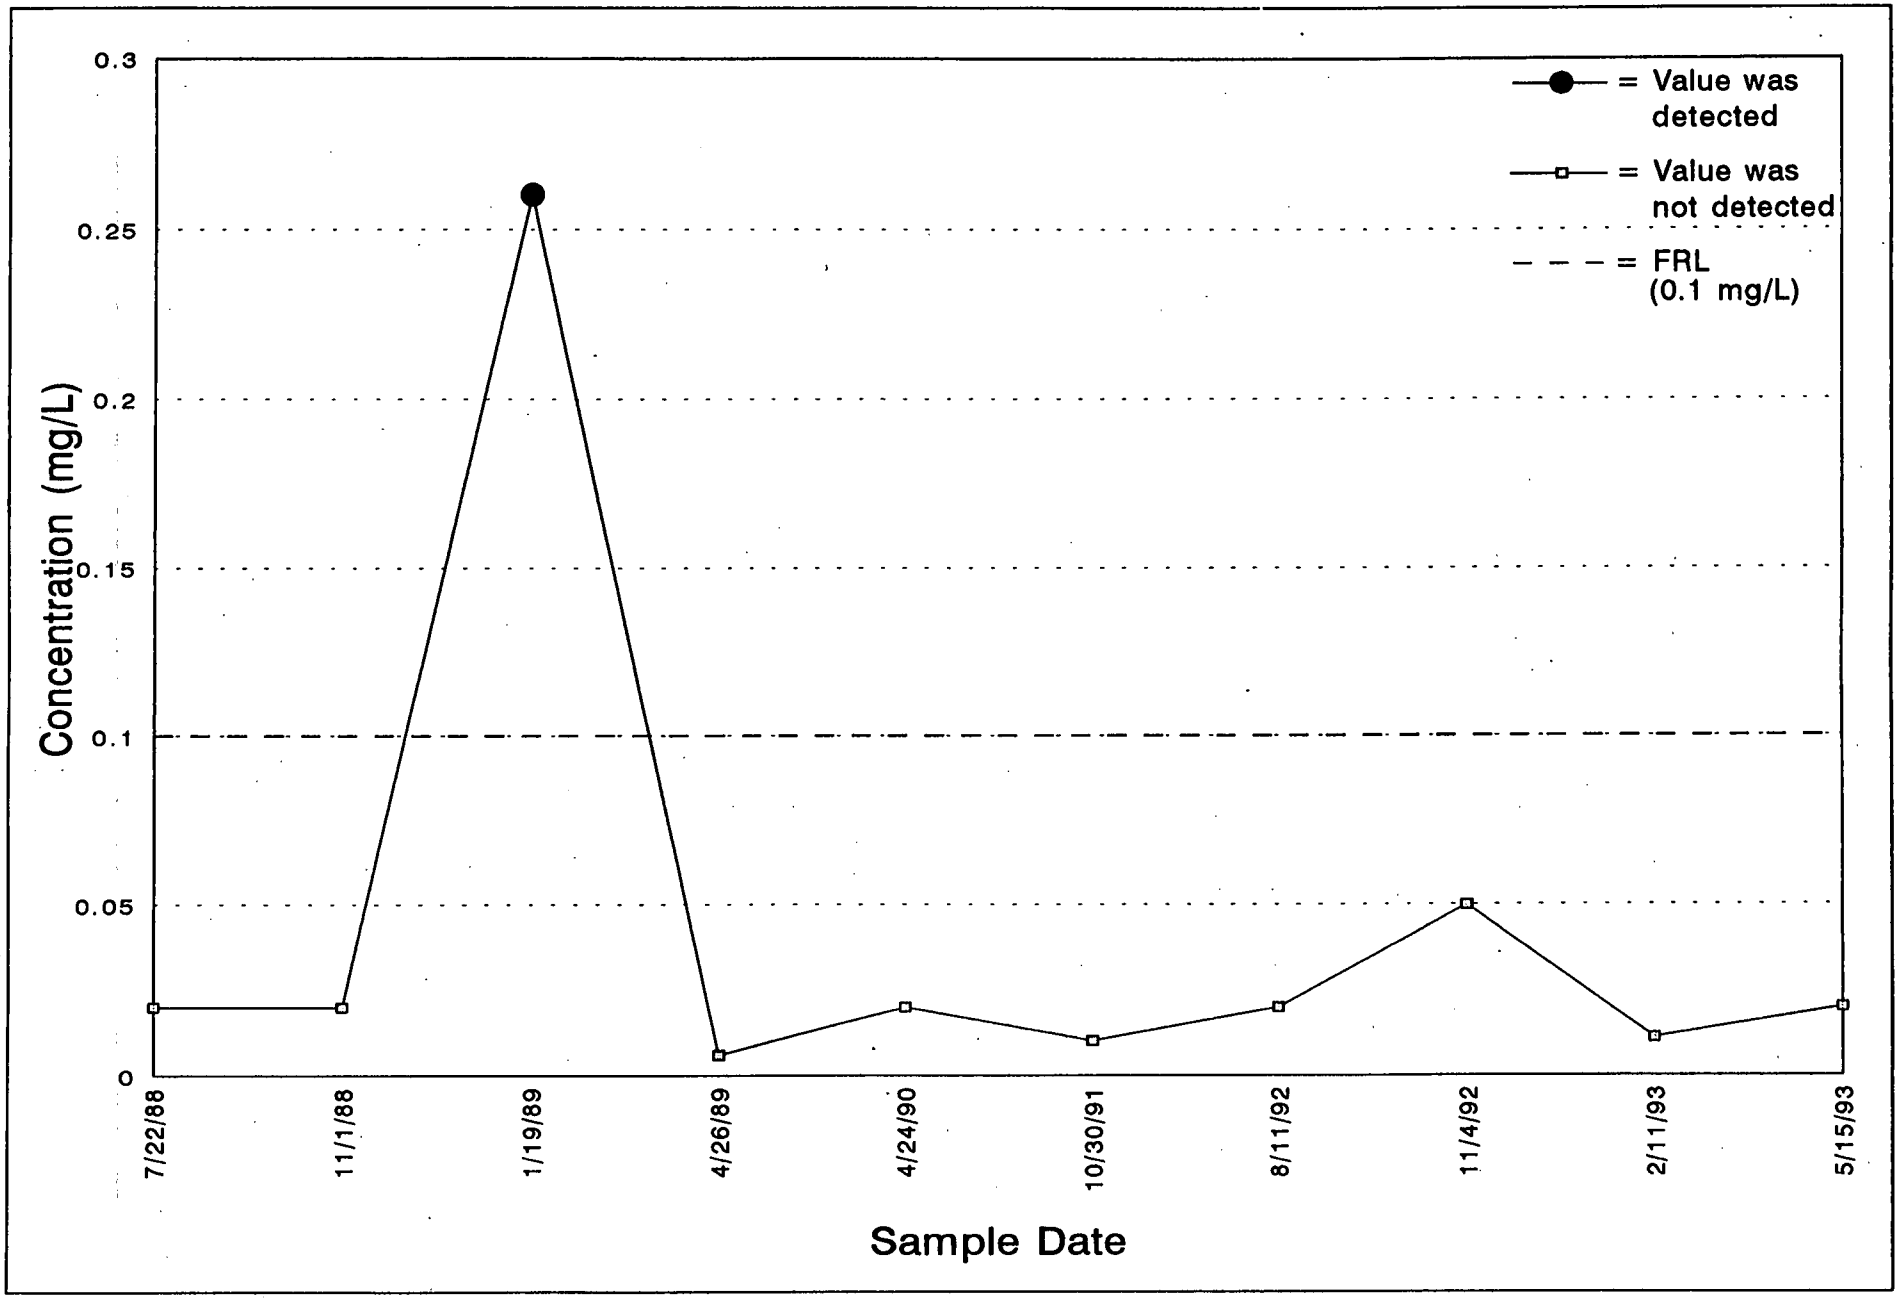

FIGURE A.3-37. NICKEL CONCENTRATION VS. TIME, WELL 3092

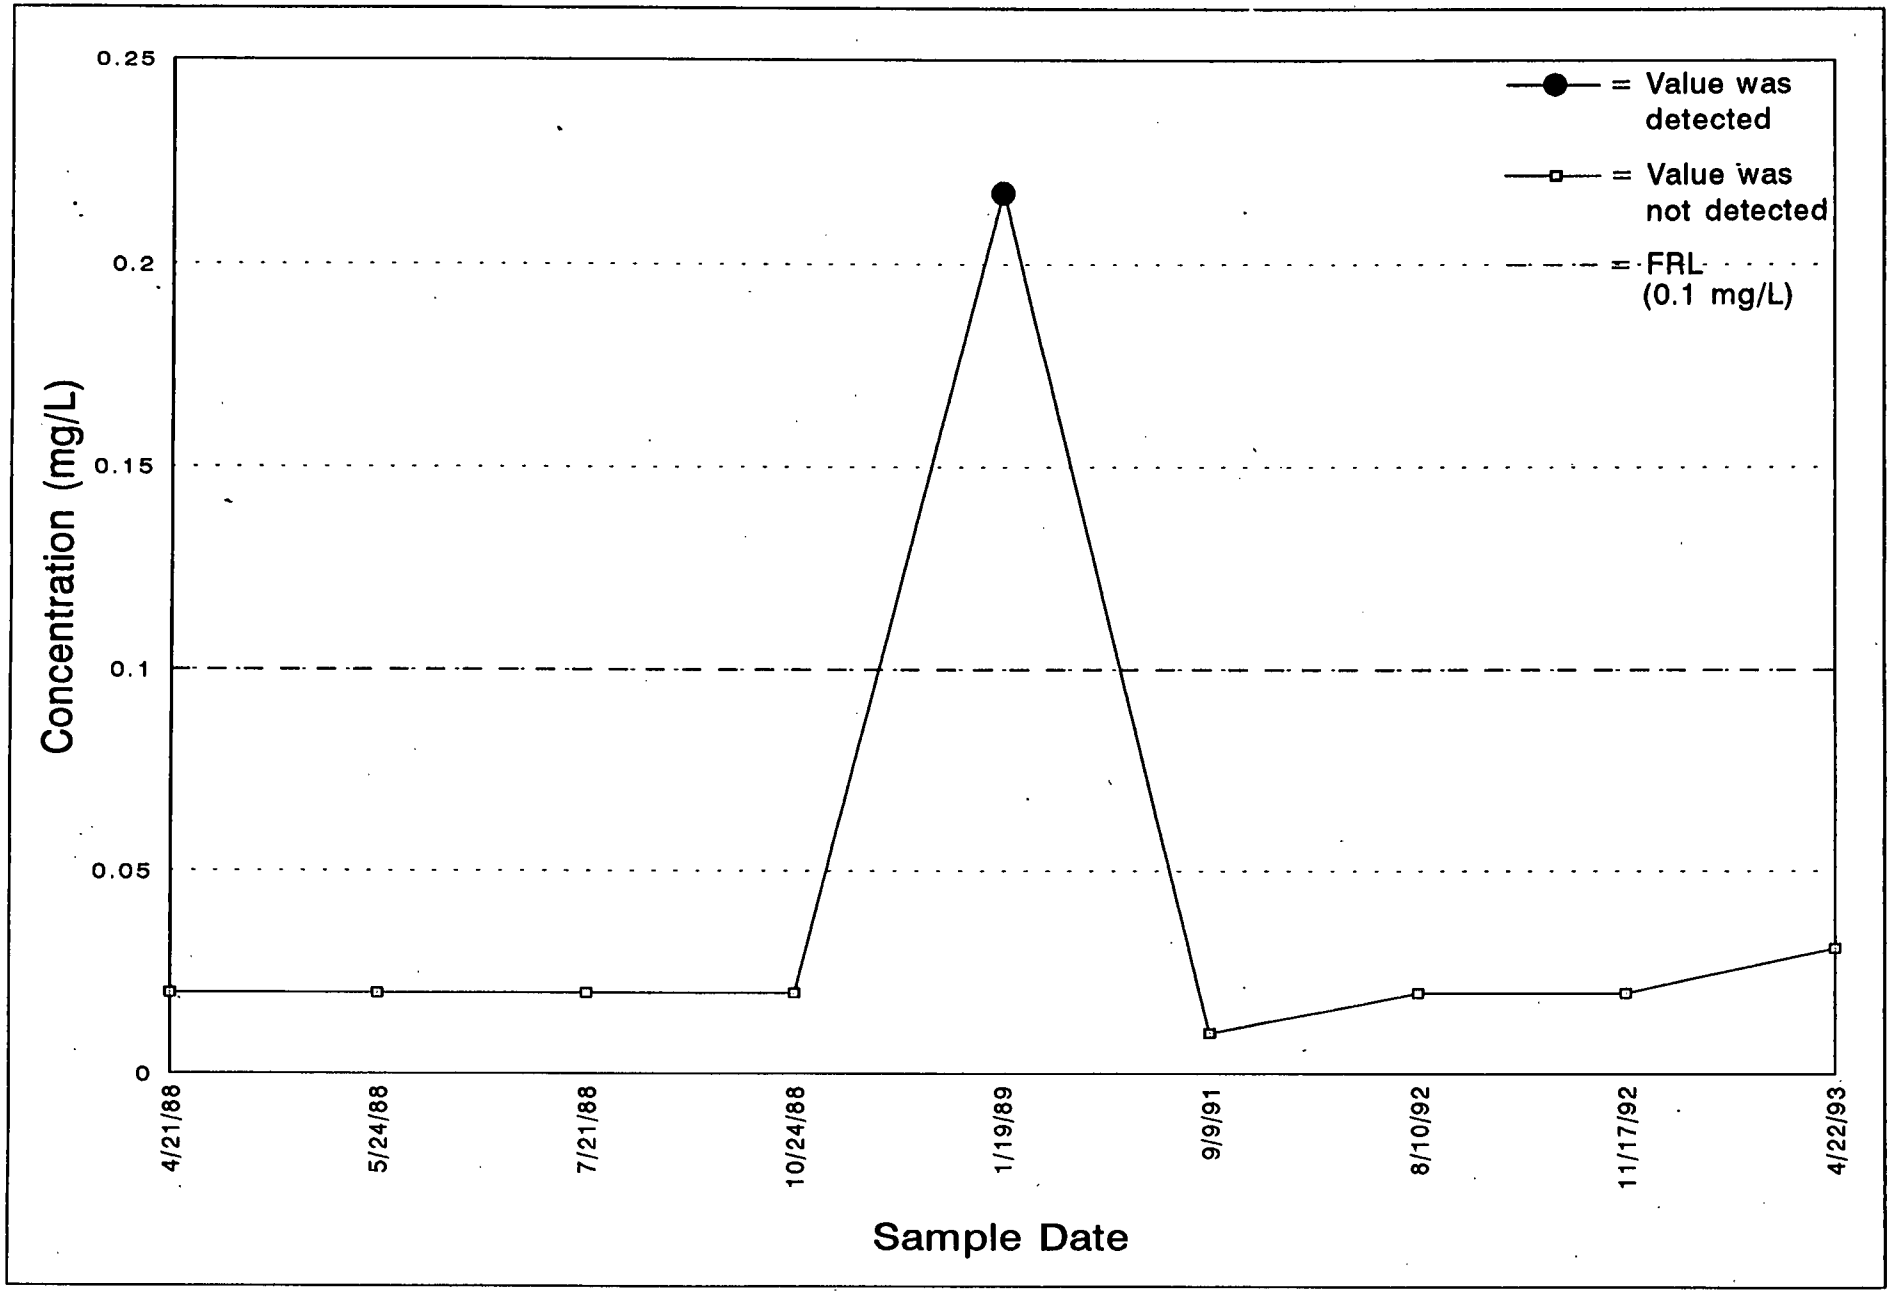

FIGURE A.3-38. NICKEL CONCENTRATION VS. TIME, WELL 2067

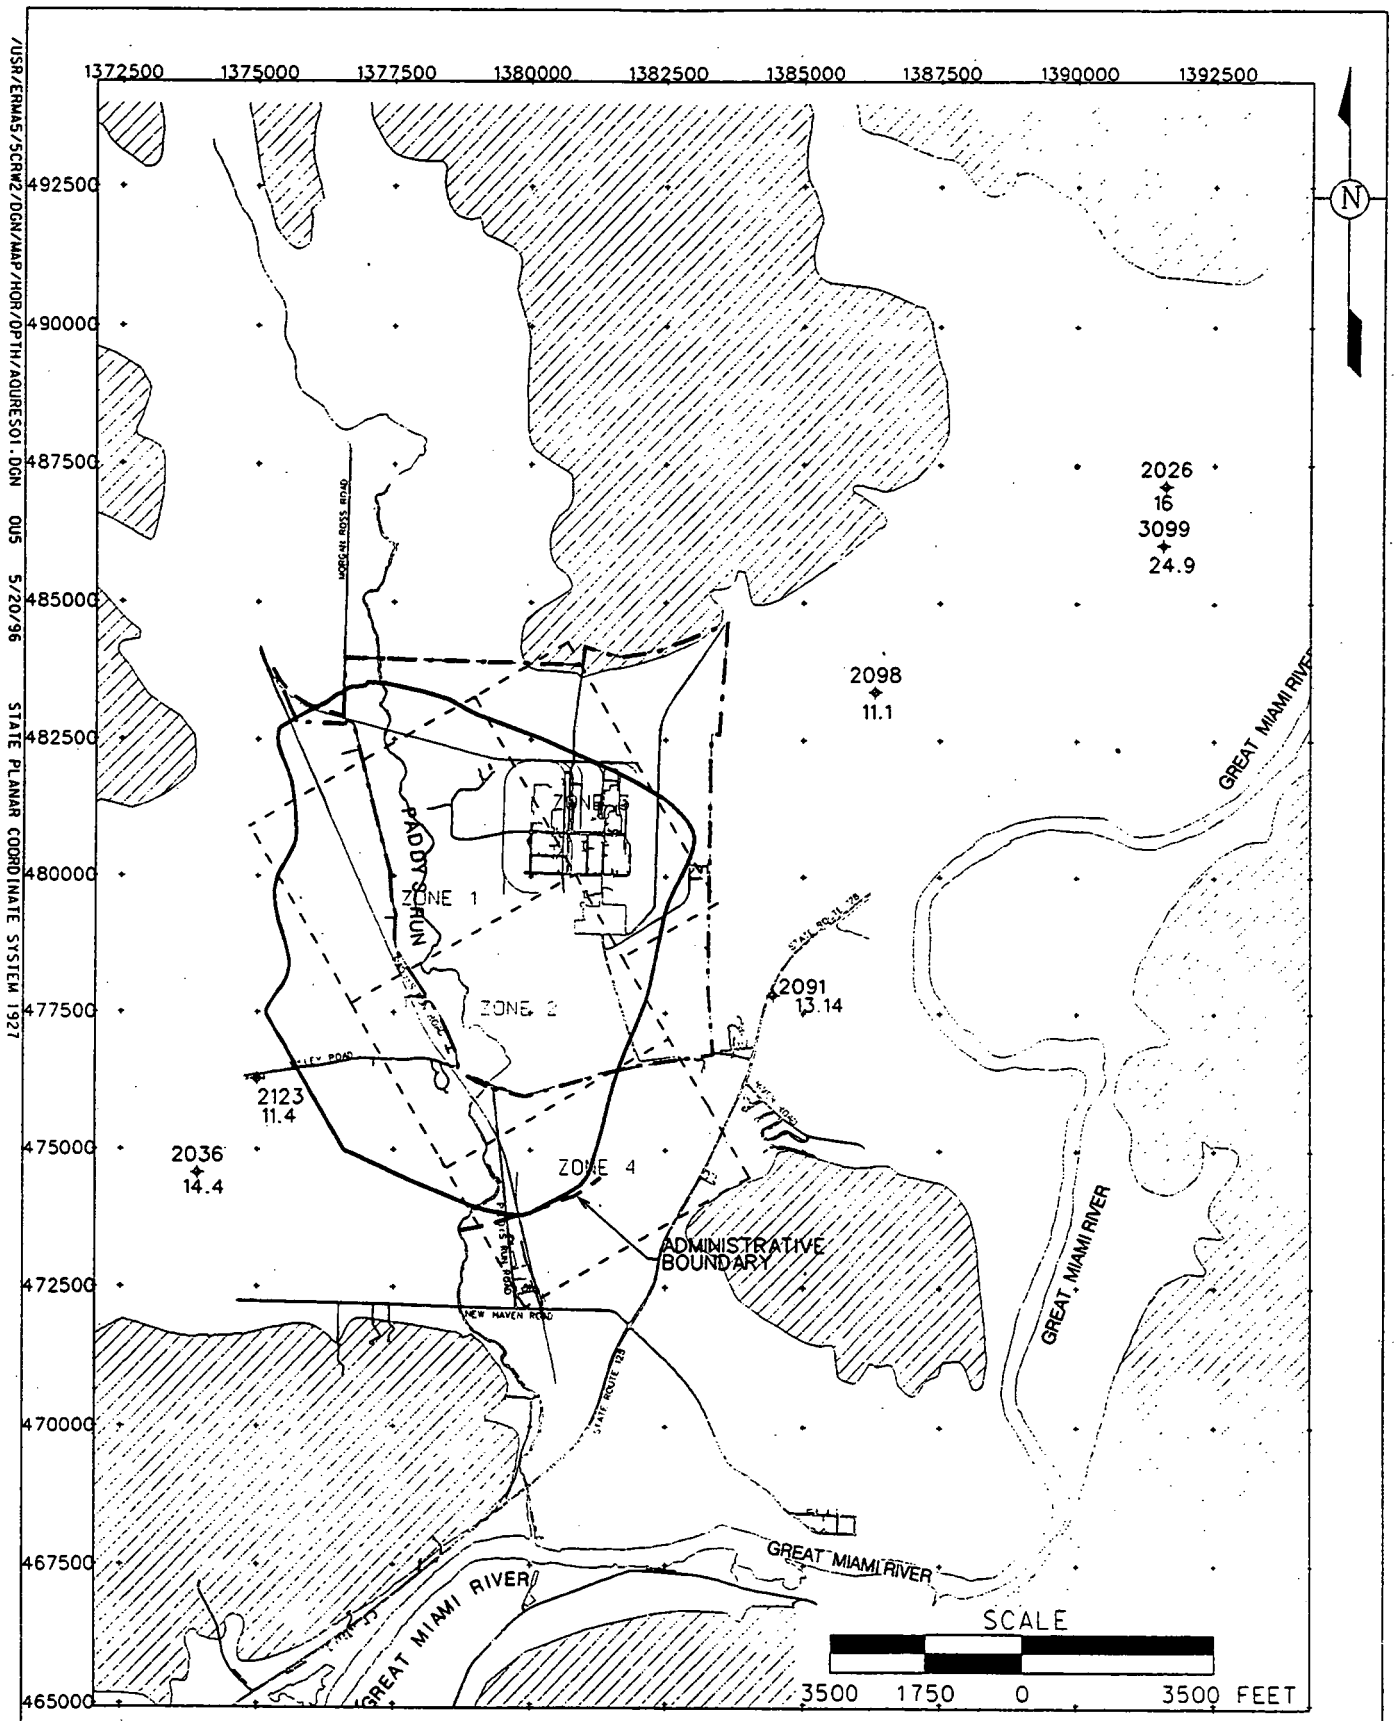

LEGEND:

FEMP BOUNDARY

2127 GROUNDWATER MONITORING WELL

12.8 NITRATE (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-39. FRL EXCEEDENCES FOR NITRATE LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

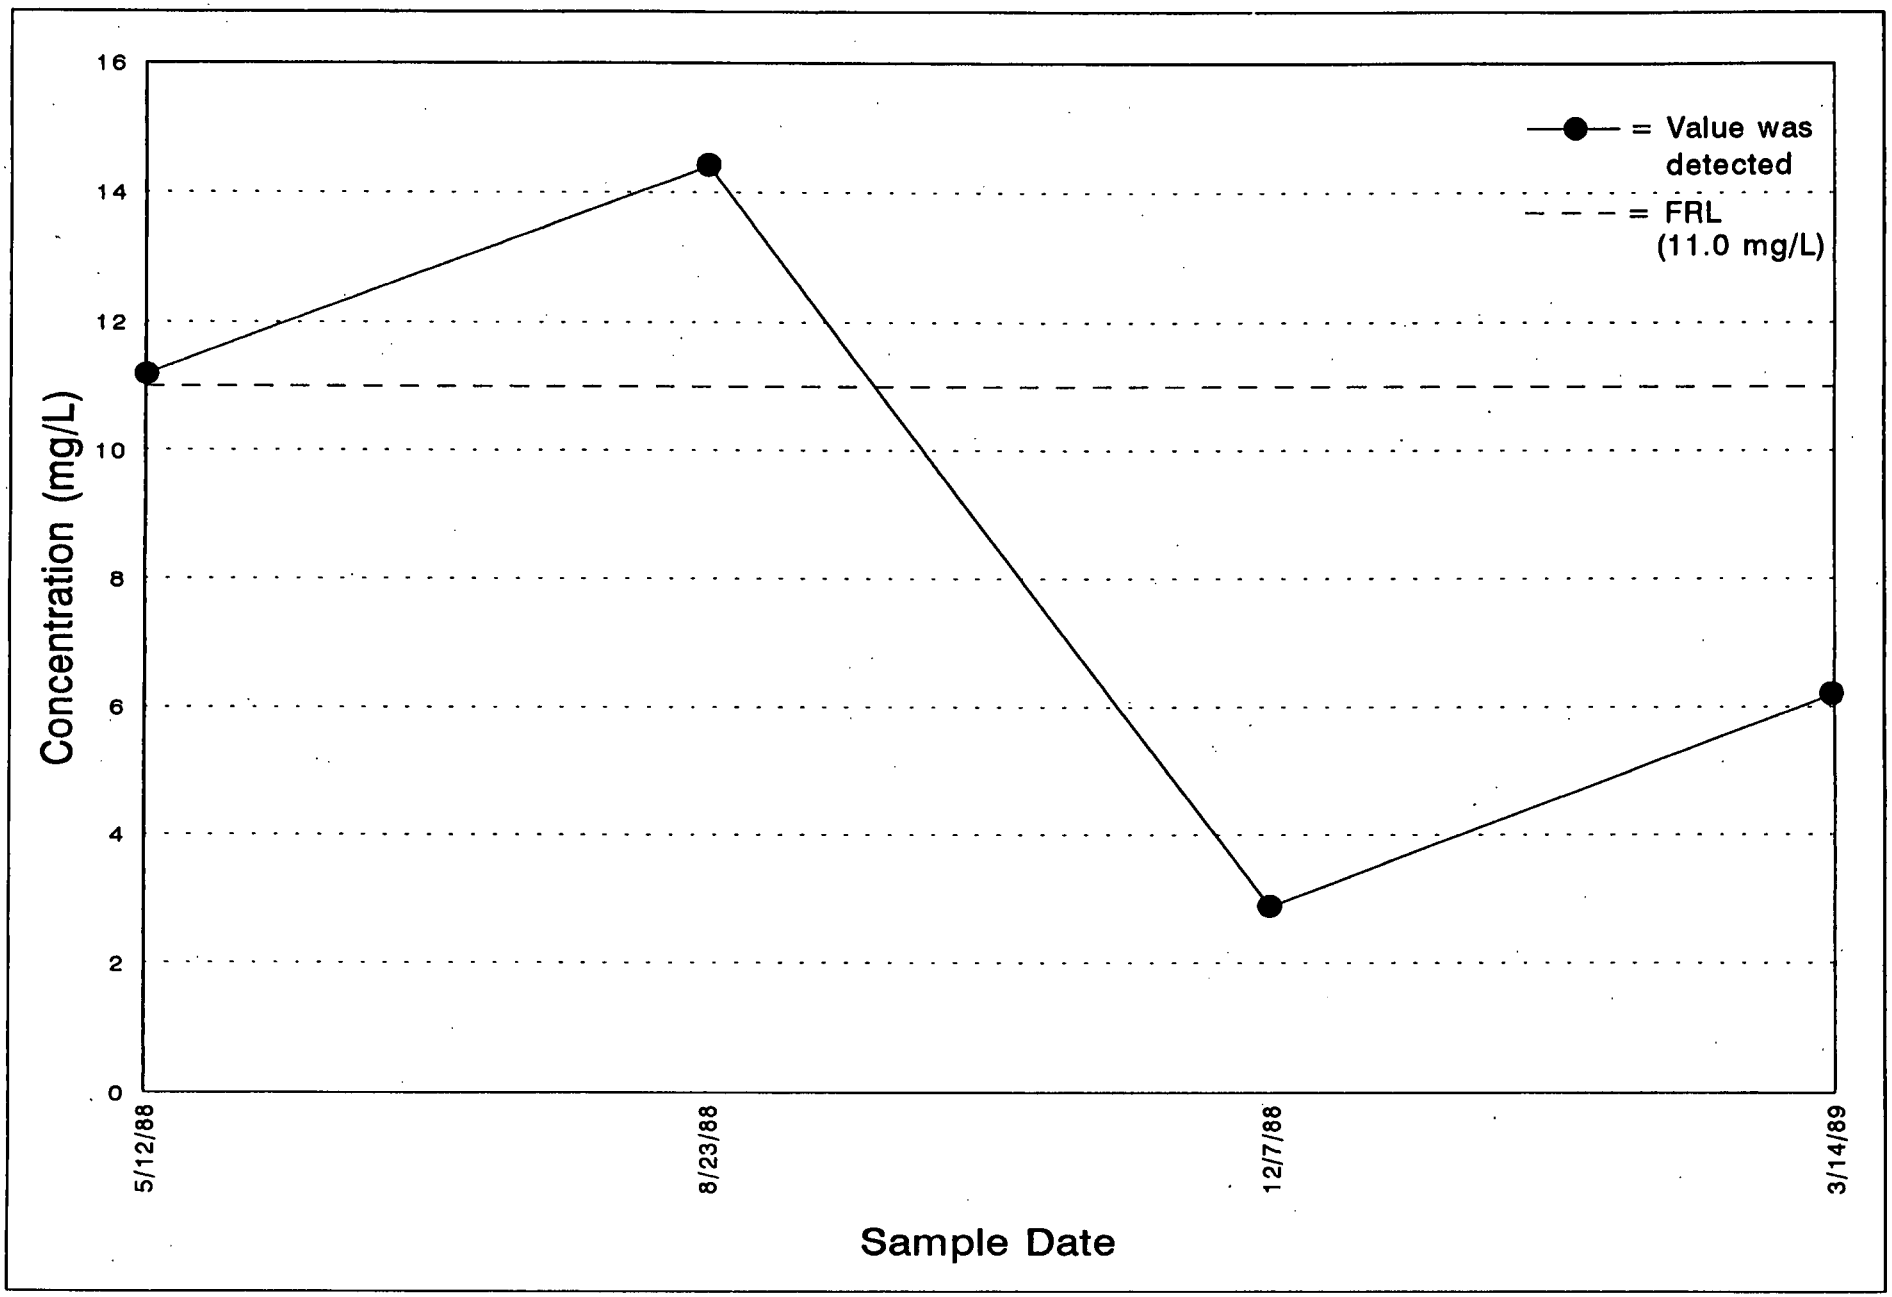

FIGURE A.3-40. NITRATE CONCENTRATION VS. TIME, WELL 2036

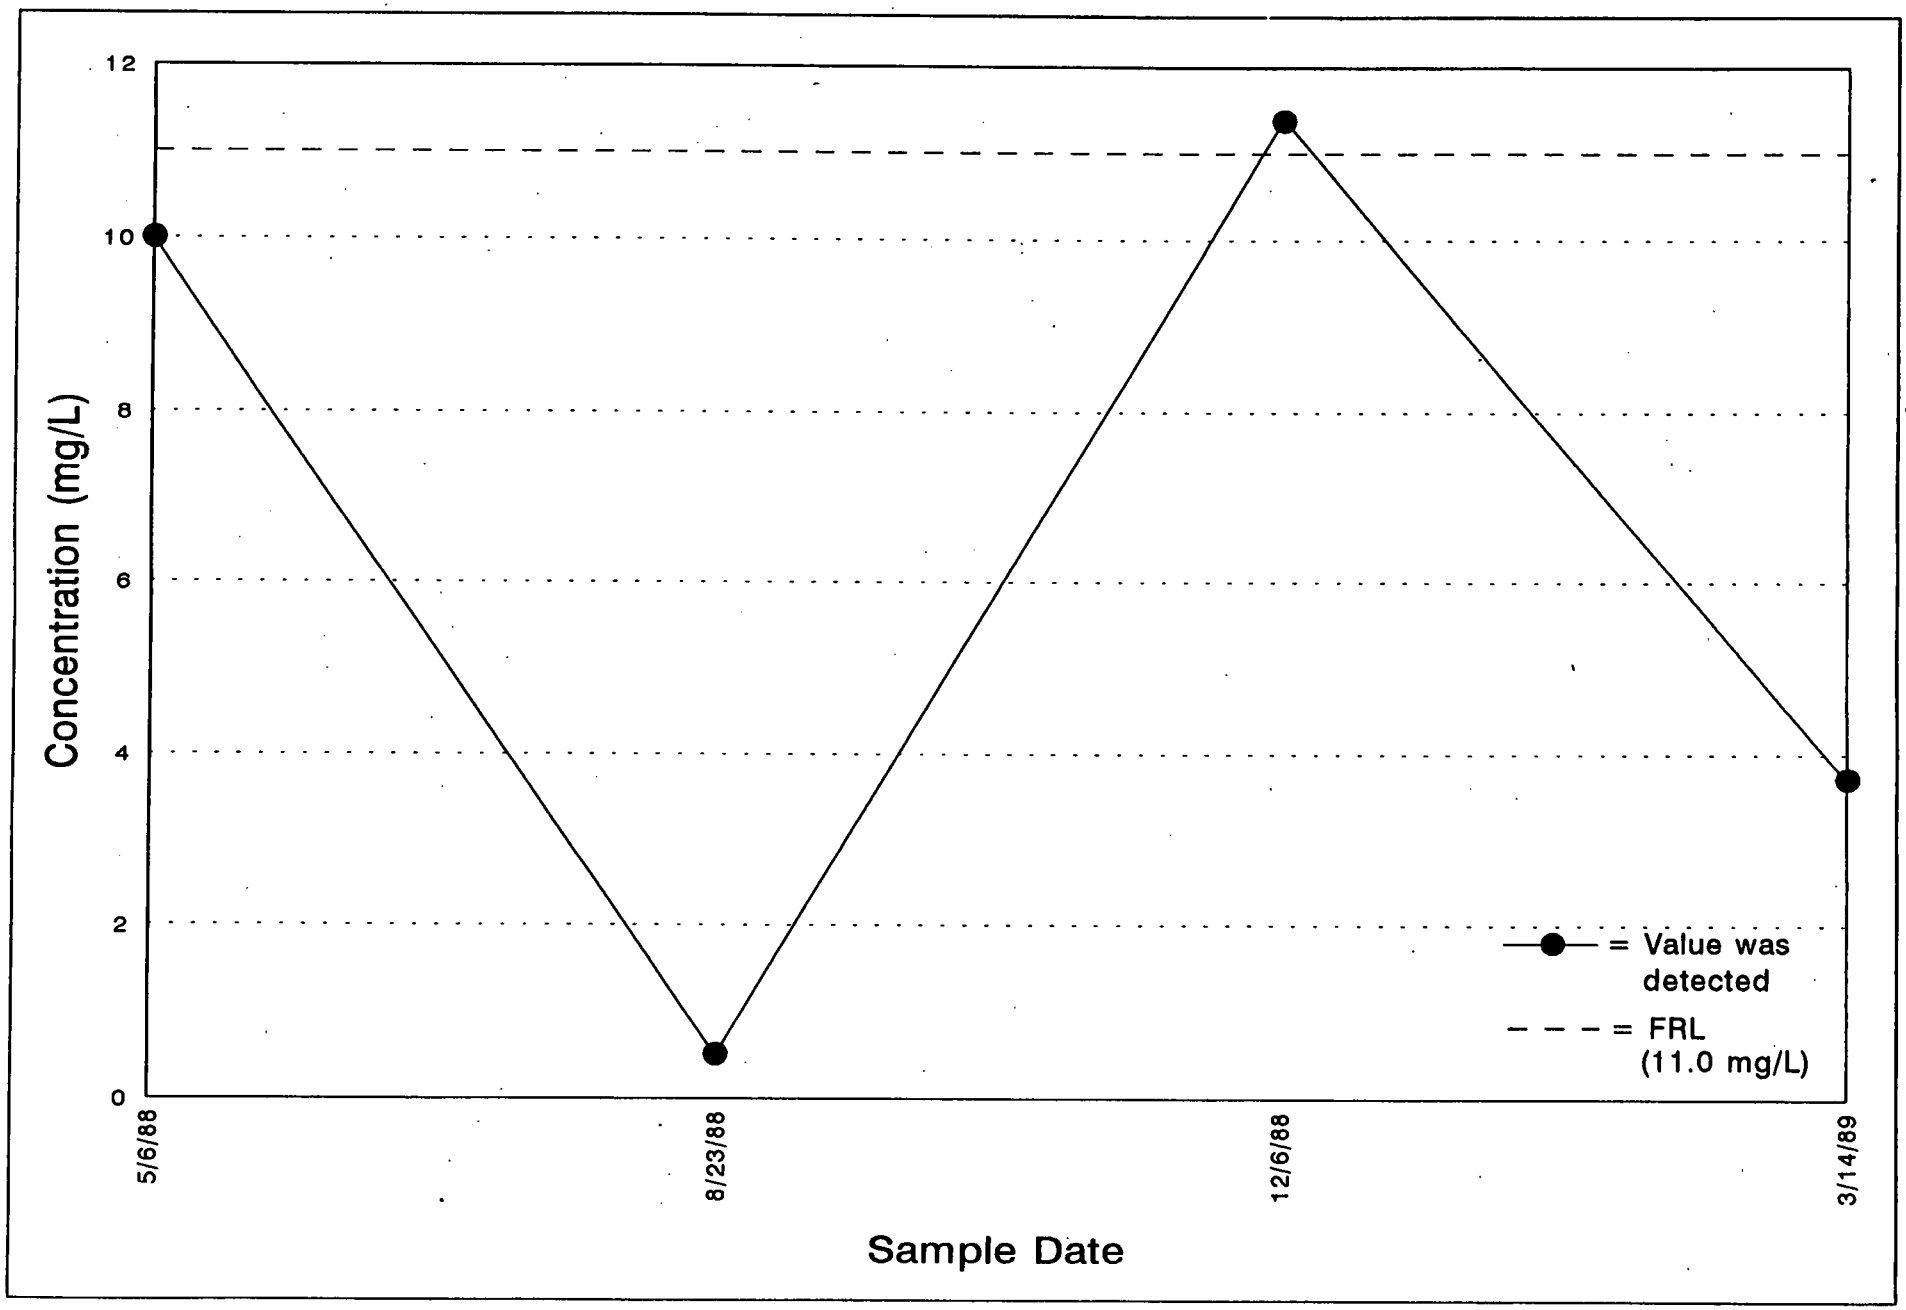

FIGURE A.3-41. NITRATE CONCENTRATION VS. TIME, WELL 2123

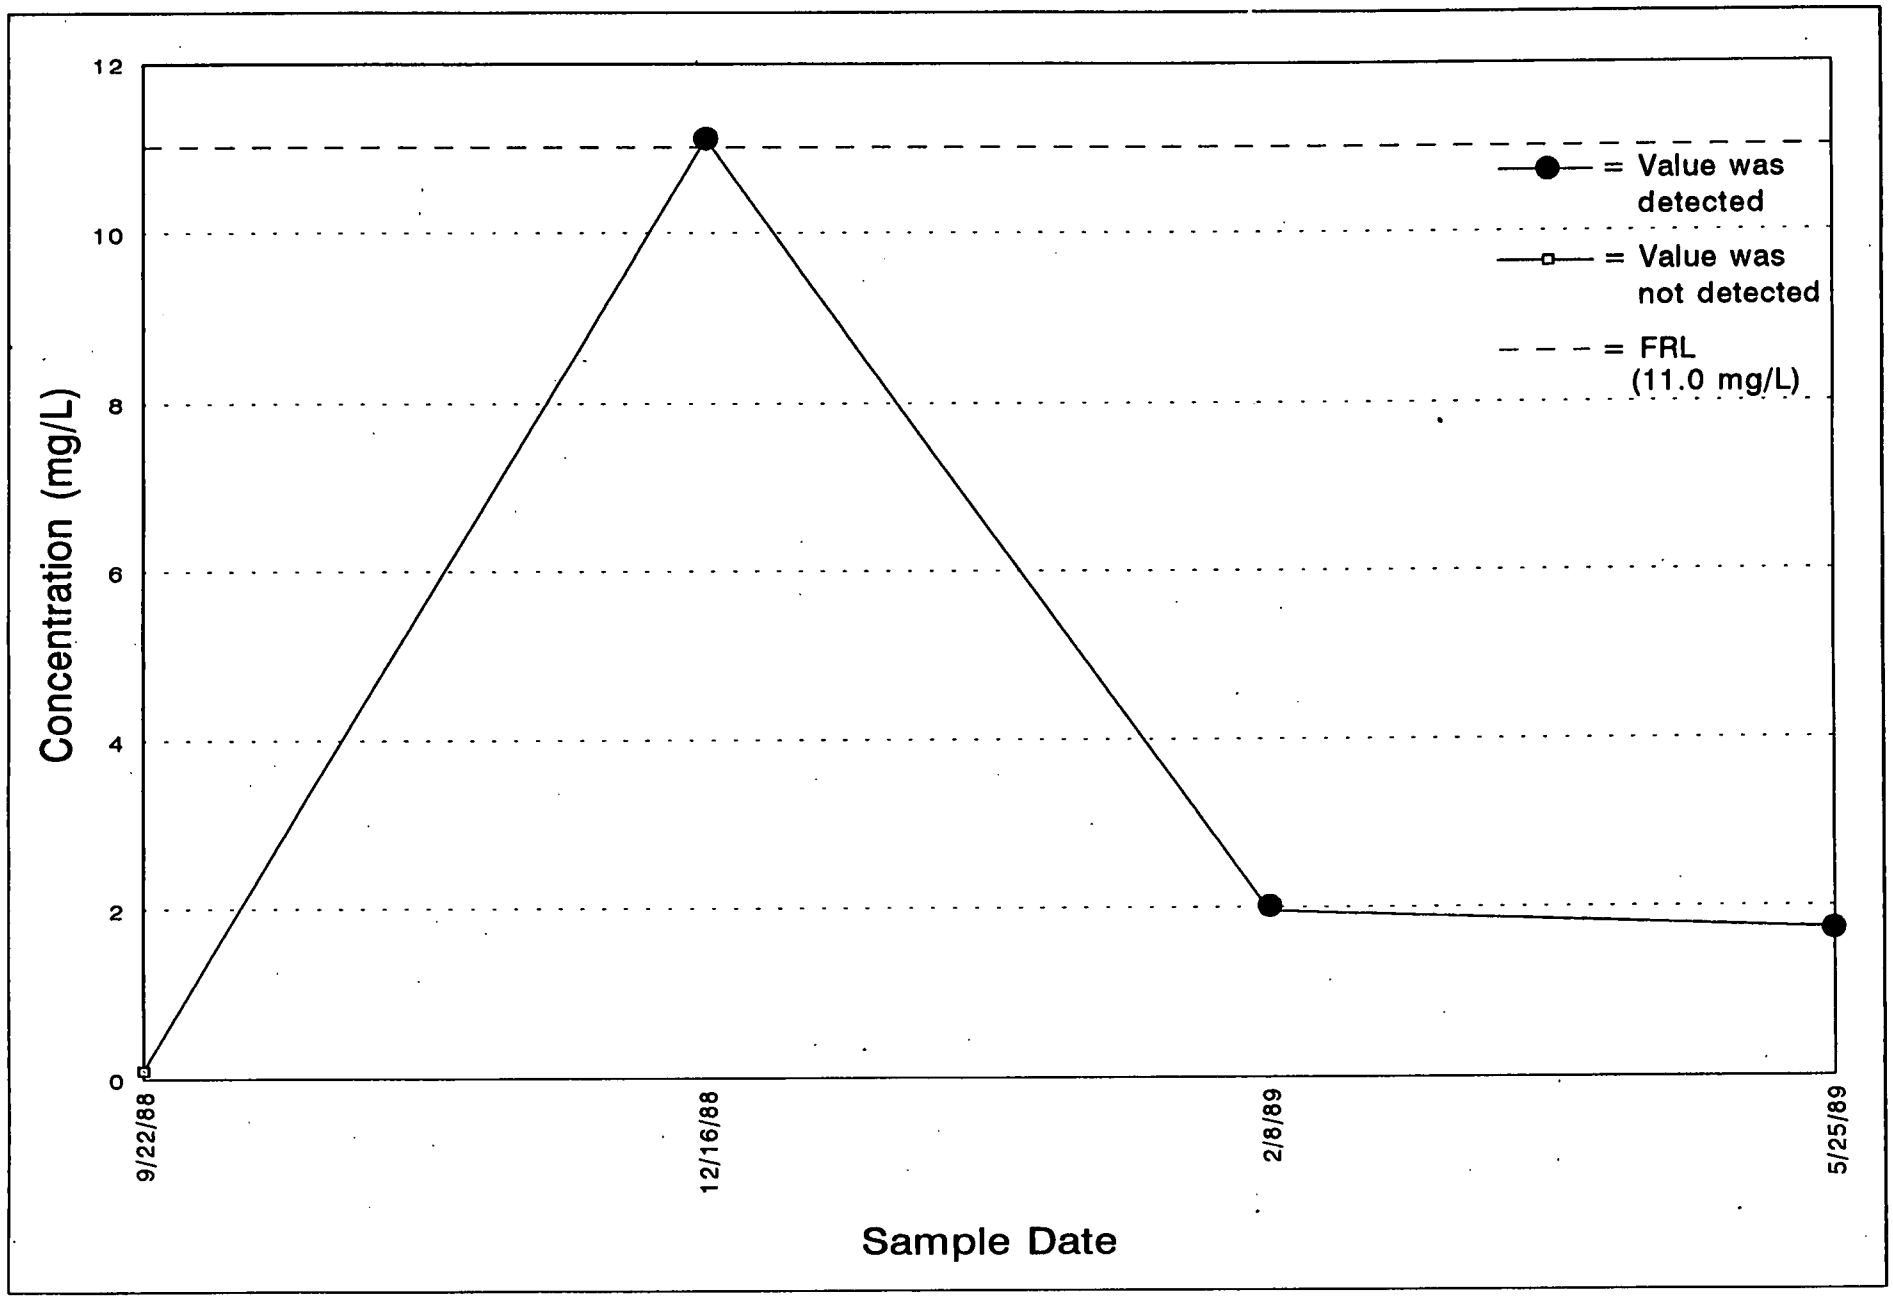

FIGURE A.3-42. NITRATE CONCENTRATION VS. TIME, WELL 2098

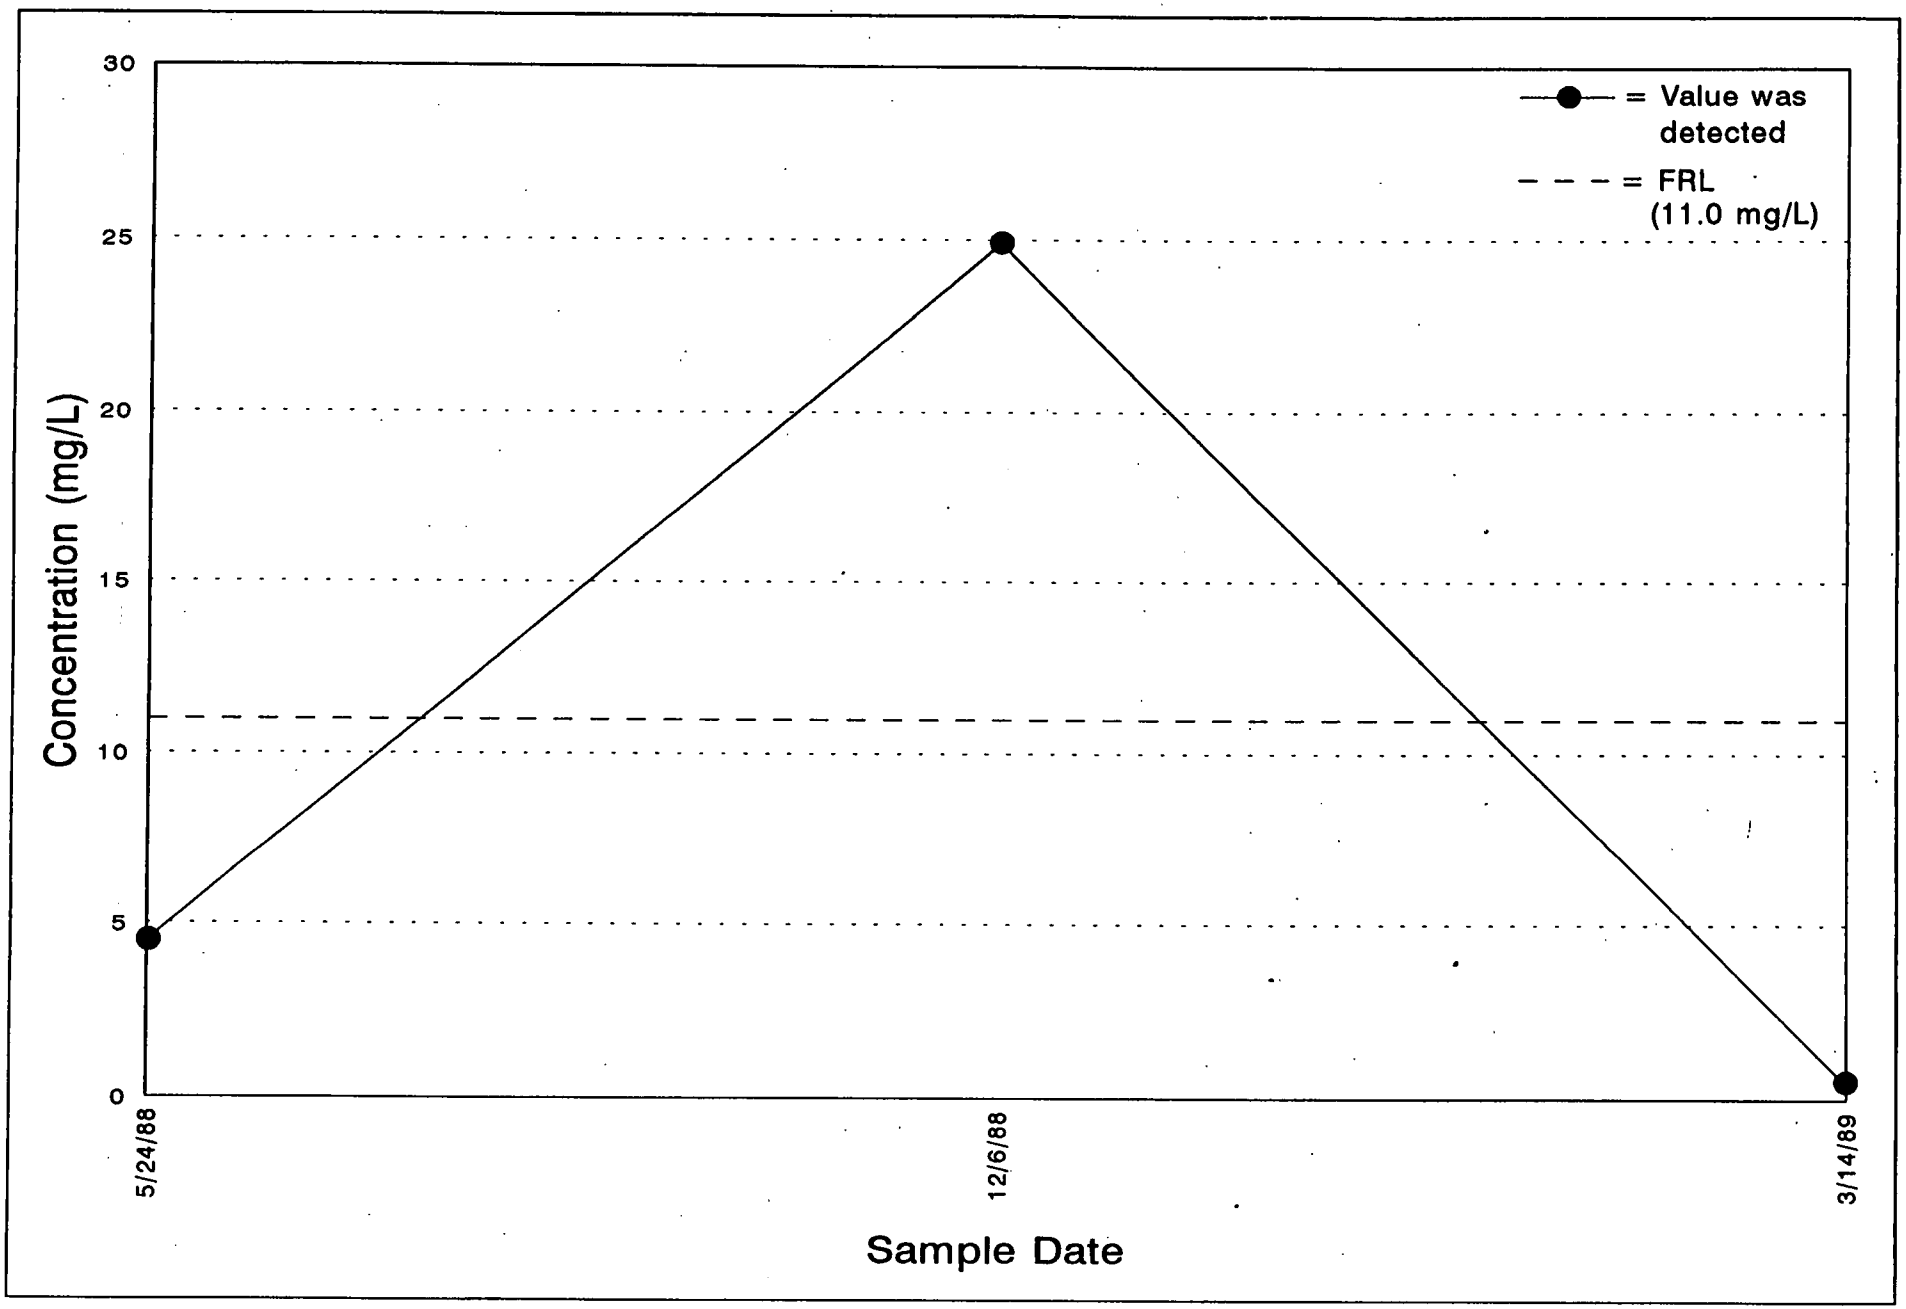

FIGURE A.3-43. NITRATE CONCENTRATION VS. TIME, WELL 3099

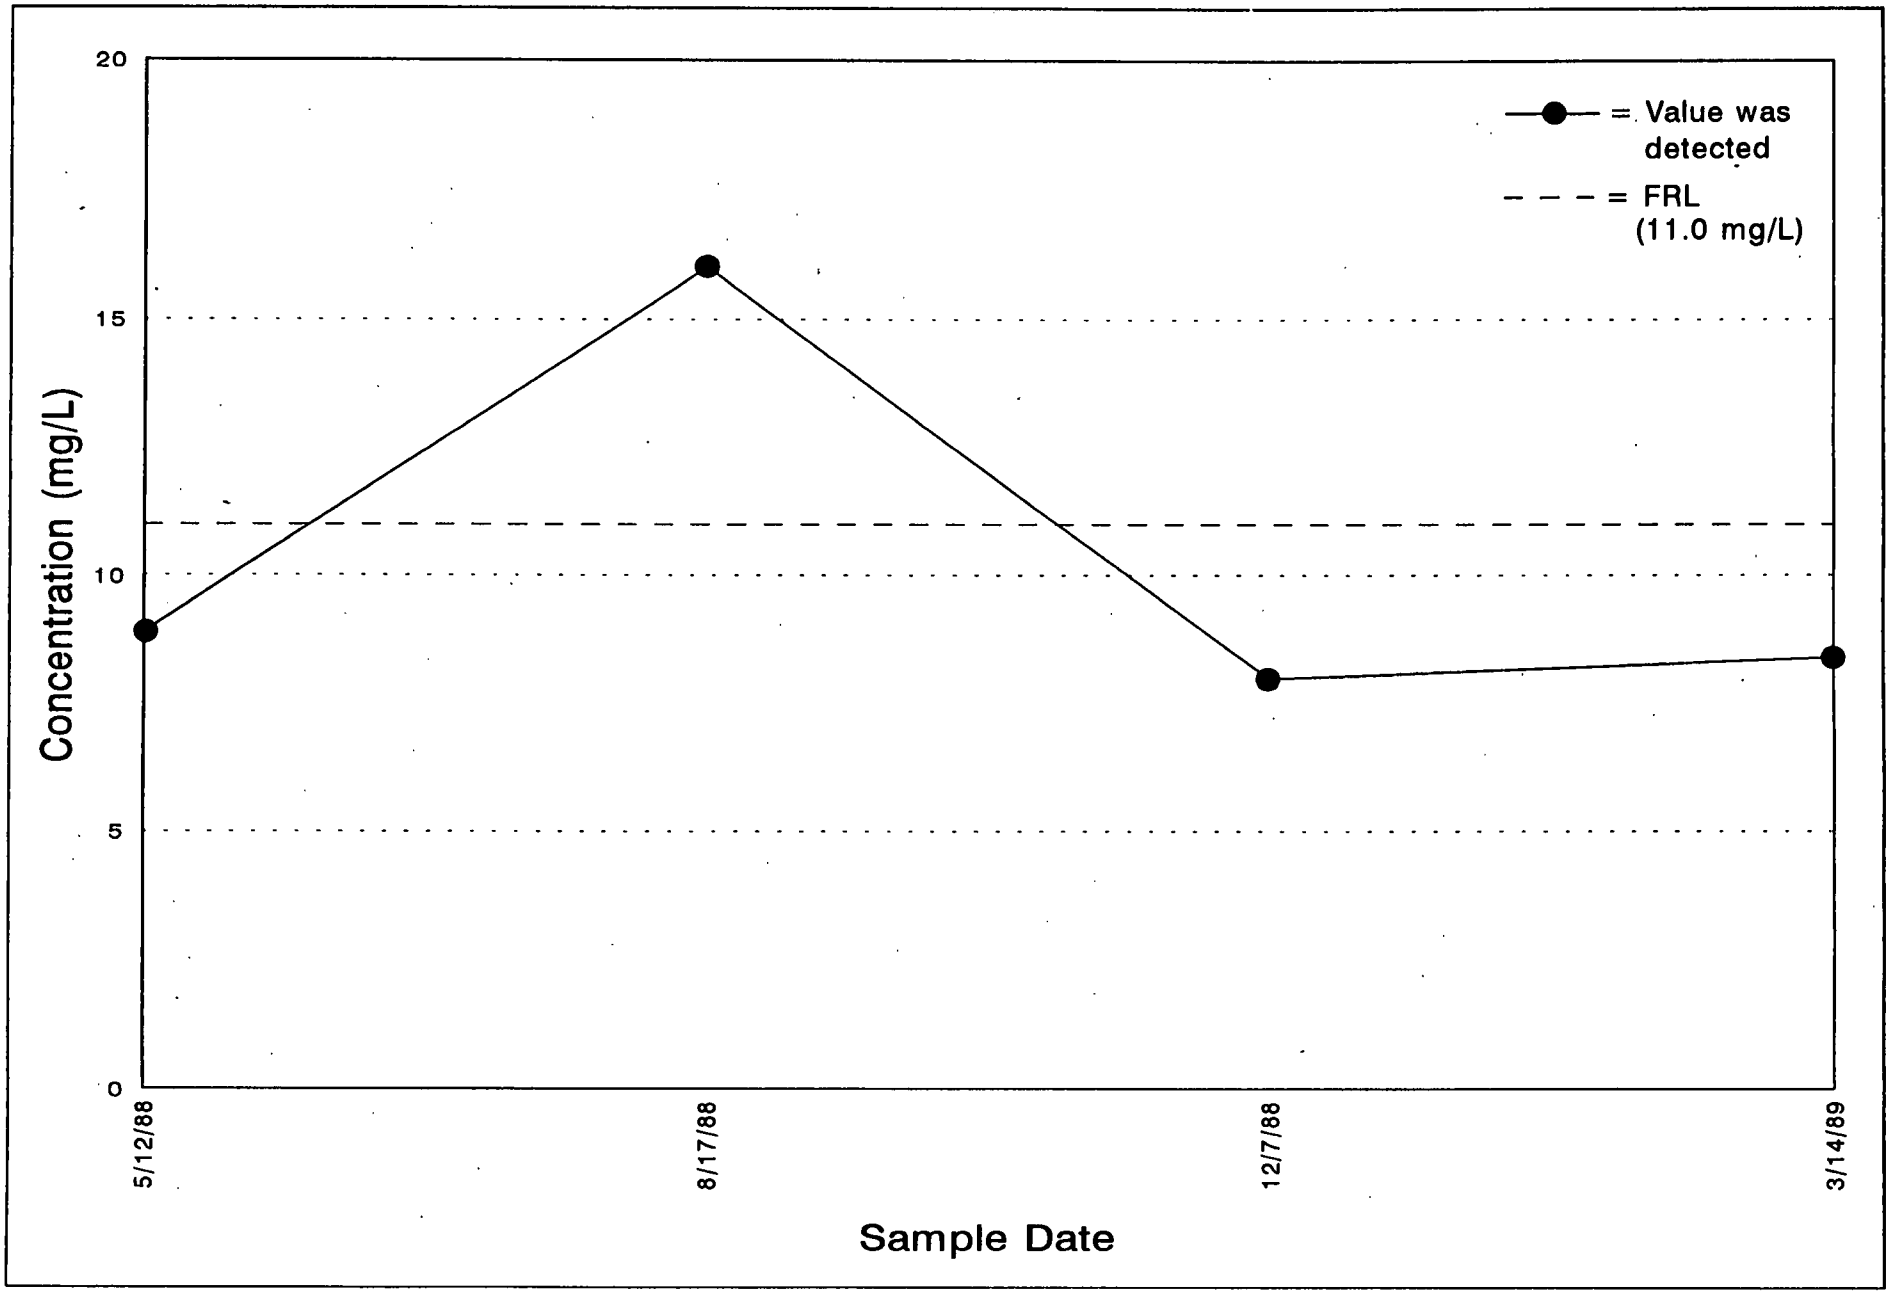

FIGURE A.3-44. NITRATE CONCENTRATION VS. TIME, WELL 2026

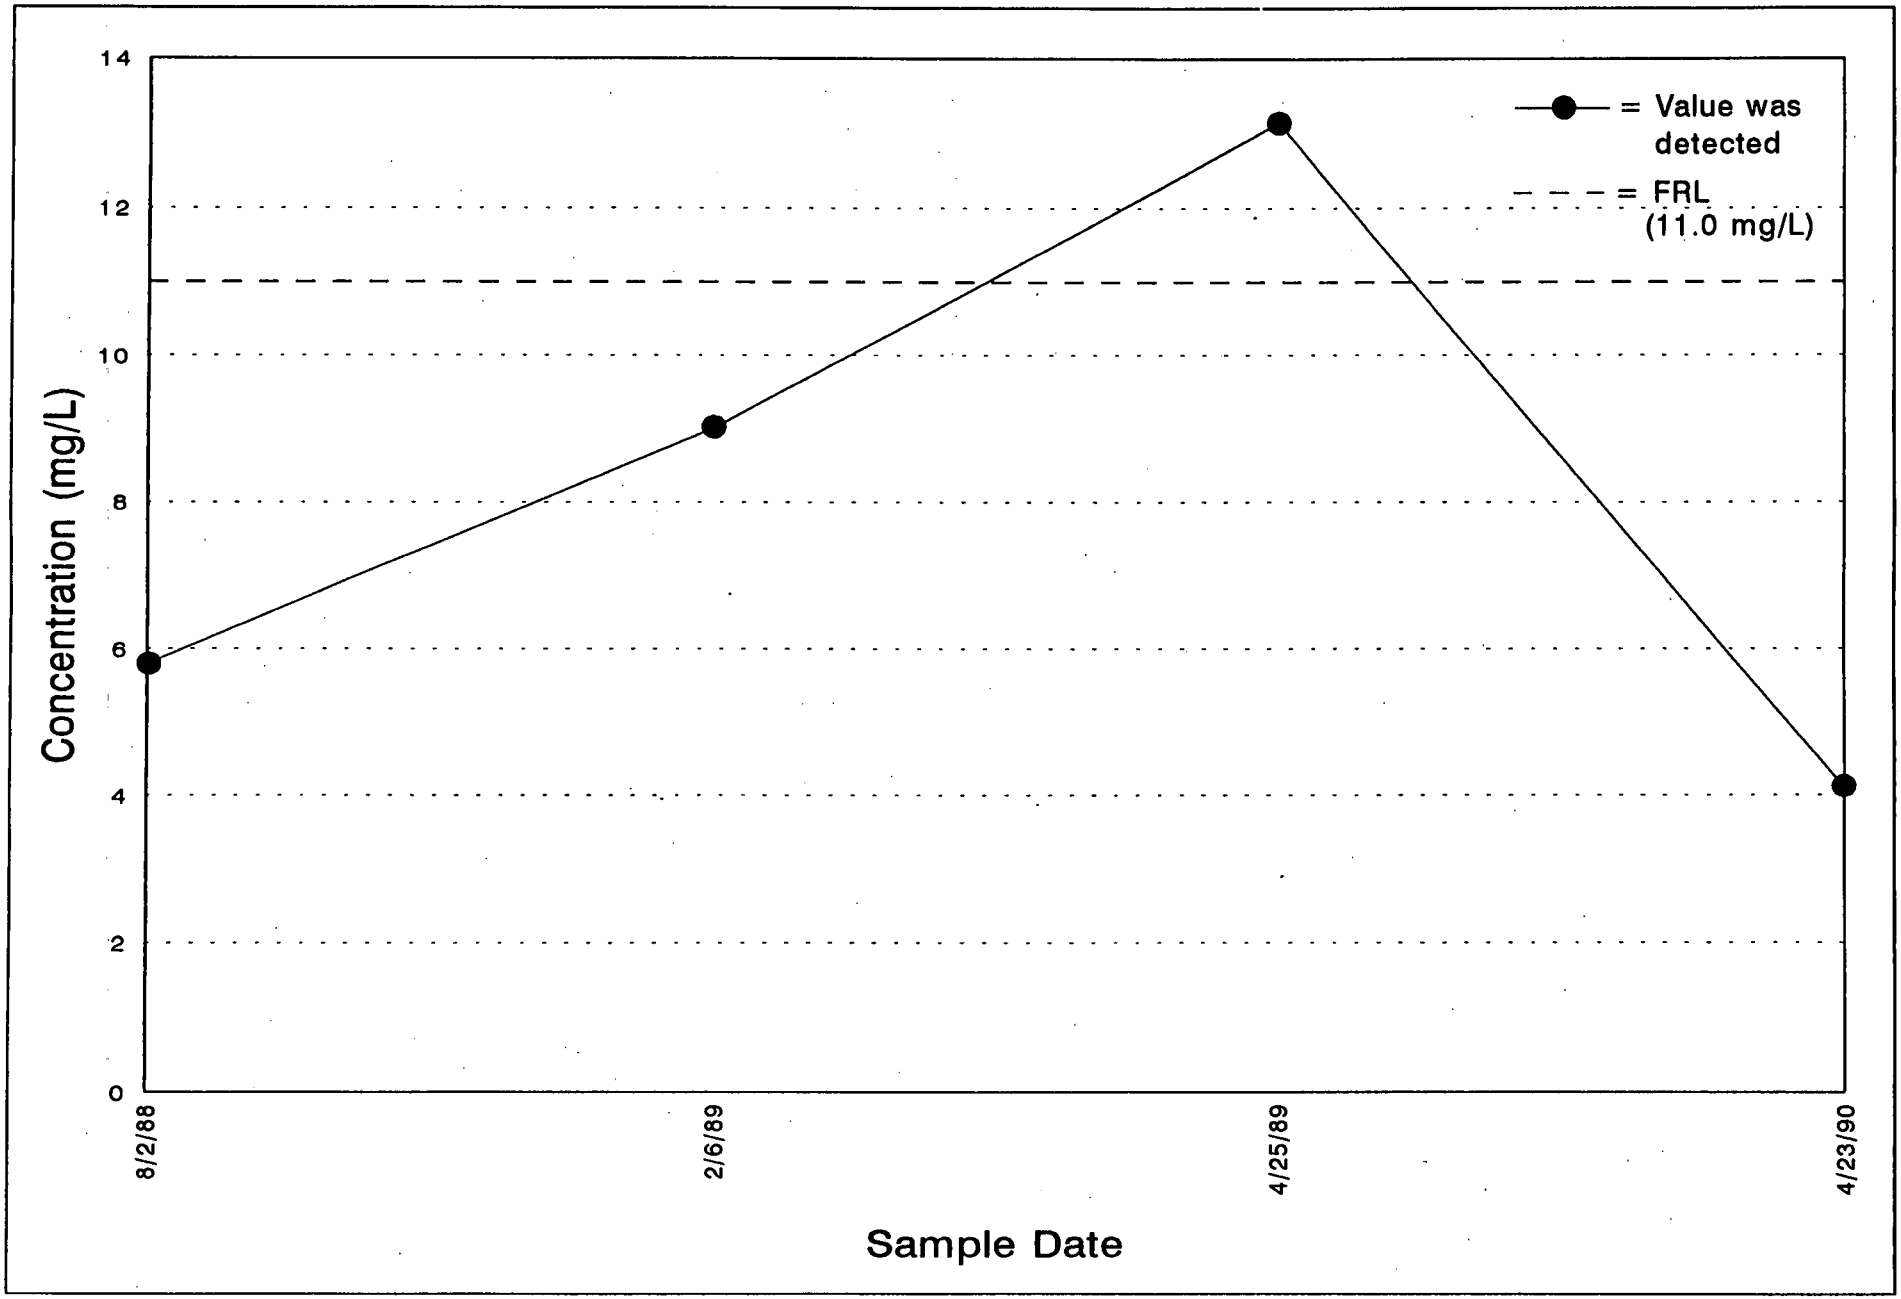

FIGURE A.3-45. NITRATE CONCENTRATION VS. TIME, WELL 2091

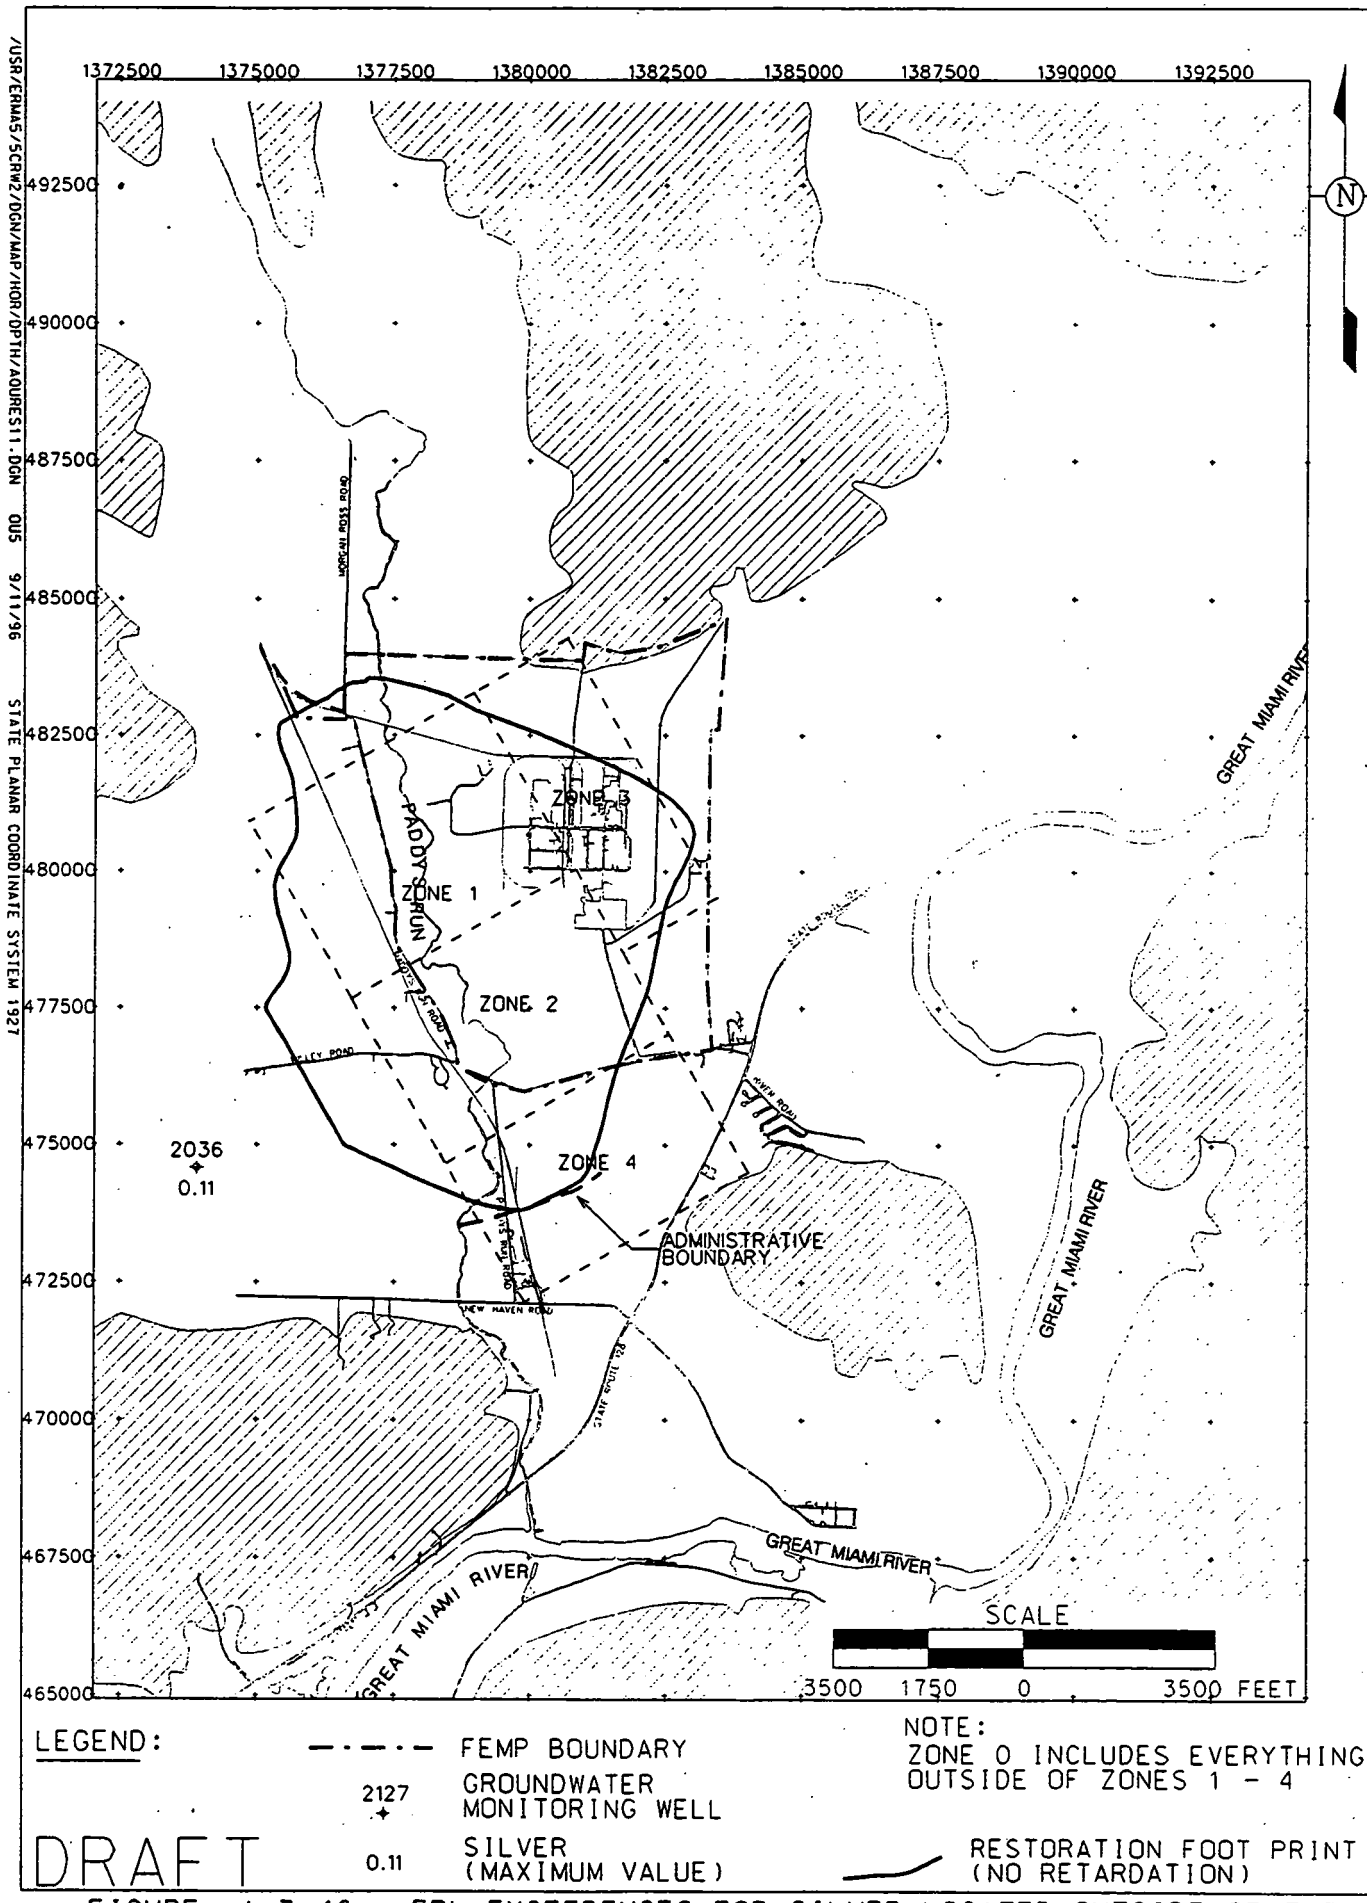

FIGURE A.3-46. FRL EXCEEDENCES FOR SILVER LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

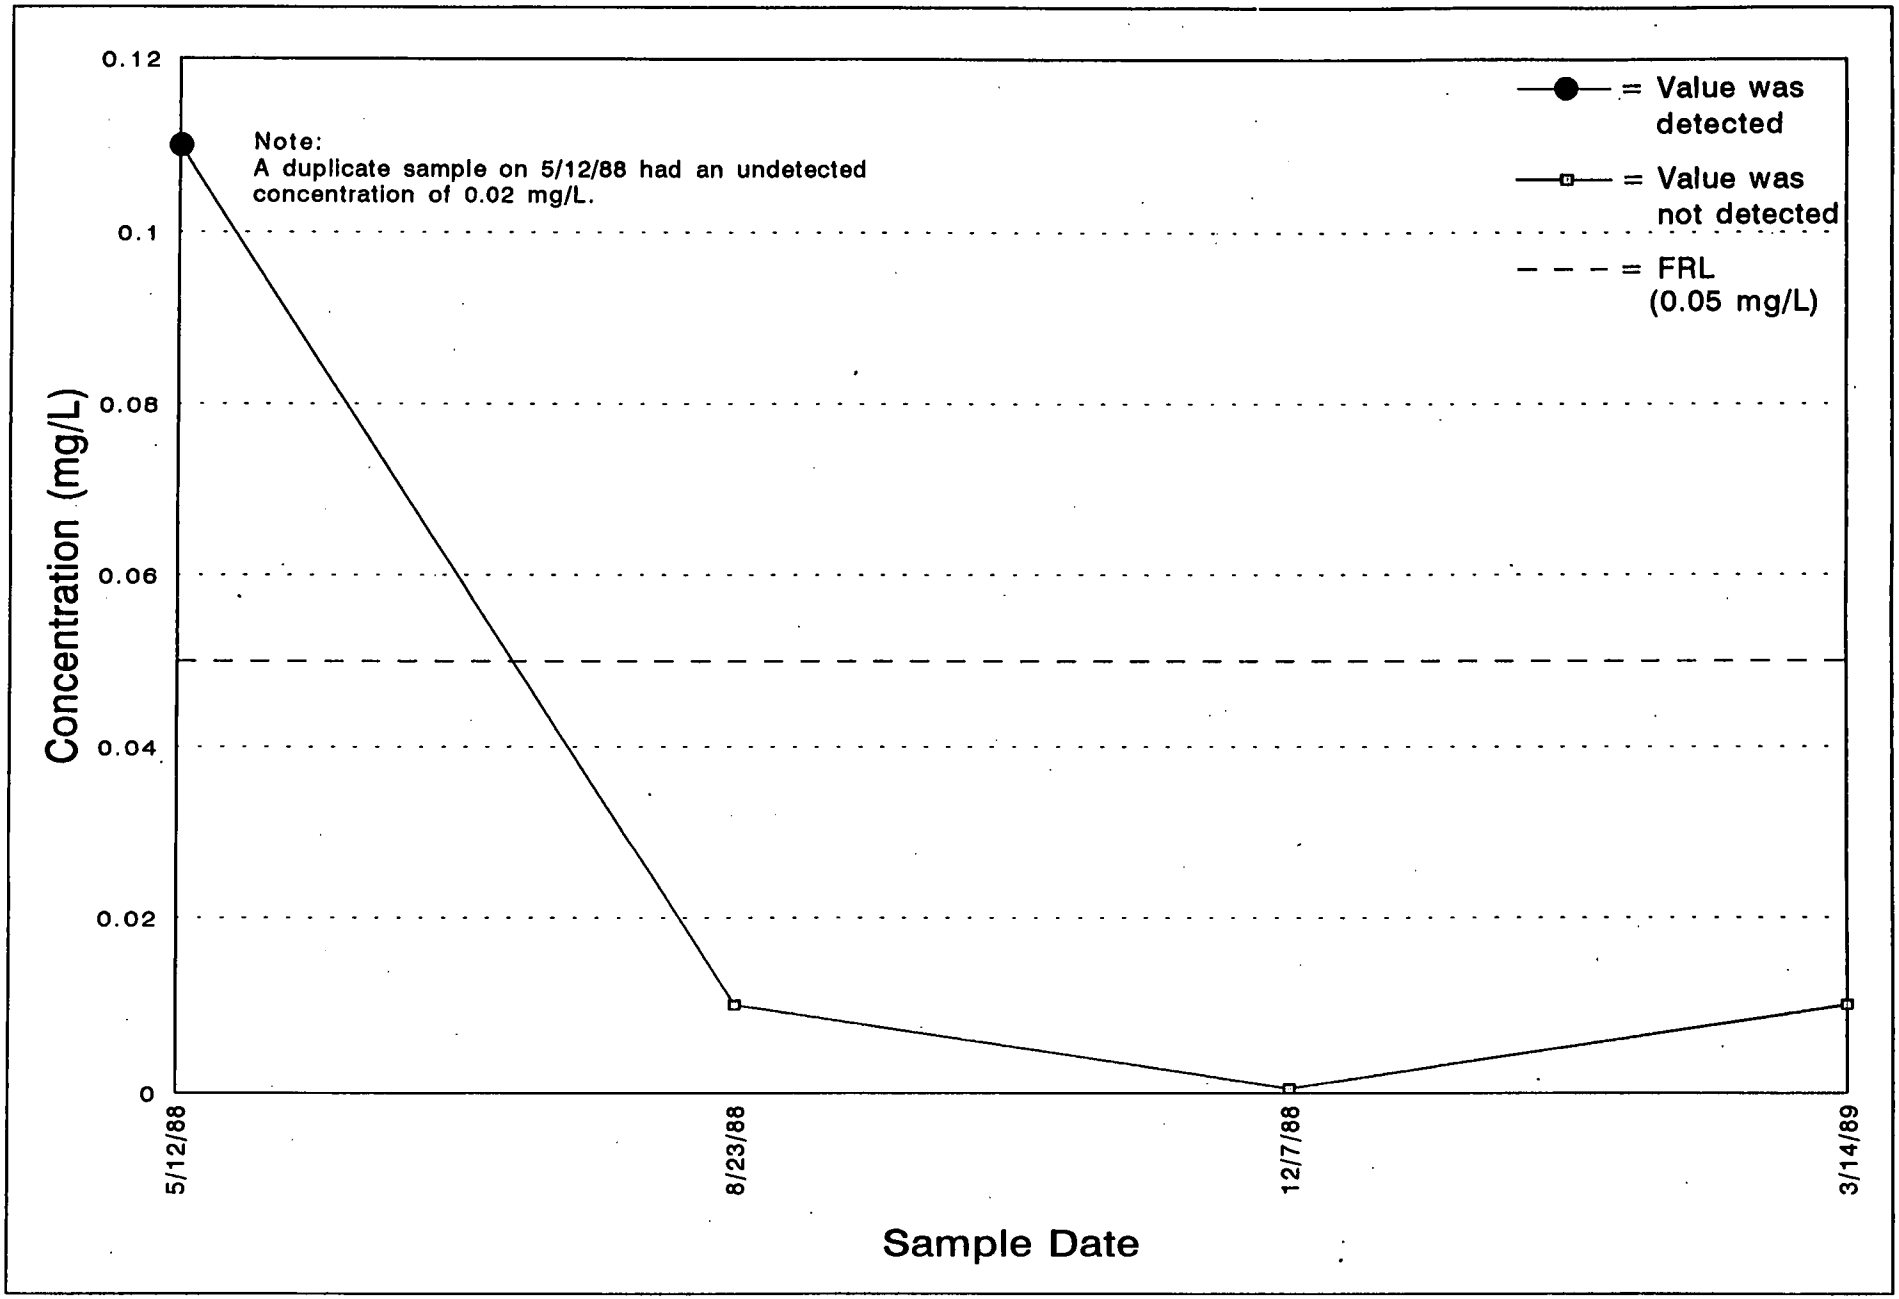

FIGURE A.3-47. SILVER CONCENTRATION VS. TIME, WELL 2036

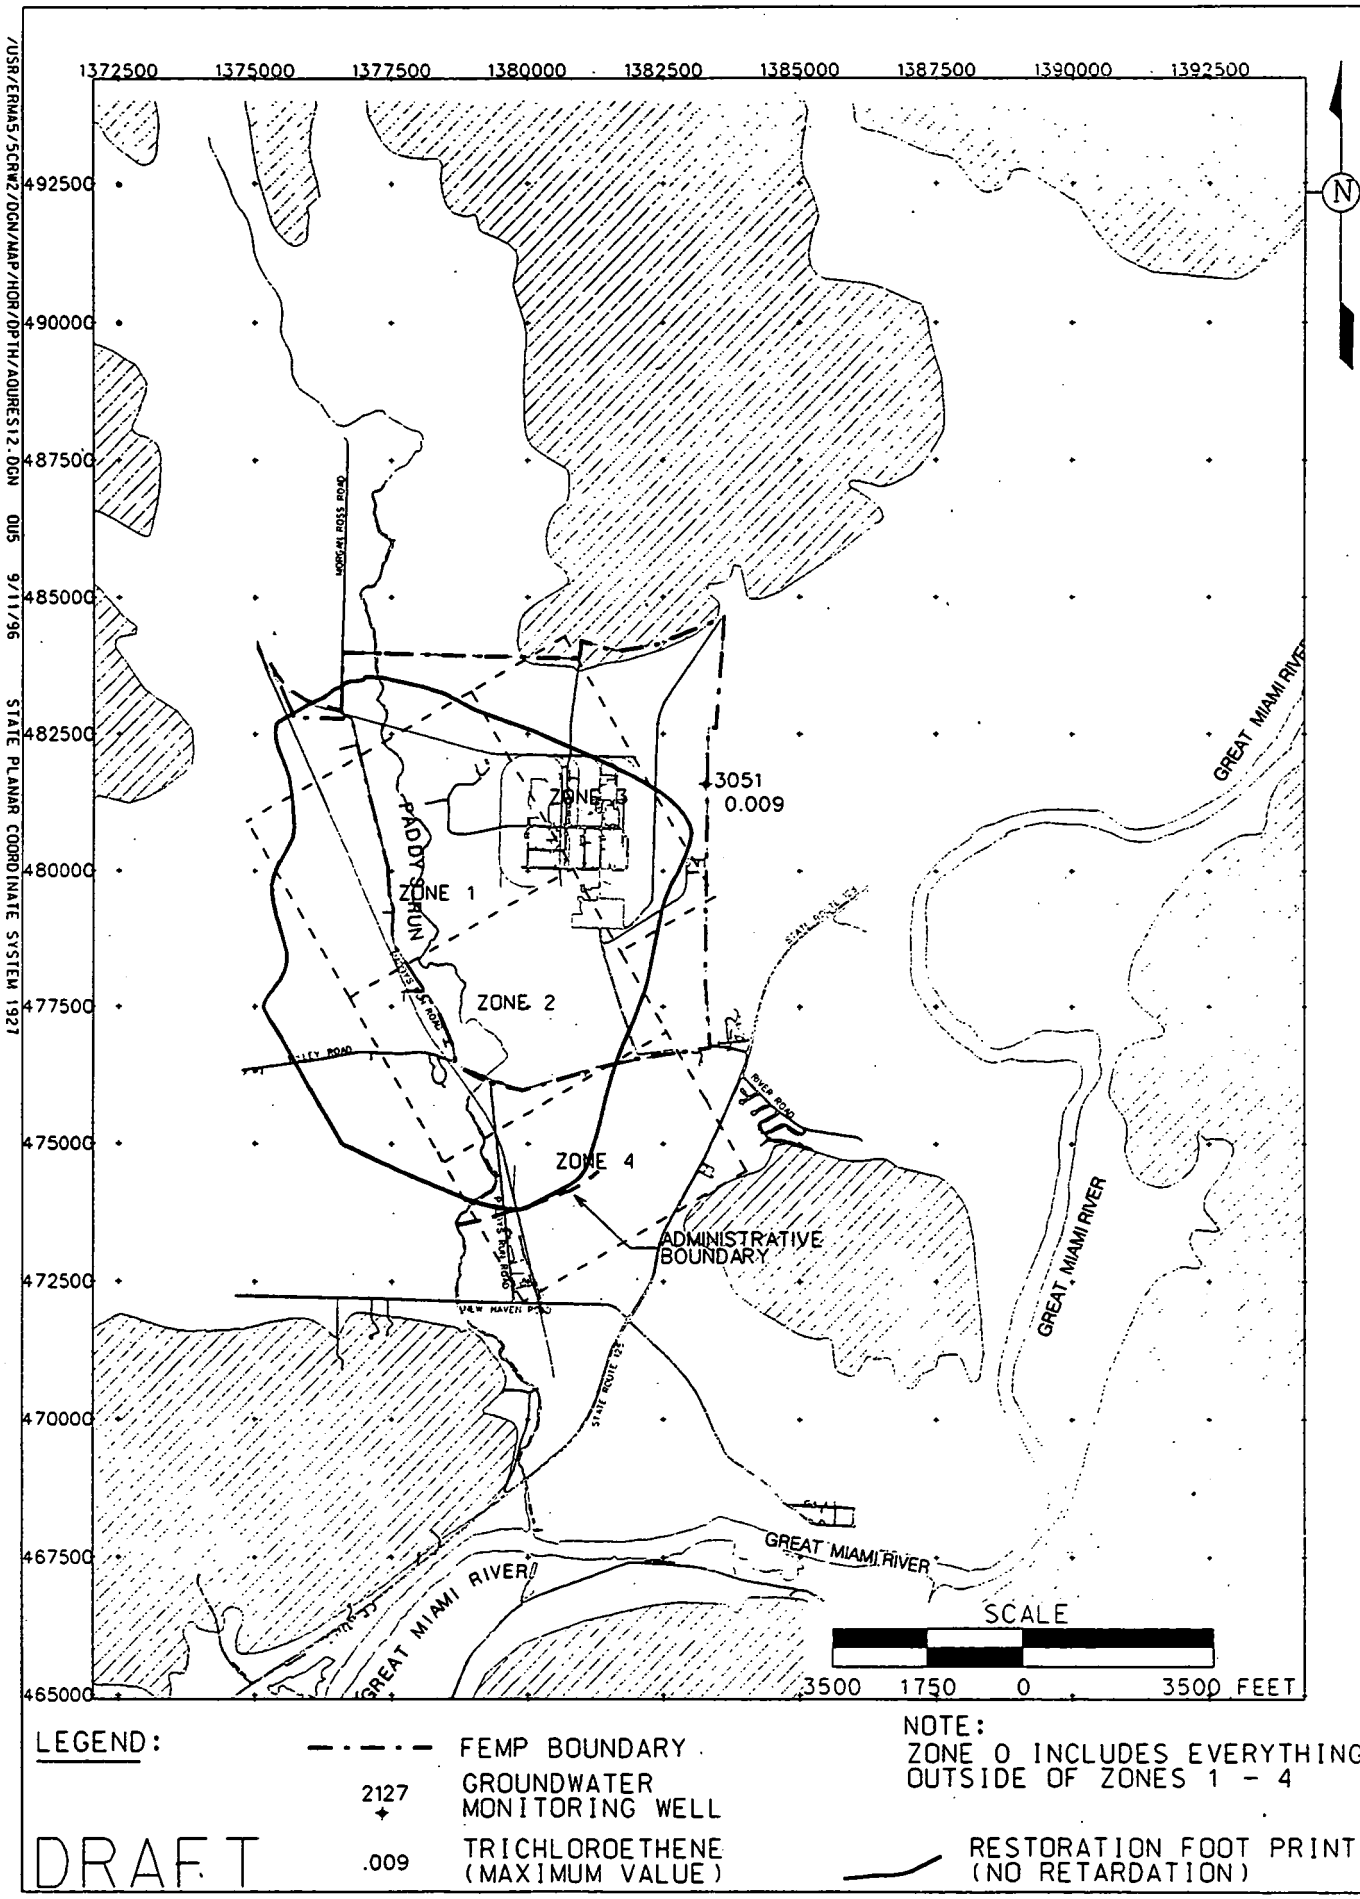

FIGURE A.3-48. FRL EXCEEDENCES FOR TRICHLOROETHENE LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

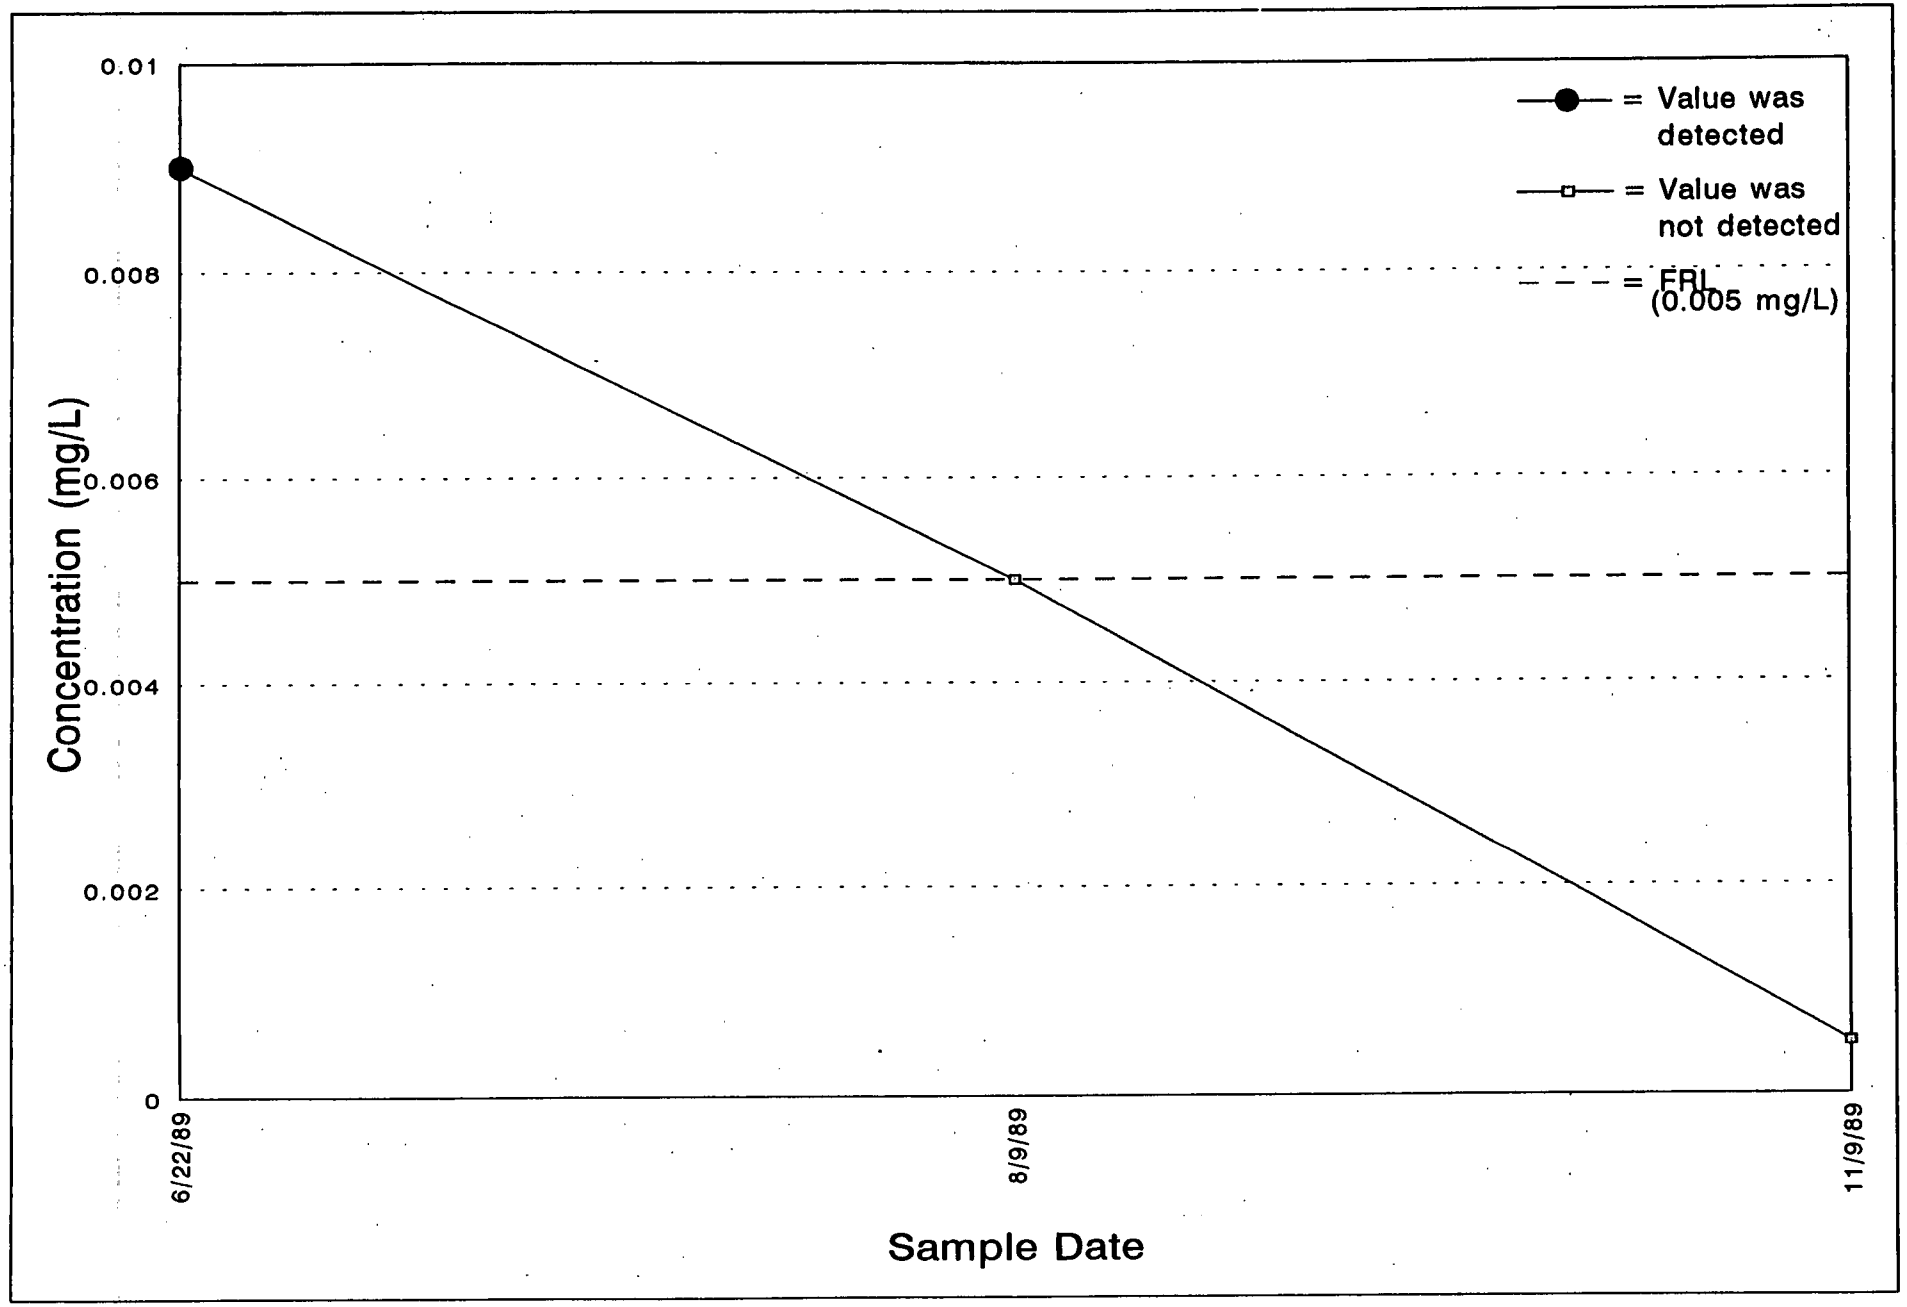

FIGURE A.3-49. TRICHLOROETHENE CONCENTRATION VS. TIME, WELL 3051

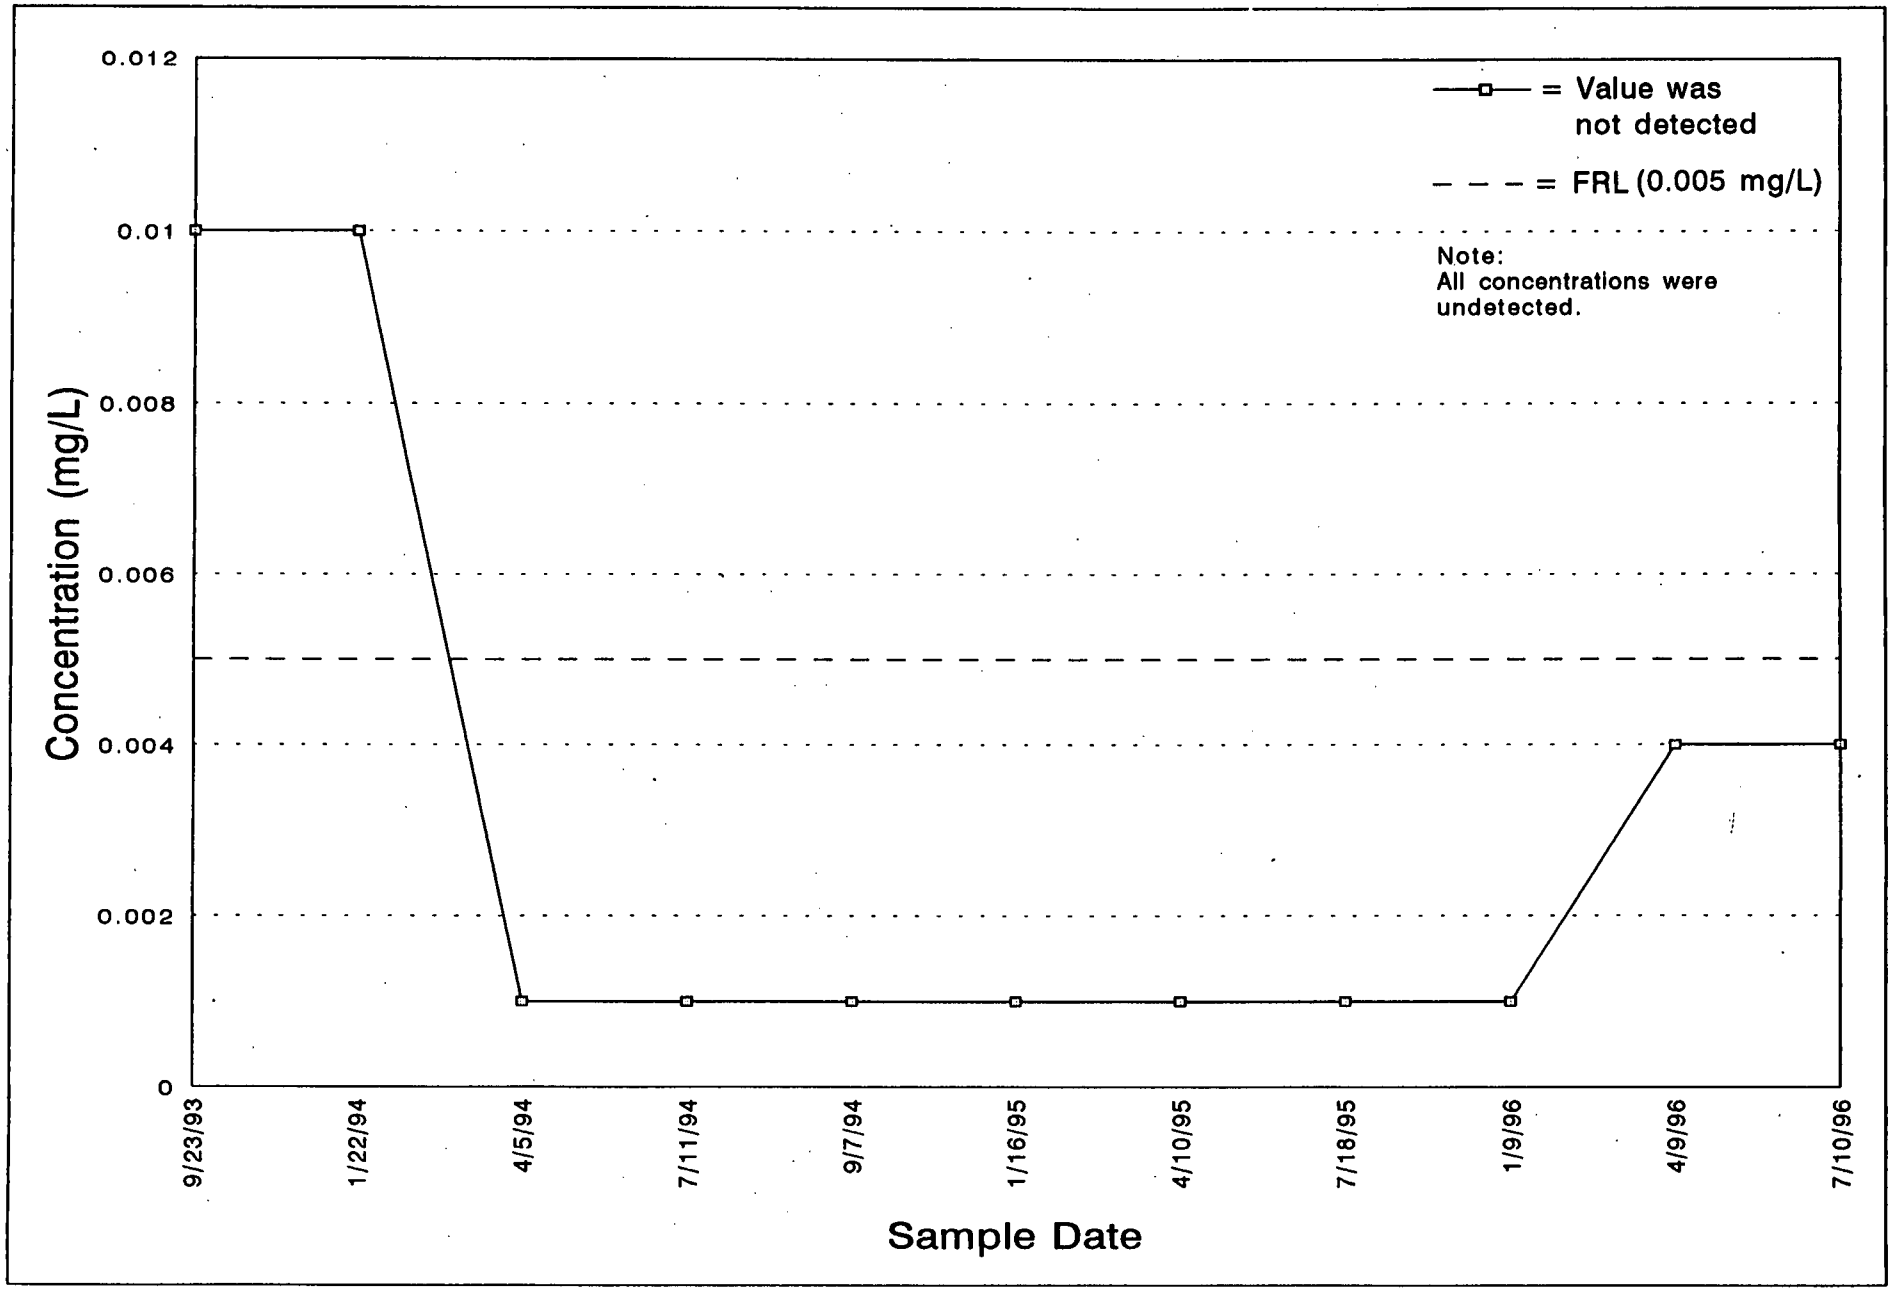

FIGURE A.3-50. TRICHLOROETHENE CONCENTRATION VS. TIME, WELL 31217

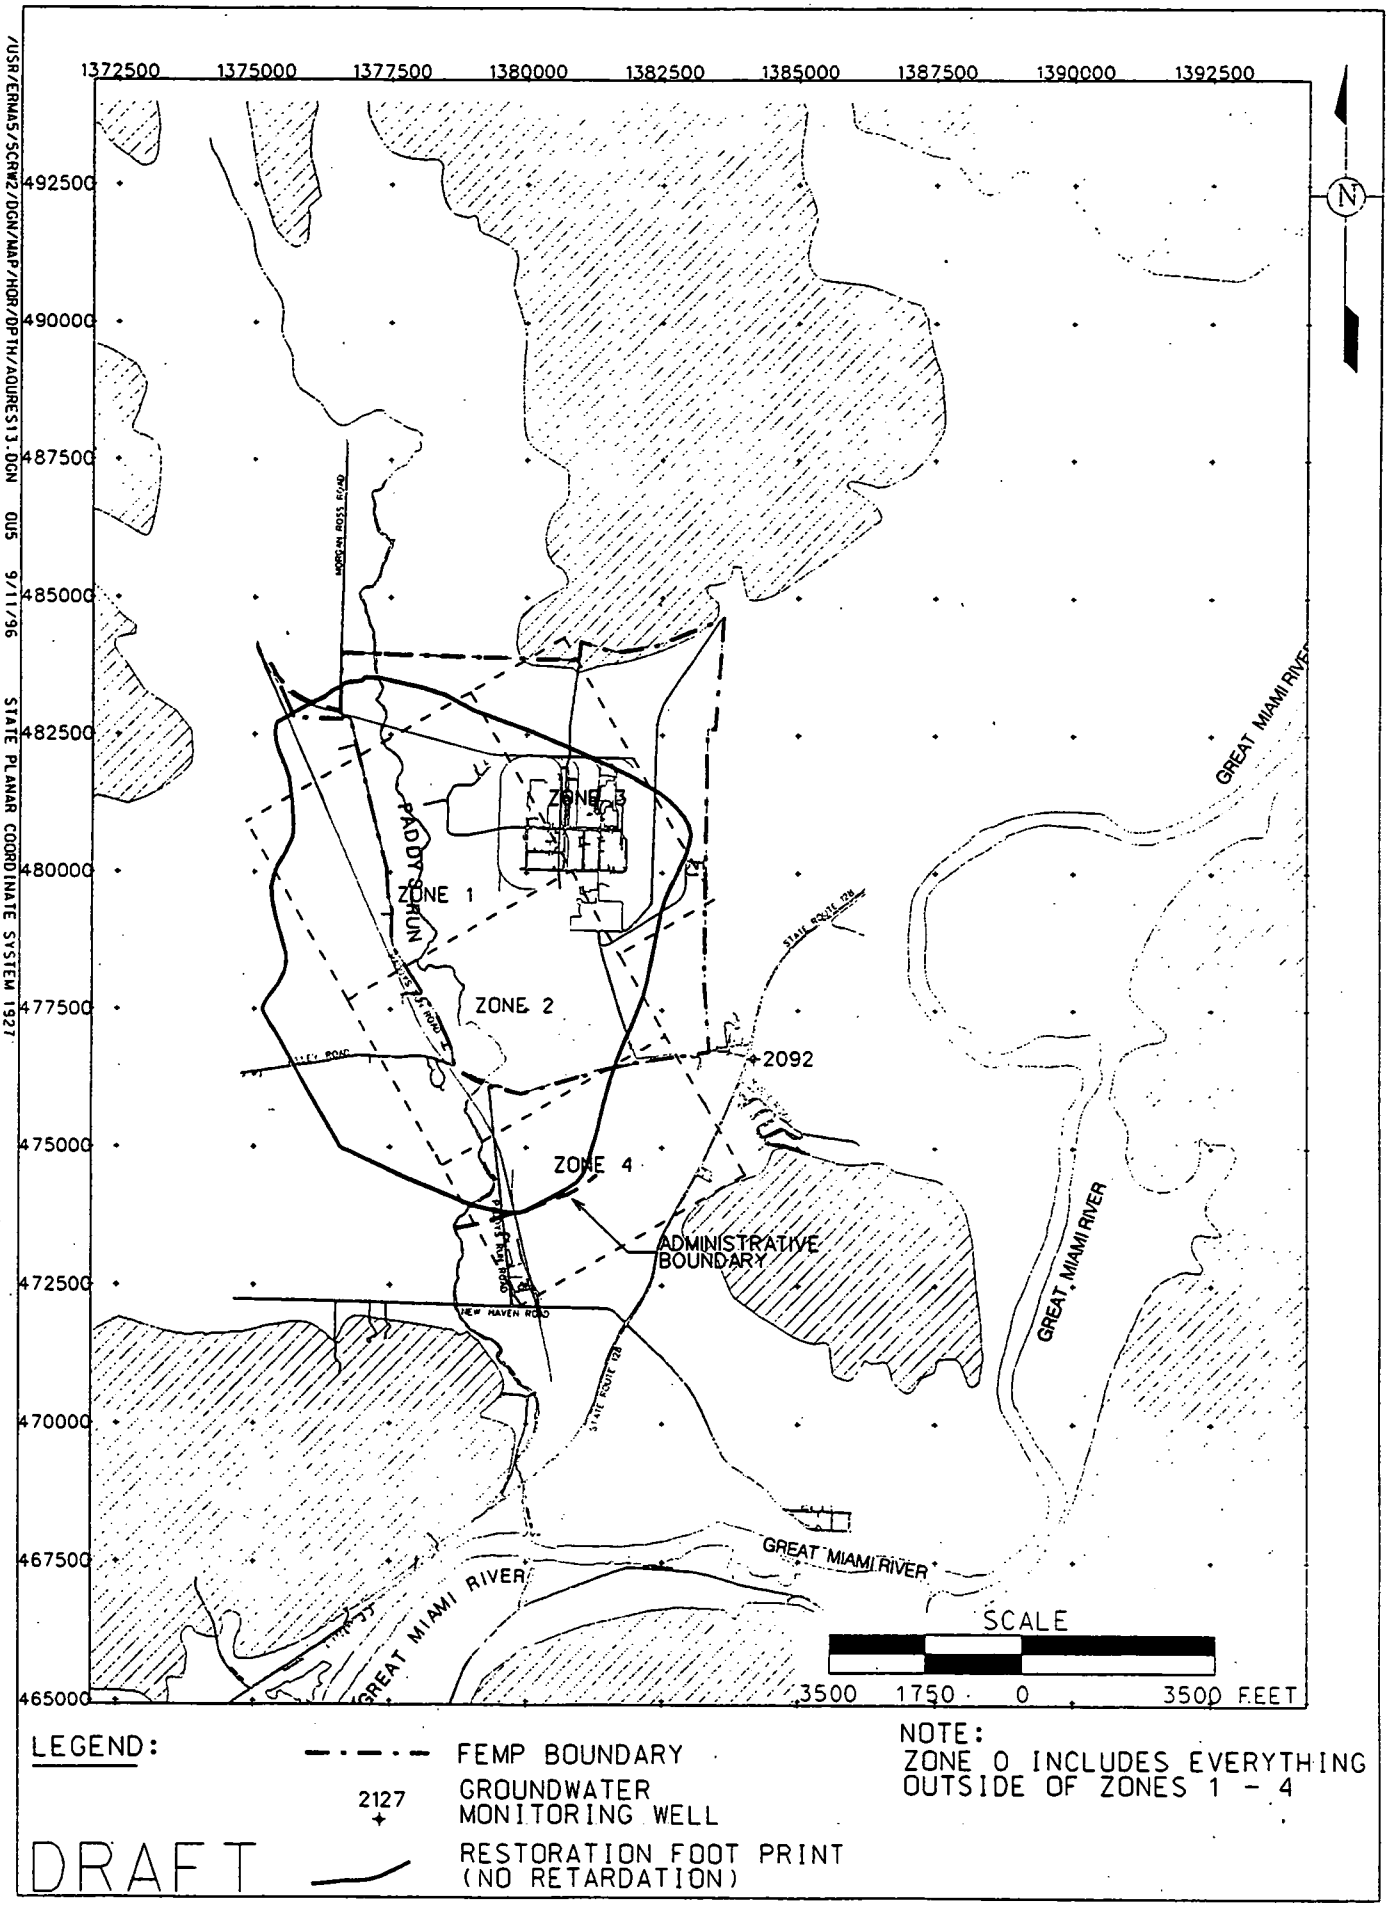

FIGURE A.3-51. LOCATION OF FRL EXCEEDENCES FOR THORIUM-228 AND THORIUM-232 LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

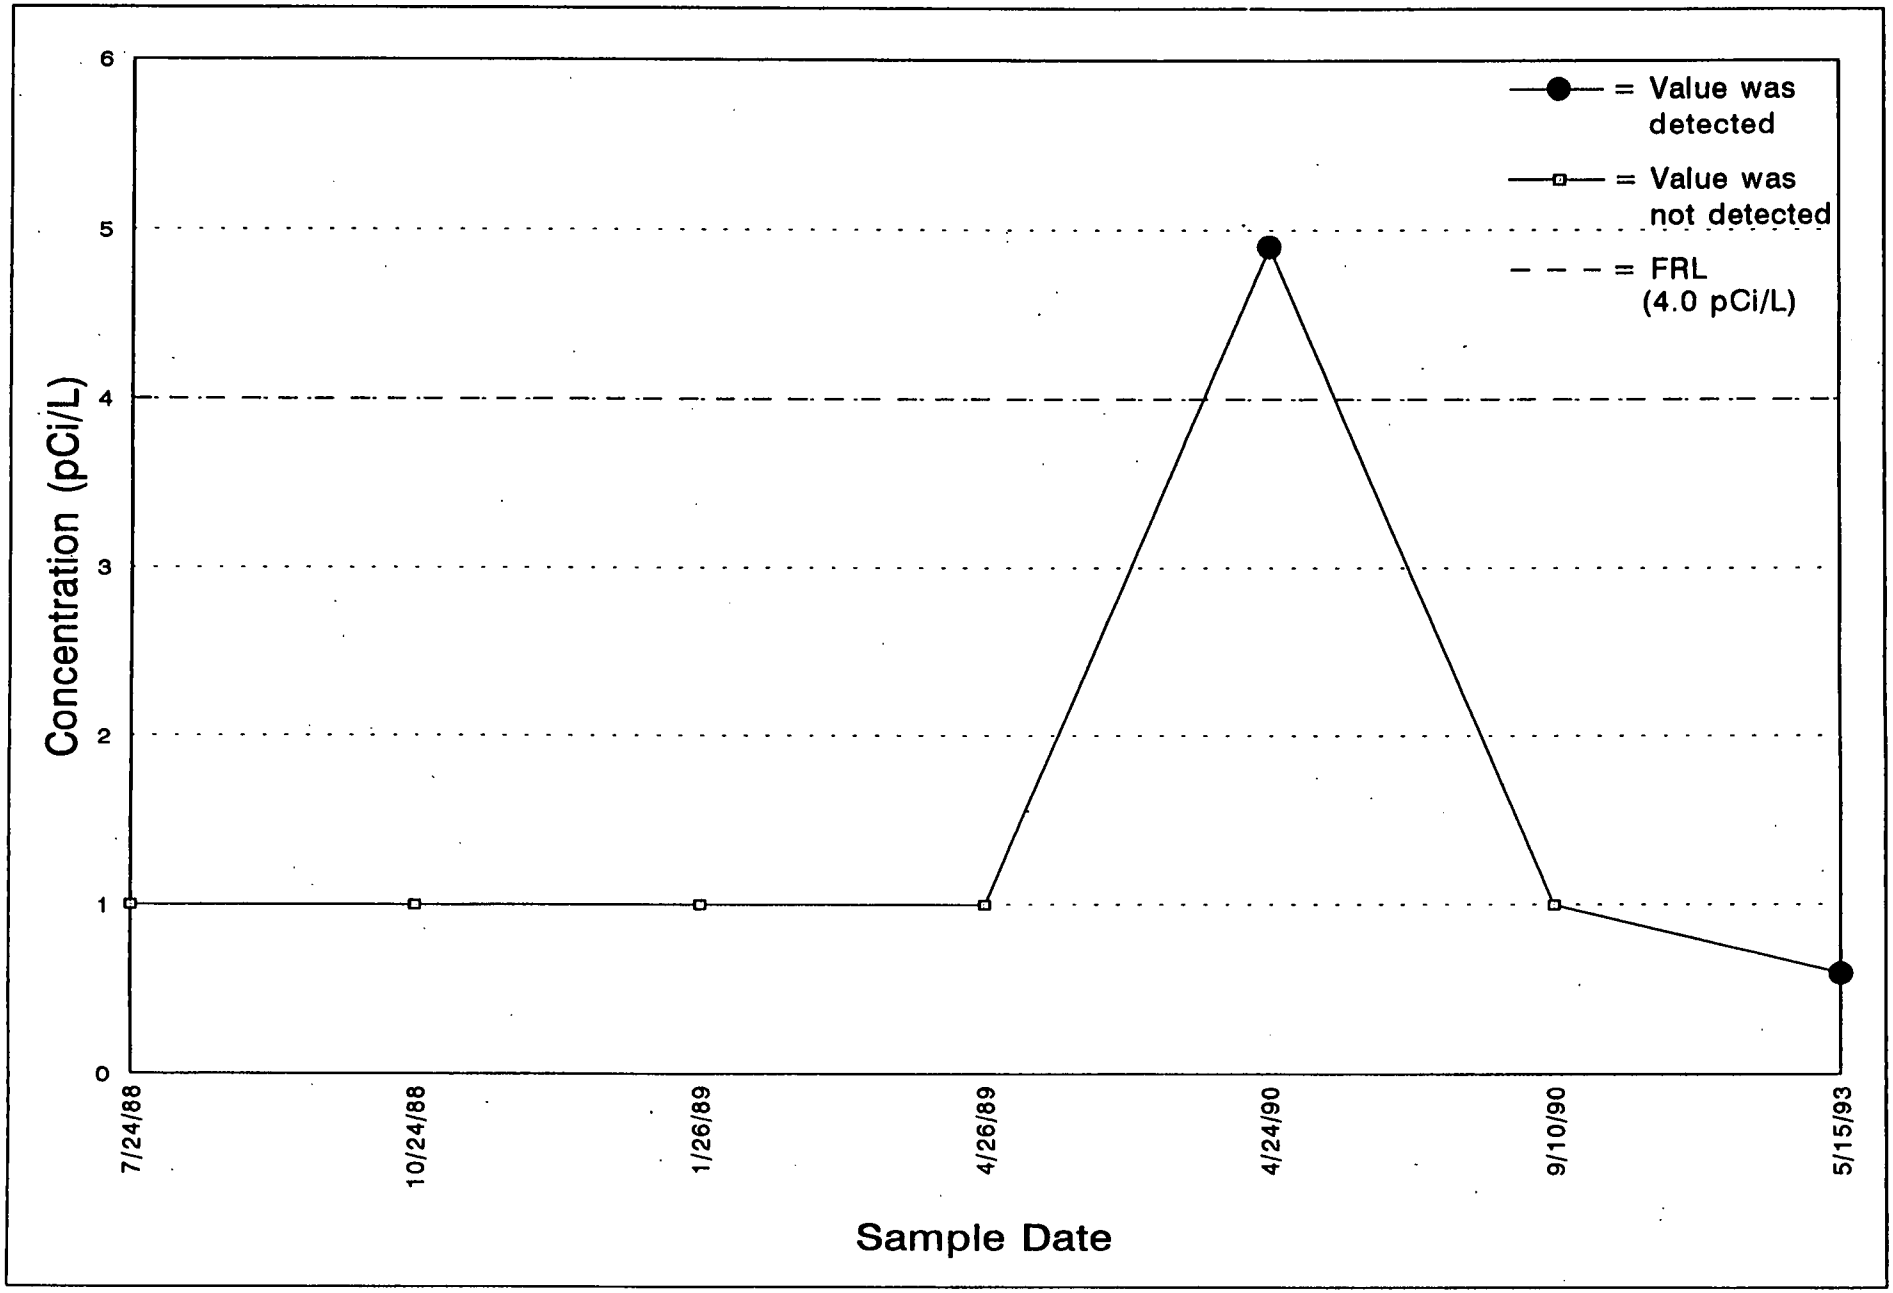

FIGURE A.3-52. THORIUM-228 CONCENTRATION VS. TIME, WELL 2092

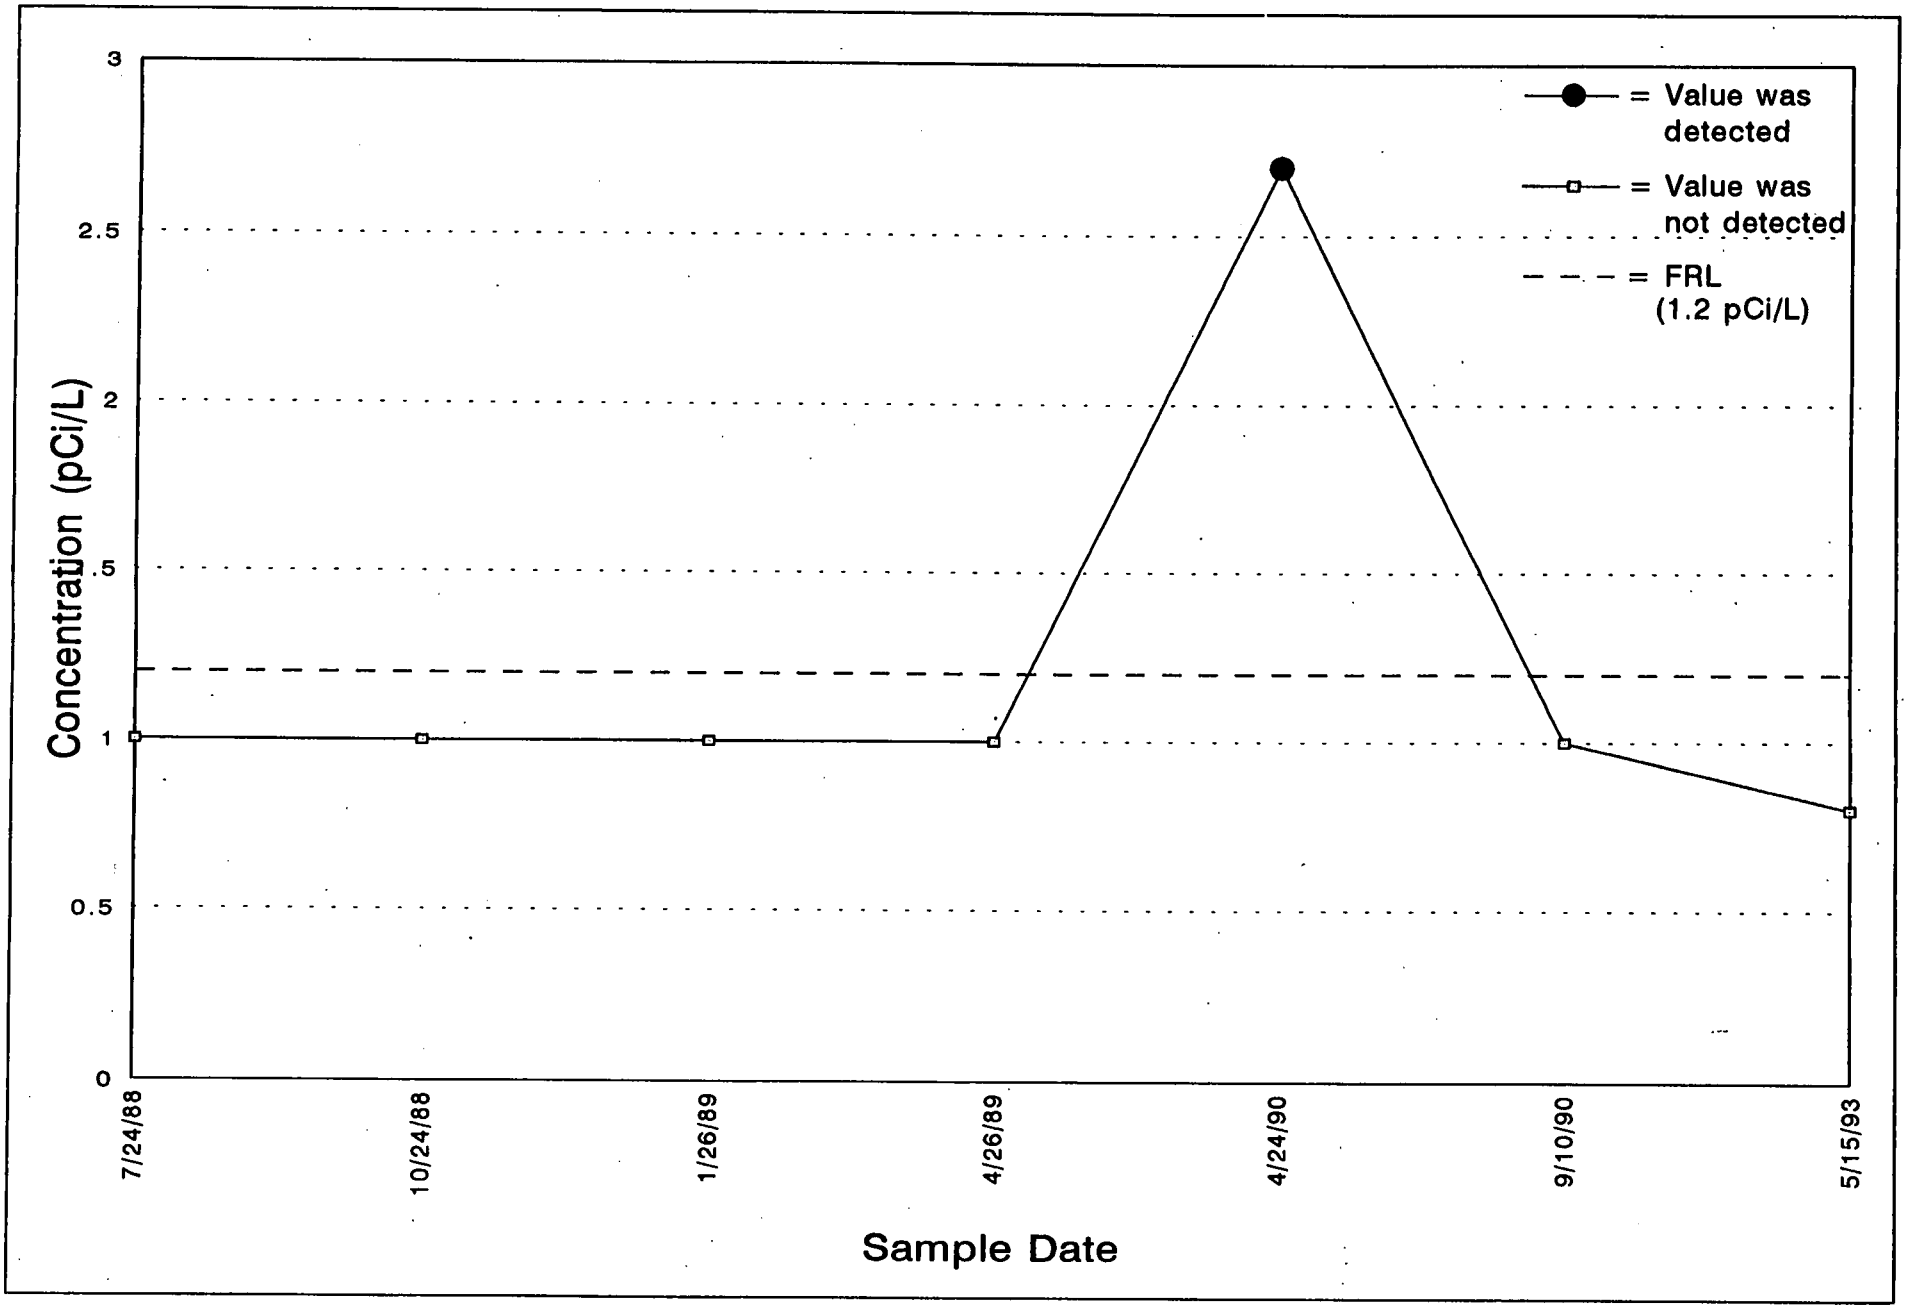

FIGURE A.3-53. THORIUM-232 CONCENTRATION VS. TIME, WELL 2092

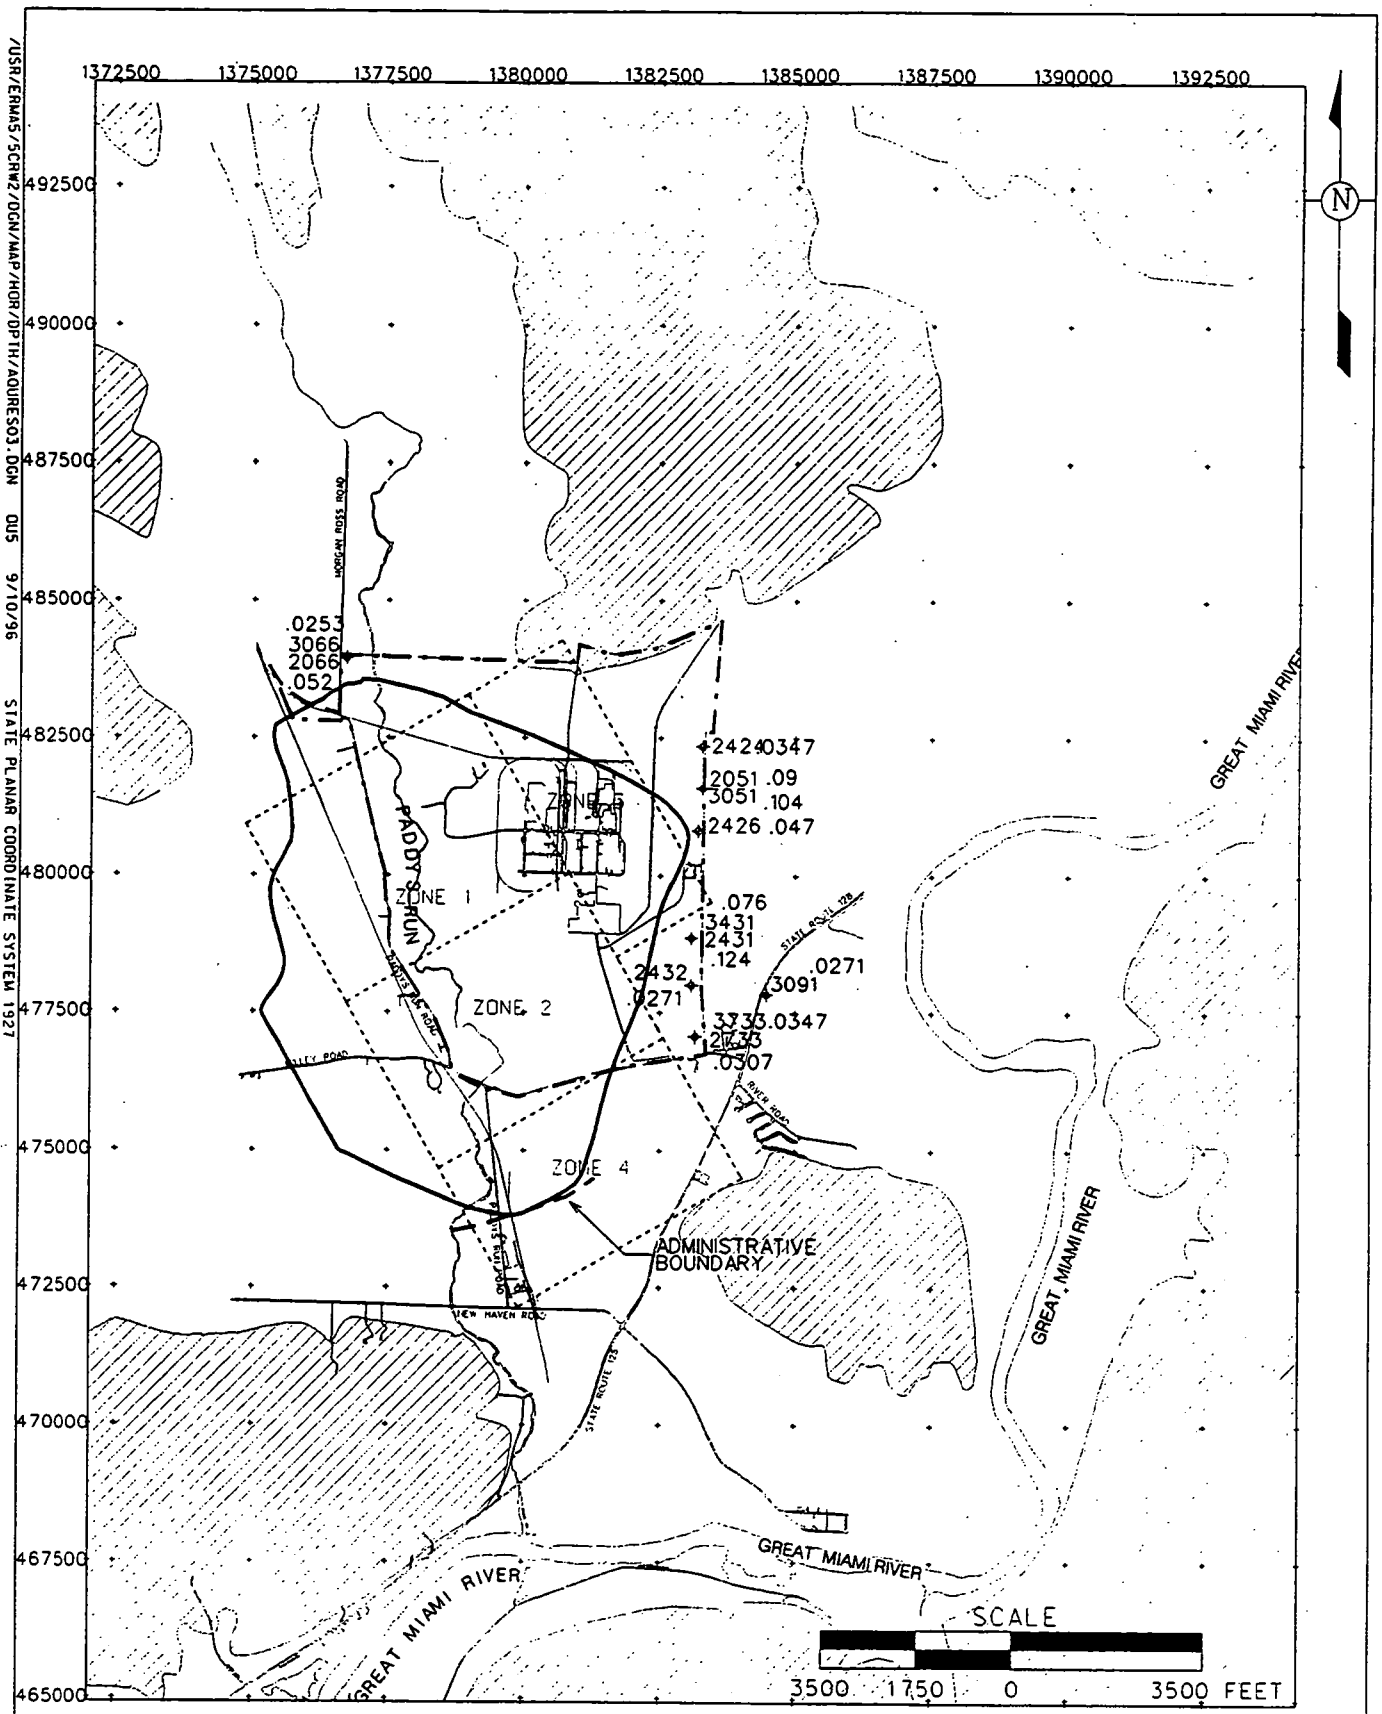

LEGEND:

FEMP BOUNDARY

2127 GROUNDWATER MONITORING WELL

12.8 ZINC (MAXIMUM VALUE)

RESTORATION FOOT PRINT (NO RETARDATION)

NOTE:
ZONE 0 INCLUDES EVERYTHING OUTSIDE OF ZONES 1 - 4

DRAFT

FIGURE A.3-54. FRL EXCEEDENCES FOR ZINC LOCATED OUTSIDE OF THE RESTORATION FOOTPRINT AND NORTH OF ADMINISTRATION BOUNDARY

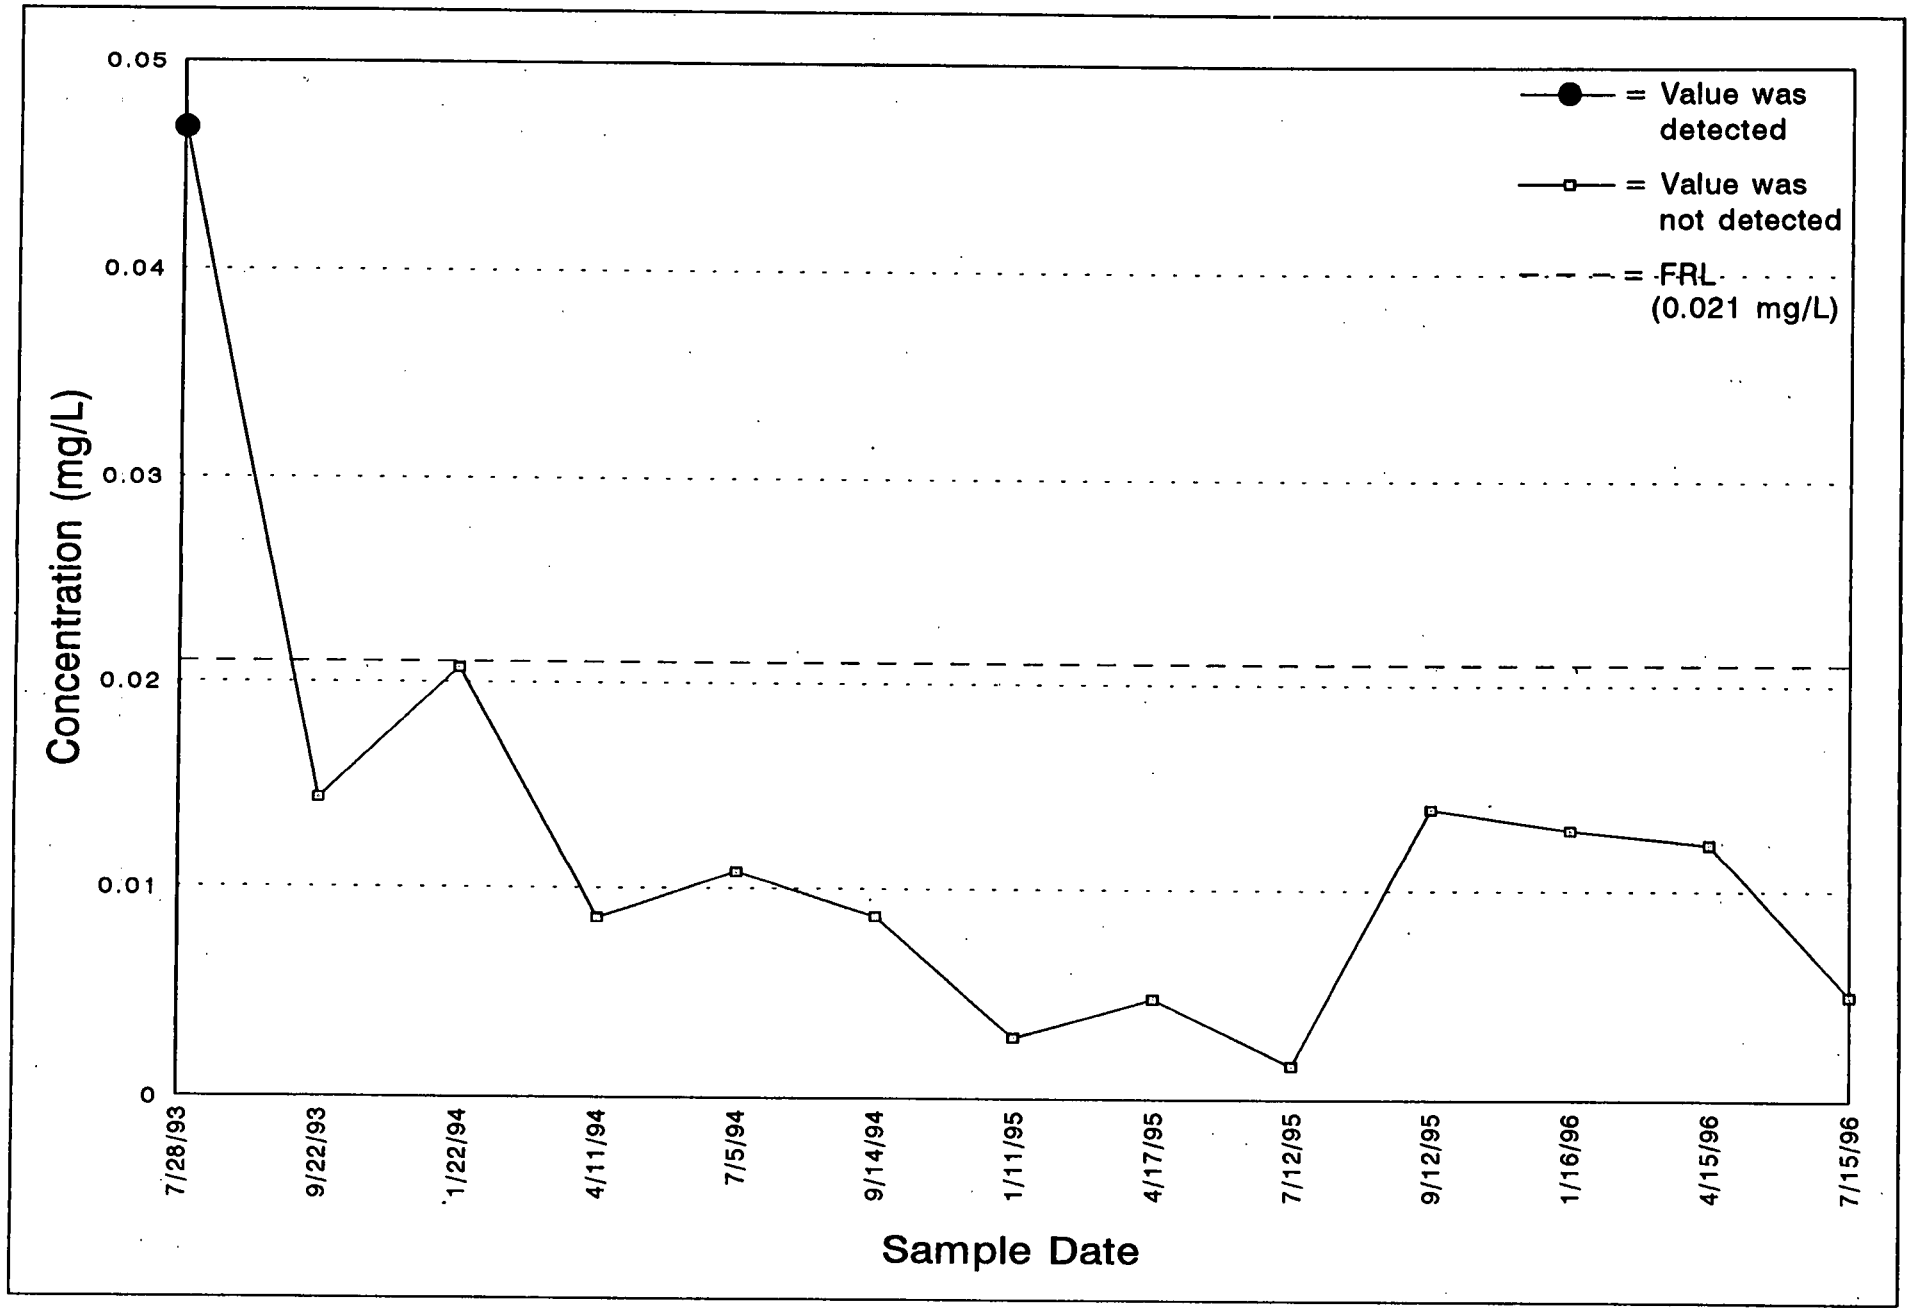

FIGURE A.3-55. ZINC CONCENTRATION VS. TIME, WELL 2426

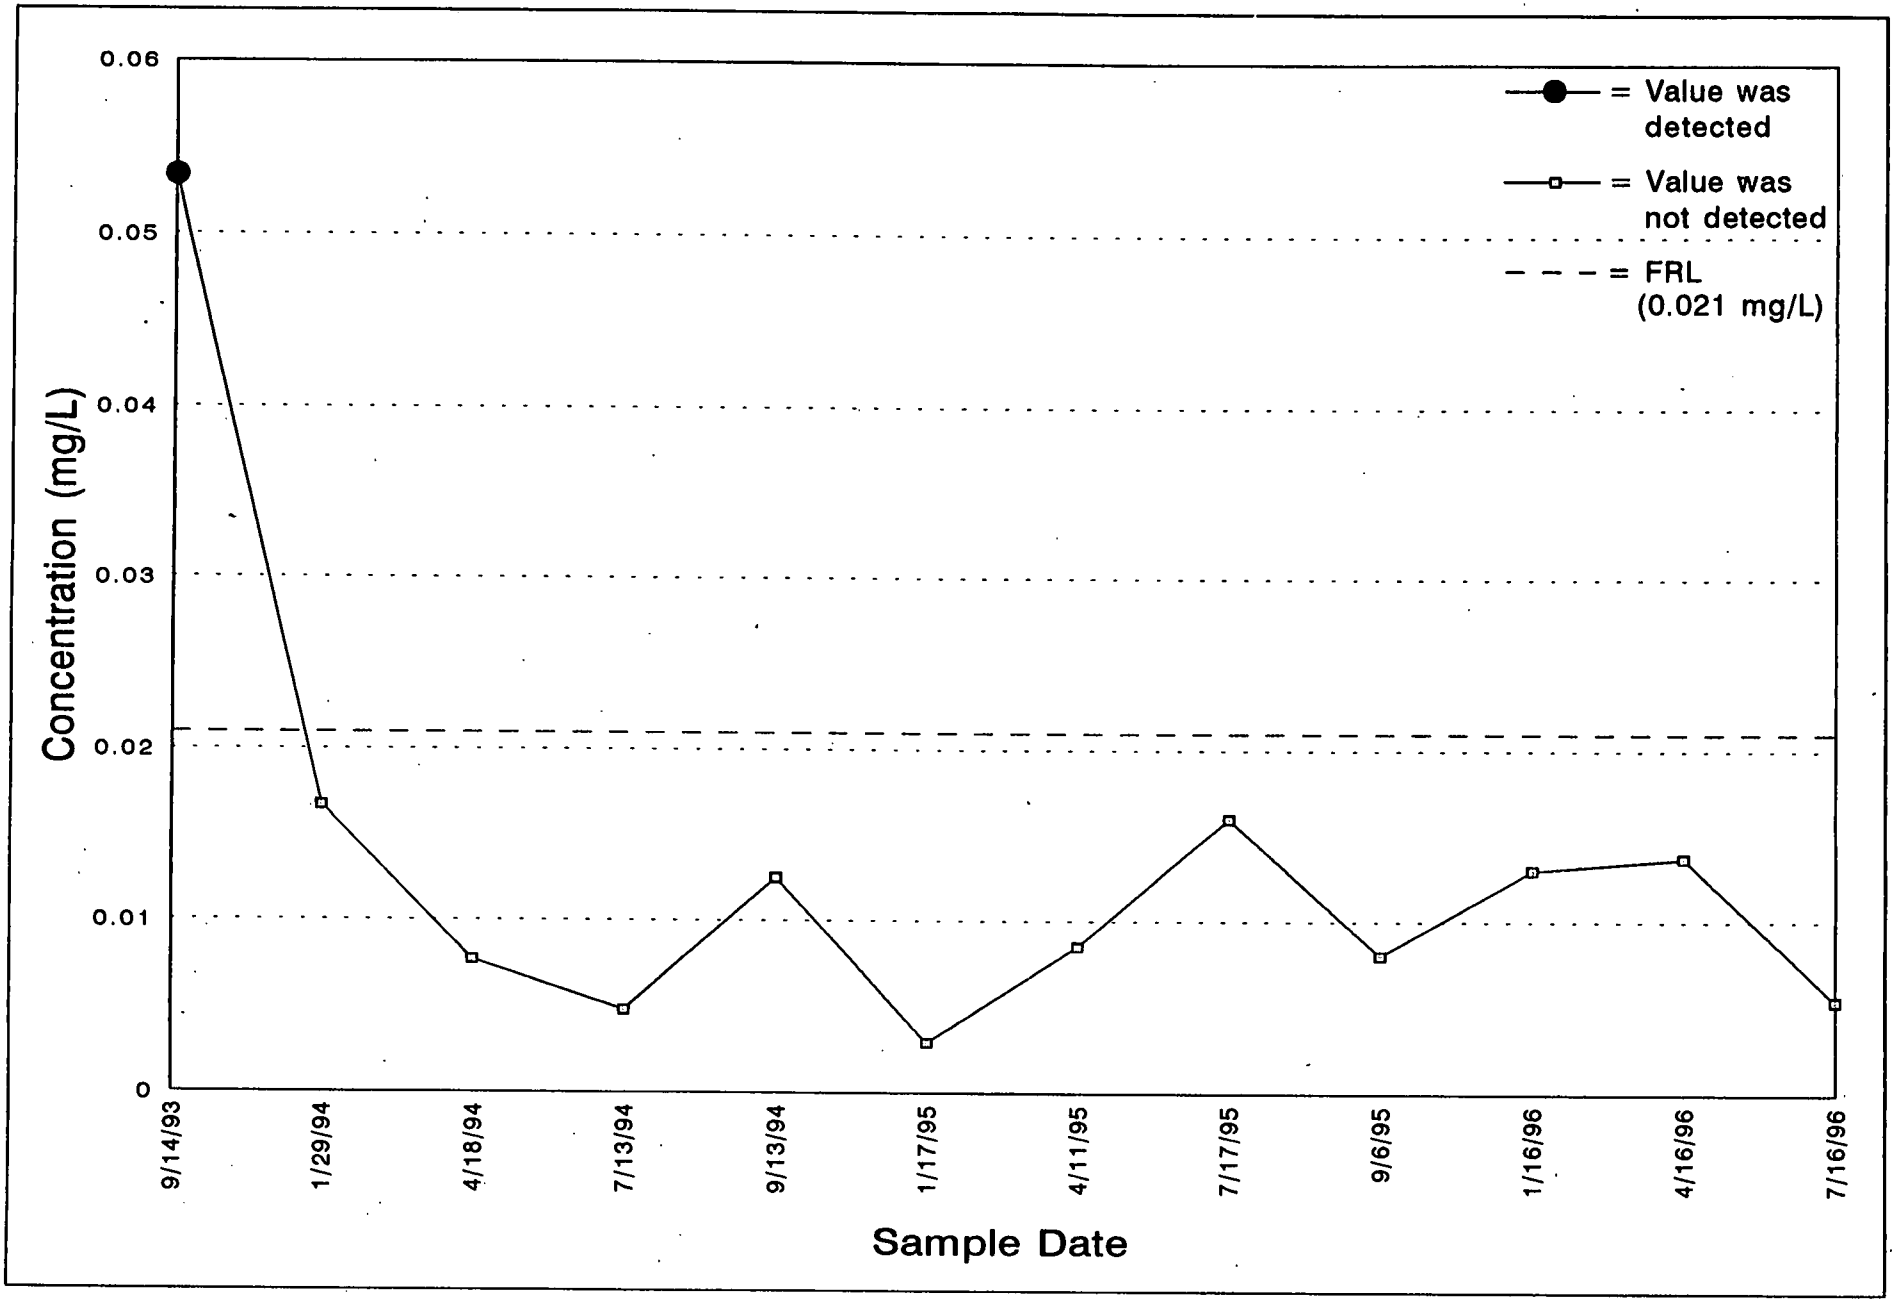

FIGURE A.3-56. ZINC CONCENTRATION VS. TIME, WELL 2431

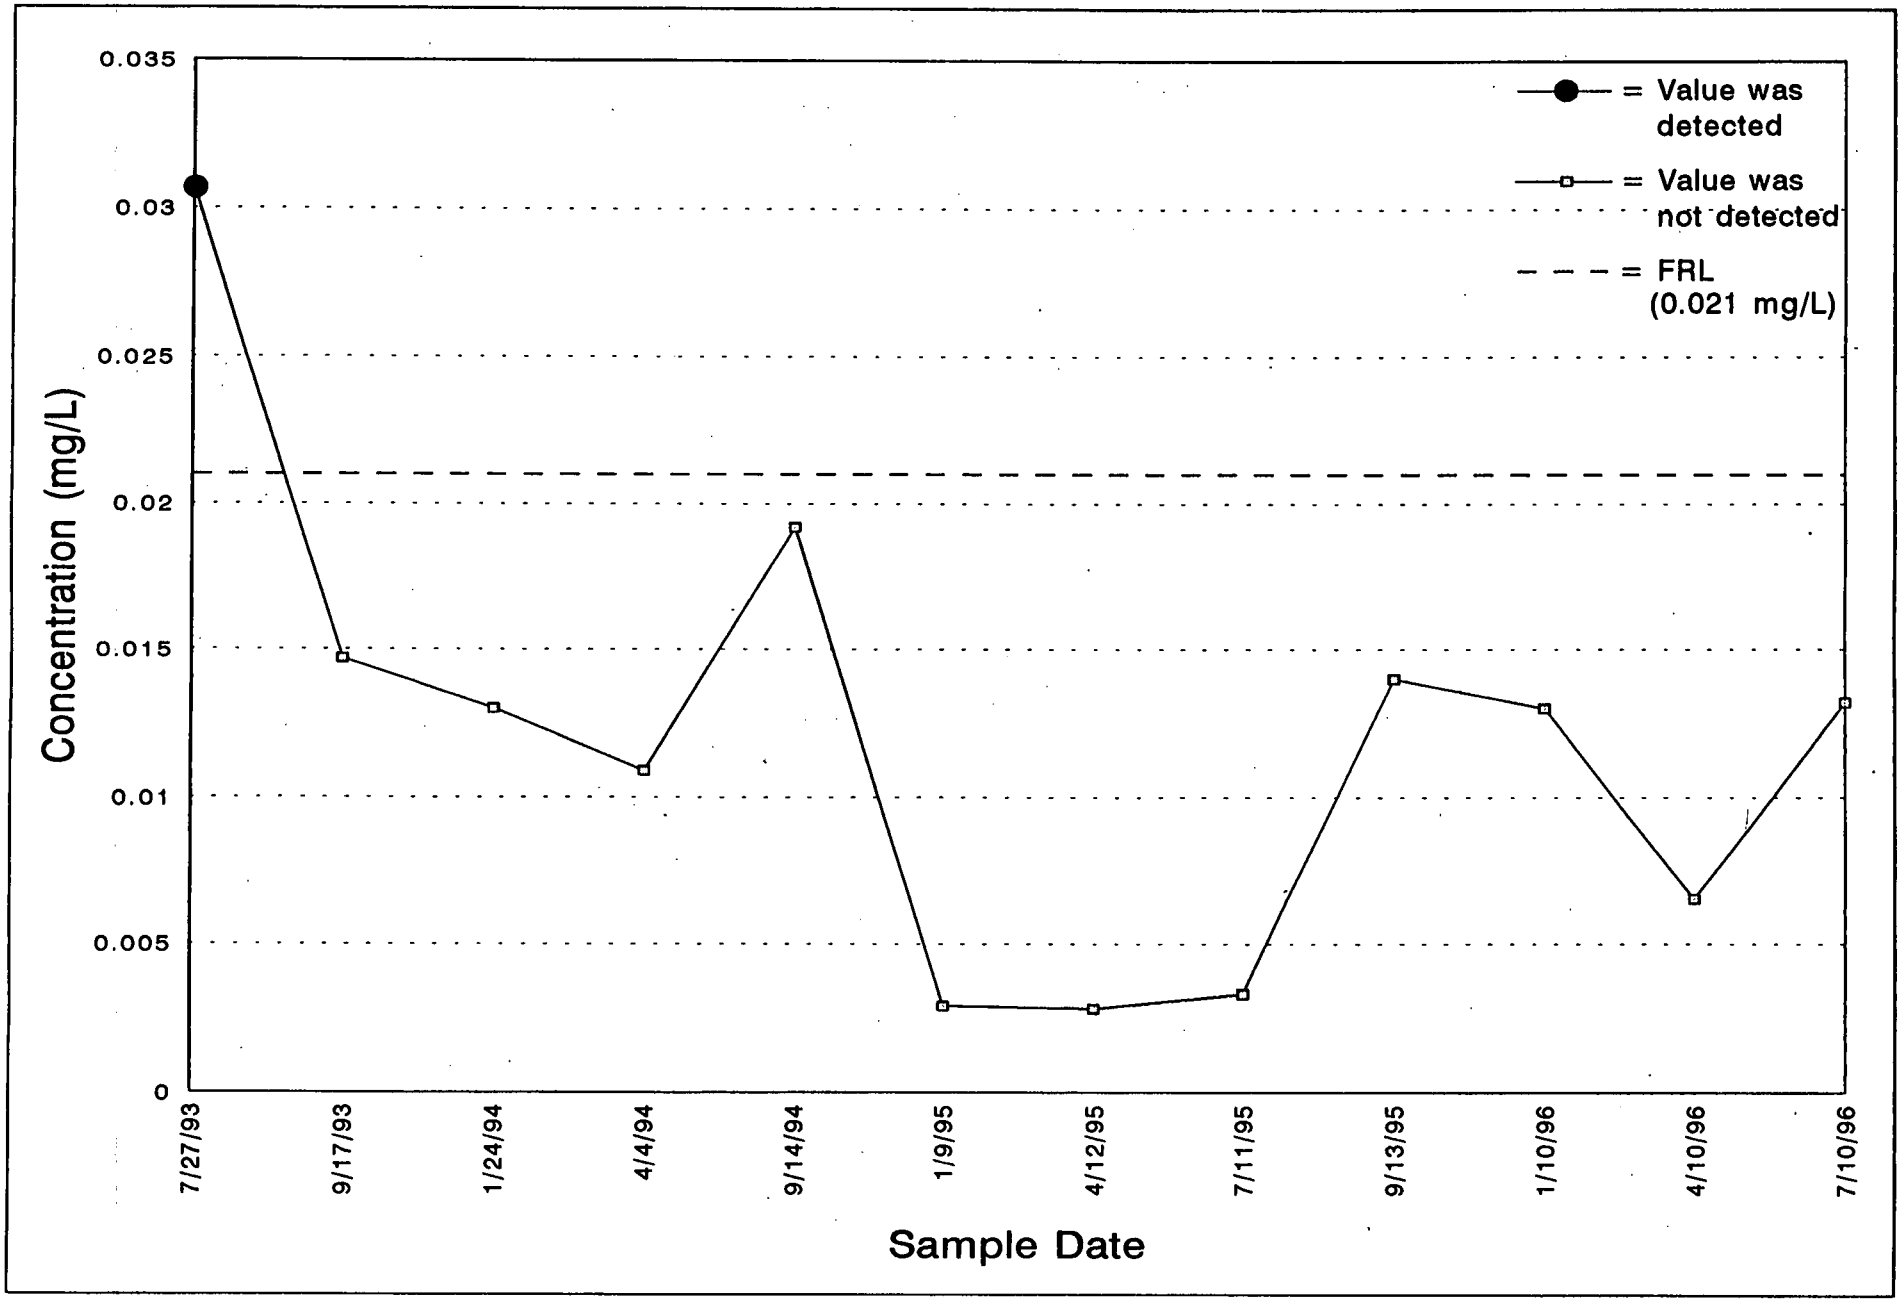

FIGURE A.3-57. ZINC CONCENTRATION VS. TIME, WELL 3733

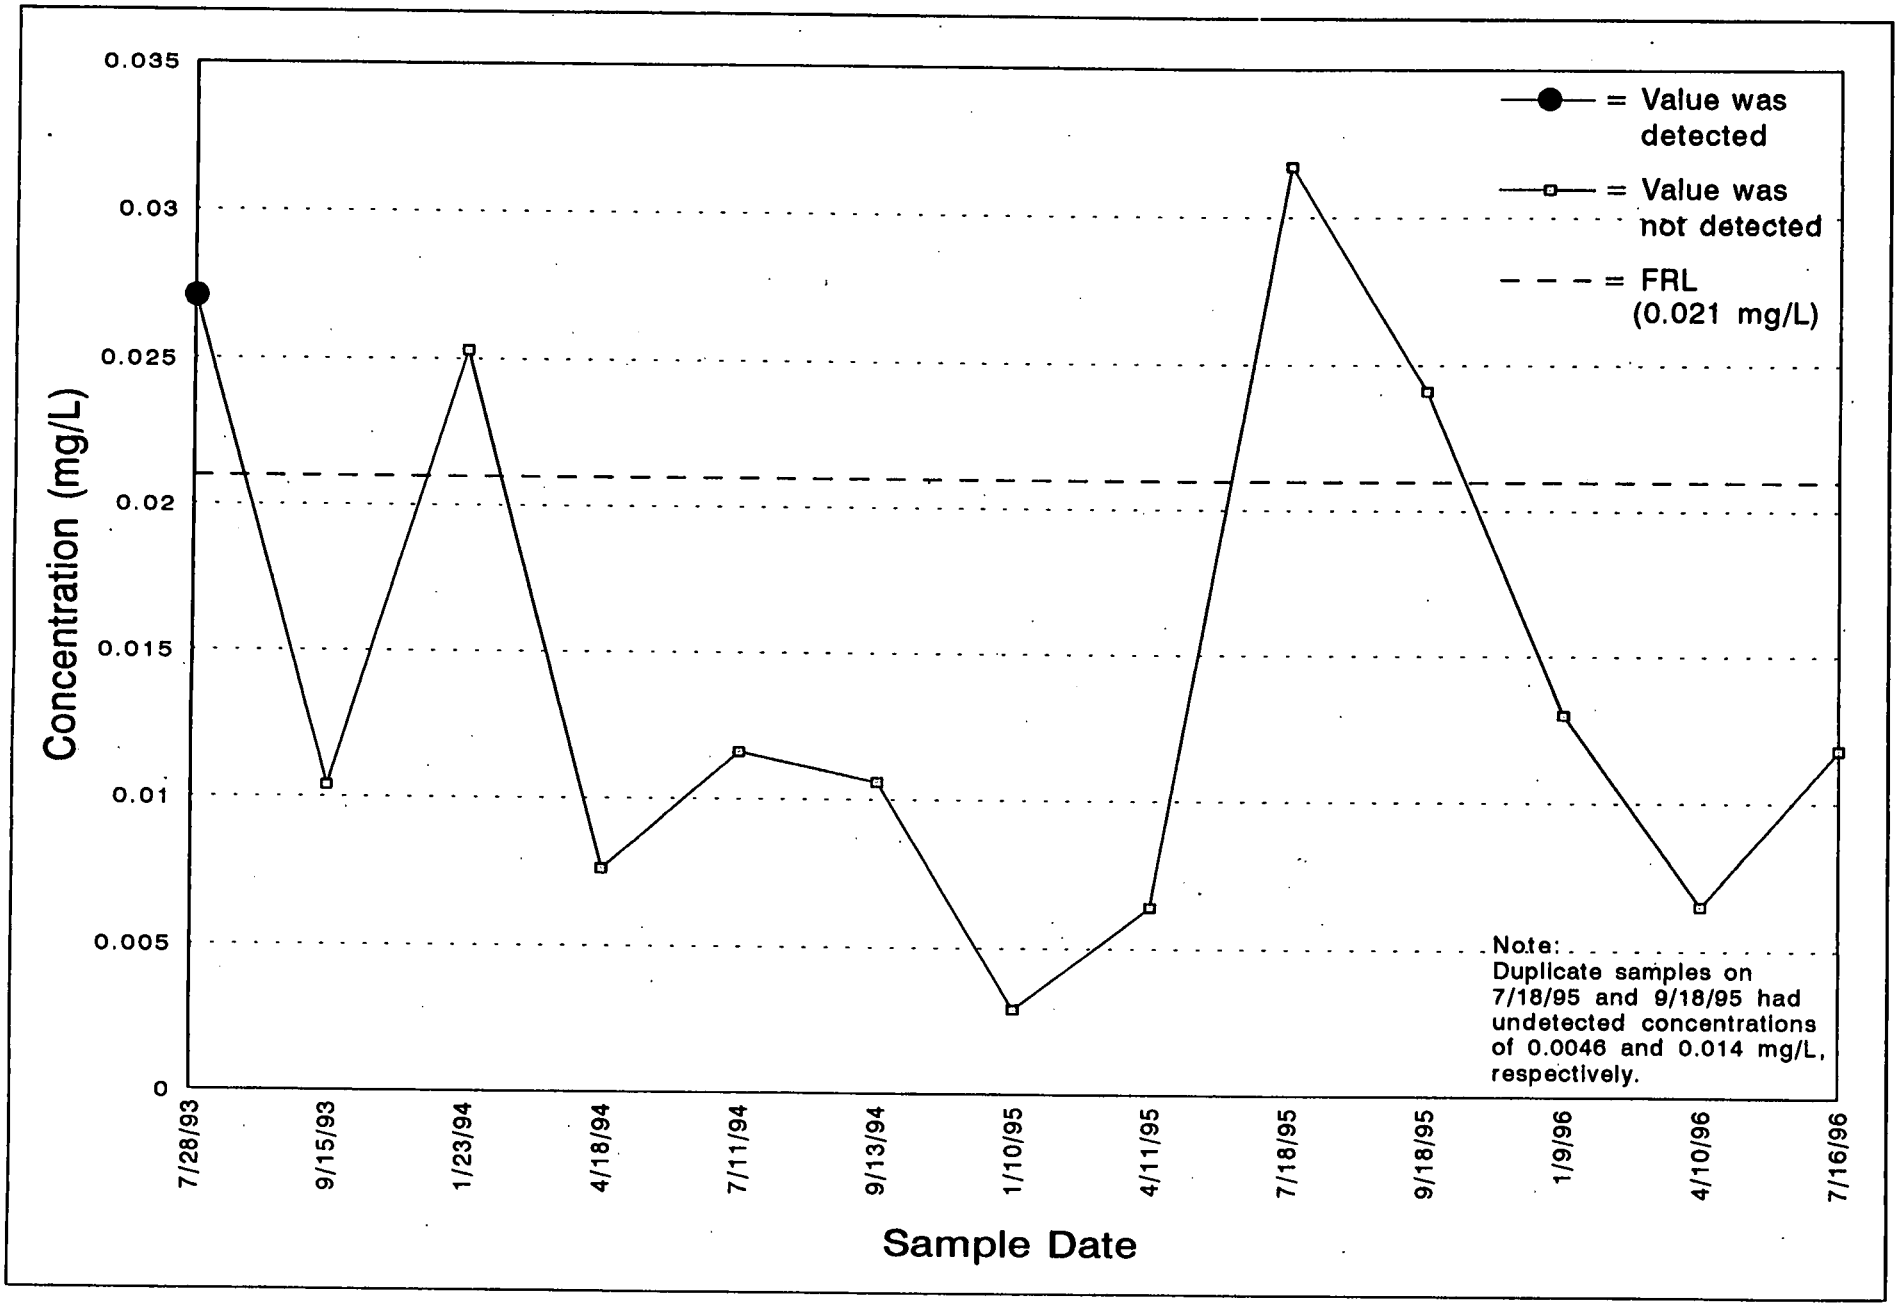

FIGURE A.3-58. ZINC CONCENTRATION VS. TIME, WELL 2432

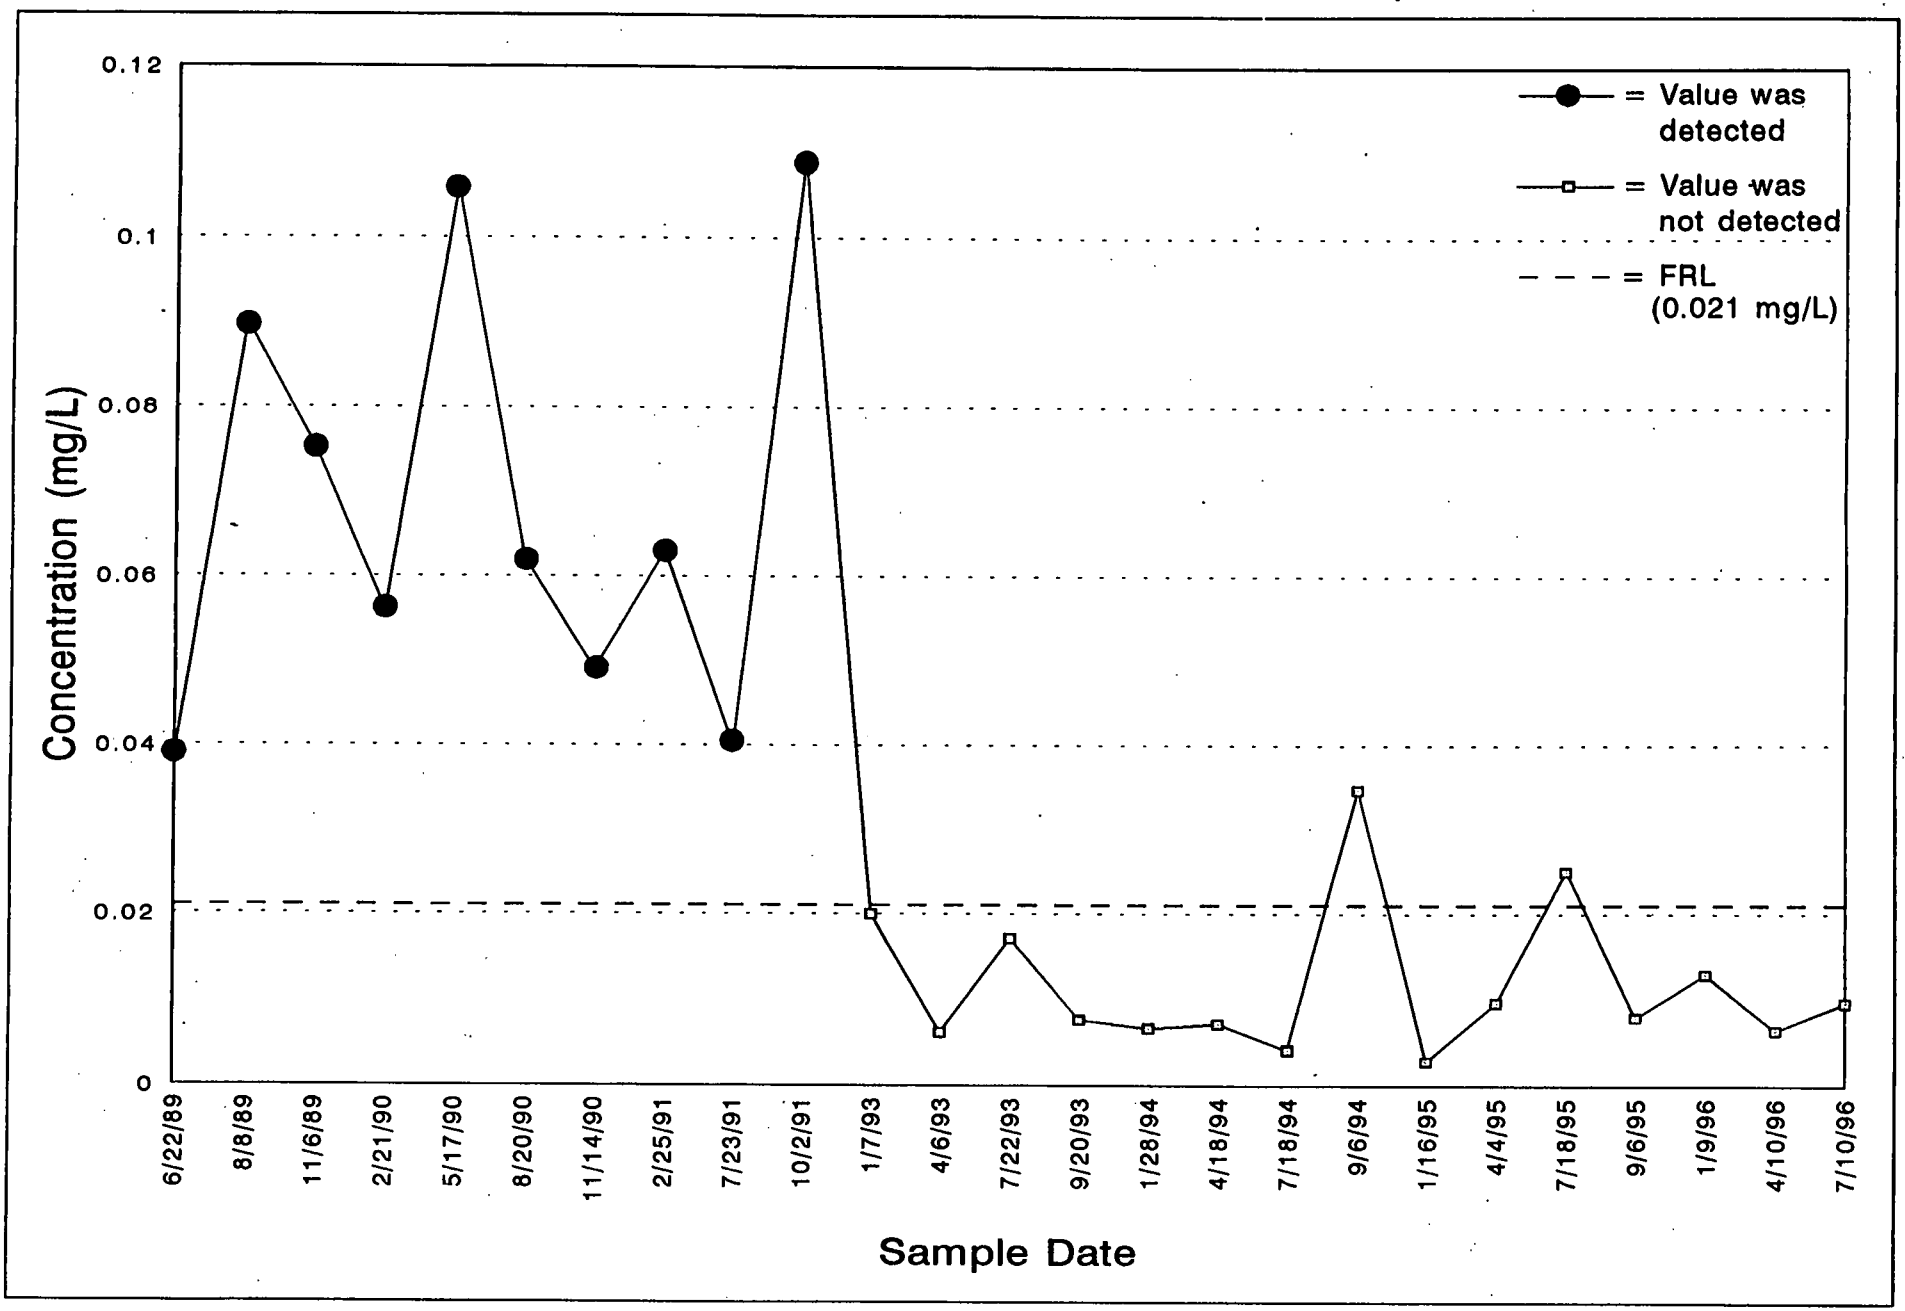

FIGURE A.3-59. ZINC CONCENTRATION VS. TIME, WELL 2051

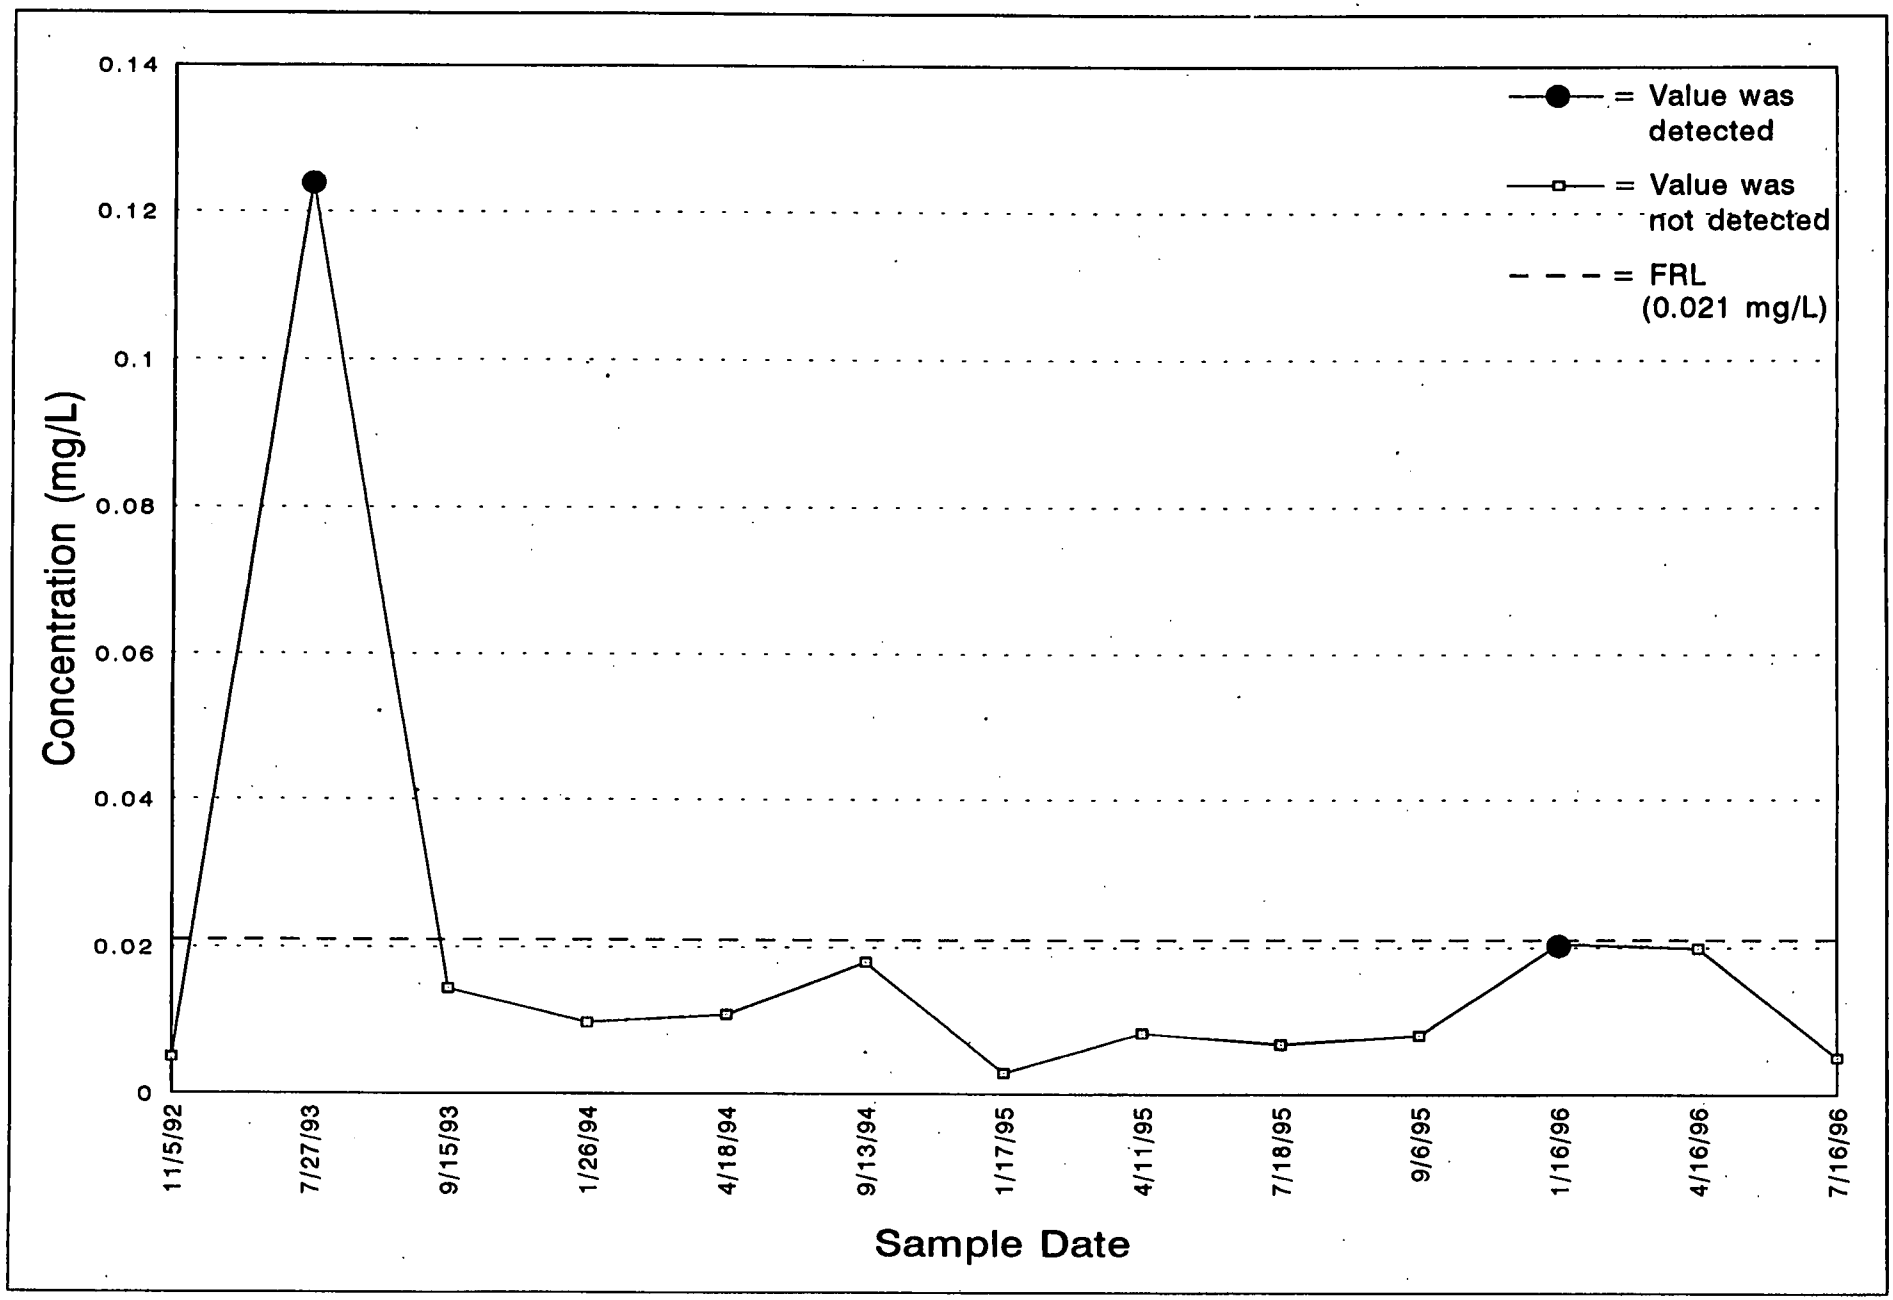

FIGURE A.3-60. ZINC CONCENTRATION VS. TIME, WELL 3431

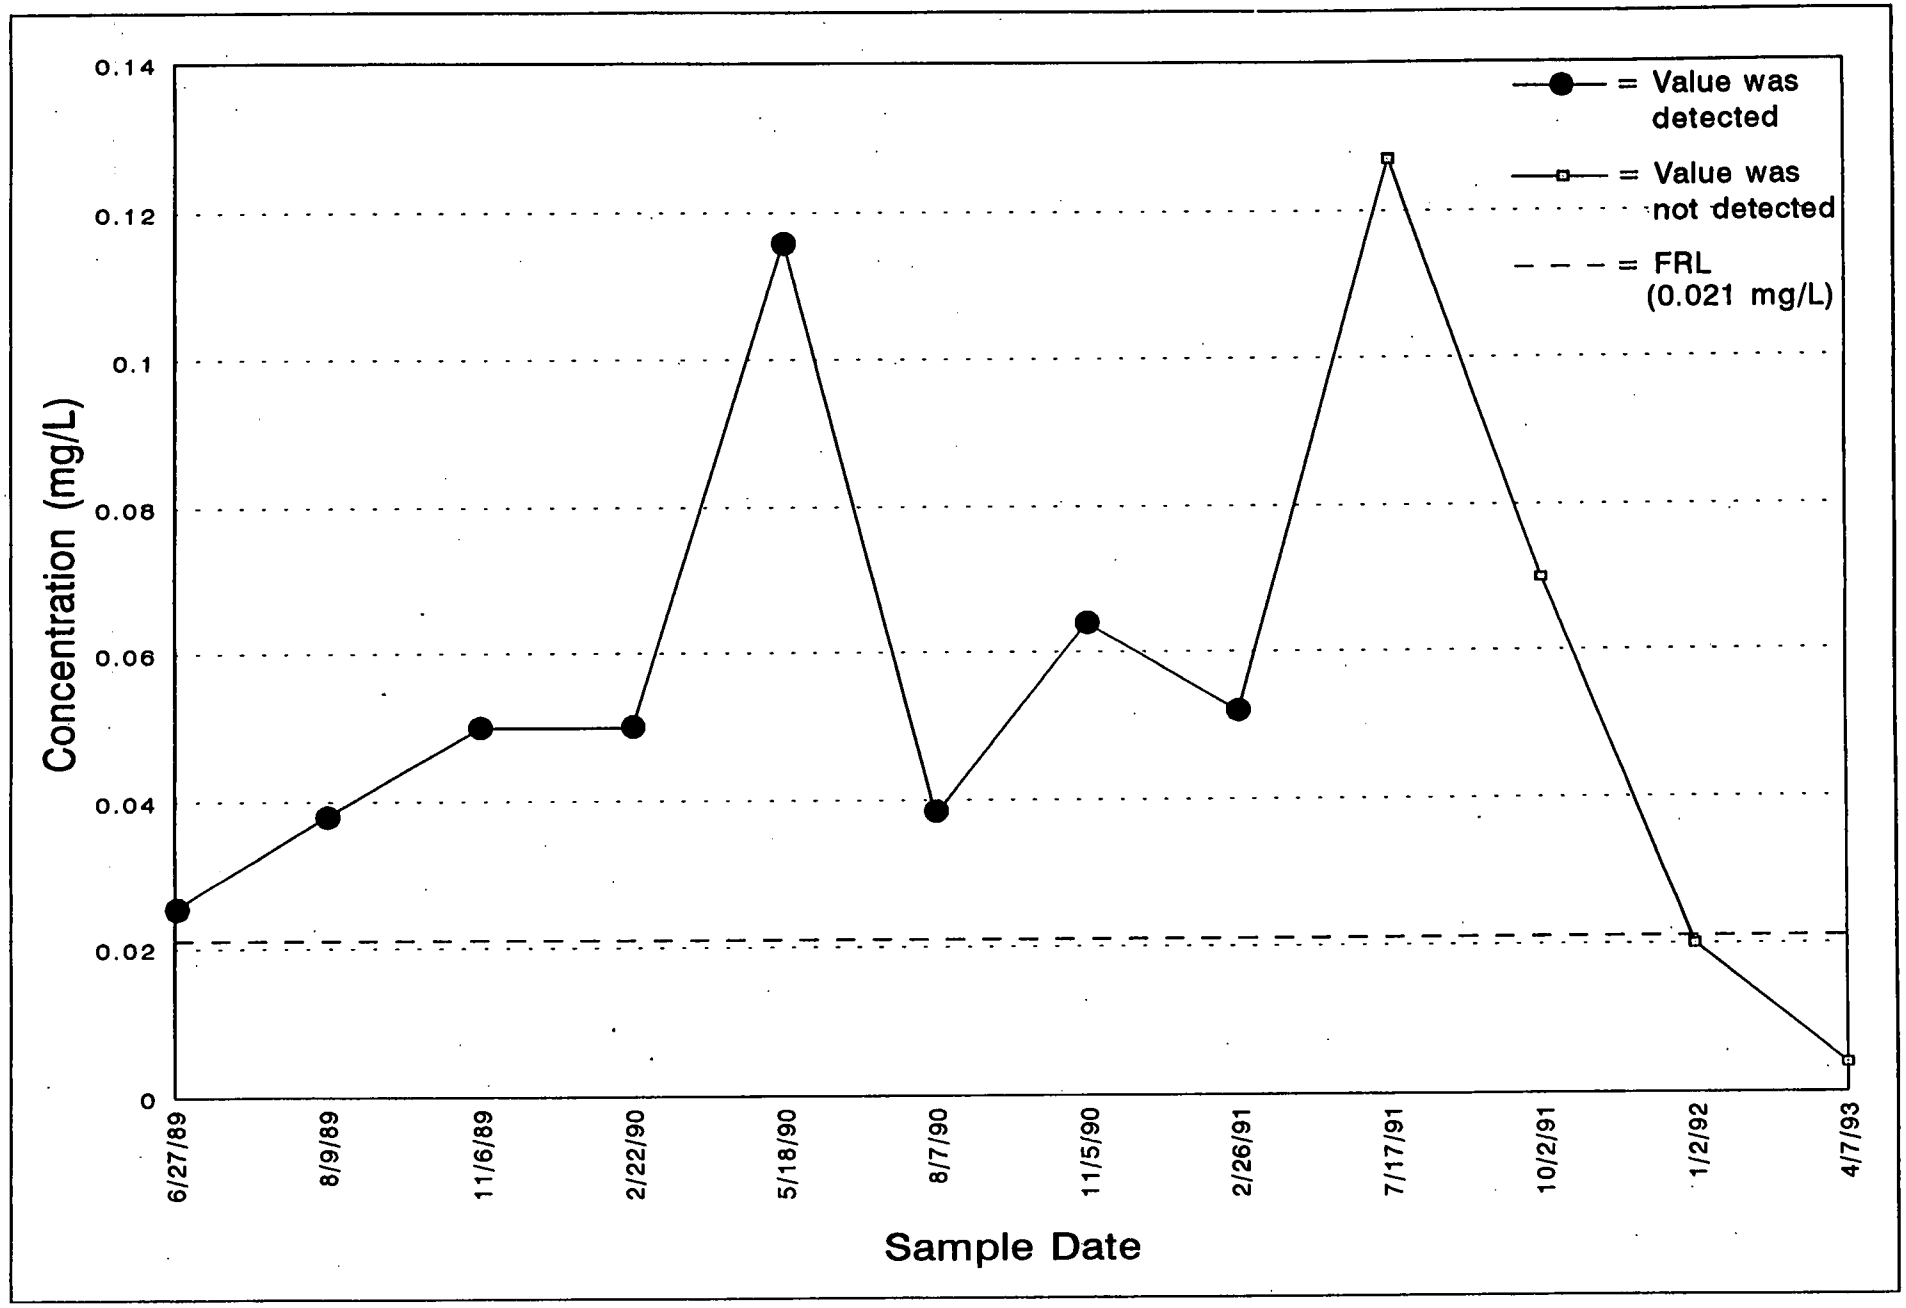

FIGURE A.3-61. ZINC CONCENTRATION VS. TIME, WELL 3066

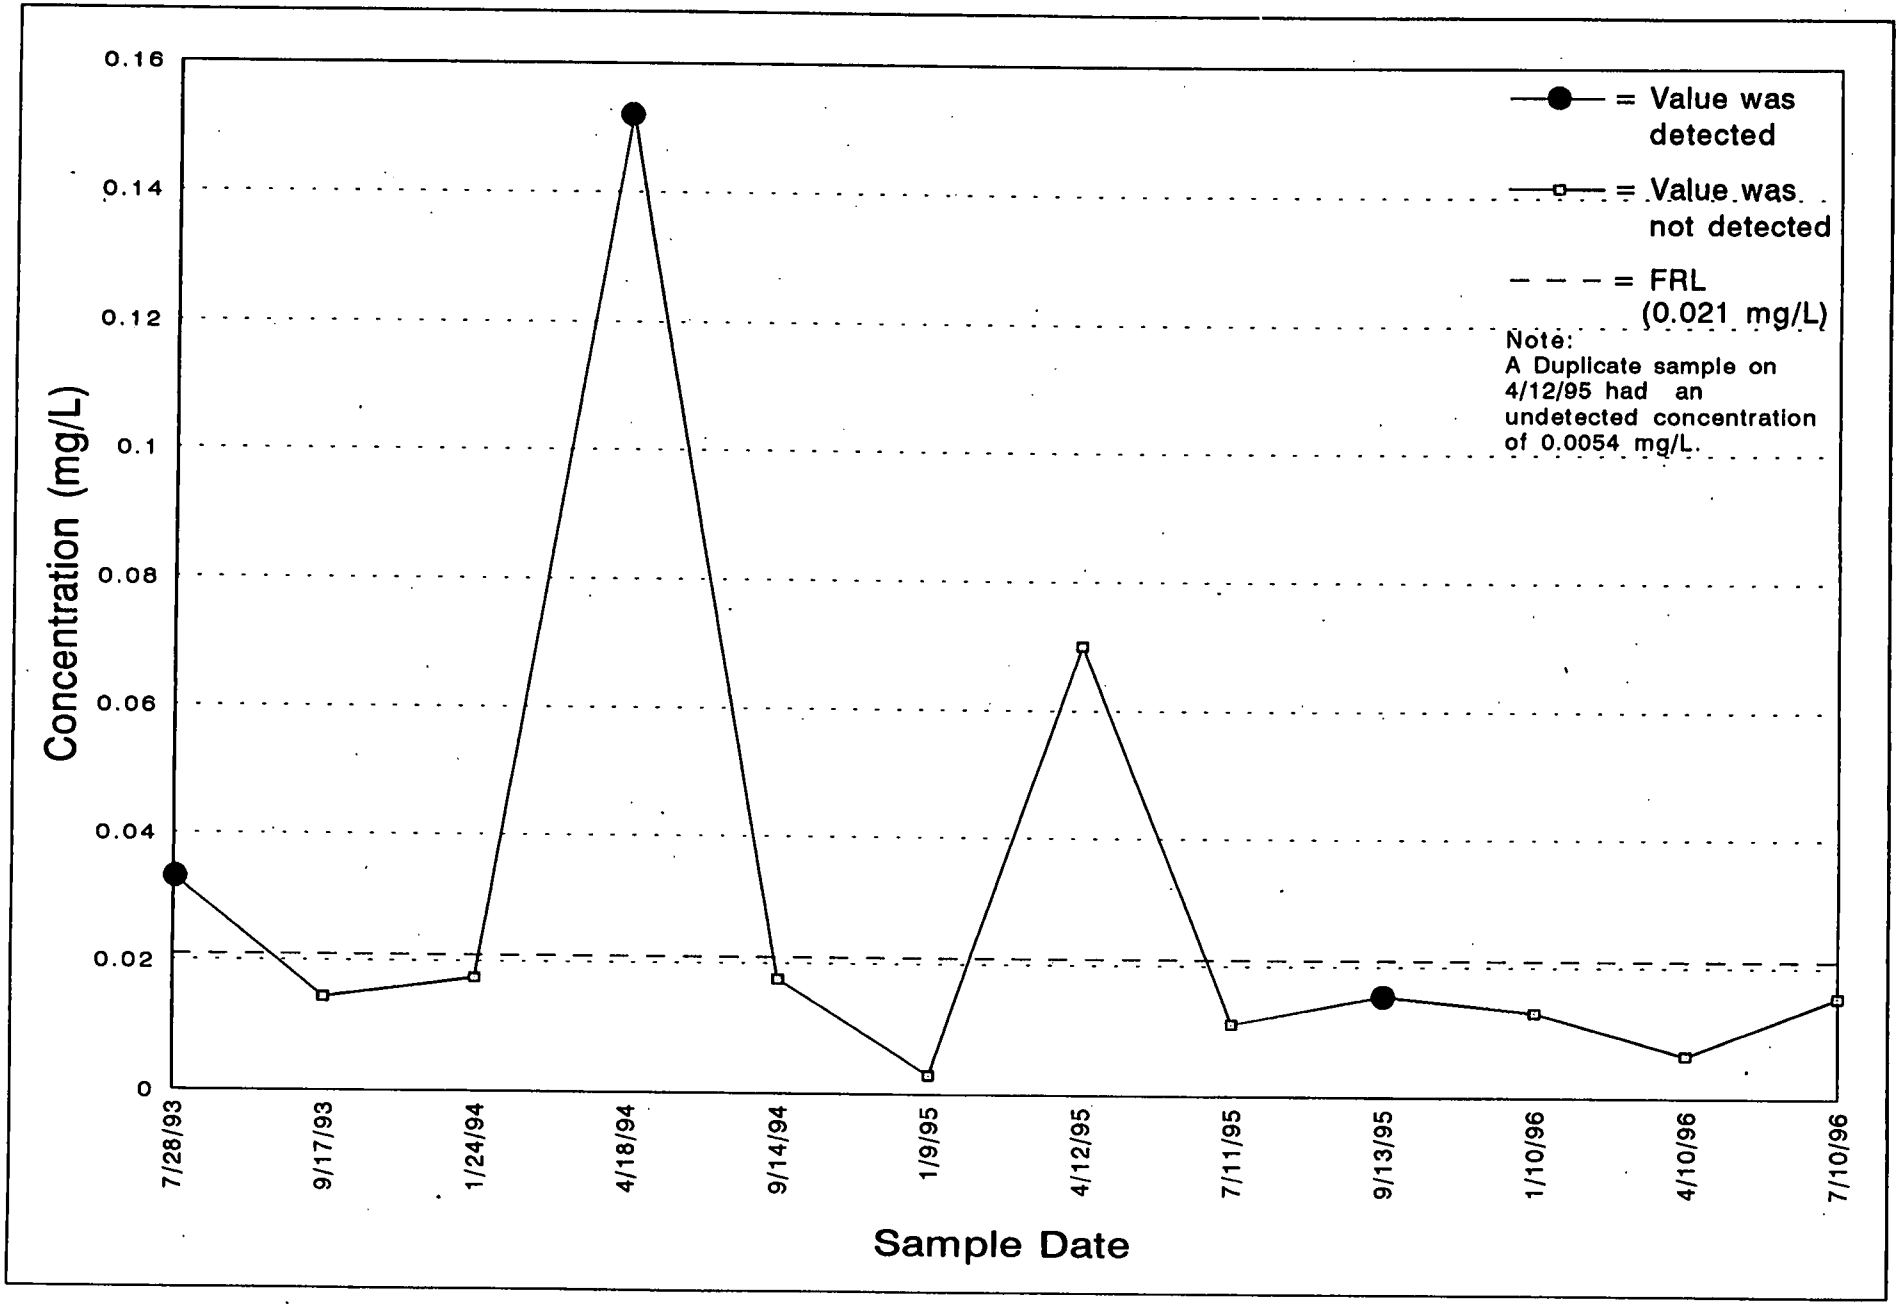

FIGURE A.3-62. ZINC CONCENTRATION VS. TIME, WELL 2733

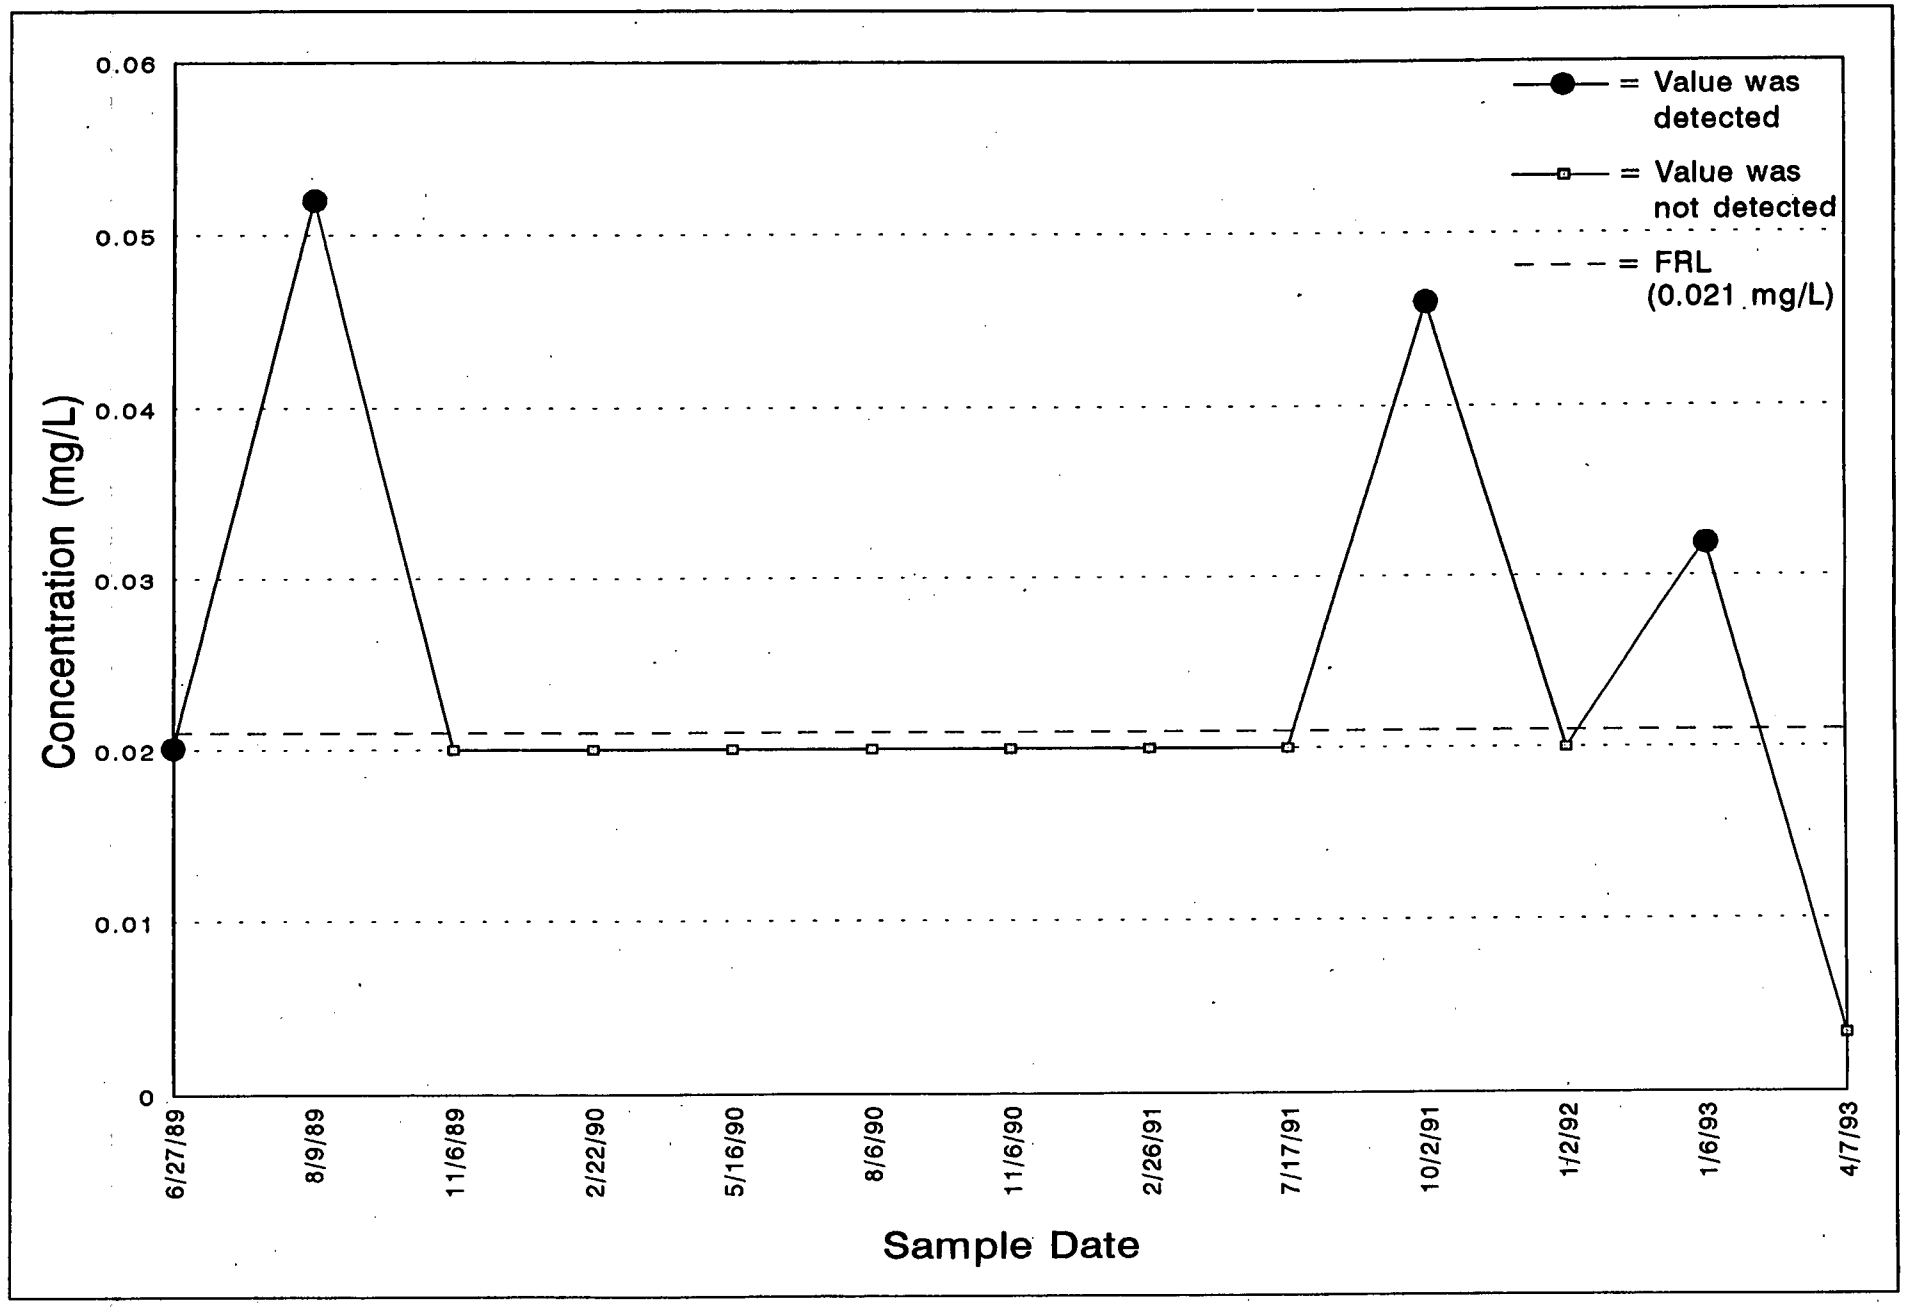

FIGURE A.3-63. ZINC CONCENTRATION VS. TIME, WELL 2066

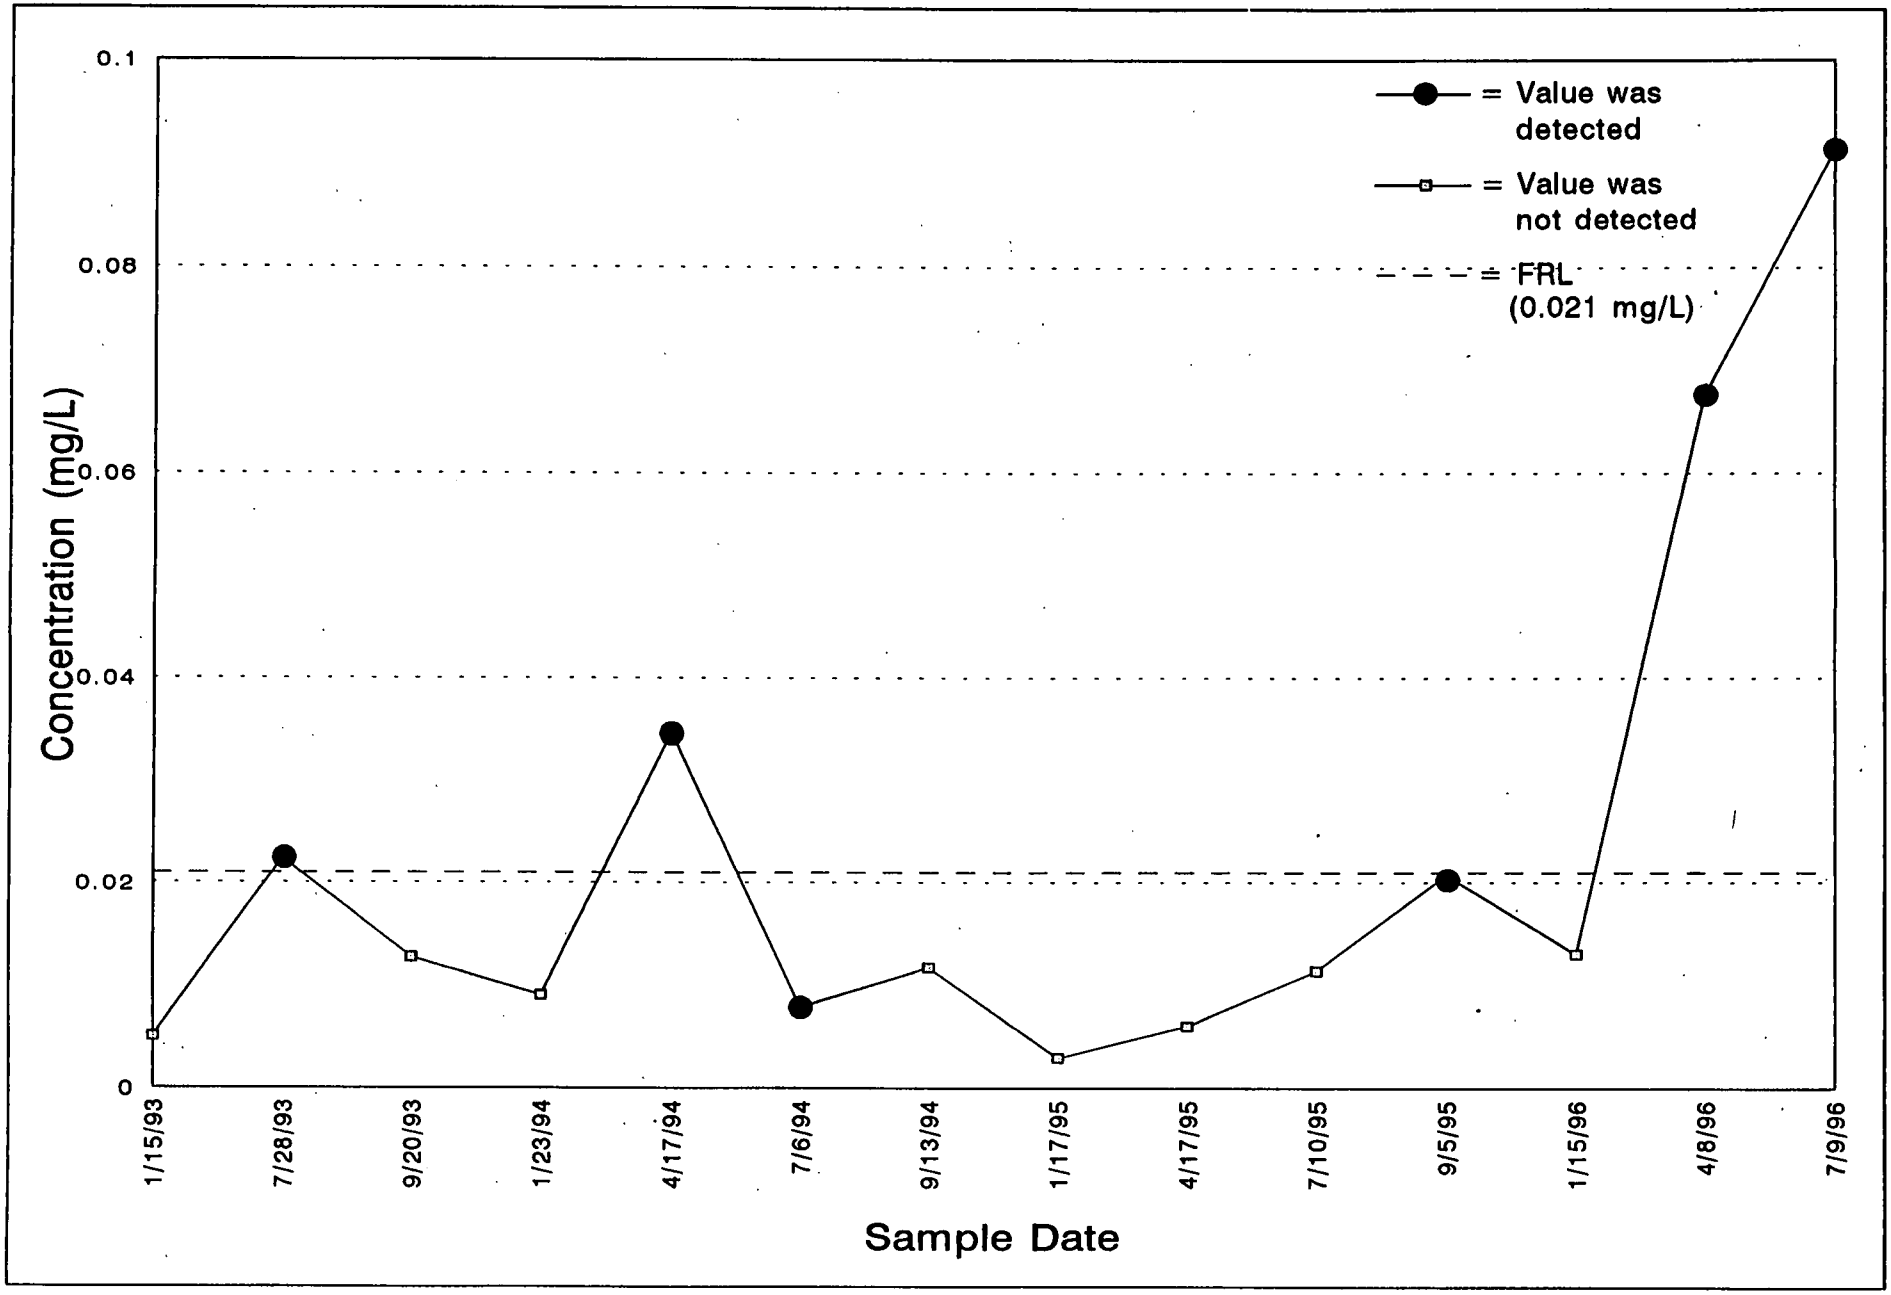

FIGURE A.3-64. ZINC CONCENTRATION VS. TIME, WELL 2424

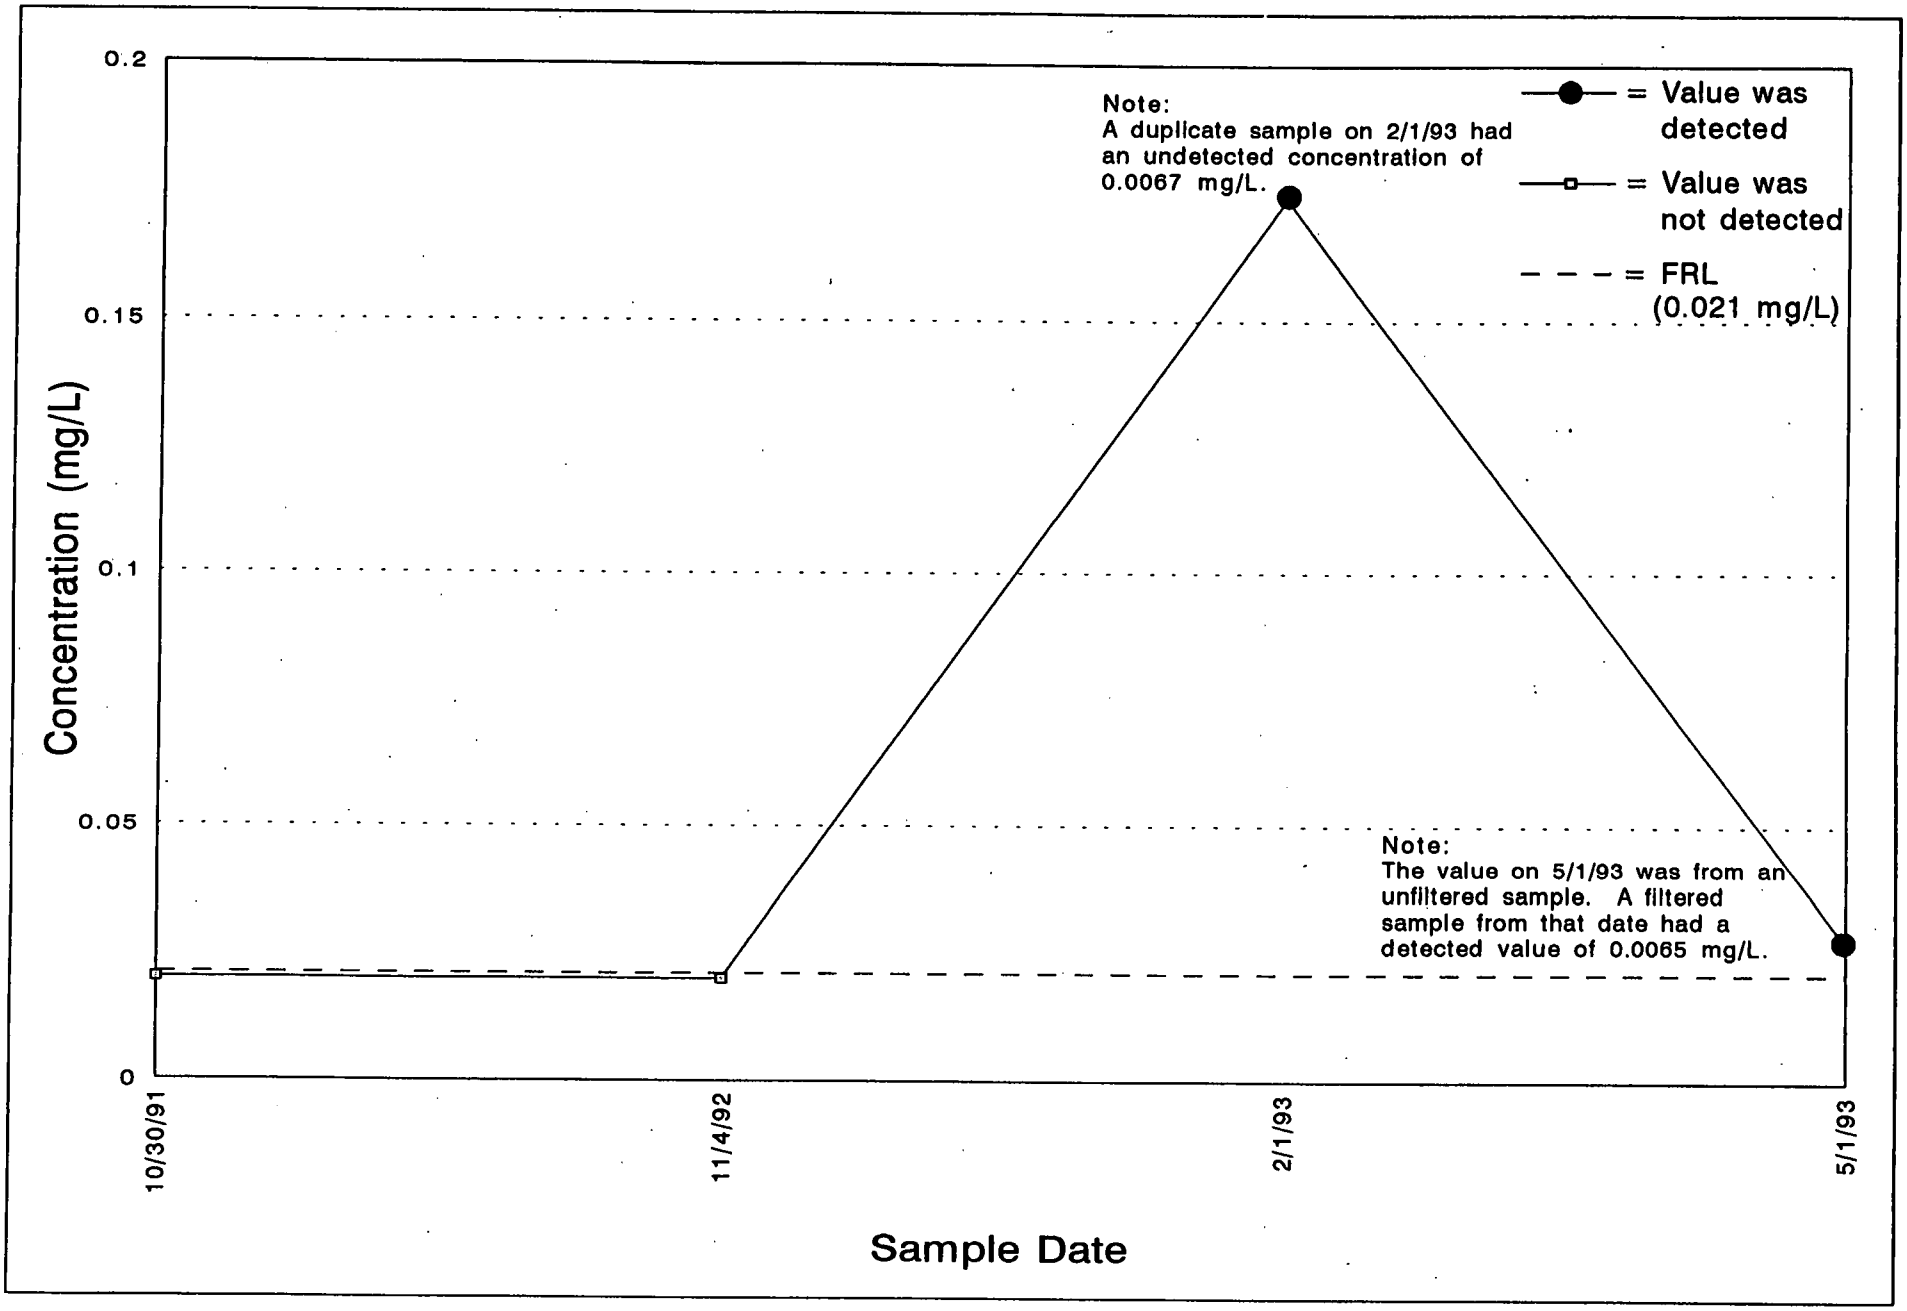

FIGURE A.3-65. ZINC CONCENTRATION VS. TIME, WELL 3091

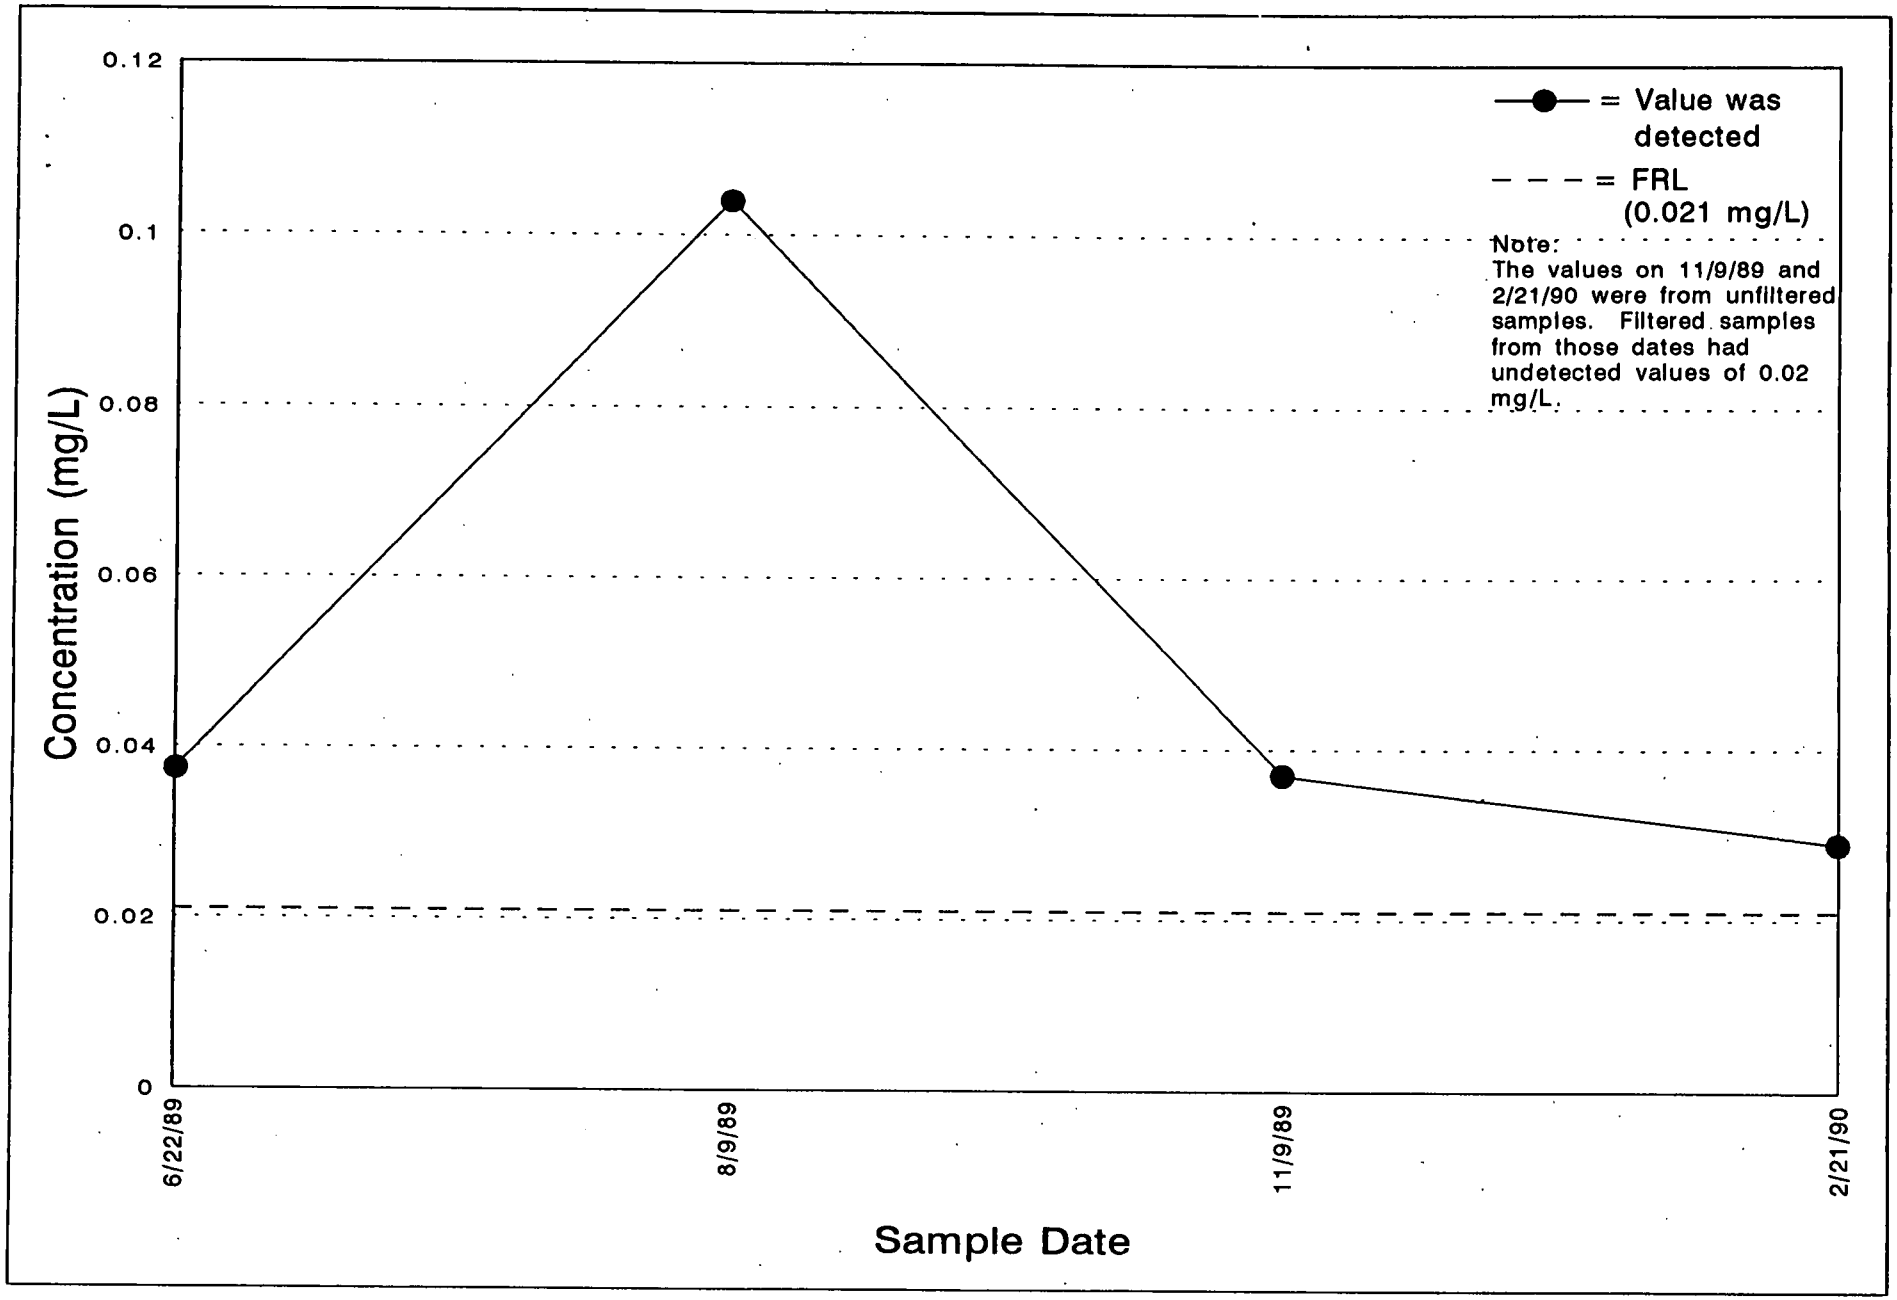

FIGURE A.3-66. ZINC CONCENTRATION VS. TIME, WELL 3051

APPENDIX B

MODELING INFORMATION TO SUPPORT THE SELECTION OF THE LEAD FRL

APPENDIX B

This Appendix presents modeling results evaluated to support the selection of the SDWA action level of 15 μg/L as the risk-based final remediation level (FRL) for lead in groundwater. The modeling was conducted using the most recent version (version 99D) of the EPA's IEUBK Model for lead (Publication #9285.7-15-2, PB93-963511, February, 1994). Because of the absence of published toxicity criteria (reference doses and cancer slope factors), commonly accepted risk algorithms for direct exposure could not be used to develop an FRL for lead in groundwater. Site-specific and model default parameters for lead in air, water, soil, dust, diet, paint, and other sources were used to predict blood lead levels in children 6 months to 7 years old.

The IEUBK Model for lead looks at a target-blood lead level in conjunction with a biokinetic slope factor. The model uses various exposure inputs to estimate a geometric blood lead level and a plausible distribution of blood lead concentrations. It is a risk assessment tool frequently used to evaluate exposure to lead for children in a residential setting. Preliminary remediation goals can also be developed using the model by combining available site-specific information and the model's various default parameters.

The model was run using three scenarios of model input parameters for soil/dust:

1) Model default of 200 mg/kg for soil and dust concentration equal to the default for soil

2) Site-specific background concentration of 26.4 mg/kg for surface soil (95th percentile) and dust concentration equal to the soil concentration

3) Site-specific background concentration of 26.4 mg/kg for surface soil and model's multisourcing technique to estimate the dust concentration.

Groundwater concentrations utilized or determined were as follows:

a) 2.0 μg/L - current background based lead FRL

b) 15.0 μg/L - SDWA Action Level for lead

c) Concentration corresponding to the EPA established action level of 5 percent of children with estimated blood lead level > 10 μg/dL (i.e., the blood lead level of concern)

All other defaults for the model were used. A summary of the results of the analysis are provided in Table B-1. Modeling output for each model run is provided in Attachments B1 through B9.

TABLE B-1

MODELING RESULTS

Model Run	Scenario	Drinking Water Input Concentration (μg/L)	Soil Input Concentration (mg/kg)	Dust Input Concentration (mg/kg)	Geometric Mean Blood Lead Level (μg/dL)	Predicted Percent of Population Exceeding 10 μg/dL Level of Concern
1	1a	2.0	200	200	3.6	1.31
2	1b	15.0	200	200	4.5	4.15
3	***1c***	***18.0***	***200***	***200***	***4.7***	***5***
4	2a	2.0	26.4	26.4	1.6	0
5	2b	15.0	26.4	26.4	2.7	0.22
6	***2c***	***43.0***	***26.4***	***26.4***	***4.7***	***5***
7	3a	2.0	26.4	28.5	1.7	0
8	3b	15.0	26.4	28.5	2.7	0.23
9	***3c***	***43.0***	***26.4***	***28.5***	***4.7***	***5***

As shown in Table B-1, Scenarios 1b, 2b, and 3b utilized the SDWA action level for lead (15 μg/L) as the drinking water concentration in conjunction with the various other input parameters indicated above. All of the "b" Scenarios indicate that the SDWA action level is an appropriate, health protective level for lead in groundwater at the FEMP in that they predict the action level of 5 percent of the child population with blood lead levels exceeding 10 μg/dL will not be reached. Of particular note are the results of Scenario 1b using the 15 μg/L water concentration, along with the IEUBK default concentrations for lead in soil and dust (both set at 200 mg/kg which is about an order of magnitude higher than the actual site background concentration in soil of 26.4 mg/kg). The Scenario 1b results indicate that less than 5 percent (4.15 percent) of the potentially exposed child population would have blood lead concentrations greater than the 10 μg/dL level of concern. Scenarios 1c, 2c, and 3c have been bolded in Table B-1 because they show the combinations of water, soil, and dust concentrations which reached the action level of 5 percent of the child population exceeding the 10 μg/dL level of concern. All the drinking water concentrations for the "c" Scenarios are greater than the SDWA action level of 15 μg/L. This further substantiates the protectiveness of the SDWA lead action level of

15 μg/L and validates its' use as the Final Remediation Level (FRL) for lead in groundwater at the FEMP.

115

ATTACHMENT B1
Modeling Output
For Model Run 1

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 2.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	200.0	200.0
1-2	200.0	200.0
2-3	200.0	200.0
3-4	200.0	200.0
4-5	200.0	200.0
5-6	200.0	200.0
6-7	200.0	200.0

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	4.0	7.43	4.69
1-2:	4.4	10.51	7.39
2-3:	4.1	11.00	7.46
3-4:	3.9	11.02	7.55
4-5:	3.2	9.16	5.71
5-6:	2.8	8.86	5.17
6-7:	2.5	8.93	4.90

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.54	0.18	0.00	0.02
1-2:	2.63	0.46	0.00	0.03
2-3:	2.99	0.48	0.00	0.06
3-4:	2.91	0.49	0.00	0.07
4-5:	2.86	0.52	0.00	0.07
5-6:	3.04	0.56	0.00	0.09
6-7:	3.36	0.57	0.00	0.09

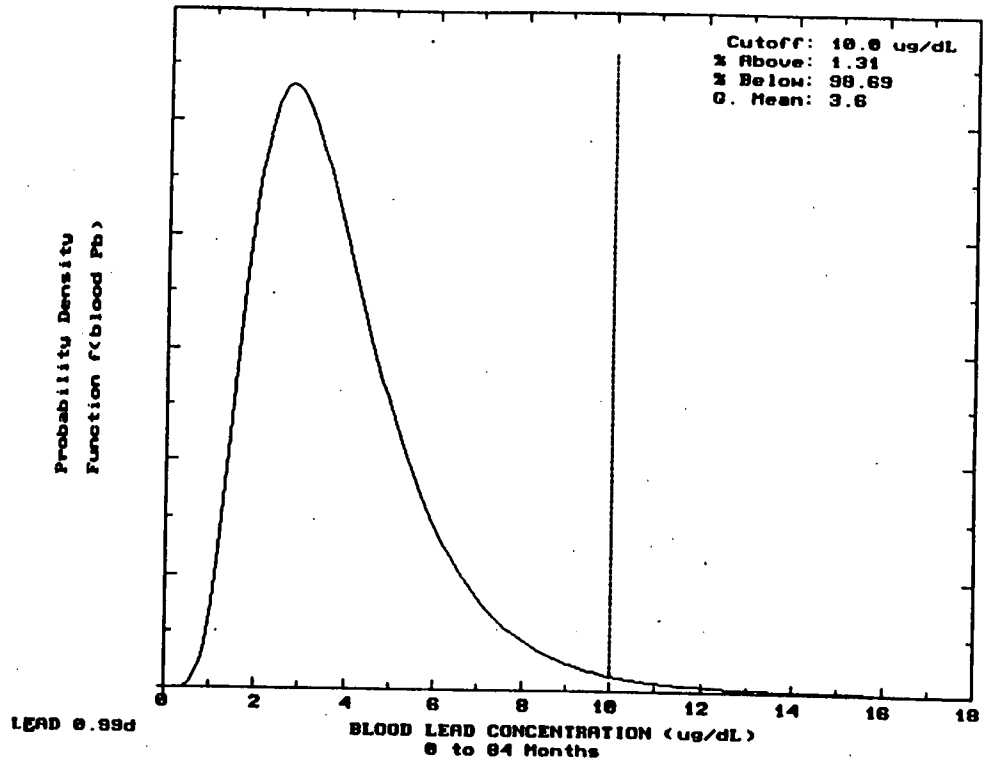

ATTACHMENT B2
Modeling Output
For Model Run 2

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 15.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	200.0	200.0
1-2	200.0	200.0
2-3	200.0	200.0
3-4	200.0	200.0
4-5	200.0	200.0
5-6	200.0	200.0
6-7	200.0	200.0

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	4.6	8.52	4.63
1-2:	5.4	13.16	7.21
2-3:	5.1	13.81	7.30
3-4:	4.9	13.97	7.41
4-5:	4.3	12.34	5.61
5-6:	3.8	12.27	5.09
6-7:	3.5	12.42	4.83

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.51	1.36	0.00	0.02
1-2:	2.57	3.34	0.00	0.03
2-3:	2.93	3.52	0.00	0.06
3-4:	2.85	3.64	0.00	0.07
4-5:	2.81	3.86	0.00	0.07
5-6:	2.99	4.10	0.00	0.09
6-7:	3.31	4.19	0.00	0.09

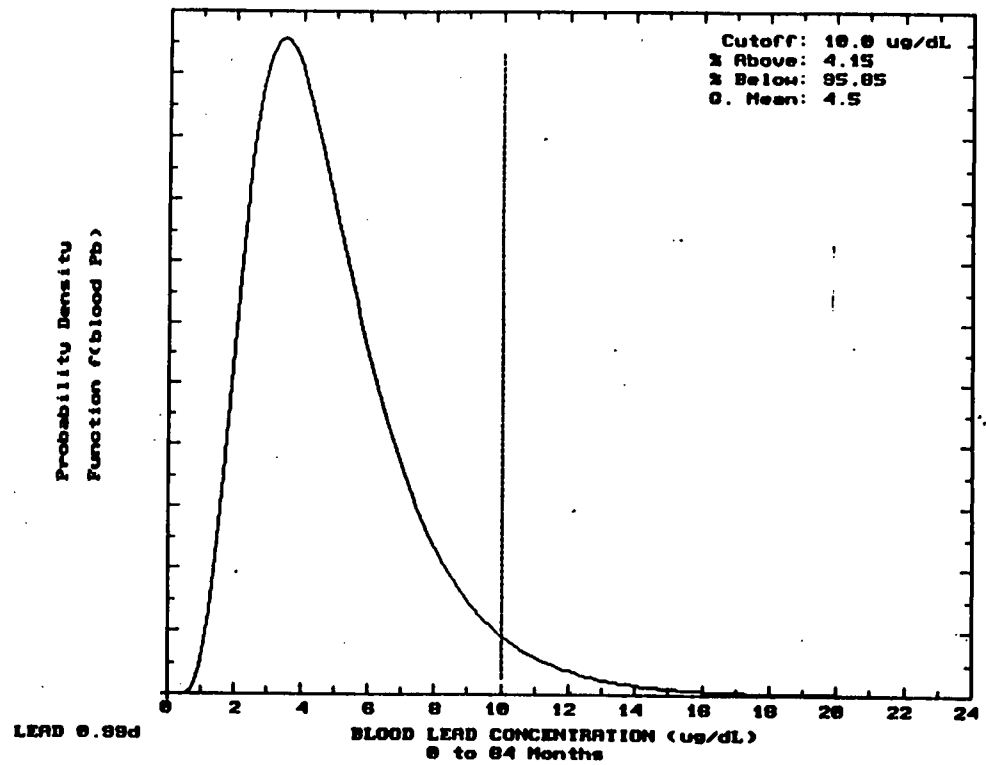

ATTACHMENT B3
Modeling Output
For Model Run 3

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 18.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	200.0	200.0
1-2	200.0	200.0
2-3	200.0	200.0
3-4	200.0	200.0
4-5	200.0	200.0
5-6	200.0	200.0
6-7	200.0	200.0

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	4.7	8.76	4.61
1-2:	5.6	13.75	7.17
2-3:	5.3	14.44	7.27
3-4:	5.1	14.63	7.38
4-5:	4.5	13.06	5.59
5-6:	4.1	13.04	5.07
6-7:	3.7	13.21	4.81

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.50	1.63	0.00	0.02
1-2:	2.56	3.98	0.00	0.03
2-3:	2.91	4.20	0.00	0.06
3-4:	2.84	4.34	0.00	0.07
4-5:	2.80	4.61	0.00	0.07
5-6:	2.98	4.90	0.00	0.09
6-7:	3.30	5.01	0.00	0.09

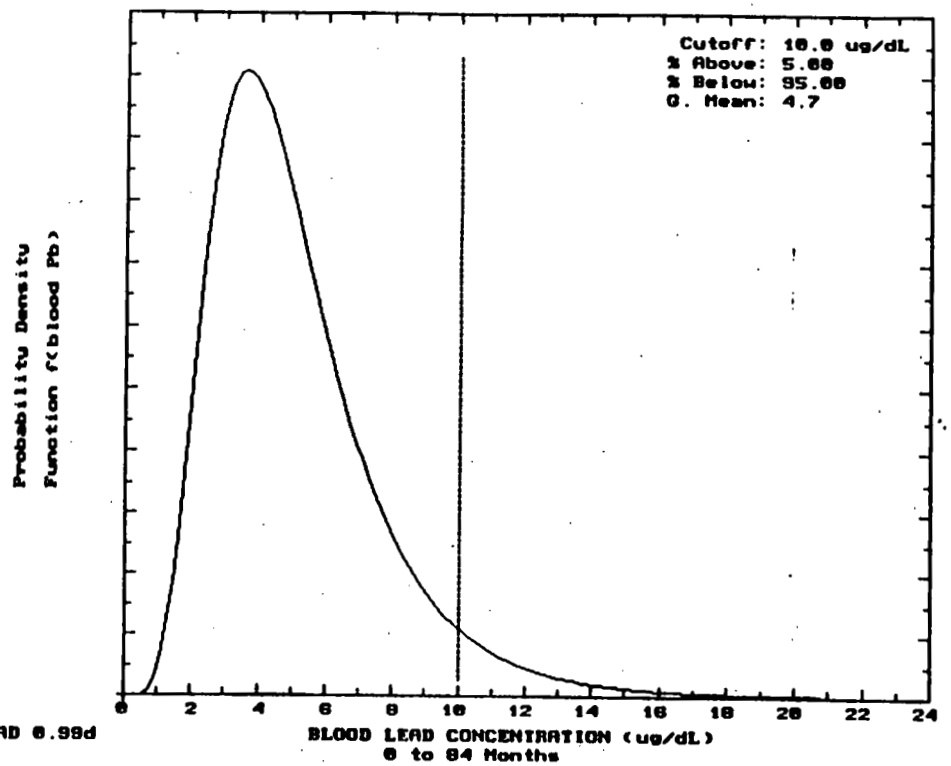

ATTACHMENT B4
Modeling Output
For Model Run 4

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 2.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	26.4
1-2	26.4	26.4
2-3	26.4	26.4
3-4	26.4	26.4
4-5	26.4	26.4
5-6	26.4	26.4
6-7	26.4	26.4

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	1.9	3.52	0.65
1-2:	1.9	4.33	1.03
2-3:	1.8	4.73	1.03
3-4:	1.6	4.65	1.04
4-5:	1.5	4.31	0.77
5-6:	1.4	4.46	0.70
6-7:	1.3	4.76	0.66

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.66	0.19	0.00	0.02
1-2:	2.78	0.48	0.00	0.03
2-3:	3.13	0.50	0.00	0.06
3-4:	3.03	0.51	0.00	0.07
4-5:	2.94	0.54	0.00	0.07
5-6:	3.10	0.57	0.00	0.09
6-7:	3.43	0.58	0.00	0.09

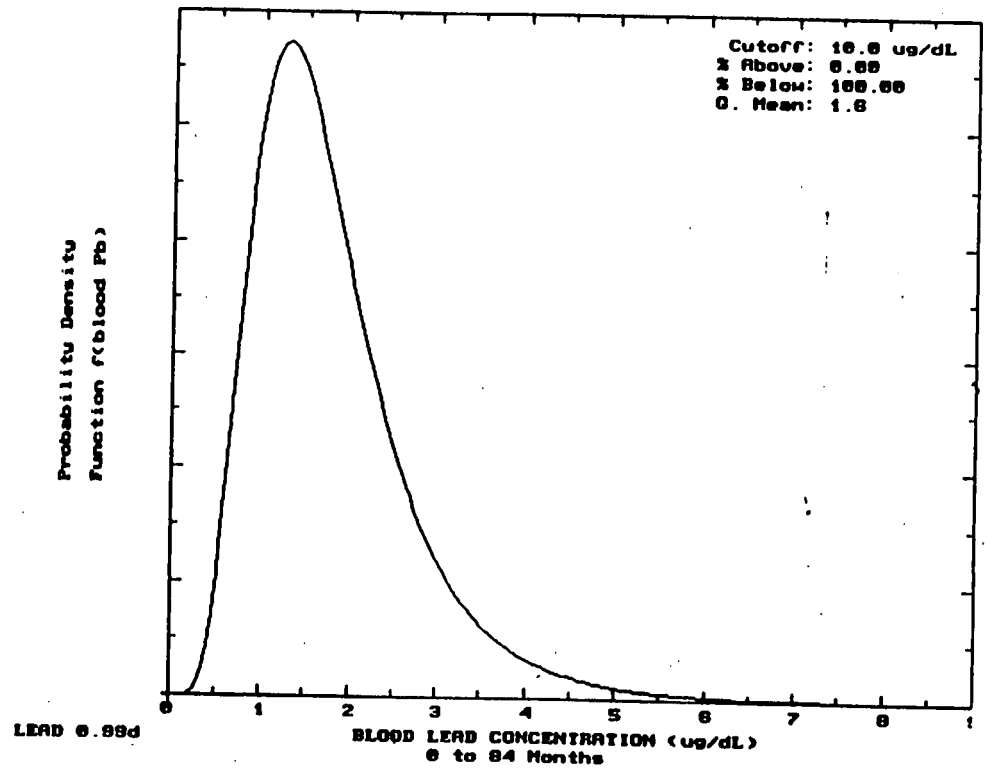

ATTACHMENT B5
Modeling Output
For Model Run 5

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 15.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	26.4
1-2	26.4	26.4
2-3	26.4	26.4
3-4	26.4	26.4
4-5	26.4	26.4
5-6	26.4	26.4
6-7	26.4	26.4

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	2.6	4.70	0.64
1-2:	3.0	7.27	1.00
2-3:	2.9	7.82	1.01
3-4:	2.8	7.84	1.02
4-5:	2.6	7.67	0.76
5-6:	2.5	8.02	0.69
6-7:	2.3	8.38	0.65

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.62	1.42	0.00	0.02
1-2:	2.71	3.52	0.00	0.03
2-3:	3.06	3.68	0.00	0.06
3-4:	2.97	3.78	0.00	0.07
4-5:	2.88	3.96	0.00	0.07
5-6:	3.05	4.19	0.00	0.09
6-7:	3.37	4.26	0.00	0.09

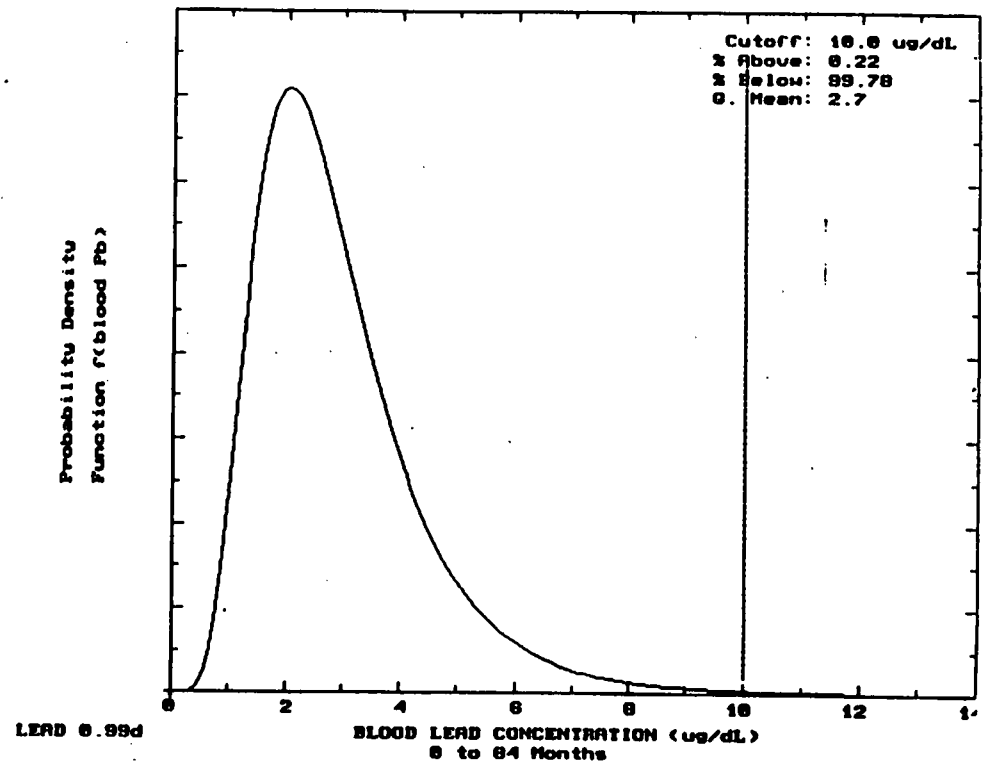

ATTACHMENT B6
Modeling Output
For Model Run 6

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 43.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: constant conc.

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	26.4
1-2	26.4	26.4
2-3	26.4	26.4
3-4	26.4	26.4
4-5	26.4	26.4
5-6	26.4	26.4
6-7	26.4	26.4

Additional Dust Sources: None DEFAULT

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	3.9	7.15	0.62
1-2:	5.3	13.13	0.95
2-3:	5.2	14.01	0.96
3-4:	5.0	14.29	0.98
4-5:	4.8	14.49	0.73
5-6:	4.6	15.28	0.66
6-7:	4.4	15.80	0.63

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.55	3.96	0.00	0.02
1-2:	2.57	9.57	0.00	0.03
2-3:	2.92	10.07	0.00	0.06
3-4:	2.85	10.40	0.00	0.07
4-5:	2.78	10.92	0.00	0.07
5-6:	2.94	11.58	0.00	0.09
6-7:	3.26	11.82	0.00	0.09

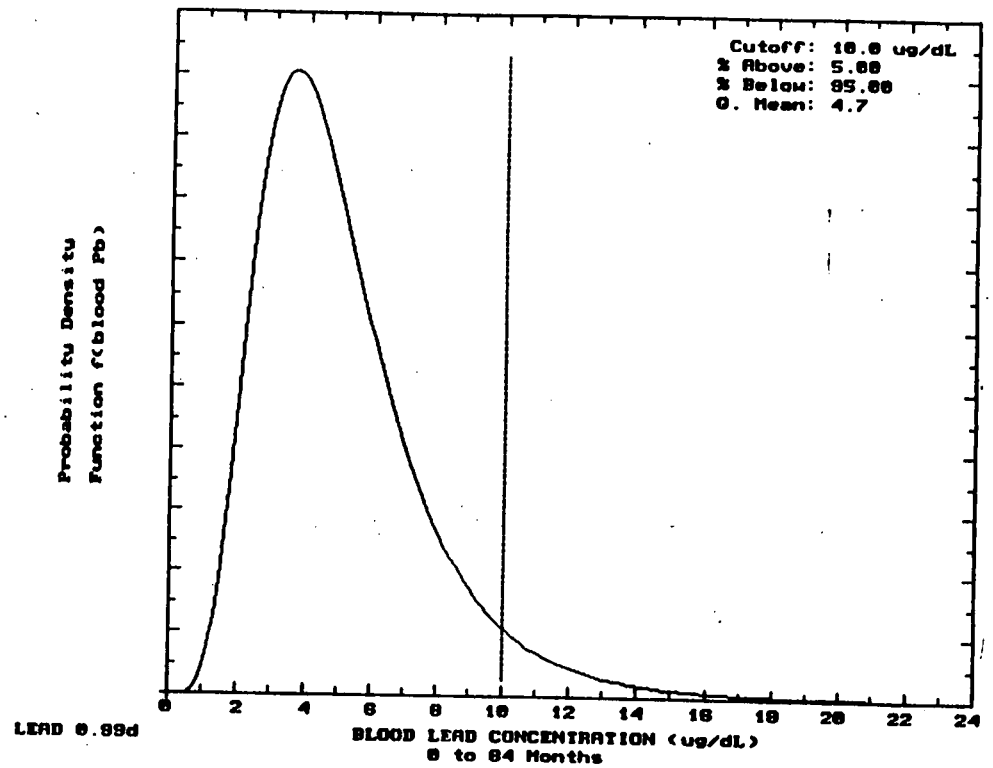

ATTACHMENT B7
Modeling Output
For Model Run 7

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 2.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: Multiple Source Analysis

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	28.5
1-2	26.4	28.5
2-3	26.4	28.5
3-4	26.4	28.5
4-5	26.4	28.5
5-6	26.4	28.5
6-7	26.4	28.5

Additional Dust Sources: None DEFAULT
Soil contribution conversion factor: 0.70
Air contribution conversion factor: 100.0

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	1.9	3.54	0.67
1-2:	1.9	4.37	1.07
2-3:	1.8	4.78	1.08
3-4:	1.7	4.69	1.08
4-5:	1.5	4.35	0.81
5-6:	1.4	4.49	0.73
6-7:	1.3	4.79	0.69

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.66	0.19	0.00	0.02
1-2:	2.78	0.48	0.00	0.03
2-3:	3.13	0.50	0.00	0.06
3-4:	3.03	0.51	0.00	0.07
4-5:	2.94	0.54	0.00	0.07
5-6:	3.10	0.57	0.00	0.09
6-7:	3.43	0.58	0.00	0.09

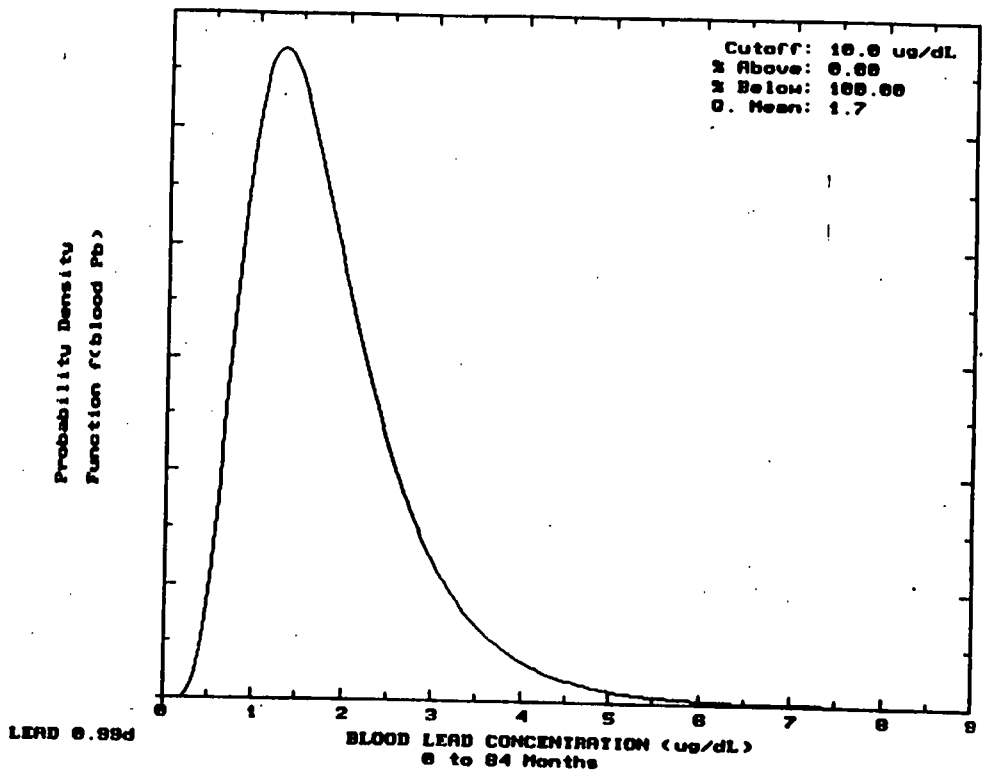

ATTACHMENT B8
Modeling Output
For Model Run 8

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 15.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: Multiple Source Analysis

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	28.5
1-2	26.4	28.5
2-3	26.4	28.5
3-4	26.4	28.5
4-5	26.4	28.5
5-6	26.4	28.5
6-7	26.4	28.5

Additional Dust Sources: None DEFAULT
Soil contribution conversion factor: 0.70
Air contribution conversion factor: 100.0

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	2.6	4.73	0.67
1-2:	3.0	7.31	1.05
2-3:	2.9	7.86	1.05
3-4:	2.8	7.88	1.06
4-5:	2.6	7.70	0.79
5-6:	2.5	8.04	0.72
6-7:	2.4	8.41	0.68

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.62	1.42	0.00	0.02
1-2:	2.71	3.52	0.00	0.03
2-3:	3.06	3.68	0.00	0.06
3-4:	2.97	3.78	0.00	0.07
4-5:	2.88	3.96	0.00	0.07
5-6:	3.05	4.19	0.00	0.09
6-7:	3.37	4.26	0.00	0.09

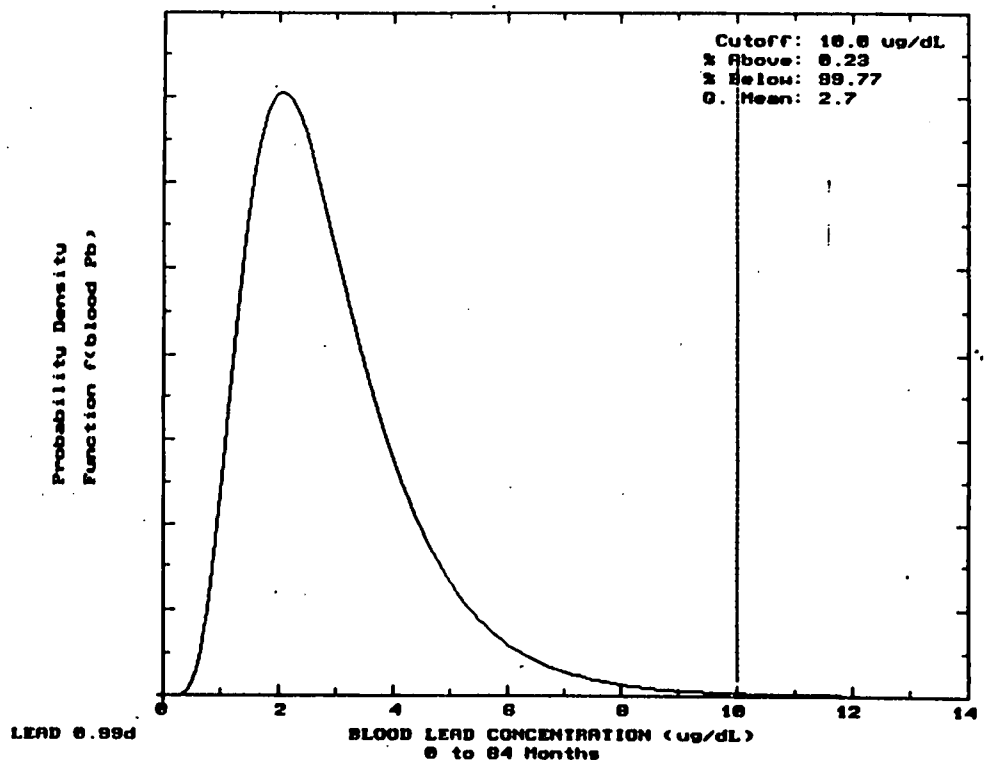

123

ATTACHMENT B9
Modeling Output
For Model Run 9

LEAD MODEL Version 0.99d

AIR CONCENTRATION: 0.100 ug Pb/m3 DEFAULT
Indoor AIR Pb Conc: 30.0 percent of outdoor.
Other AIR Parameters:

Age	Time Outdoors (hr)	Vent. Rate (m3/day)	Lung Abs. (%)
0-1	1.0	2.0	32.0
1-2	2.0	3.0	32.0
2-3	3.0	5.0	32.0
3-4	4.0	5.0	32.0
4-5	4.0	5.0	32.0
5-6	4.0	7.0	32.0
6-7	4.0	7.0	32.0

DIET: DEFAULT

DRINKING WATER Conc: 43.00 ug Pb/L
WATER Consumption: DEFAULT

SOIL & DUST:
Soil: constant conc.
Dust: Multiple Source Analysis

Age	Soil (ug Pb/g)	House Dust (ug Pb/g)
0-1	26.4	28.5
1-2	26.4	28.5
2-3	26.4	28.5
3-4	26.4	28.5
4-5	26.4	28.5
5-6	26.4	28.5
6-7	26.4	28.5

Additional Dust Sources: None DEFAULT
Soil contribution conversion factor: 0.70
Air contribution conversion factor: 100.0

PAINT Intake: 0.00 ug Pb/day DEFAULT

MATERNAL CONTRIBUTION: Infant Model
Maternal Blood Conc: 2.50 ug Pb/dL

CALCULATED BLOOD Pb and Pb UPTAKES:

YEAR	Blood Level (ug/dL)	Total Uptake (ug/day)	Soil+Dust Uptake (ug/day)
0.5-1:	3.9	7.18	0.65
1-2:	5.3	13.17	0.99
2-3:	5.2	14.05	1.00
3-4:	5.0	14.33	1.02
4-5:	4.8	14.52	0.76
5-6:	4.6	15.30	0.69
6-7:	4.4	15.83	0.65

YEAR	Diet Uptake (ug/day)	Water Uptake (ug/day)	Paint Uptake (ug/day)	Air Uptake (ug/day)
0.5-1:	2.55	3.96	0.00	0.02
1-2:	2.57	9.57	0.00	0.03
2-3:	2.92	10.06	0.00	0.06
3-4:	2.85	10.40	0.00	0.07
4-5:	2.77	10.92	0.00	0.07
5-6:	2.94	11.58	0.00	0.09
6-7:	3.26	11.82	0.00	0.09

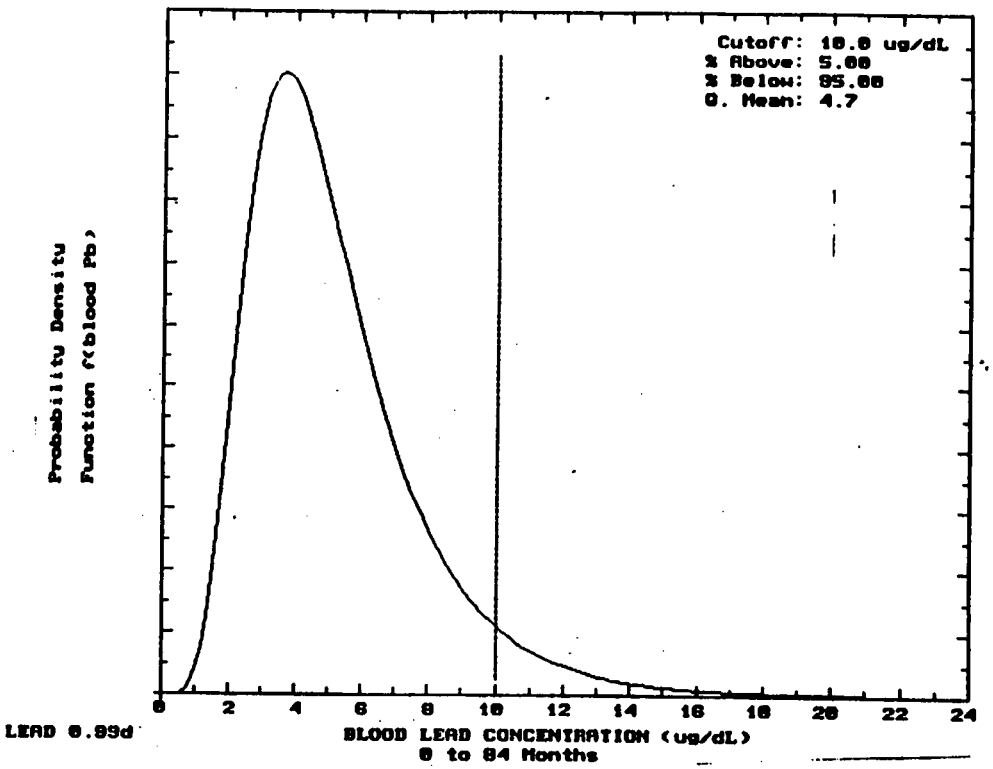

APPENDIX C

REMEDIAL DESIGN FACT SHEET -

GROUNDWATER FRLs FOR FLUORIDE AND LEAD

FERNALD ENVIRONMENTAL MANAGEMENT PROJECT

Remedial Design Fact Sheet for Operable Unit 5 Aquifer Restoration - Groundwater FRLs for Fluoride and Lead

May 1997

OVERVIEW

This Remedial Design Fact Sheet documents a change to the Operable Unit 5 Record of Decision (ROD) established groundwater Final Remediation Levels (FRLs) for fluoride and lead.

- The groundwater FRL for fluoride will change from 0.89 mg/L (background concentration) to the Safe Drinking Water Act (SDWA) established Maximum Contaminant Level (MCL) of 4 mg/L.
- The groundwater FRL for lead will change from 0.002 mg/L (background concentration) to the SDWA established Action Level of 0.015 mg/L .

Note that these FRL changes pertain only to the groundwater FRLs, soil and surface water FRLs for fluoride and lead will remain consistent with those established in the Operable Unit 5 ROD (DOE 1996).

Both changes are consistent with the FRL selection process outlined in the Operable Unit 5 Feasibility Study. The need for these changes was discovered during the design process for preparing the detailed design for the Operable Unit 5 Great Miami Aquifer Remedy. These particular FRL changes have been identified as "non-significant post-ROD changes," as they do not significantly alter the scope, performance or cost of the remedy. This optional Fact Sheet was prepared in accordance with US EPA's Guide to Addressing Pre-ROD and Post-ROD Changes (OSWER Publication 9355.3-02FS-4, April 1991), which accommodates refinements to the remedy discovered to be necessary after ROD signature.

BASIS FOR THE FRL CHANGES As identified in the Operable Unit 5 Feasibility Study, the intent of the groundwater FRL selection process was to utilize the regulatory standards of MCLs, proposed MCLs, or nonzero MCL Goals (MCLGs) as target cleanup values. For those Constituents of Concern with no MCLs, proposed MCLs, or nonzero MCLGs, a Target Risk Level of 10^{-5} and a Hazard Index of 0.2 to a resident farmer was considered. If the background concentration or analytical detection limit for a particular constituent was higher than the established regulatory standard or risk based concentration then the background or analytical detection limit was selected.

Fluoride: In the development of the groundwater FRL for fluoride, the MCL for fluoride (4 mg/L) was inadvertently overlooked. According to the FRL selection process, the fluoride MCL is the appropriate value for the FRL. Because the MCL was overlooked, the groundwater FRL for fluoride, presented in the Operable Unit 5 ROD, was inadvertently established based on the background concentration of fluoride, which is 0.89 mg/L.

Lead: In the development of the groundwater FRL for lead, the Safe Drinking Water Act Action Level for lead (0.015 mg/L) was inadvertently overlooked. According to the FRL selection process, the action level should have been considered for the groundwater FRL. However, because the action level is not a promulgated MCL, the EPA and OEPA requested that DOE support the selection of this value for the groundwater FRL by deriving a risk-based remedial level utilizing existing data and established models for evaluating lead exposure. DOE utilized the EPA's Integrated Exposure Uptake Biokinetic Model (IEUBK) for Lead in Children, Publication 9285.7-15-1, U.S. EPA, February, 1994. The IEUBK model results confirmed that the SDWA Action Level of 15 μg/L is an appropriately conservative value for the groundwater FRL for lead at the FEMP.

With these refinements, the Operable Unit 5 groundwater remedy continues to provide remediation levels for the Great Miami Aquifer that are health protective. The changes enhance the Operable Unit 5 groundwater remedy in that they correct inconsistencies in the application of the FRL selection process and provide more realistically achievable groundwater FRLs for fluoride and lead.

For additional information concerning these changes please contact Mr. Gary Stegner, DOE FEMP Public Affairs at (513) 648-3153 or refer to the Restoration Area Verification Sampling Program Project Specific Plan, Appendices A and B. This Plan is located at the FEMP Public Environmental Information Center, JAMTEK Building, 10845 Hamilton-Cleves Highway, Harrison, Ohio 45030, Telephone: 513-738-0164 or 0165.
