FERNALD CITIZENS ADVISORY BOARD

FRIDAY MAILING

2/6/98

INCLUDED IN THIS MAILING ARE:

- ❑ Technical Report Summary: Closure Fund Management Plan
- ❑ Technical Report Summary: Nevada Test Site Intermodal Transportation Facility Site and Routing Evaluation Study
- ❑ Monitoring Committee Meeting Summary: January 7, 1998
- ❑ Article from **Inside Energy**, "Stick with Alm Plan, Board Tells DOE"
- ❑ Newsclippings

CAB MEETINGS:

- ❑ **WASTE TRANSPORTATION COMMITTEE MEETING**: The Waste Transportation Committee will meet after the Monthly Progress Briefing on Tuesday, February 10, 1998. All members should try to attend the Monthly Progress Briefing.
- ❑ **STEERING COMMITTEE MEETING**: The next meeting of the Steering Committee will be held on Wednesday, February 11, 1998, from 6:30 to 8:30 p.m. in the Jamtek Building.

OTHER MEETINGS:

- ❑ **FERNALD CLEANUP PROGRESS BRIEFING**: The February Fernald Monthly Cleanup Progress Briefing will be held on Tuesday, February 10, 1998, at 6:30 p.m. in the Alpha Building, 10967 Hamilton-Cleves Highway.

QUESTIONS:
Please call John at [redacted] or Doug at [redacted] with questions or concerns.
You may also fax or e-mail us at:

John	Fax: 281-3331	E-Mail:	*john.applegate@law.uc.edu*
Doug	Fax: 648-3629	E-Mail:	[redacted]

FERNALD CITIZENS ADVISORY BOARD

What is the Closure Fund Management Plan?

The Closure Fund Management Plan was produced in response to the US Congress Appropriations Committee's request that DOE provide a plan on how it would reduce bureaucracy and manage the two closure sites: Fernald and Rocky Flats. This report outlines the new management approach and highlights improvements in the management of all the Environmental Management Projects. EM has recognized that in order to succeed in achieving site cleanup at most sites by the year 2006, it will have to change its management system in a fundamental way. EM has created a streamlined management system called the Integrated Planning, Accountability, and Budgeting System (IPABS). The IPABS should structure and streamline formerly independent management systems into a single cohesive integrated system.

What does IPABS encompass?

The IPABS includes:

- Focusing on completion of projects as the basic element of work (A projects is defined as a group of similar or associated activities, each of which has a defined scope, a schedule, and a cost estimate. This project focus is meant to increase efficiency, reduce cost, and provide a more stable and understandable reporting structure.)
- Eliminating "stove-pipe" funding and management (i.e. place more emphasis on the site).
- Creating matrixed headquarters teams to support field work.
- Resolving issues in an expedited manner.

The IPABS will focus on the site and will hopefully lead to rapid decision-making and elimination of micromanagement. Communications between the site and Headquarters should also increase. Keys to the success of this plan are the development of technically sound baselines in the Waste Disposition Plan, the identification of critical path projects/activities, and the identification of programmatic risk.

What other activities will be necessary to achieve for the 2006 cleanup goal?

- Plutonium must be moved from Rocky Flats in the near future, which will require actions from other field offices.
- Depleted, normal, and low enriched uranium at Fernald must be disposed of prior to 2000.
- Future contracts must be structured to support site closure.
- Some materials must be transported from site to site in an expeditious and predictable manner.
- Low-level and mixed low-level waste must have suitable disposal options.
- The Waste Isolation Pilot Plant (WIPP) must open in 1998.
- Adequate and stable funding must be available.

Technical Report Summary:

Closure Fund Management Plan

USDOE, December 1997

FERNALD CITIZENS ADVISORY BOARD

What is the Nevada Test Site Intermodal Transportation Facility Site and Routing Evaluation Study?

The Nevada Test Site Intermodal Transportation Facility Site and Routing Evaluation Study analyzes potential rail-to-truck transfer sites and the associated truck routes for the transportation of low-level waste from Fernald to the Nevada Test Site (NTS). Fernald was selected as the originator of these wastes because this site ships the most low-level wastes to the NTS. Currently, these wastes are shipped to NTS from Fernald by truck and enter Nevada on US Highway 93 at the Hoover Dam and continue through the Boulder City, Henderson, Las Vegas, and the Paiute Tribe Reservation. This study attempts to identify a method of intermodal transport that does not route wastes through the Las Vegas Valley. Original studies on intermodal transport of these wastes suggested the use of the Valley facility in North Las Vegas for the intermodal transfer station. Stakeholders strongly objected to this plan. This study evaluates the possible use of the Valley transfer station as well as potential transfer sites at Caliente (Nevada), Apex (Nevada), Dunn (California), and Yermo (California).

What were the bases of evaluation for these sites?

The potential intermodal transfer sites were evaluated on four criteria:

- **Site Capabilities-** This includes the availability and accessibility of a suitable area and infrastructure for transfer-point operations, availability of intermodal equipment, and the ease of making logistical and institutional arrangements.
- **Cost-** Cost was not considered an overriding factor in selecting an intermodal facility.
- **Public Safety and Environmental Protection-** This included an evaluation of seven safety and environmental protection issues. Information for evaluating the type and proximity of man-made hazards and the proximity of difficult-to-evacuate facilities could not be obtained for some sites.
- **Community Acceptance-** Representatives from potentially affected communities were asked to provide information about their communities' degrees of acceptance of a nearby intermodal transfer facility and/or the associated truck routes.

The evaluation did not include a description of emergency management resources in each area. Information utilized was limited to that which was easily available.

What were the conclusions of the study?

The study found that:

- Relative to site capability, Valley, Yermo, and Caliente were the most feasible candidate sites. Yermo and Valley have existing intermodal facilities. Caliente has a good location near US 93, a good surface for a transfer facility, and Union Pacific (UP) ownership.
- Use of any of the sites would cost less than current truck transport.
- The Yermo and Caliente sites pose the least safety and health risks to the public and the environment. Use of Apex or Valley would require the transport and transfer of low-level wastes in or near highly congested areas. Continued use of the truck-only option will result in ongoing safety, health and environmental risks due to routing over the Hoover Dam and through the Las Vegas Valley.
- The Caliente option showed the most community acceptance.

Technical Report Summary:

Nevada Test Site Intermodal Transportation Facility Site and Routing Evaluation Study

US DOE- Nevada, January 1998

What are the cost associated with intermodal transport?

DOE-NV requested information on costs from both UP and Burlington Northern Santa Fe Railroad (BNSF). BNSF estimates were based on railroad transportation only. BNSF estimated a cost of $1,750 to $1,800 per 20-foot container if 900 containers per year were shipped. UP estimates included truck transport to NTS. UP estimates ranged from $2,850 per container at Caliente to $3,500 per container at Dunn and Yermo. Current truck shipments average $3,600 per 20-foot container.

How has this study been used?

The results of this study have been used to develop alternatives which will be evaluated in a more thorough NEPA (National Environmental Policy Act) analysis. This NEPA analysis will evaluate the following four alternatives:

- No action, which means continued truck transport along current routes.
- An intermodal transfer site at Caliente and the associated truck routes.
- An intermodal transfer site at Yermo and the associated truck routes.
- Two intermodal transfer sites: one at Caliente and one at Yermo.

FERNALD CITIZENS ADVISORY BOARD

Topics:

- Discuss Sitewide Monitoring and Sampling
- Discuss the Quarterly Integrated Environmental Monitoring Plan (IEMP) Report

Attendees:

CAB members:	Pam Dunn
	Darryl Huff
	Doug Sarno
	Bob Tabor
DOE:	Johnny Reising
	Kathi Nickel
Fluor Daniel Fernald:	Mark Cherry
	Terry Hagen
	Bill Hertel
OEPA:	Donna Bohannon

Meeting Summary:

Mark Cherry began the meeting with a discussion of the Quarterly IEMP Report. The December 1997 document is the first of the comprehensive IEMP reports under the new framework. There will be four quarterly reports and an annual report, which will provide a historical summary for the whole year. This new framework was implemented in August 1997.

The report is organized so that the four major media, groundwater, surface water, air, and natural resources are discussed in detail. Sediments and biota will only be discussed in the annual report since they are sampled only once a year. The report extensively utilizes graphs and charts. Graphs and charts will be easier to update quarterly than will text. Mark asked the committee to review the document for improvements in the utilization of these graphs and charts. Any comments will be incorporated in the next quarterly report.

Groundwater

Bill Hertel discussed the groundwater monitoring program under the IEMP. Although the South Plume Module has had some maintenance problems over the past year, these have been resolved and two new wells will be coming on line this summer. The groundwater monitoring program utilizes two types of wells: Type 2 and Type 3. The Type 2 wells are located near the top of the water table and Type 3 wells go down about 50 feet into the water table. These different wells are used to help determine the level of the contamination within the water table. Groundwater monitoring also utilizes geoprobes which start at the water table and go down about 10 feet. These are used to supplement monitoring especially in northern areas of the site where the remedial designs have not been completed. These monitoring activities have shown that the main portion of the South Plume is being captured but there is still some uncertainty about what is occurring in the northeast.

The reinjection system was also discussed. The purpose of this project is to flush the aquifer and thus shorten the total remediation time. Off-site contamination will be flushed back to the wells on site. There are several reinjection wells being used, but not all have the same capacity. The target date for full scale reinjection is this summer. Bob Tabor pointed out that reinjection may appear to actually increase the levels of contaminants at first, since it may break contamination away from the sediment. He pointed out that many people may not understand this. The reinjection system also will lower the water table somewhat; monitoring shows that now it is lowered about 2 feet in the areas undergoing reinjection.

Members of the Committee were also interested in the homeowner wells being utilized for monitoring. Right now there are only three of these wells being sampled. Much of this sampling has been replaced by monitoring wells because they produce higher quality data. The three homeowner wells are still being used because of their location.

The RCRA Boundary Data showed that there were still exceedences of the final remediation levels (FRLs) for total chromium, manganese, and zinc. OSDF Baseline Sampling did not represent a full year's worth of sampling and sampling occurred every couple of weeks.

Surface Water

The NPDES (National Pollutant Discharge Elimination System) Permit Compliance showed that permits were achieved 99.8% of the time. Before the IEMP was implemented, a monthly report of discharges of both chemical and nutrient constituents was complied. FDF has tried to integrate these monthly reports into a quarterly report.

For the FFCA (Federal Facilities Compliance Agreement) and OU5 ROD (Record of Decision) Compliance, only 19% of what was allowed under the ROD was discharged. Compliance was achieved with the 20μg/L uranium. This requirement will become more difficult to achieve as more wells are brought on line and the treatment capacities are maximized. Right now there are four wells, but eventually the number will increase to sixteen.

No exceedences were found in surveillance monitoring although there were occasional exceedences of on property drainages to Paddys Run. The Pilot Plant Drainage Ditch has historically had high releases, so a sump was installed.

Air

The basis for the Radiological Air Particulate Monitoring Program has changed. Historically, modeling was used to determine levels of radioactive particulates. Now, however, the source of these emissions is more diffuse. Thus, monitoring has become the preferred approach for determining these levels. There is currently a network of 18 monitors in and around the site. The data obtained from these monitors will be used to show compliance with NESHAP (National Emissions Standards for Hazardous Air Pollutants) rules. OEPA is also operating five monitors: three are located on-site and two are off-site. Doug Sarno was concerned that FDF was not making the decontamination process visible to citizens so that they would know that contamination has been removed from vehicles, etc., and is not leaving the site. Pam Dunn inquired as to whether portable monitoring equipment can be used to monitor air contamination off-site in the event of a high reading on the property line. In the case of such an event, FDF will determine from where the release is coming and deal with it by using additional controls. Doug suggested that FDF develop materials to help people understand the concept that whereas contamination from smokestacks used to travel far and wide, today's contamination is ground based and will travel differently.

To monitor for radon, radon emissions are measured over a period of time. There have been three exceedences of the 100pCi/L level. These are not unusual and all are associated with the K-65 Silos. Pam noted that people will want additional radon monitoring as remediation activities continue. The amount of radon monitoring can be reevaluated in two years when the IEMP is revised.

Natural Resources

The habitat of Sloan's Crayfish is being protected. The IEMP will provide a running tally of all habitats that are being impacted. There have been five unexpected cultural resources found during the course of remediation. Also an additional 0.5 acres of wetlands have been identified.

REPRODUCED WITH THE PERMISSION OF INSIDE ENERGY, McGRAW, HILL COMPANY

1256

Inside Energy/

An exclusive weekly report on the U.S. Department of Energy

January 26, 1998

STICK WITH ALM PLAN, BOARD TELLS DOE

Assistant Secretary for Environmental Management Alvin Alm received a strong endorsement of his legacy at DOE last week, as an advisory board called upon the department to stick with his plan for accelerating the cleanup of contaminated nuclear-weapons facilities after he leaves office this week.

The Environmental Management Advisory Board unanimously approved a resolution supporting the plan, which calls for completion of cleanups at most of DOE's contaminated sites by the year 2006, as well as motions endorsing key components of the plan, such as privatization and technology deployment.

While the endorsement itself was not surprising, in light of the board's involvement in the plan's development, it was timely, with Alm scheduled to leave DOE Friday.

"The one thing the program needs now is stability and execution," EMAB Co-Chair David Bodde said after the board's meeting in Washington Wednesday. "We know what to do. We've got a reasonable plan."

"The underlying message at that meeting was concern over continuity," the board's other co-chair, Douglas Costle, said later. "There's been a lot of frustration over getting this

(Continued on page 11)

STICK WITH ALM PLAN, BOARD TELLS DOE . . . . . begins on page 1

program on a schedule, with milestones and accomplishments, so that work is actually getting done, instead of just policymaking."

"There's always concern in an agency when a new team arrives," Costle, chairman of the Institute for Sustainable Communities and former administrator of the Environmental Protection Agency, added. "The question is how to educate them so that they can interact intelligently."

Alm called the board's endorsements "very positive," and added that they "will be very helpful" in persuading his successor to stick with the so-called National 2006 Plan.

The board's votes followed several reports on a draft version of the plan, including one specifically warning DOE not to allow the new assistant secretary for environmental management to abandon Alm's strategy. As of last week, the White House had not decided on a replacement for Alm, who joined the department in 1996.

"[The year] 1998 will inevitably bring about substantial change for the EM program, not the least of which will be a transition to a new assistant secretary and key staff," a report from EMAB 2006 Strategic Planning Committee said. "Through this year, though, we foresee a need for continuity, to allow several components of the program time to mature — to be tried and improved upon rather than changed substantially."

Brian Costner, of the Energy Research Foundation in South Carolina, who chaired the 2006 Strategic Planning Committee, urged Alm to "get this message to your replacement as soon as possible, and ... in a

7

way that gets his or her attention."

Alm proposed the 2006 Plan last year out of concern that Congress and the public eventually would lose interest in the cleanup program and cut funding for it. He reiterated last week that the program is more likely to receive continued support if it establishes clear and realistic goals for accelerating its work and completing as many of its projects as possible by 2006.

DOE plans to release a revised draft of the plan to Congress and the public in February or March, Alm said.

The report by Costner's committee applauded the plan's emphasis on specific projects, rather than the program's traditional focus on broad activities, and suggested that any changes should be kept to a minimum. "Although refinements may well be needed to improve the performance of the management system, for example, in [the] definition of projects and in DOE oversight, changes this year should be small, to provide time to adequately evaluate the system," the report said.

The plan's reliance on project management also was praised in another EMAB report examining that specific issue. "Pushing responsibilities and focus down to the project level is not only possible, but it is the right way to go," said the Integrated Planning, Accountability and Budgeting System Committee, which investigated activities at Fernald Environmental Management Project in Ohio and the Rocky Flats Environmental Technology Center in Colorado.

"As DOE picks the best contractors available to implement Plan 2006, the contractors (rather than the government employees) should in most cases provide 'project managers' at the site level," the report said. " ... As we were hoping for, we did see clear indications that, at Fernald and Rocky Flats, this approach is in fact in place or clearly developing."

The committee, which was chaired by Joel Bennett, of Parsons Brinckerhoff Inc., offered advice on ways of improving project management, including making sure DOE allows contractors to hire enough qualified personnel to complete the cleanup activities and alleviate "severe restrictions" on security clearances, which the panel said are interfering with work at Fernald and Rocky Flats, and possibly at other sites.

EMAB also approved a resolution supporting efforts by the Environmental Management division to promote the deployment of new technologies needed for its projects, as well as a motion urging EM to hire personnel specialized in privatization.

Edgar Berkey, of Concurrent Technologies Corp., who chaired an EMAB committee which reviewed the technology-deployment initiative, said it had not received sufficient support among individuals managing DOE's cleanup projects. Berkey cited several reasons for the tepid response, including the belief among some managers that "the technologies being developed are not addressing their specific needs."

"It takes time," Berkey said of DOE's attempts to build support for the technology-deployment program, adding his committee found some progress. For example, officials working on high-level-waste technologies have done "an excellent job," he said. "Other focus areas have been successful to a lesser extent," he added.

Alm, however, stressed the urgency of implementing new technologies, especially in light of congressional criticism that the program has been a failure. "If we don't show some progress in deployment, first, we're not going to achieve the goals of the 2006 program, and we also risk losing the technology program. There are enough critics of the program and of the lack of deployment ... ," he said.

An EMAB committee studying privatization criticized EM for beginning complex initiatives, such as the Tank Waste Remediation System project at the Hanford Site, without adequate foresight or expertise. The panel's report said it found "no DOE-wide (much less DOE/EM) policy to encourage or reward privatization," adding "procedural and cultural barriers exist."

The resolution on privatization approved by EMAB calls on EM to hire personnel familiar with contract, financial, insurance, labor, legal and other topics associated with such activities. Such personnel, committee members said, would work in conjunction with an existing department-wide Contract Reform and Privatization Office. — *Bill Loveless*

REPRODUCED WITH THE PERMISSION OF INSIDE ENERGY, McGRAW, HILL COMPANY

8

February 3, 1998
The Cincinnati Enquirer
Page A4
"Clinton adds $16M for cleanup"
Reporter: Paul Barton

1256

Fernald

Clinton adds $16M for cleanup

BY PAUL BARTON
Enquirer Washington Bureau

WASHINGTON — The cleanup of the former uranium processing facility at Fernald would receive a $16.6 million increase under the president's proposed 1999 budget released Monday.

Funding for the site would increase from $258.70 million per year to $275.34 million.

The increase reflects the Energy Department's desire to keep the cleanup on schedule for completion by 2005, officials said.

Key activities in 1999 are expected to include continued placement of radioactive wastes in on-site facilities, shipment of Operable Unit 1 waste, complete remediation of part of the site, and acting on remaining low enriched uranium nuclear material inventories, the department said in budget documents.

"We're extremely pleased with the president's proposal," said department spokesman Gary Stegner.

He added, "I think they see Fernald as one of the projects that can be completed, for the most part, with existing technology."

Energy Secretary Federico Pena has designated Fernald as a site to be included in the department's "accelerated closure" initiative, meaning it will be one of the first Cold War nuclear weapons sites scheduled for completion of cleanup.

February 4, 1998
The Cincinnati Enquirer
Hometown, Page B3
"Leaks to be discussed"
Reporter:

- 1256

Leaks to be discussed

CROSBY TOWNSHIP — Department of Energy representatives Tuesdaywill discuss the results of an investigation of a December incident where several containers in trucks bound from the Fernald cleanup site for Nevada leaked low-level radioactive waste.

The February Cleanup Progress briefing on the "leaking white metal box waste containers" starts at 6:30 p.m. in Classroom D of the Alpha Building, 10967 Hamilton-Cleves Highway.

February 5, 1998
Journal News
Education, A6
"High schools headed to science bowls"
Reporter:

High schools headed to science bowls

Science teams from three school districts in Butler County will compete Saturday in two Science Bowls sponsored by the U.S. Department of Energy and Fluor Daniel Fernald.

Science teams from the Ross and Lakota West high schools will compete against science teams from 22 other Ohio, Kentucky and Indiana districts from 9 a.m. to 2:30 p.m. Saturday, at Cincinnati State Technical and Community College, 3520 Central Parkway, Cincinnati.

The competition consists of several oral question-and-answer rounds in which two teams attempt to outscore each other with the number of correctly answered questions.

In addition, the science team from Hamilton High School will compete against the science teams from 31 Ohio, Kentucky and Indiana school districts. The competition will take place from 9 a.m. to 2:30 p.m. Feb. 21 at the University of Dayton.

February 6, 1998
The Cincinnati Enquirer
Hometown, Page C3
"Kits teach physics"
Reporter: Lew Moores

The Cincinnati Enquirer/Saed Hindash

Brandi Hibbard, 11, uses a Dacta construction kit to build a machine at Crosby Elementary School.

Kits teach physics

Fluor Daniel helps buy construction sets

BY LEW MOORES
The Cincinnati Enquirer

CROSBY TOWNSHIP — The building construction sets are opened and spread out on work tables in the classroom at Crosby Elementary, a school surrounded by flat farmland.

The 28 disassembled sets are a collage of colored plastic pieces. Sixth-graders study the parts, check directions and begin assembling; there is logic to the play, with the functional gears, wheels, axles, levers, pulleys.

"This is actually using their concepts of what simple machines are," said Ron Mangus, their science and math teacher. "Things like how levers work and help us to do work easier. How to use a ramp, what purpose wheels serve and the axle that attaches the two wheels."

The sets, made by Dacta, a division of Lego, are among the fruits of a partnership between Fluor Daniel Fernald Inc., the company doing the cleanup at the nearby Fernald uranium processing plant, and elementary schools in Southwest Local School District.

The partnership yielded a program that would be funded with $9,900 from Fluor Daniel, with Crosby Elementary receiving $1,780. The money would be used for teaching equipment, an educational field trip and a workshop for teachers.

Susan Walpole, public affairs administrator for Fluor Daniel, said the idea is to increase interest in science and the goal is to make students science-literate.

"Schools need this kind of community involvement," said Ms. Walpole, who taught for more than 15 years in the area.

At Crosby, 24 sixth-graders arranged themselves at six tables and began assembling the pieces into miniature working equipment: a lawn mower, a carousel, a conveyor belt, a crane.

Scott Gallant, 11, made a lawn mower, nimbly putting together wheels and axles. He was first to finish.

"I have a lot of Legos at my house," said Scott, who lives in Crosby Township, is a talented math student and at this point in his life wants to be a toy designer. "This is simple. It shows how wheels and axles, gears and levers work. But it's neat actually getting to build it."

Justin Lawler, 12, of Fairfield, tried a carousel.

"I can finish them pretty quick because I have a lot of Legos at home," said Justin.

Alex Hearing, 11, of Okeana, also has experience with Legos, as does Kris Berry, 12, Okeana, and Eric Anderson, 12, of Harrison. Eric built a lawn mower, which he now adds to his repertoire of model cars and space rovers.

"It's real life, hands on," said Mr. Mangus. "They'll go home and talk about where ramps and where levers are being used. A bottle opener is a lever. . . . a fishing rod, a bat are all examples, and how they're allowing you to perform work and do it easier than if you didn't have it."

12

FLUOR DANIEL FERNALD

D. Paine, FDF, MS52-4
D. L. Painter, FDF, MS44-1
L. A. Parnell, FDF, MS80-3
L. A. Peet, FDF, MS44-1
N. E. Pennington, FDF, MS44-1
B. S. Perkins, FDF, MS67
S. M. Peterman, FDF, MS52-4
P. J. Pettit, FDF, MS50
W. H. Previty, FDF, MS51
Public Env. Info. Center, FDF, MS78
N. R. Reeves, FDF, MS52-2
F. A. Renk, FDF, MS31
S. Reutcke, FDF, MS90
L. C. Rogers, FDF, MS31
S. H. Shirley, FDF, MS51
J. L. Smets, FDF, MS52-4
C. K. Smith, FDF, MS44-1
K. A. Solomon, FDF, MS19
K. D. Spring, FDF, MS52-2
R. G. Stengel, FDF, MS52-1
J. M. Stevens, FDF, MS44-1
J. E. Stone, FDF, MS51
V. D. Stultz, FDF, MS50
M. L. Sucher, FDF, MS8
S. G. Sullivan, FDF, MS31
C. Sutton, FDF, MS35
T. Thompson, FDF, MS7
J. L. Trujillo, FDF, MS67
C. L. Turner, FDF, MS44-1
B. D. Varchol, FDF, MS90
J. M. Venditti, FDF, MS52-3
T. J. Walsh, FDF, MS65-2
H. E. Weeks, FDF, MS52-4
D. R. Whisler, FDF, MS52-3
R. E. Whitaker, FDF, MS52-3
K. Wilkerson, FDF, MS65-2
L. A. Winkler, FDF, MS51
K. N. Wintz, FDF, MS20
L. M. Woeste, FDF, MS52-2
E. E. Zobrist, FDF, MS9

To update distribution list, please contact Wayne Reed at 648-6225.

FLUOR DANIEL FERNALD

bcc:

A. B. Attuquayefio, FDF, MS52-9
D. R. Austin, FDF, MS26
R. L. Baker, FDF, MS80-5
R. E. Bauer, FDF, MS69
T. M. Beasley, FDF, MS44-1
D. R. Berg, FDF, MS80-3
T. A. Biscup, FDF, MS15
S. L. Blankenship, FDF, MS75
T. D. Borgman, FDF, MS44-1
J. B. Bradburne, FDF, MS52-3
D. J. Brettschneider, FDF, MS52-5
L. Brown, FDF, MS81-1
G. A. Cantwell, FDF, MS44-1
D. P. Capelle, FDF, MS65-2
D. J. Carr, FDF, MS52-5
M. J. Cherry, FDF, MS90
J. D. Chiou, FDF, MS52-5
M. L. Church, FDF, MS52-3
T. R. Clark, FDF, MS52-3
A. G. Clines, FDF, MS44-1
M. G. Connors, FDF, MS52-4
P. A. Cupp, FDF, MS44-1
J. E. Curry, FDF, MS65-3
S. A. Deller, FDF, MS44-1
W. R. Den Herder, FDF, MS52-3
D. W. Duderstadt, FDF, MS52-8
J. A. Ellinghausen, FDF, MS44-1
R. Fellman, FDF, MS52-1
W. F. Fick, FDF, MS52-8
K. S. Fritts, FDF, MS31
V. T. Furlong, FDF, MS71-3
Y. G. Gale, FDF, MS52-4
J. W. Gibson, FDF, MS80-2
E. Green, FDF, MS40
T. D. Hagen, FDF, MS65-2
C. L. Hale, FDF, MS31
R. O. Hammack, FDF, MS67
L. H. Hampshire, FDF, MS52-3
R. Hanson, FDF, MS1
J. E. Harmon, FDF, MS90
M. M. Heath, FDF, MS14
R. P. Heck, FDF, MS2
R. L. Henry, FDF, MS44-1
M. J. Hickey, FDF, MS64
S. L. Hinnefeld, FDF, MS2
S. K. Holliday, FDF, MS69
L. L. Honigford, FDF, MS16-2
D. W. Hooper, FDF, MS52-1
M. S. Howard, FDF, MS69
M. S. Hundley, FDF, MS44-1
A. Hunt, FDF, MS52-5
R. A. Hunt, FDF, MS66
W. B. Jameson, FDF, MS24
M. A. Jewett, FDF, MS52-5
M. J. King, FDF, MS6
P. R. Kraus, FDF, MS67
M. Lee, FDF, MS3
M. Thomas Lee, FDF, MS81-1
J. W. Legge, FDF, MS49
J. A. Lester, FDF MS52-3,
R. A. Markus, FDF, MS52-5
R. L. Maurer, FDF, MS52-4
C. McDaniel, FDF, MS80-5
A. J. Meyer, FDF, MS35
M. L. Miller, FDF, MS30
T. D. Miller, FDF, MS80-3
P. E. Mohr, FDF, MS81-1
C. S. Molnar, FDF, MS52-3
M. E. Morris, FDF, MS52-9
W. L. Morris, FDF, MS69
A. R. Murphy, FDF, MS69
R. E. Nagel, FDF, MS18
S. W. Neumann, FDF, MS31
R. M. Nichols, FDF, MS44-1

D. A. Nixon, FDF, MS52-4
A. C. Noble, FDF, MS81-3
M. W. Page, FDF, MS44-1

FLUOR DANIEL FERNALD

c: **With Attachment:**
N. Akgunduz, MS45, DOE-FEMP
S. Fauver, MS45, DOE-HQ
R. J. Janke, MS45, DOE-FEMP
M. J. Kuntz, MS51, FDF
D. A. Lojek, MS45, DOE-FEMP
W. E. Pasko, MS45, DOE-FEMP
C. W. Reed, MS80-3, FDF
J. W. Reising, MS45, DOE-FEMP
J. M. Sattler, MS45, DOE-FEMP
P. A. Shirley, OSE 350 G, DOE-OH
J. H. Trygier, MS45, DOE-FEMP
P. S. Van Loan, OSE 345, DOE-OH
R. D. Warner, MS45, DOE-FEMP
H. R. Youngmeyer, MS45, DOE-FEMP
File Record Storage Copy 106.4.32.3

W/Out Attachment:
L. E. Parsons, DOE Contract Specialist

To update distribution list, please contact Wayne Reed at 648-6225.

FLUOR DANIEL FERNALD P.O. Box 538704 Cincinnati, Ohio 45253-8704 (513) 648-3000

February 6, 1998

Fernald Environmental Management Project
Letter No. C:OOTP:98-0061

Mr. Jack R. Craig, Director
Department of Energy
Fernald Area Office
P. O. Box 538705
Cincinnati, Ohio 45253-8705

Dear Mr. Craig:

CONTRACT DE-AC24-920R21972, MILESTONE SCHEDULE/STATUS REPORT FOR THE PERIOD ENDING JANUARY 18, 1998

Reference: Contract DE-AC24-920R21972, Section J, Attachment B, Reporting Requirements, "Milestone Schedule/Status".

The purpose of this letter is to transmit the Milestone Schedule/Status Report for the period ending January 18, 1998. The following schedule formats are attached:

- Sitewide Master Schedule, FY1998
- Level 1 Milestones, FY1998
- Level 1 Milestones, FY1999 - FY2006
- Level 0/1/2 Milestones, FY1998
- Level 0/1/2 Milestones, FY1999 - FY2006
- EA Milestones, FY1998
- EA Milestones, FY1999 - FY2006

Please note the forecast and baseline columns contain the early dates from both the current and baseline schedules. In an effort to be consistent with the sitewide reporting of baseline schedule data, the early dates will be used in this and future milestone reporting.

If you have any questions, please contact Mike J. Kuntz at extension 648-4775.

Sincerely,

John Bradburne
President

JCB:LAP:lgm
Attachment

Sitewide Master Schedule

FY 1998

Activity ID	Activity Description	Rem Dur	Percent Complete	Baseline Start	Forecast Start	Baseline Finish	Forecast Finish	Total Float
FACILITIES CLOSURE & DEMOLITION								
FACILITY DEMOLITION PROJECTS								
3D07CON131	THORIUM/PLANT 9 COMPLEX SUBCONTRACTOR	194	4	15SEP97	22DEC97A	25MAR99	31DEC98	127
3D07CON132	D&D SUBCONTRACTOR OPTION 1	36	0	02MAR98*	02MAR98*	30APR98	30APR98	262
3D08C01010	BOILER & WATER PLANT COMPLEX	141	62	10MAR97*	03MAR97A	24SEP99	24SEP98	44
3D09M01001	MAINT/TANK FARM D&D IMPLEMENTATION PLAN TO EPA	0	0	04MAR98*	04MAR98*			1
3D05M01001	PLANT 5 IMPLEMENTATION PLAN TO EPA	0	0	18JUL98	18JUL98			0
3D17M01001	STP IMPLEMENTATION PLAN TO EPA	0	0	02APR98	02APR98*			337
3D17C01010	SEWAGE TREATMENT PLANT COMPLEX D&D	52	0	01JUL98	15JUL98	30SEP98	14OCT98	311
SAFE SHUTDOWN								
3S00400000	PLANT 2/3 SAFE SHUTDOWN SUMMARY FY98	69*	44	01OCT96	01OCT96A	11JUN98	27APR98	2,608
3S00500000	PLANT 6 SAFE SHUTDOWN SUMMARY	458*	24	02JAN97	13MAY97A	14DEC98	12NOV99	37
3S00600000	PLANT 8 UTILITY DISCONNECT SUMMARY FY97	37*	65	19MAY97	20JUN97A	24JUL98	11MAR98	2,640
3SPCM01200	PLANT 8 SAFE SHUTDOWN ACTIVITIES COMPLETE	0	0			24JUL98	30MAR98	461
SOILS & WATER								
WASTE PITS REMEDIATION								
1CBA400000	ONSITE RAIL CONSTRUCTION – 1CBA4	88*	73	24OCT96	08OCT96A	22MAY98	22MAY98	384
1CBA600000	OFF SITE RAIL UPGRADE – 1CBA6	30*	77	18NOV96	13FEB97A	20JAN98	02MAR98	442
1C1DEB1000	ARASA SUBCONTRACTOR PATH FORWARD – 1DEB1	0*	100	01OCT96	01OCT96A	18SEP97	20OCT97A	
1CBB102051	ARASA PRE-OPERATIONS – 1CBB1	276*	13	19SEP97	21OCT97A	26FEB99	24FEB99	0
1CBB121219	FDF SUBMIT FINAL DRAFT RD DELIVERABLES TO DOE	0	0			09MAR98	09MAR98	17
1C1DEC1000	OPERATIONS PLANNING – 1DEC1	355*	46	01OCT96	01OCT96A	24MAY99	17JUN99	323
1C1DEC1779	TRANSPORTATION AND DISPOSAL PLAN (EA MILESTONE)	0	0			27APR98*	27APR98*	209
ON SITE DISPOSAL CELL								
2AN7250	Initiate First Waste Placement in the OSDF(EA)	0	100	27MAR98	23DEC97A			
2AF73500	DISPOSAL FACILITY RA WORK PLANS	0*	100	01OCT96	03OCT96A	15JUL97	01OCT97A	
2AN7205	DISPOSAL FACILITY - Construct OSDF	2,237*	7	02JUN97	15MAY97A	29DEC06	29DEC06	0
AQUIFER RESTORATION								
5ACGW6H000	South Plume Optimization (SPO)	112*	42	01OCT96	01OCT96A	13JUL98	26JUN98	45
5ACSF30010	Construction - Pipeline (Subcontractor)	90	29	10SEP97	25AUG97A	18APR98	18APR98	0
5ACSF40010	Start Up - Pipeline	15	0	27APR98	20APR98	23JUL98	08MAY98	65
5AFEM5H000	Groundwater Remediation Footprint Verification	33*	92	01OCT96	24OCT96A	05MAR98	05MAR98	0

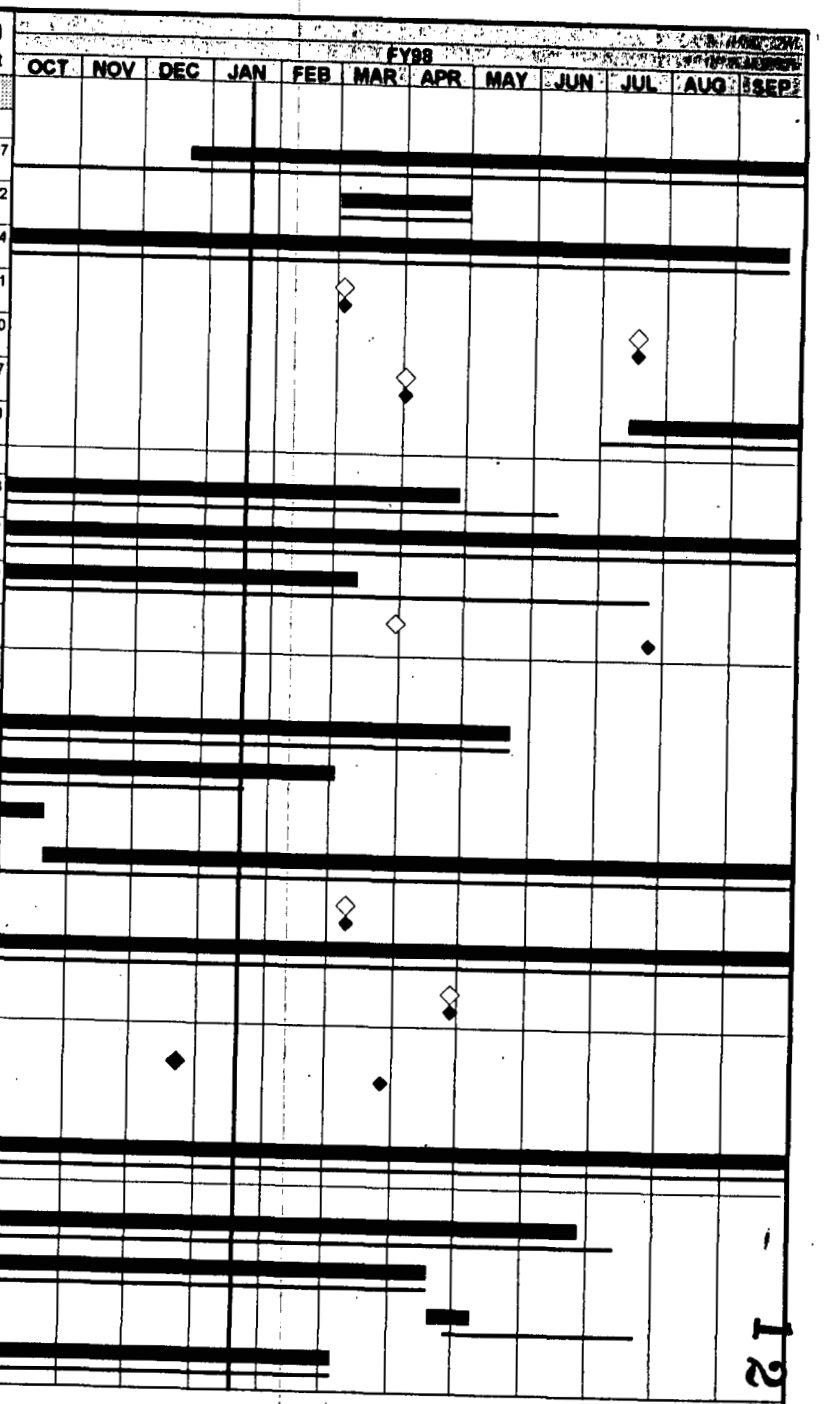

Project Start	01OCT95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	03FEB98

Current
Baseline
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C011

FLUOR DANIEL FERNALD

MASTER SCHEDULE (FY1998 Only)

JANUARY 1998 STATUS

Sheet 1 of 4

FERNALD Environmental Management Project

125

Activity ID	Activity Description	Rem Dur	Percent Complete	Baseline Start	Forecast Start	Baseline Finish	Forecast Finish	Total Float
AWWT / WASTEWATER								
5BBTP0H000	Sewage Treatment Plant	123*	74	01OCT96	01OCT96A	26DEC97	14JUL98	55
5BBWD6H000	Sludge Removal System	254*	5	01APR97	28APR97A	26MAY98	22JAN99	188
5BBWD9H000	VOC Treatment System	300*	1	01APR97	01APR97A	30MAR99	30MAR99	128
5BBWP1H000	Uranium Removal from Water (LOE)	255	78	01OCT96	01OCT96A	30SEP98	30SEP98	0
5BCTP30010	Construction-AWWT Expan (Subcontractor: DeBra)	58	81	16FEB97	14FEB97A	17FEB98	17MAR98	2
5BCTP4H000	Start Up - AWWT Expansion	62*	12	18JUL97	01DEC97A	17FEB98	16APR98	2
5BDAG1H000	AWWT Regeneration System	51*	97	01OCT96	01OCT96A	31OCT97	31MAR98	127
5BBWP1010X	Treatmnt Operations & Routine Mainten (FY98-06)	2,922	0	30SEP98*	30SEP98*	29SEP06	29SEP06	0
SOILS CHARACTERIZATION & EXCAVATION								
5CW7202	SWU SITE PREP CONSTRUCTION ACTIVITIES	0*	100	04AUG97*	15SEP97A	17OCT97	17OCT97A	
5C2CWC1170	IFP Excavation	126	0	01MAY98	01JUN98	30NOV98	30NOV98	112
5CF63512	SWU IMPLEMNT PLAN: SUBMIT DRAFT PKG TO EPA(CA)	0	100			20OCT97	23OCT97A	
5CF63513	SWU : SBMT FNL IMPLEMNT PLN/DESGN PKG TO EPA(CA)	0	0			13FEB98	25FEB98	121
5CD51505	WASTE UNITS TITLE I/II DESIGN	27*	82	01OCT96	01OCT96A	13FEB98	25FEB98	121
5CD51598	SWU: SUBMIT PREFNL/90% DSGN PKG TO EPA(CA)	0	100			20OCT97	23OCT97A	
5CD515M02	SWU: SUBMIT FINAL/CFC DSGN PKG TO EPA(CA)	0	100				17DEC97A	
5C2FM12H01	SWU: Predesign (Plng/Smplng/Analys/Data Mgmt)	19*	80	21JUL97	21JUL97A	15OCT97	12FEB98	262
5CCRA1H010	Sitewide Excavation Plan	93*	75	01OCT96	01OCT96A	17DEC97	01JUN98	85
5C2F63500	AREA I-II: RA WORK PLAN	65*	62	18FEB97	05MAY97A	21APR98	21APR98	323
5C2F63502	AREA I-II RA WP: SUBMIT DRAFT PKG TO EPA(CA)	0	100			21NOV97	21NOV97A	
5CCRA5H000	Area 3: Implementation Plan - PRIOR TO CP02	0*	100	31JUL97	14JUL97A	17OCT97	19DEC97A	
5CCRA5H001	Area 3: Implementation Plan	613*	0	17FEB98	20MAR98	17AUG00	29AUG00	22
5C2D51505	AREA I-II: TITLE I/II DESIGN	54*	85	07OCT96	07OCT96A	27MAR98	03APR98	273
5C2D51595	Area 1-II:Submit 90%/Prefnl Dsgn Pkg to EPA (CA)	0	100			21NOV97	21NOV97A	
5CCSV1H010	Area 1-I: A/B/B1/D1/A1/A2/A3/SB/PS/N.A.Rd	53*	99	28OCT96	28OCT96A	02JAN98	02APR98	125
5CCU210300	Area 1-II: Lead Treatability/Treatment (ETC)	138	0		17MAR98*		30SEP98	285
5CCU210200	Area 1-II: Sector 1A Site Prep-Civil Work (ETC)	40	0		05MAY98*		30JUN98	274
5C5CSA2110	A1 Pit Site Prep	61	0	01SEP98	30JUN98	30NOV98	24SEP98	214
5CCU210250	Area 1-II: Sector 1/2 Excavation (ETC)	64	0		01JUL98		30SEP98	285

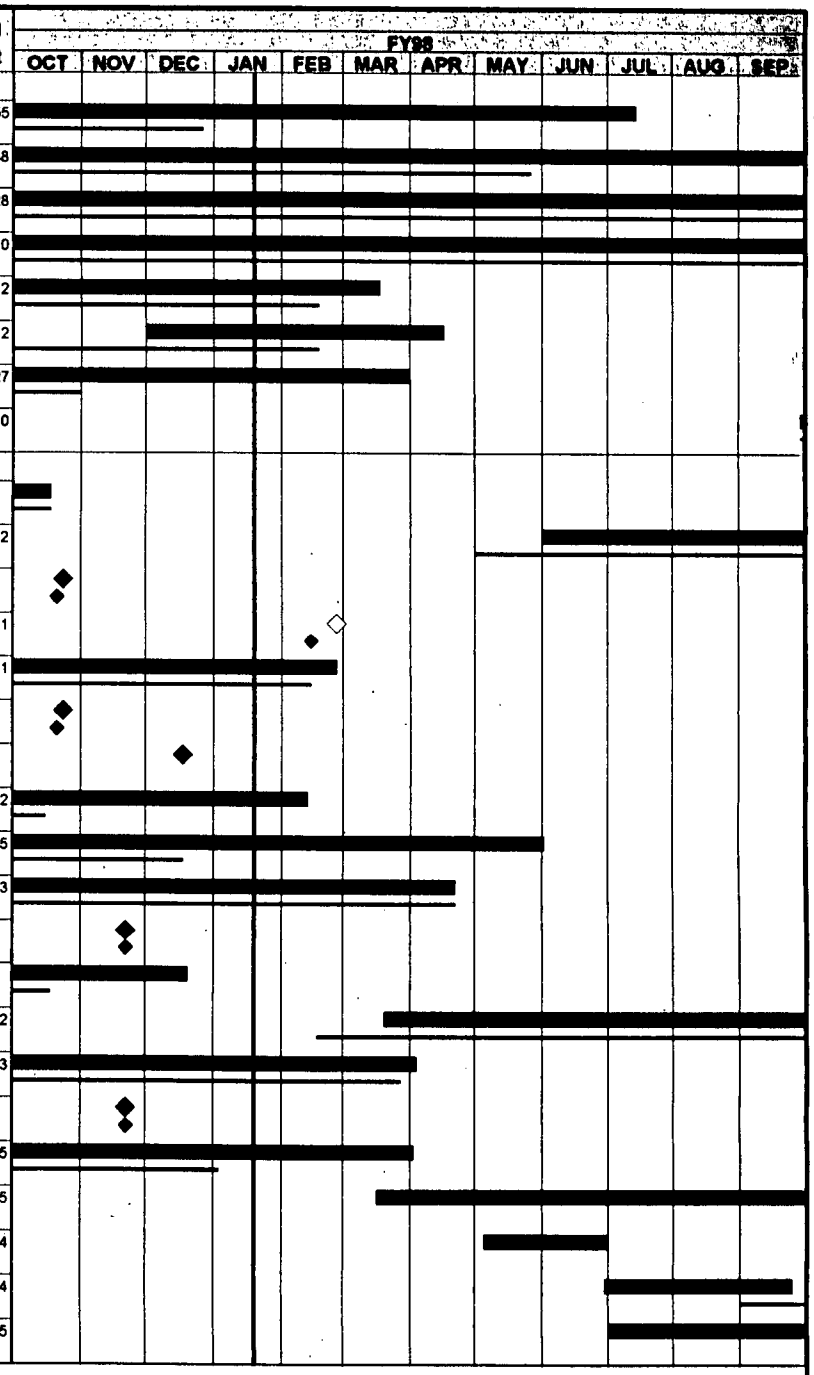

Project Start	01OCT95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	03FEB98

Current
Baseline
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C011

FLUOR DANIEL FERNALD

MASTER SCHEDULE (FY1998 Only)

JANUARY 1998 STATUS

FERNALD
Environmental Management Project

Activity ID	Activity Description	Rem Dur	Percent Complete	Baseline Start	Forecast Start	Baseline Finish	Forecast Finish	Total Float
WASTE MANAGEMENT & SILOS								
SILOS								
4A5ZFC01	VITPP FACILITY MAINTENANCE	178*	29	01OCT97	01OCT97A	30SEP98	30SEP98	2,499
4A5ZFC02	VITPP WASTE DISPOSITION	94*	25	01OCT97	01OCT97A	02JUN98	02JUN98	2,583
4A5ZFC03	TARP & SCAFFOLDING REMOVAL	44*	10	01OCT97	01OCT97A	27OCT97	20MAR98	2,631
4A5AFC14	SILO 1,2,3 CORE SAMPLE	110*	10	01OCT97	01OCT97A	06MAR98	24JUN98	-76
4A5AFC05	SILO 4 CORE BORING TEST REPORT	0	100	01OCT97	01OCT97A	26NOV97	02DEC97A	
4A5AFC15	SILO 1,2,3 CORE SAMPLE TEST REPORT	30*	0	09MAR98	25JUN98	20APR98	06AUG98	-76
4A5L0005	FACILITY OWNERSHIP - FY '98	178*	29	01OCT97*	01OCT97A	30SEP98	30SEP98	2,499
4A5T0005	SITE INTEGRATION- FY '98	178*	29	01OCT97*	01OCT97A	30SEP98	30SEP98	2,499
4A5AFC11	UPDATE SAFETY BASIS	30*	72	01OCT97	01OCT97A	02JAN98	02MAR98	-40
4A5LR010	TRAILER UP-GRADE SCOPE	5	70	01OCT97*	01OCT97A	16JAN98	23JAN98	2,602
4A5AFC07	INFRASTRUCTURE DESIGN	63*	25	01OCT97	02OCT97A	03FEB98	17APR98	-26
4A5AFC09	INFRASTRUCTURE CONSTRUCTION BID/AWARD	42*	0	11FEB98	06JUL98	13APR98	01SEP98	-49
4A5AFC10	INFRASTRUCTURE CONSTRUCTION	172*	0	14APR98	02SEP98	11DEC98	12MAY99	-49
4A5S2014	SILO 4 DEMONSTRATION	179*	0	01OCT97	19JAN98	23JUN98	01OCT98	2,498
4A5C2000	DEVELOP EMERGENCY RECOVERY PLAN	171*	0	01OCT97	31OCT97A	12AUG98	21SEP98	2,506
4A2AS122	PROOF OF PRINCIPLE RFP	29	75	01OCT97*	01OCT97A	14APR98	27FEB98	2,566
4A2AS126	COMPOUND ANALYSIS-SILO#2	24	99	01OCT97*	24NOV97A	10OCT97	20FEB98	2,653
4A2AS127	COMPOUND ANALYSIS - SILO#2 REPORT	0	90	13OCT97	02JAN98A	01DEC97	20FEB98	2,653
4A2AS123	PROOF OF PRINCIPLE BID/AWARD	82	0	15APR98	02MAR98	10AUG98	25JUN98	2,566
4A2H0528	AWARD MULTI-TECH PROOF OF PRINCIPLE CONTRACT	0	0			10AUG98	25JUN98	2,566
4A2H0544	PROOF OF PRINCIPLE TESTING - MULTI-TECH	100	0	26AUG98*	26AUG98*	21JAN99	21JAN99	1,977
4A2AS101	DRAFT FS/PP	200	26	01OCT97*	13OCT97A	30OCT98	30OCT98	2,477
4A3BH010	SILO 3 ESD DEVELOPMENT	10*	90	01OCT97	01OCT97A	20MAR98	30JAN98	14
4A3CH020	SILO #3 R.D.W.P.	137*	0	17DEC97	19JAN98	29JUL98	03AUG98	5
4A3BH110	SILO #3 ESD APPROVAL PROCESS	25*	0	23MAR98	02FEB98	27APR98	09MAR98	37
4A3WH065	SILO 3 SMALL SCALE WASTE RETRIEVAL	62*	50	01OCT97	01OCT97A	04FEB98	16APR98	-11
4A3DH020	PREPARE SILO 3 STABILIZATION DRAFT/FINAL RFP	133*	40	01OCT97	01OCT97A	14MAY98	28JUL98	0
4A3EH030	SILO 3 STABILIZATION BID & AWARD	185*	0	28MAY98	29JUL98	08FEB99	26APR99	0

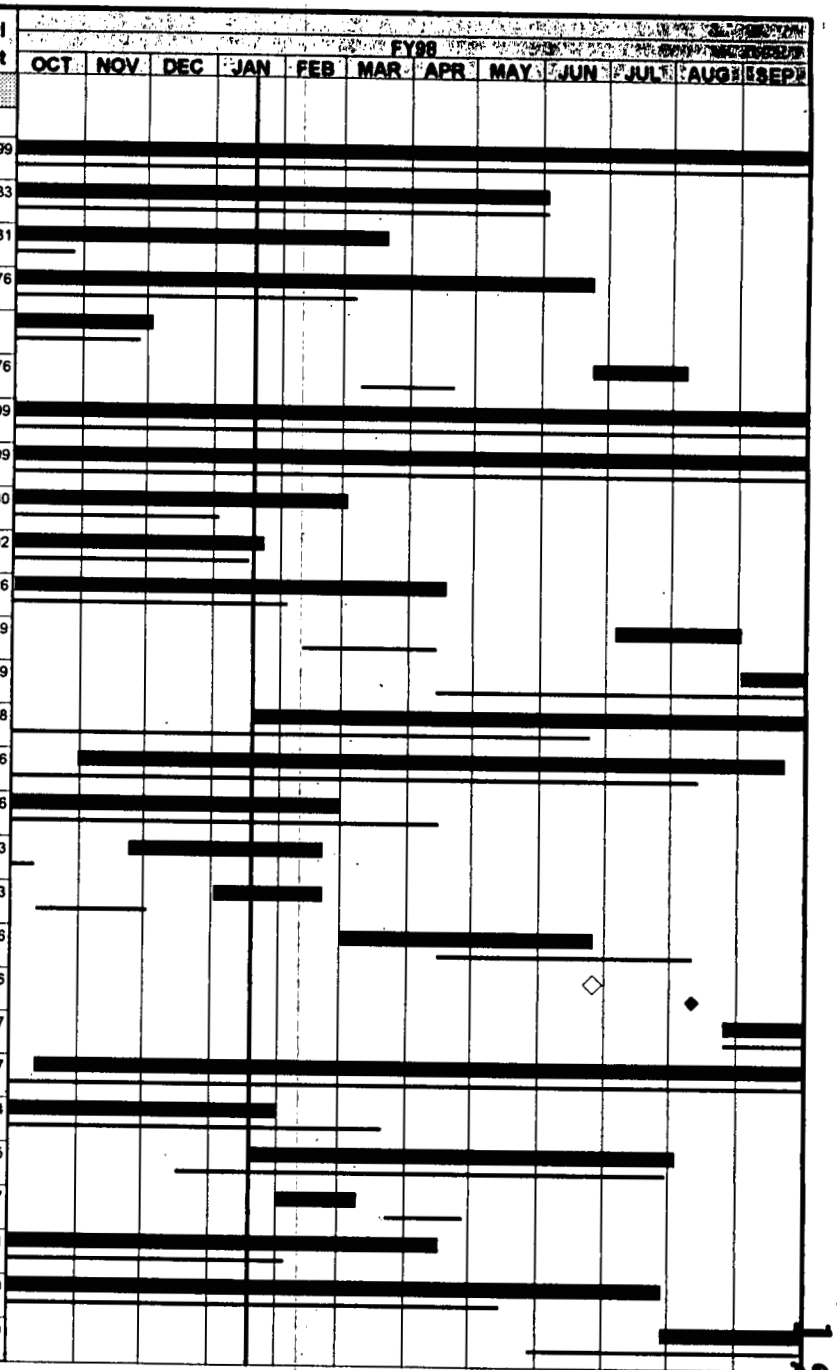

Project Start	01OCT95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	03FEB98

Current
Baseline
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C011

FLUOR DANIEL FERNALD

MASTER SCHEDULE (FY1998 Only)

JANUARY 1998 STATUS

Sheet 3 of 4

FERNALD
Environmental Management Project

Activity ID	Activity Description	Rem Dur	Percent Complete	Baseline Start	Forecast Start	Baseline Finish	Forecast Finish	Total Float
SILOS								
4A2A0010	DESIGN BASIS (CP FY97-13)	0	100	01OCT97*	01OCT97A	21NOV97	03NOV97A	
4A2W0000	RFP PROCESS	178	23	24NOV97*	20OCT97A	30SEP98	30SEP98	2,499
4A2W0020	DESIGN BASIS (CP FY98-02)	79	34	24NOV97	03NOV97A	11MAY98	11MAY98	2,598
4A2W0010	FUNCTIONAL REQUIREMENTS DOCUMENT	10	60	24NOV97*	03NOV97A	26JAN98	30JAN98	2,667
4A2W0041	ISSUE CBD	0	100	19FEB98*	09DEC97A			
4A2W0541	ISSUE AWR RFP	0	0			27MAR98*	27MAR98*	2,628
4A2W0860	PRE-BID MEETING	0	0	06APR98*	06APR98*			2,623
4A2W0080	PROJECT OVERSIGHT	754	0	20AUG98*	20AUG98*	24AUG01	24AUG01	1,774
4A2W0651	AWARD AWR CONTRACT	0	0			30SEP98*	30SEP98*	2,376
4A2CH280	RHEOLOGY TESTING	59	59	01OCT97*	01OCT97A	13APR98	13APR98	2,618
WASTE MANAGEMENT								
W8TIESS6A	REMOVE STORED WASTE FROM PLANT 6	30	100	14APR97*	19JAN98	23MAY97	02MAR98	
W8TIESS8A	REMOVE STORED WASTE FROM PLANT 8	30	0	20AUG98*	20AUG98*	01OCT98	01OCT98	0
W8ADDM900	Chemical Stabilization Treatment Complete	0	0			22JUN98	23SEP98	505

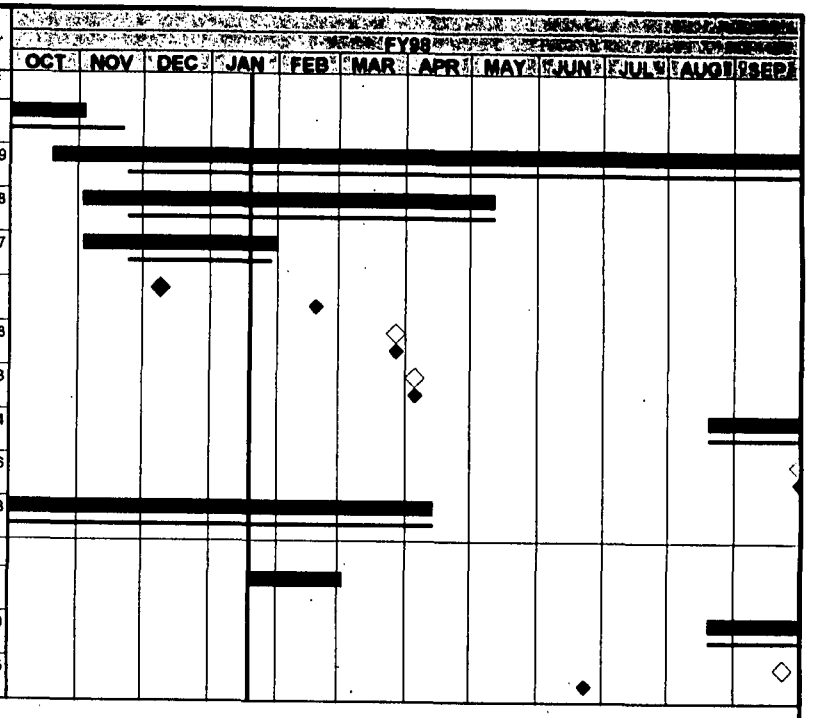

21

Project Start	01OCT95	Current
Project Finish	30SEP08	Baseline
Data Date	19JAN98	Progress Bar
Run Date	03FEB98	Critical Activity

© Primavera Systems, Inc.

C011

Sheet 4 of 4

FLUOR DANIEL FERNALD

MASTER SCHEDULE (FY1998 Only)

JANUARY 1998 STATUS

FERNALD
Environmental Management Project

Level 1 Milestones

FY 1998

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D09M01001	MAINT/TANK FARM D&D IMPLEMENTATION PLAN TO EPA	0	04MAR98*	04MAR98*			1
3D17M01001	STP IMPLEMENTATION PLAN TO EPA	0	02APR98*	02APR98			1
3D05M01001	PLANT 5 IMPLEMENTATION PLAN TO EPA	0	18JUL98	18JUL98			1
Soils and Water							
5CD51598	SWU: SUBMIT PREFNL/90% DSGN PKG TO EPA(CA)	100			23OCT97A	20OCT97	1
5CF63512	SWU IMPLEMNT PLAN: SUBMIT DRAFT PKG TO EPA(CA)	100			23OCT97A	20OCT97	1
5C2D51595	Area 1-II:Submit 90%/Prefnl Dsgn Pkg to EPA (CA)	100			21NOV97A	21NOV97	1
5C2F63502	AREA I-II RA WP: SUBMIT DRAFT PKG TO EPA(CA)	100			21NOV97A	21NOV97	1
5CD515M02	SWU: SUBMIT FINAL/CFC DSGN PKG TO EPA(CA)	100			17DEC97A		1
5CF63513	SWU : SBMT FNL IMPLEMNT PLN/DESGN PKG TO EPA(CA)	0			25FEB98	13FEB98	1
5CCRA1M012	Submit Draft Final SEP to USEPA	0	20APR98	10OCT97			1
5CCRA4M006	Submit Draft Final to USEPA-SEP Support Plans(L1	0	20APR98.	08OCT97			1
5C2F63503	AREA I-II: SBMT FNL RA WORK PLN PKG TO EPA	0			21APR98	21APR98	1
Waste Management and Silos							
4A2H0528	AWARD MULTI-TECH PROOF OF PRINCIPLE CONTRACT	0			25JUN98	10AUG98	1
W8ADDM900	Chemical Stabilization Treatment Complete	0			23SEP98	22JUN98	1

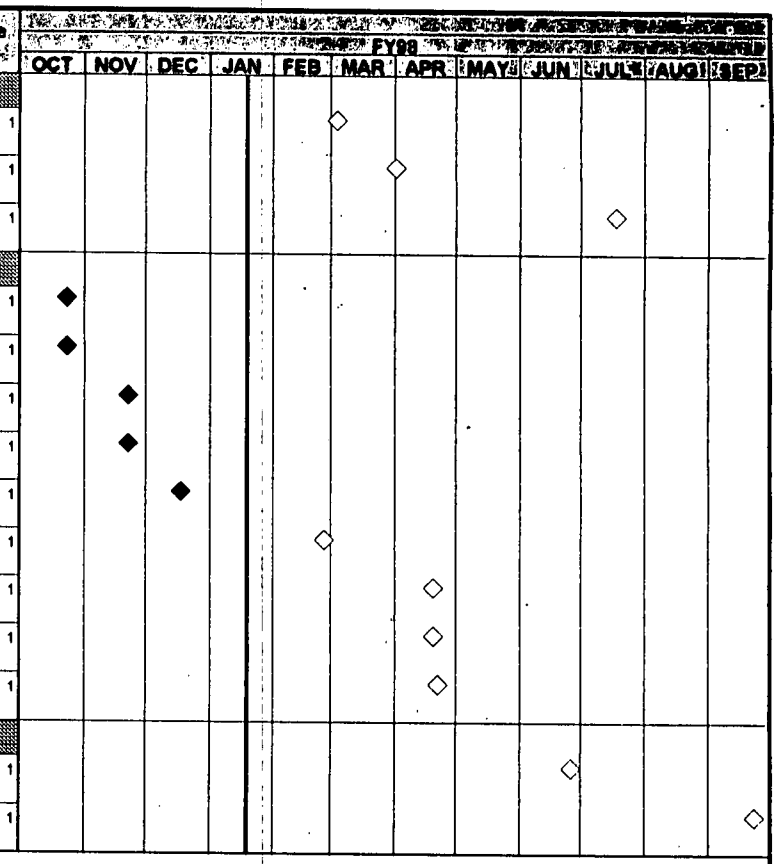

Project Start	01JAN95	Current Bar
Project Finish	30SEP08	Progress Bar
Data Date	19JAN98	Critical Activity
Run Date	04FEB98	

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 1 Milestones (FY98)

FERNALD
Environmental Management Project

1259

23

Level 1 Milestones

FY 1999 - FY 2006

12596

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D02M01001	PLANT 3 IMPLEMENTATION PLAN TO EPA	0	18NOV98	18NOV98			1
3D06M01001	PLANT 6 COMPLEX IMPLEMENTATION PLAN TO EPA	0	02APR99	02APR99			1
3D12M01001	EAST WAREHOUSE IMPLEMENTATION PLAN TO EPA	0	16JUL99	16JUL99			1
3D03M01001	PLANT 2 COMPLEX IMPLEMENTATION PLAN TO EPA	0	30JUL99	30JUL99			1
3D11M01001	PLANT 8 COMPLEX IMPLEMENTATION PLAN TO EPA	0	15SEP99	15SEP99			1
3D19M01001	PLANT 1 PHASE II IMPLEMENTATION PLAN TO EPA	0	29SEP99	29SEP99			1
3D20M01001	GENERAL SUMP COMP. IMPLEMENTATION PLN TO EPA	0	15DEC99	15DEC99			1
3D04M01001	PILOT PLANT COMPLEX IMPLEMENTATION PLN TO EPA	0	13JAN00	13JAN00			1
3D21M01001	LIQUID STOR COMPLEX IMPLEMENTATION PLN TO EPA	0	30SEP00	30SEP00			1
3D10M01001	ADMIN. COMPLEX IMPLEMENTATION PLN TO EPA	0	12DEC00	12DEC00			1
3D16M01001	ELECTRICAL COMPLEX IMPLEMENTATION PLN TO EPA	0	31MAR01	31MAR01			1
3D14M01001	LABORATORY COMPLEX IMPLEMENTATION PLN TO EPA	0	28APR01	28APR01			1
3DOU4M1001	OU4 COMPLEX IMPLEMENTATION PLAN TO EPA	0	15JAN03*	15JAN03*			1
3D0U1M1001	OU1 COMPLEX IMPLEMENTATION PLAN TO EPA	0	11FEB04	11FEB04			1
Soils and Water							
5CCRA5M002	Submit Draft to USEPA-Area 3 & LSP Imp Plan (CA)	0			31MAR00	31MAR00	1
5CCSD1M030	AREA 3 AND LSP: PREFINAL DESIGN PKG TO EPA-L1	0			31MAR00	31MAR00	1
5CCRAX4M01	Area 4/5: Submit Draft RA WP to EPA	0			15NOV00*	15NOV00*	1
5CCSDX4M01	Area 4/5: Submit Prefinal Design Pkg to EPA (L1)	0			15NOV00*	15NOV00*	1
5CCRAX6M01	Area 6,7,1-III,2-II-2,SWL: Submit Drft IP to EPA	0			15JAN01*	15JAN01*	1
5CCSDX6M01	Area 6,7,1-III,2-II-2,SWL:Submit Pre Dsgn to EPA	0			15JAN01*	15JAN01*	1
5AB19X5091	Submit Site Wide Residual RA Work Plan to EPA	0	28MAY02	28MAY02			1
5AB19X5093	Submit Draft Final SiteWide Residual RAWP to EPA	0	26AUG02	26AUG02			1

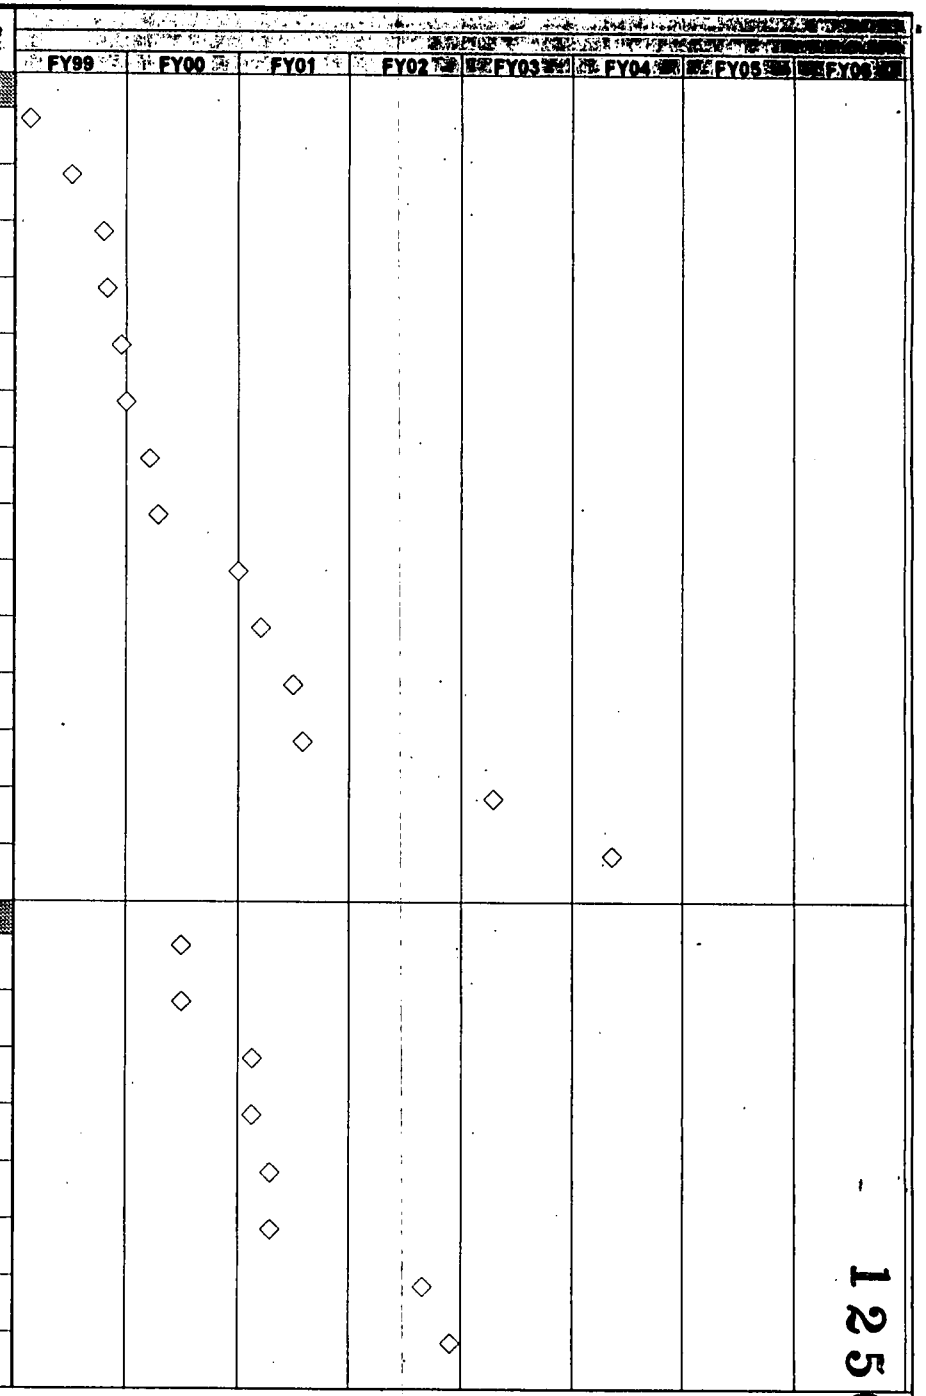

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 1 Milestones (FY99 - 06)

Sheet 1 of 2

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level	FY99	FY00	FY01	FY02	FY03	FY04	FY05	FY06
Waste Management and Silos															
4A2N0019	SUBMIT DRAFT FS/PP TO EPA	0	01FEB00*	01FEB00*			1		◇						
4A2N0059	SUBMIT ROD AMENDMENT TO EPA	0	29DEC00*	29DEC00*			1			◇					

26

Project Start	01JAN95	Current Bar
Project Finish	30SEP08	Progress Bar
Data Date	19JAN98	Critical Activity
Run Date	04FEB98	

© Primavera Systems, Inc.

C00F

Sheet 2 of 2

Integrated Site Master Schedule

Status Through 01/18/98

Level 1 Milestones (FY99 - 06)

FERNALD Environmental Management Project

Level 0/1/2 Milestones

FY 1998

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3R15NBRM10	CONST COMPL - NEBRASKA BOILER OPERABLE ON OIL	100			24NOV97A	01DEC97	2
3D08C01M01	BP/WP D&D NOTICE TO PROCEED	0	19JAN98*	10MAR97*			2
3D09M01001	MAINT/TANK FARM D&D IMPLEMENTATION PLAN TO EPA	0	04MAR98*	04MAR98*			1
3SPCM01200	PLANT 8 SAFE SHUTDOWN ACTIVITIES COMPLETE	0			30MAR98	24JUL98	2
3D17M01001	STP IMPLEMENTATION PLAN TO EPA	0	02APR98*	02APR98			1
3WNES012	SUBMIT NESHAP ANNUAL REPORT	0			30JUN98*	30JUN98*	2
3D17C01M01	STP D&D NOTICE TO PROCEED	0	01JUL98*	01JUL98*			2
3D09C01M01	MX/TF & NEW WATER STORAGE NOTICE TO PROCEED	0	15JUL98*	15JUL98*			2
3D17001000	FROM OU5: EXISTING STP OPS COMPL.	0	15JUL98	29DEC97*			2
3D05M01001	PLANT 5 IMPLEMENTATION PLAN TO EPA	0	18JUL98	18JUL98			1
3D08E02M15	BP/WP D&D - CONSTRUCTION FIELD COMPLETION	0			26SEP98*	26SEP98*	2
Soils and Water							
5AFCW2M101	Submit NPDES DMR for 9/97 to Ohio EPA	100			14OCT97A	15OCT97*	2
5CD51598	SWU: SUBMIT PREFNL/90% DSGN PKG TO EPA(CA)	100			23OCT97A	20OCT97	1
5CF63512	SWU IMPLEMNT PLAN: SUBMIT DRAFT PKG TO EPA(CA)	100			23OCT97A	20OCT97	1
5AFCW2M102	Submit NPDES DMR for 10/97 to Ohio EPA	100			14NOV97A	15NOV97*	2
5C2D51595	Area 1-II:Submit 90%/Prefnl Dsgn Pkg to EPA (CA)	100			21NOV97A	21NOV97	1
5C2F63502	AREA I-II RA WP: SUBMIT DRAFT PKG TO EPA(CA)	100			21NOV97A	21NOV97	1
5AARD1M003	OU5 ROD MS-Discharge 20 PPB Limit (JAN 1 98)	100			01DEC97A	31DEC97	2
2AD42478	Complete Construction of Roads(EA)	100			05DEC97A	27MAR98*	2
5AFCW2M103	Submit NPDES DMR for 11/97 to Ohio EPA	100			12DEC97A	15DEC97*	2
5CD515M02	SWU: SUBMIT FINAL/CFC DSGN PKG TO EPA(CA)	100			17DEC97A		1

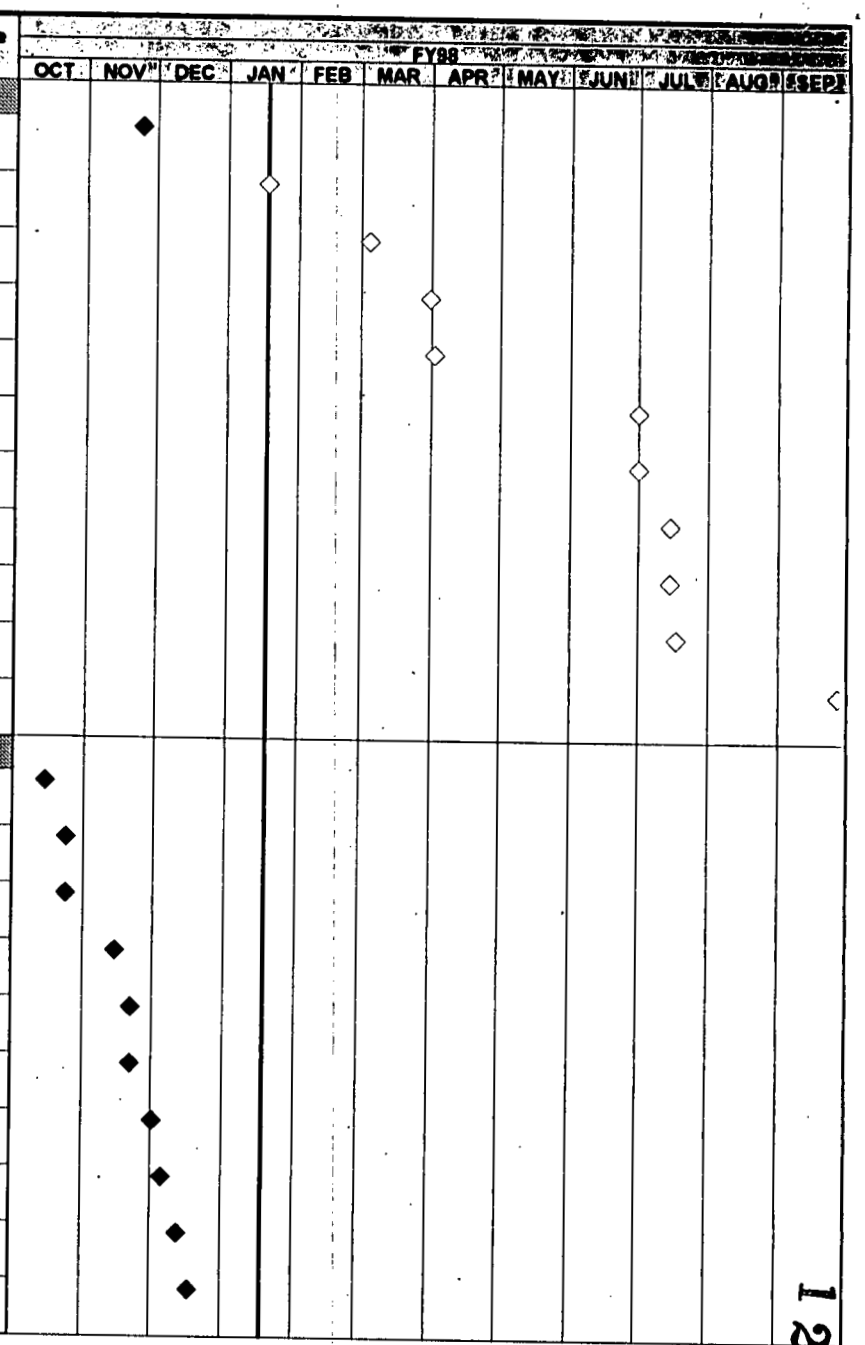

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY98)

FERNALD Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Soils and Water							
5AFCW2M104	Submit NPDES DMR for 12/97 to Ohio EPA	100			15JAN98A	15JAN98*	2
5AFEM5M001	Submit GW Remed Footprint Rpt to DOE-FN	100			16JAN98A	19JAN98	2
5AFCW2M105	Submit NPDES DMR for 1/98 to Ohio EPA	0			15FEB98*	15FEB98*	2
5CF63513	SWU : SBMT FNL IMPLEMNT PLN/DESGN PKG TO EPA(CA)	0			25FEB98	13FEB98	1
5AFEM5M002	GW Remed Footprint Report to EPA (CA)	0			05MAR98	05MAR98	2
5AFCW2M106	Submit NPDES DMR for 2/98 to Ohio EPA	0			15MAR98*	15MAR98*	2
5AFCW2M107	Submit NPDES DMR for 3/98 to Ohio EPA	0			15APR98*	15APR98*	2
5CCRA1M012	Submit Draft Final SEP to USEPA	0	20APR98	10OCT97			1
5CCRA4M006	Submit Draft Final to USEPA-SEP Support Plans(L1	0	20APR98	08OCT97			1
5C2F63503	AREA I-II: SBMT FNL RA WORK PLN PKG TO EPA	0			21APR98	21APR98	1
1C1DEC1779	TRANSPORTATION AND DISPOSAL PLAN (EA MILESTONE)	0			27APR98*	27APR98*	2
5BCTP4M001	AWWT Expansion - Commence Operations (CA)	0	30APR98*	30APR98*			2
5AFCW2M108	Submit NPDES DMR for 4/98 to Ohio EPA	0			15MAY98*	15MAY98*	2
5ACSF4M003	SFES Phase I - Commence Operations (CA)	0	16MAY98	30SEP98*			2
5CCRA1M009	USEPA Conditional Approval-SEP(L2)	0			27MAY98	03DEC97	2
5CCRA4M004	USEPA Conditional Approval-SEP Support Plans(L2)	0			27MAY98	01DEC97	2
EM7ECE1010	SUBMIT 1997 ANNUAL SITE ENVIRON REPORT TO DOE-FN	0			01JUN98*	01JUN98*	2
5AFCW2M109	Submit NPDES DMR for 5/98 to Ohio EPA	0			15JUN98*	15JUN98*	2
5BBWP3M001	START UP PUMPING FROM SOUTH FIELD WELL FIELD	0			19JUN98	21JUL98	2
5AFCW2M110	Submit NPDES DMR for 6/98 to Ohio EPA	0			15JUL98*	15JUL98*	2
5AFCW2M111	Submit NPDES DMR for 7/98 to Ohio EPA	0			15AUG98*	15AUG98*	2
5ACGW6M009	South Plume Opt - Commence Operations (CA)	0	01SEP98*	01SEP98*			2

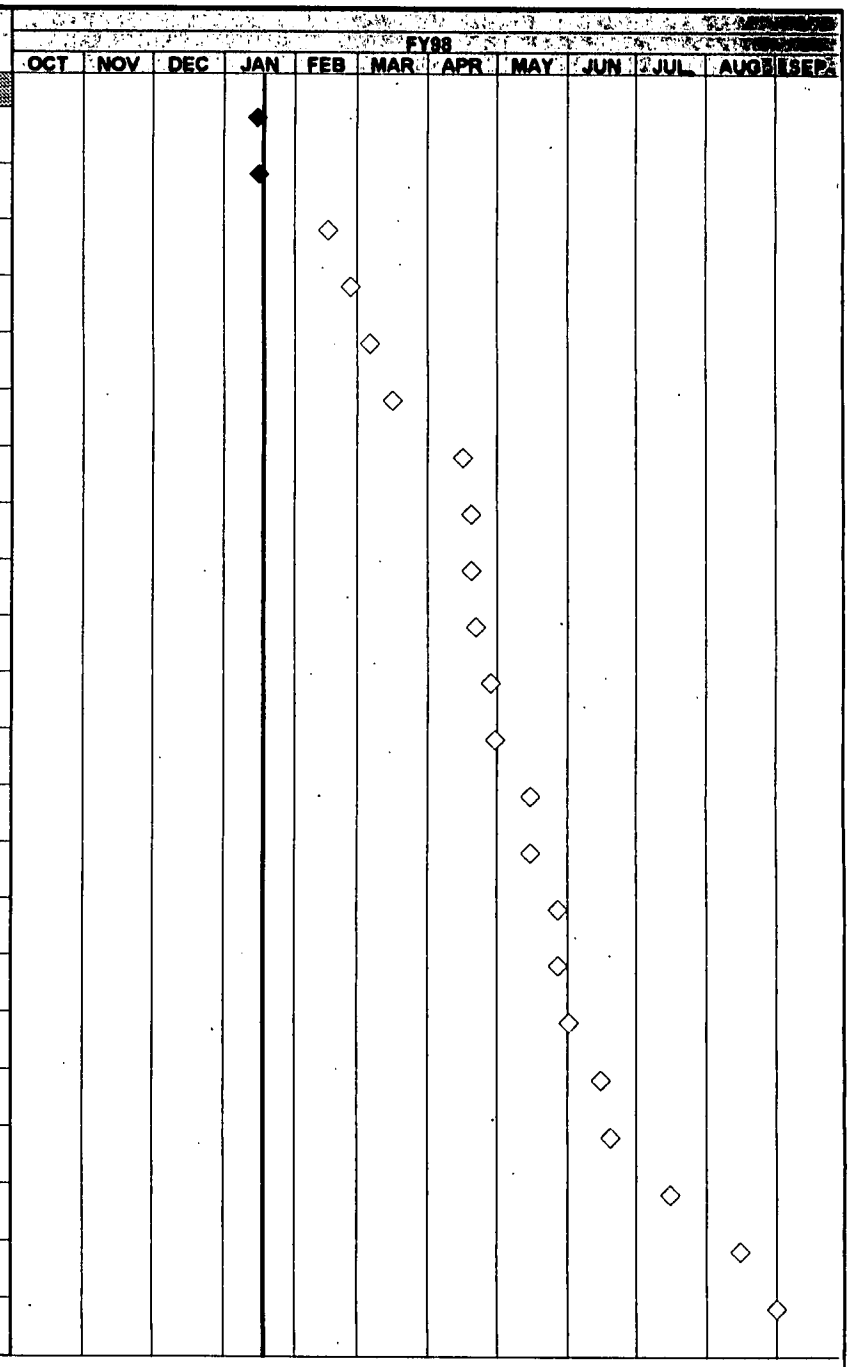

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule
Status Through 01/18/98
Level 0/1/2 Milestones (FY98)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Soils and Water							
5AFCW2M112	Submit NPDES DMR for 8/98 to Ohio EPA	0			15SEP98*	15SEP98*	2
Waste Management and Silos							
4A2H0528	AWARD MULTI-TECH PROOF OF PRINCIPLE CONTRACT	0			25JUN98	10AUG98	1
W8ADDM900	Chemical Stabilization Treatment Complete	0			23SEP98	22JUN98	1
Support and Oversight							
9AENCF9831	Monthly CA Progress Report (FDF to DOE)	100			10OCT97A	14OCT97*	2
9AENCF9858	Quarterly CA Progress Report (FDF to DOE)	100			10OCT97A	14OCT97*	2
9AENCF9832	Monthly CA Progress Report (DOE to EPA)	100			16OCT97A	21OCT97*	2
9AENCF9859	Quarterly CA Progress Report (DOE to EPA)	100			16OCT97A	21OCT97*	2
9AENCF9833	Monthly CA Progress Report (FDF to DOE)	100			12NOV97A	17NOV97*	2
9AENCF9834	Monthly CA Progress Report (DOE to EPA)	100			18NOV97A	24NOV97*	2
9A00009815	Conduct FY 1997 Year End Review	100			19NOV97A	31DEC97*	2
9AENCF9835	Monthly CA Progress Report (FDF to DOE)	100			11DEC97A	12DEC97*	2
9AENAF9717	Per.Audit: U.S.EPA Reg.5, Copy of FEMP Ad.(#1)	100			12DEC97A	30DEC97*	2
9AENCF9836	Monthly CA Progress Report (DOE to EPA)	100			16DEC97A	19DEC97*	2
9AENCF9837	Monthly CA Progress Report (FDF to DOE)	100			13JAN98A	15JAN98*	2
9AENCF9860	Quarterly CA Progress Report (FDF to DOE)	100			13JAN98A	15JAN98*	2
9AENCF9838	Monthly CA Progress Report (DOE to EPA)	100			16JAN98A	22JAN98*	2
9AENCF9861	Quarterly CA Progress Report (DOE to EPA)	100			16JAN98A	22JAN98*	2
9A00009808	Complete Affirm Action Plan-Females & Minoritie	0			02FEB98*	02FEB98*	2
9AENCF9839	Monthly CA Progress Report (FDF to DOE)	0			13FEB98*	13FEB98*	2
9AENCF9840	Monthly CA Progress Report (DOE to EPA)	0			23FEB98*	23FEB98*	2
9AECAM017	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR98*	01MAR98*	2

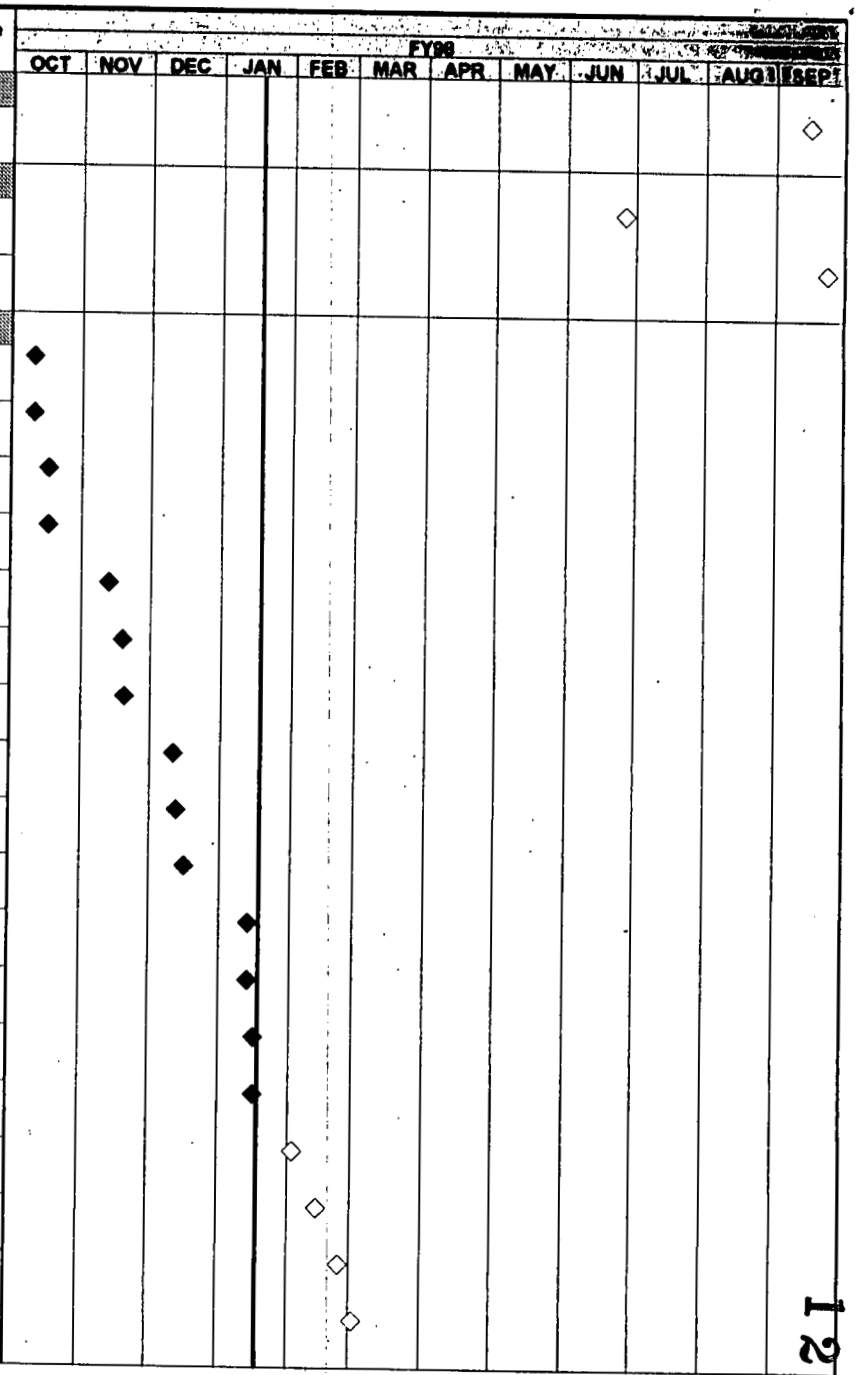

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY98)

FERNALD
Environmental Management Project

1256

20

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF9841	Monthly CA Progress Report (FDF to DOE)	0			13MAR98*	13MAR98*	2
9AENCF9842	Monthly CA Progress Report (DOE to EPA)	0			20MAR98*	20MAR98*	2
9A00009820	Complete Annual Acct. of Salaried Savings Plans	0			25MAR98*	25MAR98*	2
9AENCF9843	Monthly CA Progress Report (FDF to DOE)	0			15APR98*	15APR98*	2
9AENCF9862	Quarterly CA Progress Report (FDF to DOE)	0			15APR98*	15APR98*	2
9AENCF9844	Monthly CA Progress Report (DOE to EPA)	0			22APR98*	22APR98*	2
9AENCF9863	Quarterly CA Progress Report (DOE to EPA)	0			22APR98*	22APR98*	2
9AENCF9845	Monthly CA Progress Report (FDF to DOE)	0			14MAY98*	14MAY98*	2
9AENCF9846	Monthly CA Progress Report (DOE to EPA)	0			21MAY98*	21MAY98*	2
9A00009816	Complete Congressional Budget Submittal	0			29MAY98*	29MAY98*	2
9AENCF9847	Monthly CA Progress Report (FDF to DOE)	0			12JUN98*	12JUN98*	2
9AENCF9848	Monthly CA Progress Report (DOE to EPA)	0			19JUN98*	19JUN98*	2
9A00009813	Complete Mid-Year Review	0			30JUN98*	30JUN98*	2
9AECAM018	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL98*	02JUL98*	2
9AENCF9849	Monthly CA Progress Report (FDF to DOE)	0			15JUL98*	15JUL98*	2
9AENCF9864	Quarterly CA Progress Report (FDF to DOE)	0			15JUL98*	15JUL98*	2
9AENCF9850	Monthly CA Progress Report (DOE to EPA)	0			22JUL98*	22JUL98*	2
9AENCF9865	Quarterly CA Progress Report (DOE to EPA)	0			22JUL98*	22JUL98*	2
9A00009809	Complete Historically Black College & Univ. Pla	0			31JUL98*	31JUL98*	2
9AENCF9851	Monthly CA Progress Report (FDF to DOE)	0			14AUG98*	14AUG98*	2
9AENCF9852	Monthly CA Progress Report (DOE to EPA)	0			21AUG98*	21AUG98*	2
9A00009811	Complete Affirm Action Plan-Veterans&Handicappe	0			31AUG98*	31AUG98*	2

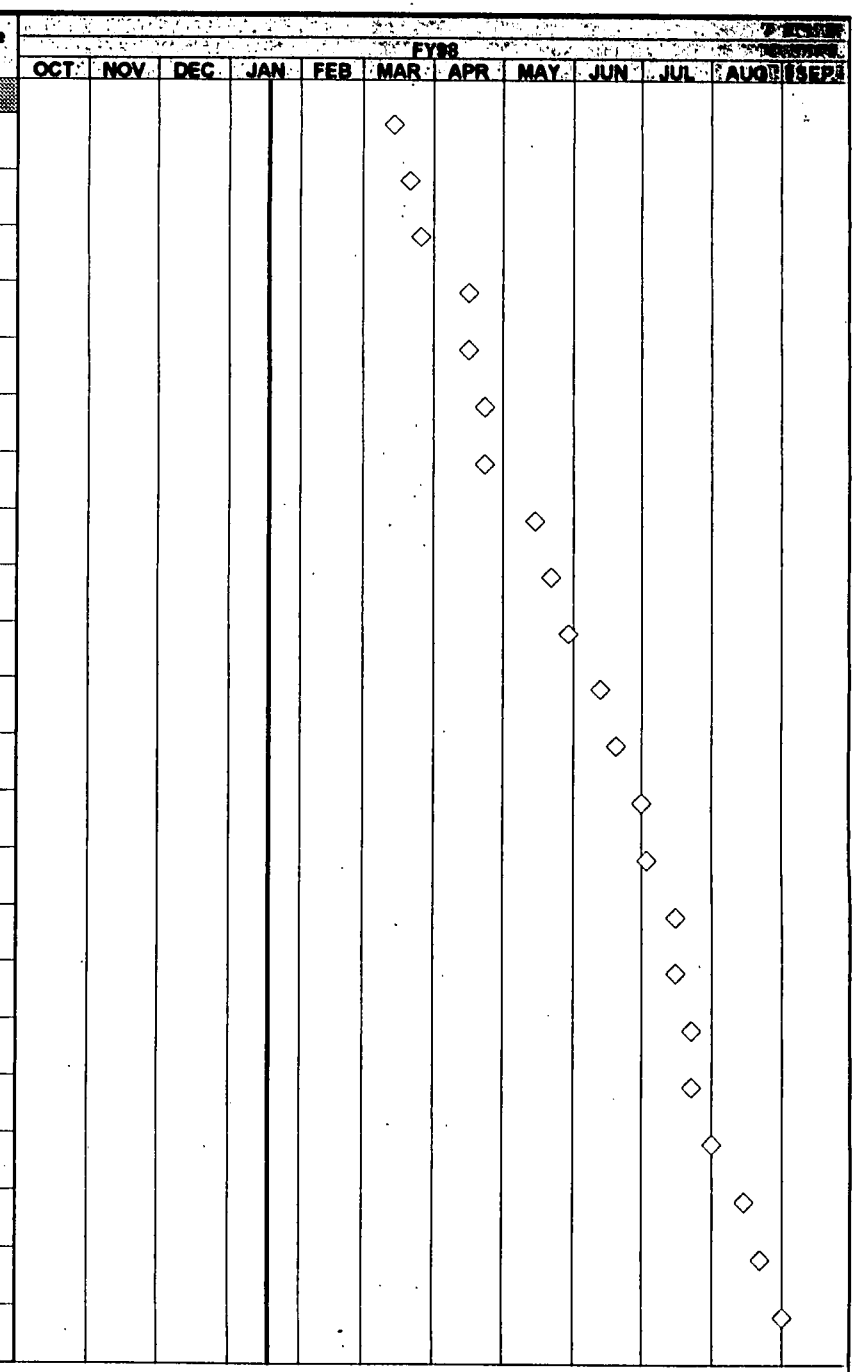

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY98)

FERNALD
Environmental Management Project

31

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF9853	Monthly CA Progress Report (FDF to DOE)	0			15SEP98*	15SEP98*	2
9AENCF9854	Monthly CA Progress Report (DOE to EPA)	0			22SEP98*	22SEP98*	2

FY98: OCT NOV DEC JAN FEB MAR APR MAY JUN JUL AUG SEP

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

© Primavera Systems, Inc.

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule
Status Through 01/18/98
Level 0/1/2 Milestones (FY98)

FERNALD
Environmental Management Project

Level 0/1/2 Milestones

FY 1999 - FY 2006

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D17E02M15	TO OU5: STP D&D - CONSTRUCTION FIELD	0			14OCT98	30SEP98	2
3D05E01M05	PLANT 5 D&D NOTICE TO PROCEED	0	16OCT98	16OCT98			2
3D02M01001	PLANT 3 IMPLEMENTATION PLAN TO EPA	0	18NOV98	18NOV98			1
3D08E03M25	BP/WP D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			23NOV98	23NOV98	2
3D17E03M25	STP D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			14DEC98	29NOV98	2
3D07PL9M02	TO OU5: TH/PLANT 9 D&D - CONSTRUCTION FIELD COMP	0			31DEC98	25MAR99	2
3D19000M05	FROM 68D1 CHEM WHSE SHUTDOWN/RELOCATED	0	04JAN99*	04JAN99*			2
3D02C01M01	PLANT 3 D&D NOTICE TO PROCEED	0	01APR99	01APR99			2
3D06M01001	PLANT 6 COMPLEX IMPLEMENTATION PLAN TO	0	02APR99	02APR99			1
3D07E03M25	TH/PLANT 9 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			24MAY99	24MAY99	2
3WNES022	SUBMIT NESHAP ANNUAL REPORT	0			30JUN99*	30JUN99*	2
3D06C01M01	PLANT 6 D&D NOTICE TO PROCEED	0	01JUL99	01JUL99			2
3D12M01001	EAST WAREHOUSE IMPLEMENTATION PLAN TO	0	16JUL99	16JUL99			1
3D03M01001	PLANT 2 COMPLEX IMPLEMENTATION PLAN TO	0	30JUL99	30JUL99			1
3D11M01001	PLANT 8 COMPLEX IMPLEMENTATION PLAN TO	0	15SEP99	15SEP99			1
3D19M01001	PLANT 1 PHASE II IMPLEMENTATION PLAN TO	0	29SEP99	29SEP99			1
3D12C01M01	EAST WAREHOUSE D&D NOTICE TO PROCEED	0	14OCT99	14OCT99			2
3D03C01M01	PLANT 2 D&D NOTICE TO PROCEED	0	28OCT99	28OCT99			2
3SPCM01100	PLANT 6 SAFE SHUTDOWN ACTIVITIES COMPLETE	0			12NOV99	14DEC98*	2
3SCOMPSS	SAFE SHUTDOWN R.A. 12 COMPLETED	0			02DEC99	11FEB99*	2
3D11C01M01	PLANT 8 D&D NOTICE TO PROCEED	0	14DEC99	14DEC99			2
3D20M01001	GENERAL SUMP COMP. IMPLEMENTATION PLN TO	0	15DEC99	15DEC99			1

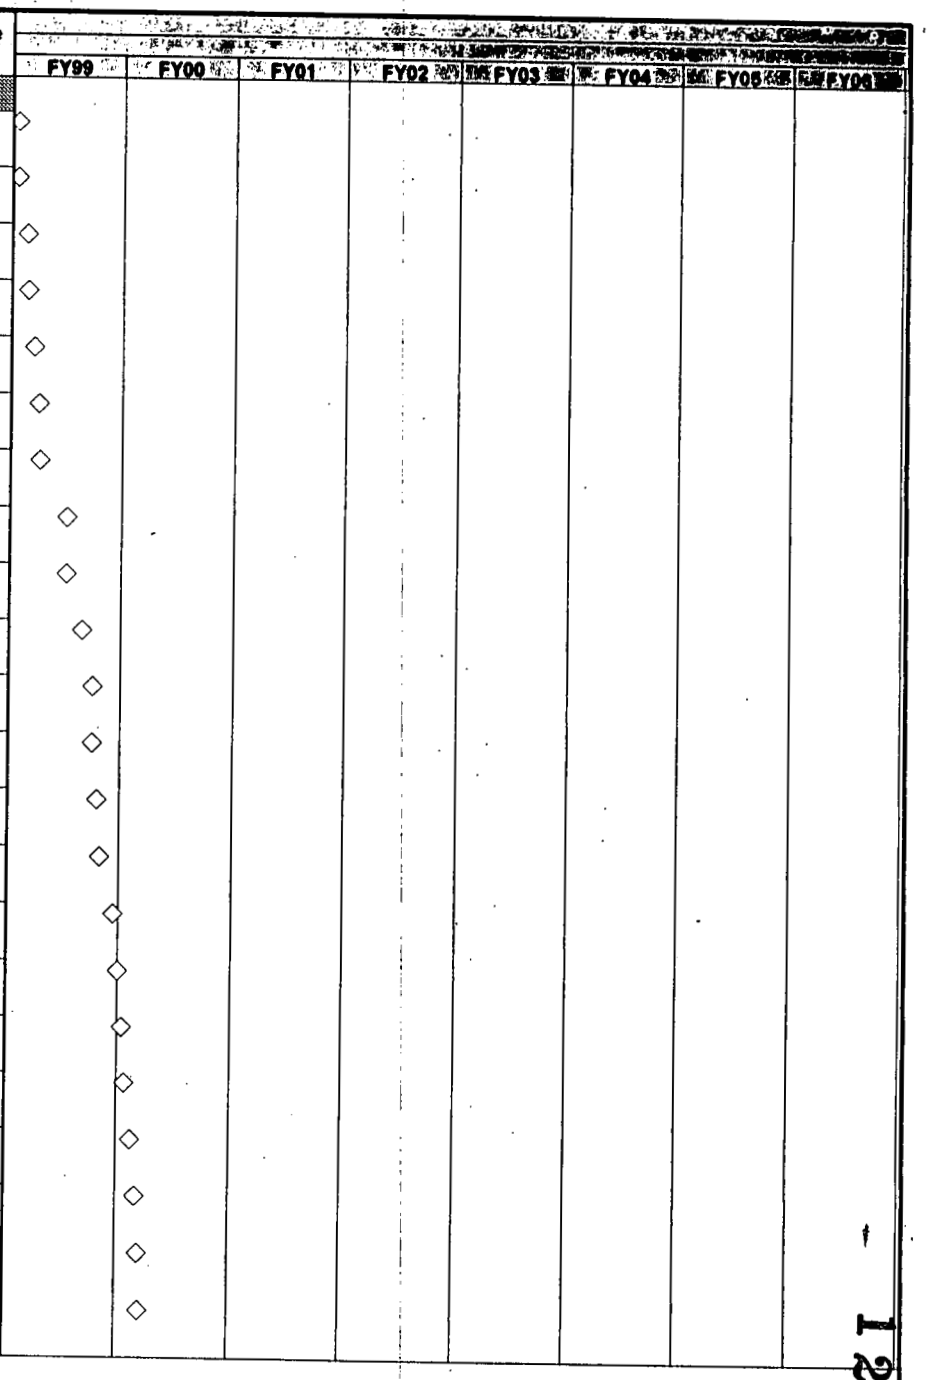

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D09E02M15	MAINT/TANK FARM D&D - CONSTR FIELD COMPLETION	0			27DEC99	27DEC99	2
3D04M01001	PILOT PLANT COMPLEX IMPLEMENTATION PLN TO	0	13JAN00	13JAN00			1
3D09E03M25	MAINT/TANK FARM D&D - DRAFT CLOSEOUT REP TO	0			25FEB00	25FEB00	2
3D19C01M01	PLANT 1 PHASE II D&D NOTICE TO PROCEED	0	01APR00	01APR00			2
3D04C01M01	PILOT PLANT D&D NOTICE TO PROCEED	0	29APR00	29APR00			2
3D12E02M15	EAST WHSE D&D - CONSTRUCTION FIELD	0			22MAY00	22MAY00	2
3WNES032	SUBMIT NESHAP ANNUAL REPORT	0			30JUN00*	30JUN00*	2
3D12E03M25	EAST WHSE D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			19JUL00	19JUL00	2
3D21M01001	LIQUID STOR COMPLEX IMPLEMENTATION PLN TO	0	30SEP00	30SEP00			1
3D10M01001	ADMIN. COMPLEX IMPLEMENTATION PLN TO	0	12DEC00	12DEC00			1
3D02E02M15	PLANT 3 D&D - CONSTRUCTION FIELD	0			01MAR01	01MAR01	2
3D05C01M10	PLANT 5 D&D - CONSTRUCTION FIELD	0	28MAR01	28MAR01			2
3D16M01001	ELECTRICAL COMPLEX IMPLEMENTATION PLN TO	0	31MAR01	31MAR01			1
3D19000301	TO OU5: PLANT 1 PHASE II D&D - CONSTR FIELD COMP	0	02APR01	02APR01			2
3D14M01001	LABORATORY COMPLEX IMPLEMENTATION PLN TO	0	28APR01	28APR01			1
3D19E03M25	PLANT 1 PHASE II D&D - DRAFT CLOSE REP TO EPAS	0			25MAY01	25MAY01	2
3D02E03M25	PLANT 3 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			31MAY01	31MAY01	2
3D05C01M12	PLANT 5 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			28JUN01	28JUN01	2
3WNES042	SUBMIT NESHAP ANNUAL REPORT	0			28JUN01*	28JUN01*	2
3D06M00100	TO OU5: PLANT 6 D&D - CONSTRUCTION FIELD	0			29JUN01	29JUN01	2
3D06E03M25	PLANT 6 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			28AUG01	28AUG01	2
3D20001000	FROM OU5: GENERAL SUMP OPS COMPLETE	0	01OCT01*	01OCT01*			2

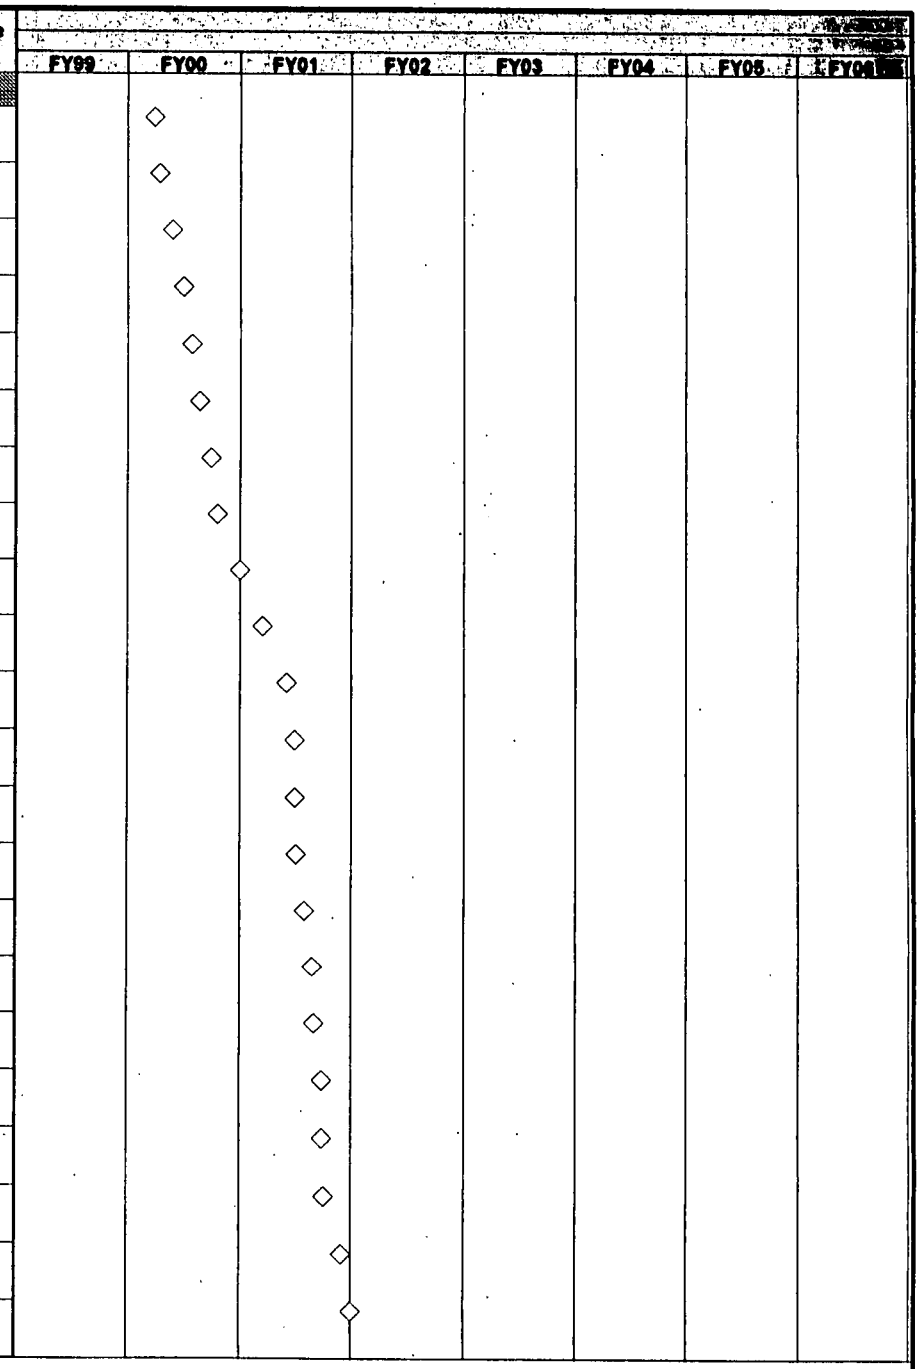

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

35

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D11E02M15	PLANT 8 D&D - CONSTRUCTION FIELD	0			12OCT01	12OCT01	2
3SCOMPFS	FACILITIES SHUTDOWN COMPLETED	0			23OCT01	27AUG01	2
3D11E03M25	PLANT 8 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			14DEC01	14DEC01	2
3D20C01M01	GENERAL SUMP D&D NOTICE TO PROCEED	0	05JAN02*	05JAN02*			2
3D21C01M01	LIQUID STORAGE D&D NOTICE TO PROCEED	0	02APR02	02APR02			2
3D10C01M01	ADMIN D&D NOTICE TO PROCEED	0	09MAY02	09MAY02			2
3D14C01M01	CHEMICAL LAB D&D NOTICE TO PROCEED	0	09MAY02	09MAY02			2
3D04000301	TO OU5: PILOT PLANT D&D - CONSTR FIELD COMPLETIO	0			17MAY02	17MAY02	2
3D03E02M15	PLANT 2 D&D - CONSTRUCTION FIELD	0			06JUN02	06JUN02	2
3WNES052	SUBMIT NESHAP ANNUAL REPORT	0			28JUN02*	28JUN02*	2
3D04E03M25	PILOT PLANT D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			16JUL02	16JUL02	2
3D03E03M25	PLANT 2 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			05AUG02	05AUG02	2
3D21E02M15	LIQUID STG D&D - CONSTRUCTION FIELD	0			26SEP02	26SEP02	2
3D21E03M25	LIQUID STG D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			25NOV02	25NOV02	2
3DOU4M1001	OU4 COMPLEX IMPLEMENTATION PLAN TO	0	15JAN03*	15JAN03*			1
3D20002000	TO OU5: GENERAL SUMP D&D - CONSTR FIELD COMPLETI	0			03APR03	03APR03	2
3D14E02M15	LAB D&D - CONSTRUCTION FIELD COMPLETION	0			07MAY03	07MAY03	2
3D20E03M25	GENERAL SUMP D&D - DRAFT CLOSEOUT REPORT TO EPA	0			05JUN03	05JUN03	2
3WNES062	SUBMIT NESHAP ANNUAL REPORT	0			30JUN03*	30JUN03*	2
3D14E03M25	LAB D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			07JUL03	07JUL03	2
3D10M00100	TO OU5: ADMIN D&D - CONSTRUCTION FIELD	0			06FEB04	06FEB04	2
3D0U1M1001	OU1 COMPLEX IMPLEMENTATION PLAN TO	0	11FEB04	11FEB04			1

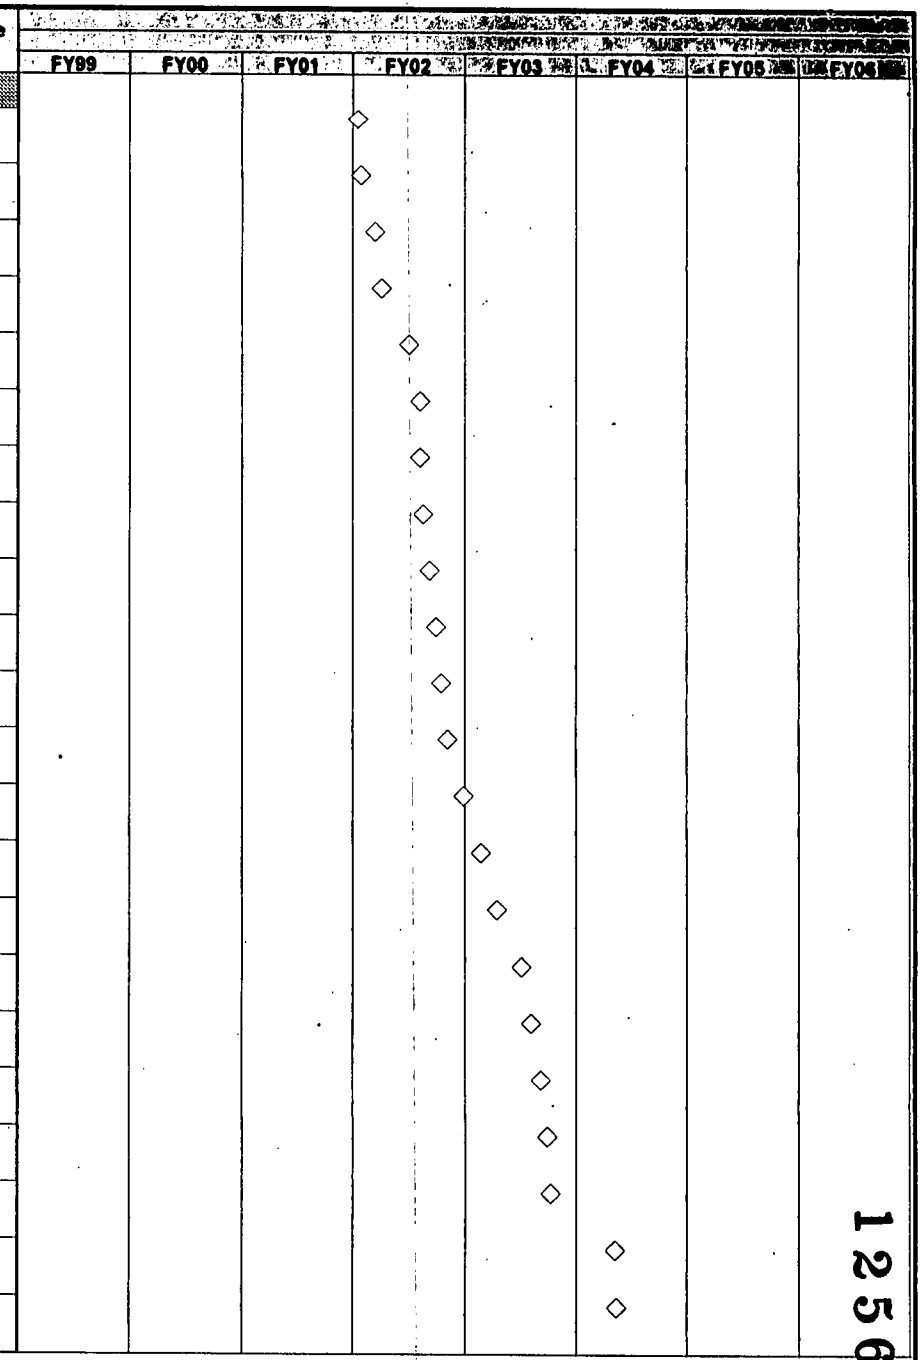

1256

Project Start	01JAN95	Current Bar
Project Finish	30SEP08	Progress Bar
Data Date	19JAN98	Critical Activity
Run Date	04FEB98	

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3D10E03M25	ADMIN D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			06APR04	06APR04	2
3DF0010020	OU1 COMPLEX D&D NOTICE TO PROCEED	0	11MAY04*	11MAY04*			2
3D39M00300	FROM OU4: HI NITRATE TANKS OPERATIONS COMPLETE	0	23JUN04*	23JUN04*			2
3WNES072	SUBMIT NESHAP ANNUAL REPORT	0			30JUN04*	30JUN04*	2
3D37M00100	FROM OU5: OU5 COMPLEX D&D NOTICE TO PROCEED	0	30SEP04	30SEP04			2
3D38M00100	FROM OU5: SPIT OPERATION COMPLETE	0	01OCT04*	01OCT04*			2
3D39M00100	FROM OU5: HI NITRATE TANKS OPERATIONS COMPLETE	0	12APR05*	12APR05*			2
3WNES082	SUBMIT NESHAP ANNUAL REPORT	0			30JUN05*	30JUN05*	2
Soils and Water							
EM7ECE1020	SUBMIT 1998 ANNUAL SITE ENVIRON REPORT TO DOE-FN	0			01JUN99*	01JUN99*	2
5CCRA5M002	Submit Draft to USEPA-Area 3 & LSP Imp Plan (CA)	0			31MAR00	31MAR00	1
5CCSD1M030	AREA 3 AND LSP: PREFINAL DESIGN PKG TO EPA-L1	0			31MAR00	31MAR00	1
5CCRAX4M01	Area 4/5: Submit Draft RA WP to EPA	0			15NOV00*	15NOV00*	1
5CCSDX4M01	Area 4/5: Submit Prefinal Design Pkg to EPA (L1)	0			15NOV00*	15NOV00*	1
5CCRAX6M01	Area 6,7,1-III,2-II-2,SWL: Submit Drft IP to EPA	0			15JAN01*	15JAN01*	1
5CCSDX6M01	Area 6,7,1-III,2-II-2,SWL:Submit Pre Dsgn to EPA	0			15JAN01*	15JAN01*	1
5AXR2M010	EPA receives Waste Stor Area Prelim Design Pkg	0	15JUN01	15JUN01			2
5AXR3M010	EPA receives Plant 6 Area Prelim Design Pkg	0	15AUG01	15AUG01			2
5AXR2M020	EPA receives Waste Stor Area Pre-Final Dsgn Pkg	0	30NOV01	30NOV01			2
5AXR3M020	EPA receives Plant 6 Area Pre-Final Design Pkg	0	30NOV01	30NOV01			2
5AB19X5090	Submit Site Wide Residual RA Work Plan to DOE	0	28JAN02*	28JAN02*			2
5AB19X5091	Submit Site Wide Residual RA Work Plan to EPA	0	28MAY02	28MAY02			1
5AB19X5092	Receive EPA Comments on Site Wide Residual RAWP	0			26JUL02	26JUL02	2

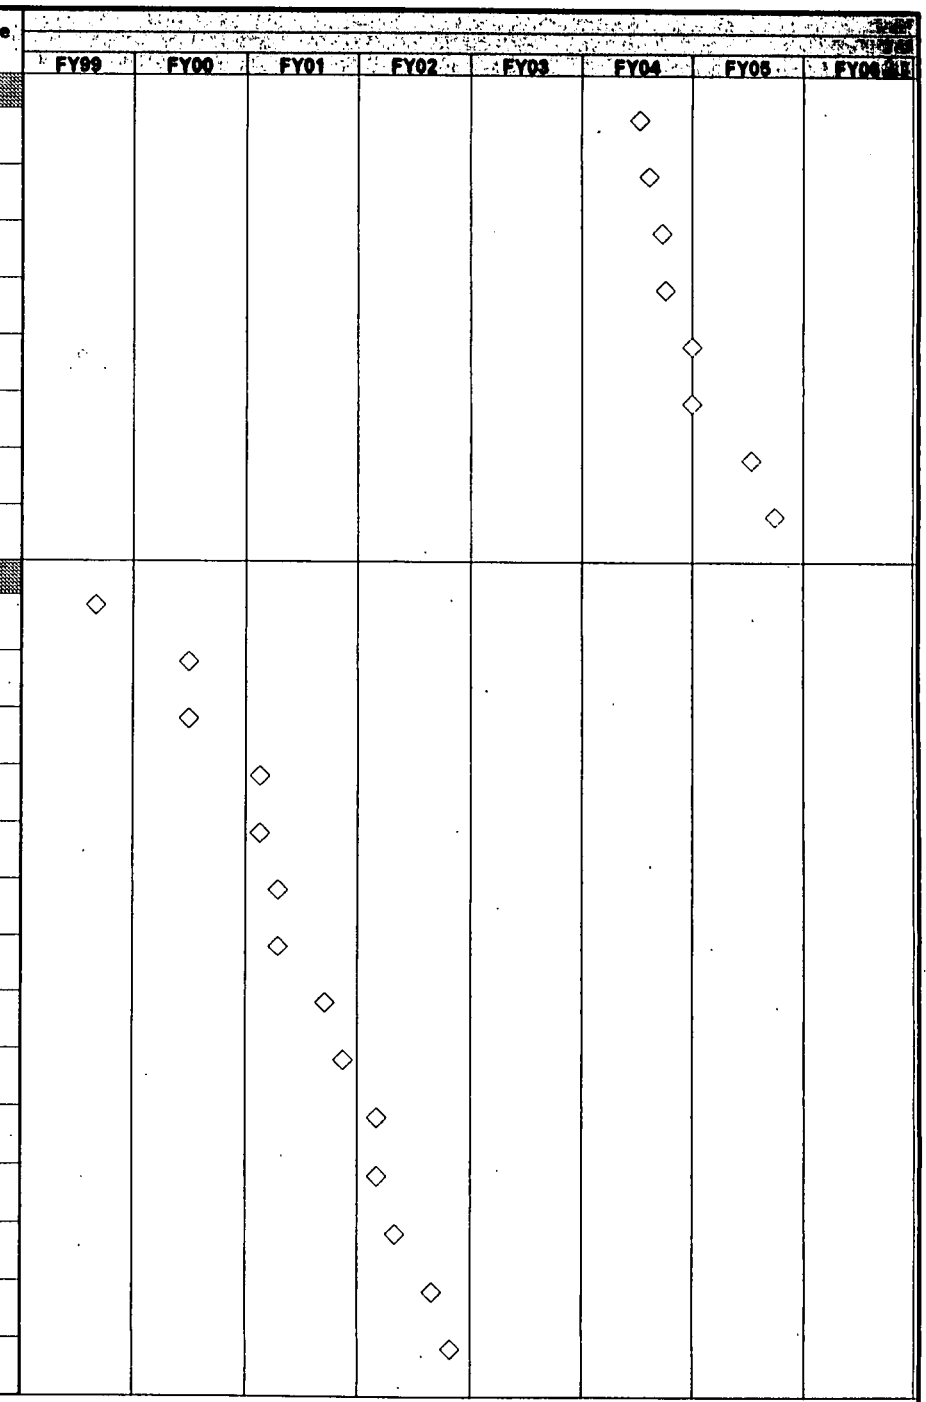

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

37

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Soils and Water							
5AB19X5093	Submit Draft Final SiteWide Residual RAWP to EPA	0	26AUG02	26AUG02			1
1CB0010318	COMPLETION OF OPERATIONS	0			31MAY05*	31MAY05*	2
Waste Management and Silos							
4A2N0019	SUBMIT DRAFT FS/PP TO EPA	0	01FEB00*	01FEB00*			1
4A2N0059	SUBMIT ROD AMENDMENT TO EPA	0	29DEC00*	29DEC00*			1
W8REGDD9C	CHEMICAL TREATMENT PROJ. - All Chem Treatmt Cmpl	0			28SEP01*	28SEP01*	2
Support and Oversight							
9AENCF9931	Monthly CA Progress Report (FDF to DOE)	0			14OCT98*	14OCT98*	2
9AENCF9958	Quarterly CA Progress Report (FDF to DOE)	0			14OCT98*	14OCT98*	2
9AENCF9932	Monthly CA Progress Report (DOE to EPA)	0			21OCT98*	21OCT98*	2
9AENCF9959	Quarterly CA Progress Report (DOE to EPA)	0			21OCT98*	21OCT98*	2
9AENCF9933	Monthly CA Progress Report (FDF to DOE)	0			16NOV98*	16NOV98*	2
9AENCF9934	Monthly CA Progress Report (DOE to EPA)	0			23NOV98*	23NOV98*	2
9AENCF9935	Monthly CA Progress Report (FDF to DOE)	0			14DEC98*	14DEC98*	2
9AENCF9936	Monthly CA Progress Report (DOE to EPA)	0			21DEC98*	21DEC98*	2
9A00009915	Conduct FY 1998 Year End Review	0			31DEC98*	31DEC98*	2
9AENCF9937	Monthly CA Progress Report (FDF to DOE)	0			15JAN99*	15JAN99*	2
9AENCF9960	Quarterly CA Progress Report (FDF to DOE)	0			15JAN99*	15JAN99*	2
9AENCF9938	Monthly CA Progress Report (DOE to EPA)	0			22JAN99*	22JAN99*	2
9AENCF9961	Quarterly CA Progress Report (DOE to EPA)	0			22JAN99*	22JAN99*	2
9A00HR9908	Complete Affirm Action Plan-Females & Minoritie	0			01FEB99*	01FEB99*	2
9AENCF9939	Monthly CA Progress Report (FDF to DOE)	0			12FEB99*	12FEB99*	2
9AENCF9940	Monthly CA Progress Report (DOE to EPA)	0			22FEB99*	22FEB99*	2

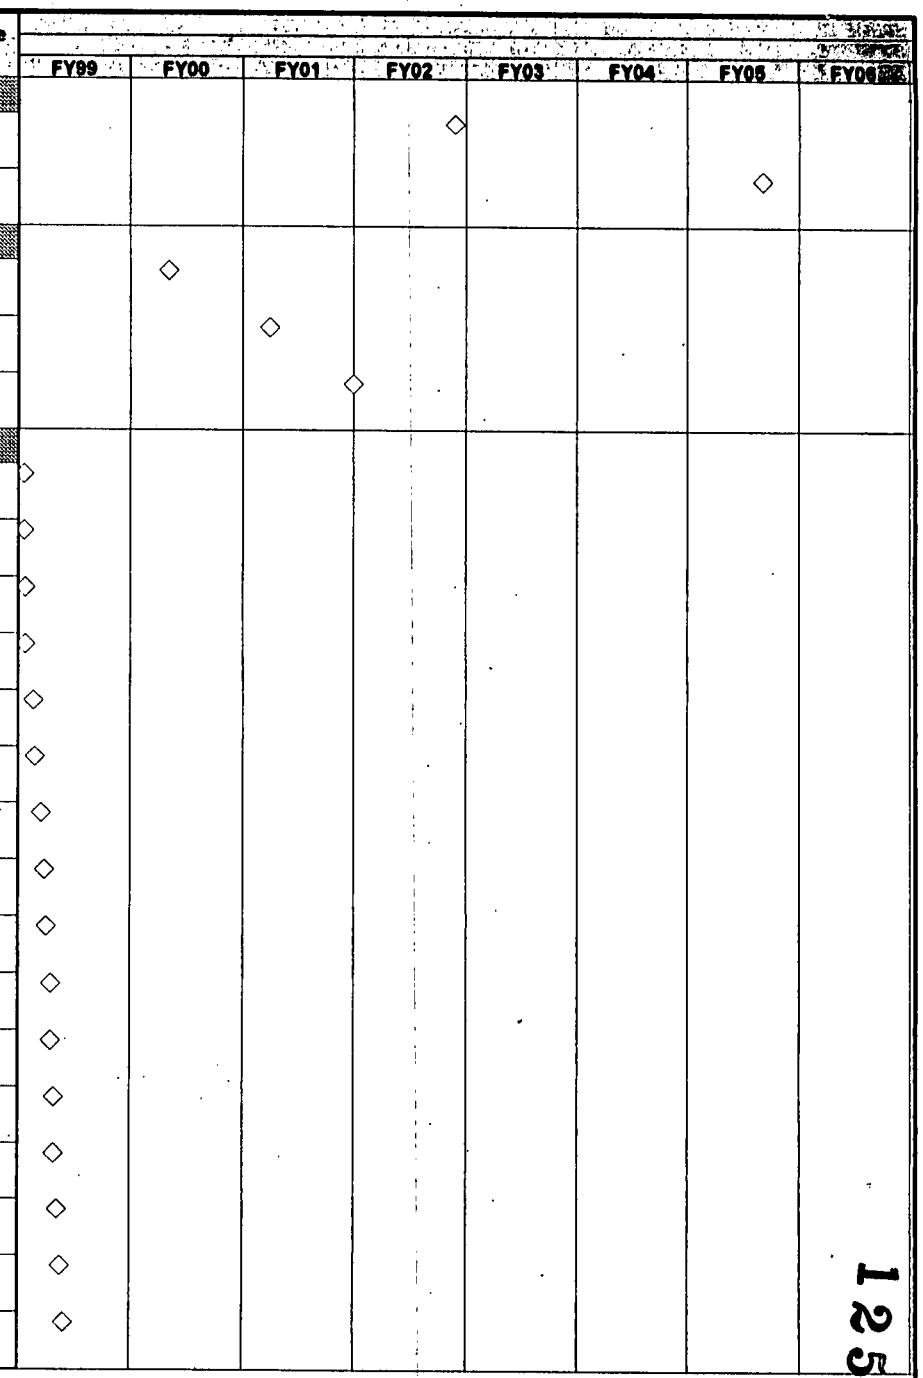

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level	FY99	FY00	FY01	FY02	FY03	FY04	FY05	FY06
Support and Oversight															
9AECAM019	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR99*	01MAR99*	2	◇							
9AENCF9941	Monthly CA Progress Report (FDF to DOE)	0			12MAR99*	12MAR99*	2	◇							
9AENCF9942	Monthly CA Progress Report (DOE to EPA)	0			19MAR99*	19MAR99*	2	◇							
9A00HR9920	Complete Annual Acct. of Salaried Savings Plans	0			25MAR99*	25MAR99*	2	◇							
9AENCF9943	Monthly CA Progress Report (FDF to DOE)	0			15APR99*	15APR99*	2	◇							
9AENCF9962	Quarterly CA Progress Report (FDF to DOE)	0			15APR99*	15APR99*	2	◇							
9AENCF9944	Monthly CA Progress Report (DOE to EPA)	0			22APR99*	22APR99*	2	◇							
9AENCF9963	Quarterly CA Progress Report (DOE to EPA)	0			22APR99*	22APR99*	2	◇							
9AENCF9945	Monthly CA Progress Report (FDF to DOE)	0			14MAY99*	14MAY99*	2	◇							
9AENCF9946	Monthly CA Progress Report (DOE to EPA)	0			21MAY99*	21MAY99*	2	◇							
9A00009916	Complete Congressional Budget Submittal	0			28MAY99*	28MAY99*	2	◇							
9AENCF9947	Monthly CA Progress Report (FDF to DOE)	0			14JUN99*	14JUN99*	2	◇							
9AENCF9948	Monthly CA Progress Report (DOE to EPA)	0			21JUN99*	21JUN99*	2	◇							
9A00009913	Complete Mid-Year Review	0			30JUN99*	30JUN99*	2	◇							
9AECAM020	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL99*	02JUL99*	2	◇							
9AENCF9949	Monthly CA Progress Report (FDF to DOE)	0			15JUL99*	15JUL99*	2	◇							
9AENCF9964	Quarterly CA Progress Report (FDF to DOE)	0			15JUL99*	15JUL99*	2	◇							
9AENCF9950	Monthly CA Progress Report (DOE to EPA)	0			22JUL99*	22JUL99*	2	◇							
9AENCF9965	Quarterly CA Progress Report (DOE to EPA)	0			22JUL99*	22JUL99*	2	◇							
9A00HR9909	Complete Historically Black College & Univ. Pla	0			02AUG99*	02AUG99*	2	◇							
9AENCF9951	Monthly CA Progress Report (FDF to DOE)	0			13AUG99*	13AUG99*	2	◇							
9AENCF9952	Monthly CA Progress Report (DOE to EPA)	0			20AUG99*	20AUG99*	2	◇							

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

34

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9A00HR9911	Complete Affirm Action Plan-Veterans&Handicappe	0			02SEP99*	02SEP99*	2
9AENCF9953	Monthly CA Progress Report (FDF to DOE)	0			15SEP99*	15SEP99*	2
9AENCF9954	Monthly CA Progress Report (DOE to EPA)	0			22SEP99*	22SEP99*	2
9AENCF0031	Monthly CA Progress Report (FDF to DOE)	0			14OCT99*	14OCT99*	2
9AENCF0058	Quarterly CA Progress Report (FDF to DOE)	0			14OCT99*	14OCT99*	2
9AENCF0032	Monthly CA Progress Report (DOE to EPA)	0			21OCT99*	21OCT99*	2
9AENCF0059	Quarterly CA Progress Report (DOE to EPA)	0			21OCT99*	21OCT99*	2
9AENCF0033	Monthly CA Progress Report (FDF to DOE)	0			15NOV99*	15NOV99*	2
9AENCF0034	Monthly CA Progress Report (DOE to EPA)	0			22NOV99*	22NOV99*	2
9AENCF0035	Monthly CA Progress Report (FDF to DOE)	0			14DEC99*	14DEC99*	2
9AENCF0036	Monthly CA Progress Report (DOE to EPA)	0			21DEC99*	21DEC99*	2
9A00000015	Conduct FY 1999 Year End Review	0			30DEC99*	30DEC99*	2
9AENCF0037	Monthly CA Progress Report (FDF to DOE)	0			14JAN00*	14JAN00*	2
9AENCF0060	Quarterly CA Progress Report (FDF to DOE)	0			14JAN00*	14JAN00*	2
9AENCF0038	Monthly CA Progress Report (DOE to EPA)	0			21JAN00*	21JAN00*	2
9AENCF0061	Quarterly CA Progress Report (DOE to EPA)	0			21JAN00*	21JAN00*	2
9A00HR0008	Complete Affirm Action Plan-Females & Minoritie	0			31JAN00*	31JAN00*	2
9AENCF0039	Monthly CA Progress Report (FDF to DOE)	0			14FEB00*	14FEB00*	2
9AENCF0040	Monthly CA Progress Report (DOE to EPA)	0			22FEB00*	22FEB00*	2
9AECAM021	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR00*	01MAR00*	2
9AENCF0041	Monthly CA Progress Report (FDF to DOE)	0			14MAR00*	14MAR00*	2
9AENCF0042	Monthly CA Progress Report (DOE to EPA)	0			21MAR00*	21MAR00*	2

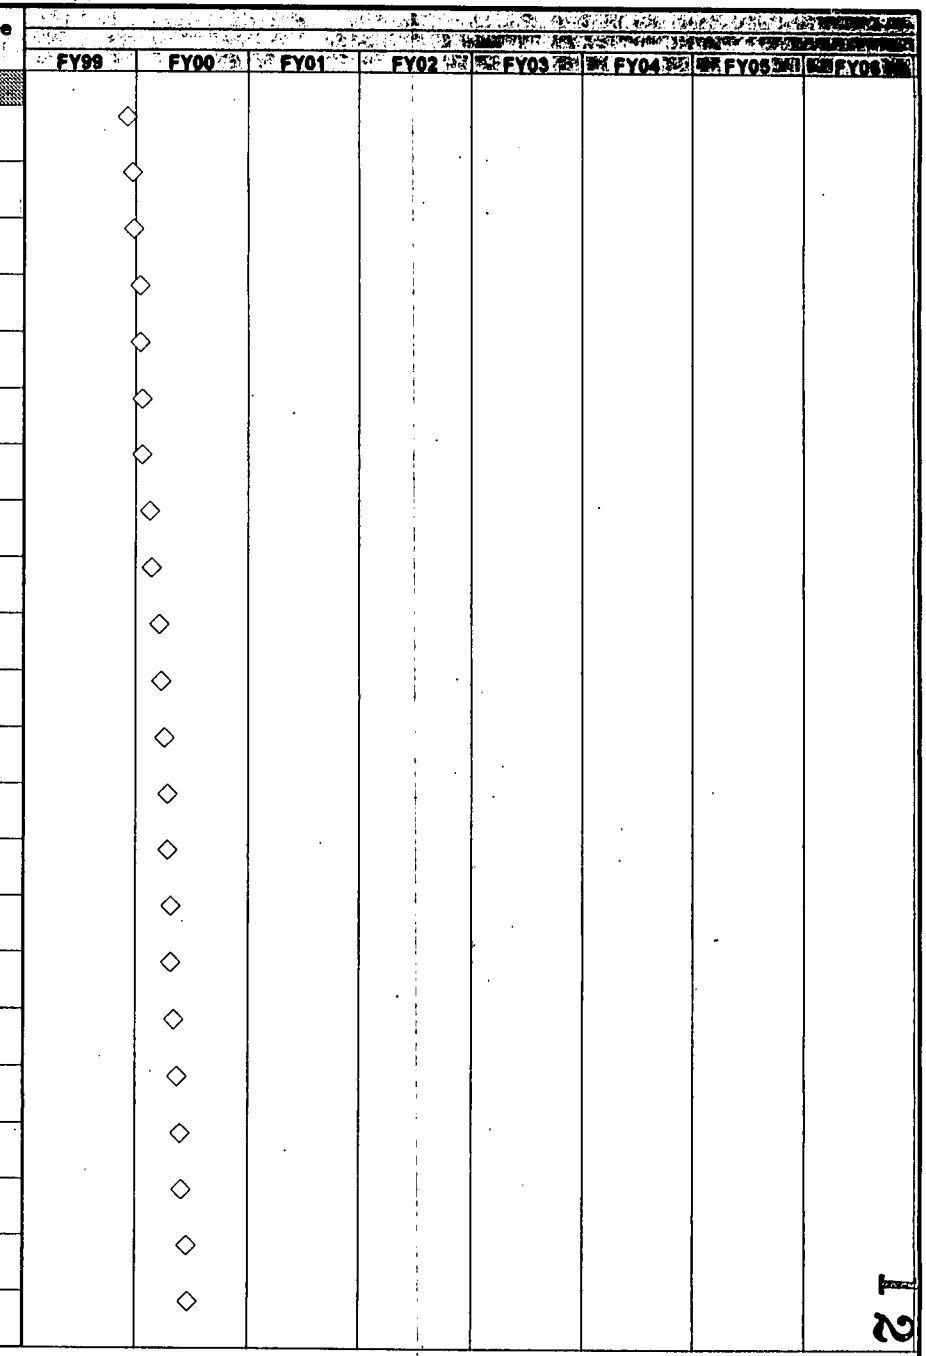

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9A00HR0020	Complete Annual Acct. of Salaried Savings Plans	0			27MAR00*	27MAR00*	2
9AENCF0043	Monthly CA Progress Report (FDF to DOE)	0			14APR00*	14APR00*	2
9AENCF0062	Quarterly CA Progress Report (FDF to DOE)	0			14APR00*	14APR00*	2
9AENCF0044	Monthly CA Progress Report (DOE to EPA)	0			24APR00*	24APR00*	2
9AENCF0063	Quarterly CA Progress Report (DOE to EPA)	0			24APR00*	24APR00*	2
9AENCF0045	Monthly CA Progress Report (FDF to DOE)	0			12MAY00*	12MAY00*	2
9AENCF0046	Monthly CA Progress Report (DOE to EPA)	0			19MAY00*	19MAY00*	2
9A00000016	Complete Congressional Budget Submittal	0			30MAY00*	30MAY00*	2
9AENCF0047	Monthly CA Progress Report (FDF to DOE)	0			14JUN00*	14JUN00*	2
9AENCF0048	Monthly CA Progress Report (DOE to EPA)	0			21JUN00*	21JUN00*	2
9A00000013	Complete Mid-Year Review	0			30JUN00*	30JUN00*	2
9AECAM022	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			03JUL00*	03JUL00*	2
9AENCF0049	Monthly CA Progress Report (FDF to DOE)	0			17JUL00*	17JUL00*	2
9AENCF0064	Quarterly CA Progress Report (FDF to DOE)	0			17JUL00*	17JUL00*	2
9AENCF0050	Monthly CA Progress Report (DOE to EPA)	0			24JUL00*	24JUL00*	2
9AENCF0065	Quarterly CA Progress Report (DOE to EPA)	0			24JUL00*	24JUL00*	2
9A00HR0009	Complete Historically Black College & Univ. Pla	0			31JUL00*	31JUL00*	2
9AENCF0051	Monthly CA Progress Report (FDF to DOE)	0			14AUG00*	14AUG00*	2
9AENCF0052	Monthly CA Progress Report (DOE to EPA)	0			21AUG00*	21AUG00*	2
9A00HR0011	Complete Affirm Action Plan-Veterans&Handicappe	0			05SEP00*	05SEP00*	2
9AENCF0053	Monthly CA Progress Report (FDF to DOE)	0			15SEP00*	15SEP00*	2
9AENCF0054	Monthly CA Progress Report (DOE to EPA)	0			22SEP00*	22SEP00*	2

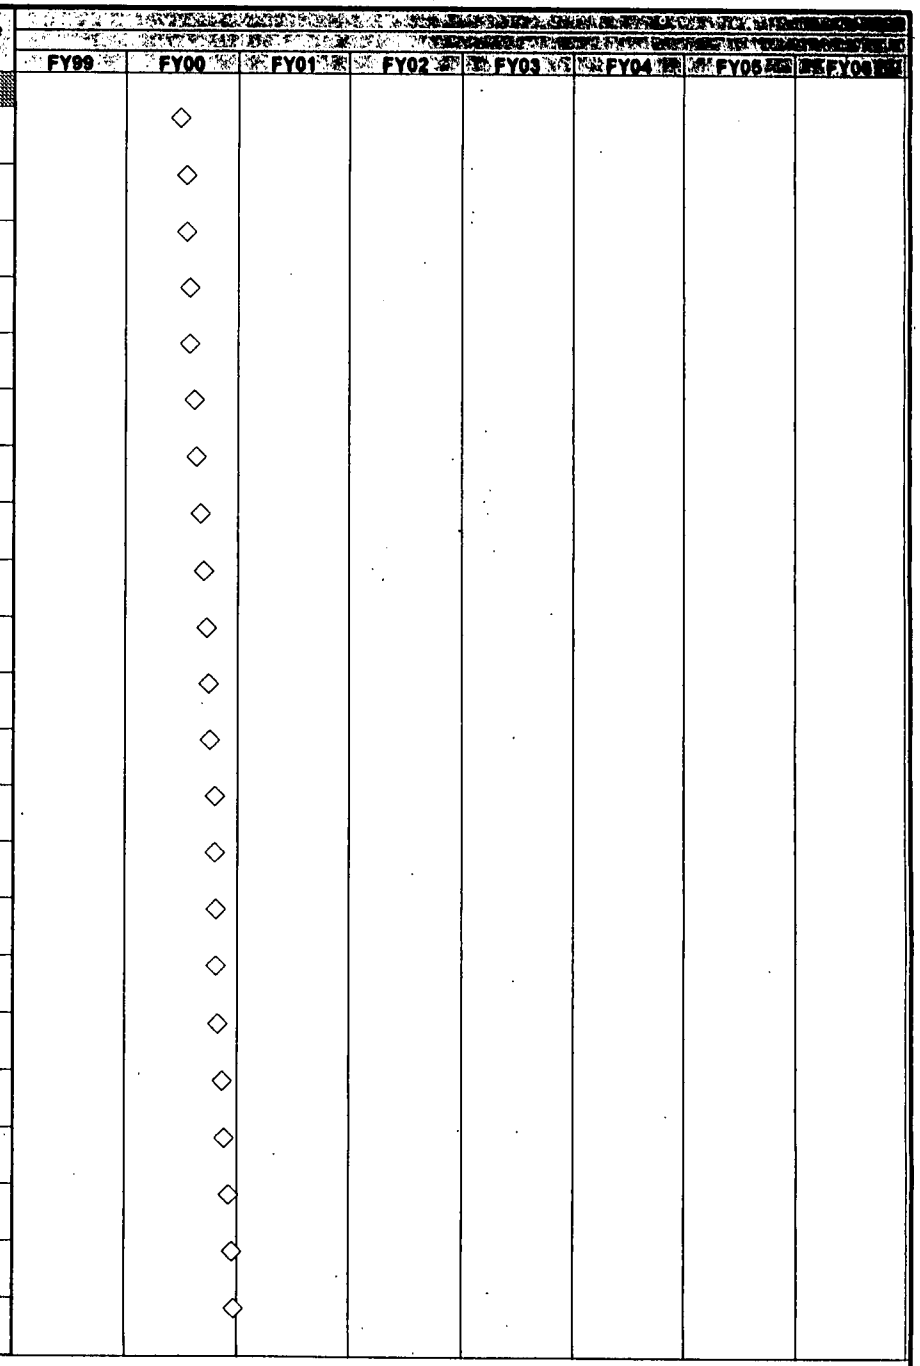

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0131	Monthly CA Progress Report (FDF to DOE)	0			13OCT00*	13OCT00*	2
9AENCF0158	Quarterly CA Progress Report (FDF to DOE)	0			13OCT00*	13OCT00*	2
9AENCF0132	Monthly CA Progress Report (DOE to EPA)	0			20OCT00*	20OCT00*	2
9AENCF0159	Quarterly CA Progress Report (DOE to EPA)	0			20OCT00*	20OCT00*	2
9AENCF0133	Monthly CA Progress Report (FDF to DOE)	0			15NOV00*	15NOV00*	2
9AENCF0134	Monthly CA Progress Report (DOE to EPA)	0			22NOV00*	22NOV00*	2
9AENCF0135	Monthly CA Progress Report (FDF to DOE)	0			14DEC00*	14DEC00*	2
9AENCF0136	Monthly CA Progress Report (DOE to EPA)	0			21DEC00*	21DEC00*	2
9A00000115	Conduct FY 2000 Year End Review	0			29DEC00*	29DEC00*	2
9AENCF0137	Monthly CA Progress Report (FDF to DOE)	0			15JAN01*	15JAN01*	2
9AENCF0160	Quarterly CA Progress Report (FDF to DOE)	0			15JAN01*	15JAN01*	2
9AENCF0138	Monthly CA Progress Report (DOE to EPA)	0			22JAN01*	22JAN01*	2
9AENCF0161	Quarterly CA Progress Report (DOE to EPA)	0			22JAN01*	22JAN01*	2
9A00HR0108	Complete Affirm Action Plan-Females & Minoritie	0			31JAN01*	31JAN01*	2
9AENCF0139	Monthly CA Progress Report (FDF to DOE)	0			15FEB01*	15FEB01*	2
9AENCF0140	Monthly CA Progress Report (DOE to EPA)	0			22FEB01*	22FEB01*	2
9AECAM023	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR01*	01MAR01*	2
9AENCF0141	Monthly CA Progress Report (FDF to DOE)	0			14MAR01*	14MAR01*	2
9AENCF0142	Monthly CA Progress Report (DOE to EPA)	0			21MAR01*	21MAR01*	2
9A00HR0120	Complete Annual Acct. of Salaried Savings Plans	0			26MAR01*	26MAR01*	2
9AENCF0143	Monthly CA Progress Report (FDF to DOE)	0			16APR01*	16APR01*	2
9AENCF0162	Quarterly CA Progress Report (FDF to DOE)	0			16APR01*	16APR01*	2

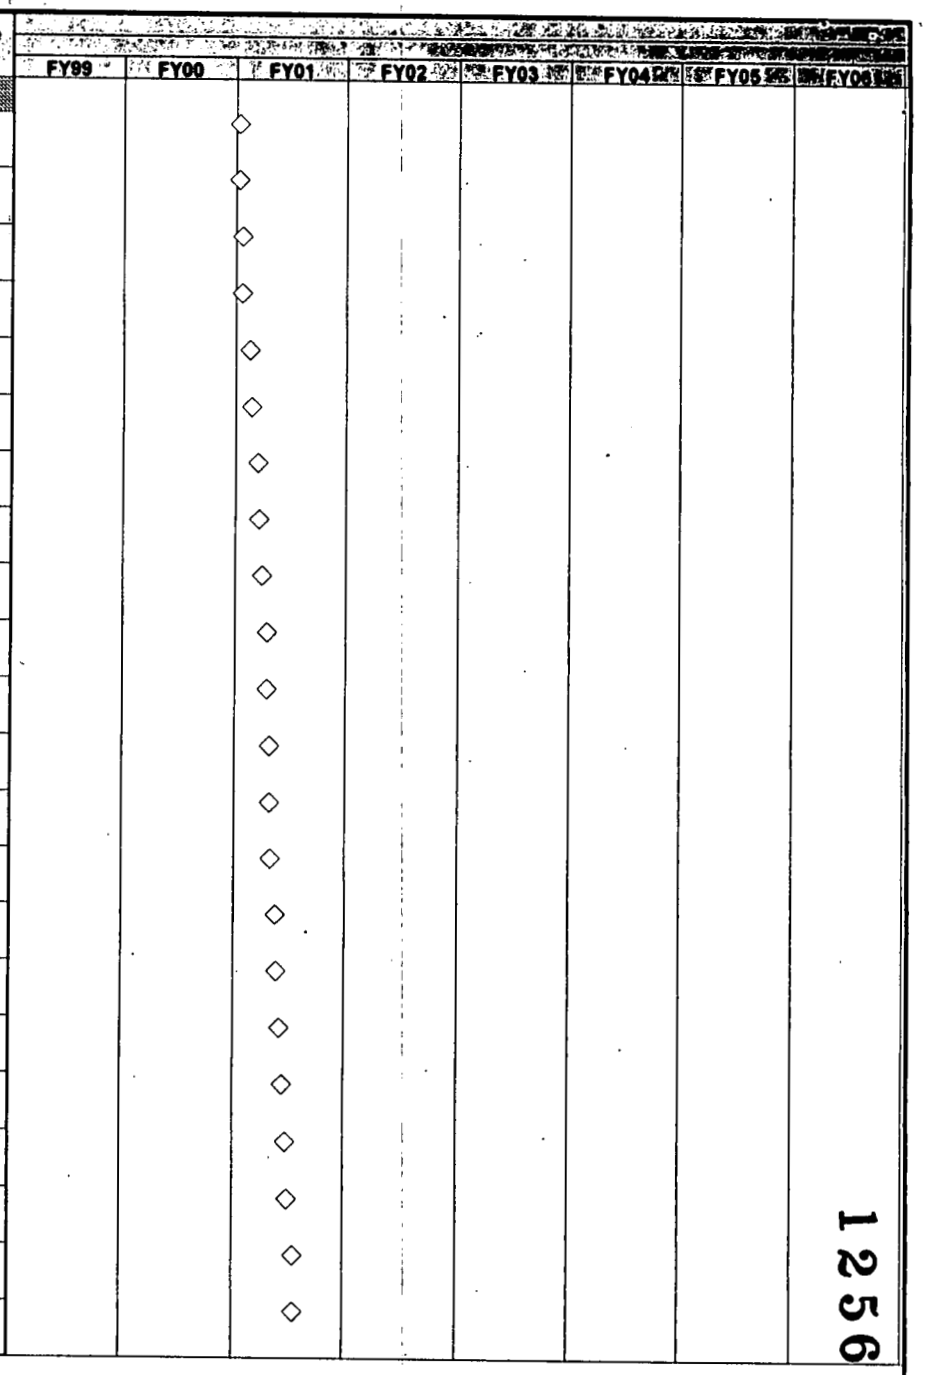

1256

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule
Status Through 01/18/98
Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0144	Monthly CA Progress Report (DOE to EPA)	0			23APR01*	23APR01*	2
9AENCF0163	Quarterly CA Progress Report (DOE to EPA)	0			23APR01*	23APR01*	2
9AENCF0145	Monthly CA Progress Report (FDF to DOE)	0			14MAY01*	14MAY01*	2
9AENCF0146	Monthly CA Progress Report (DOE to EPA)	0			21MAY01*	21MAY01*	2
9A00000116	Complete Congressional Budget Submittal	0			30MAY01*	30MAY01*	2
9AENCF0147	Monthly CA Progress Report (FDF to DOE)	0			14JUN01*	14JUN01*	2
9AENCF0148	Monthly CA Progress Report (DOE to EPA)	0			21JUN01*	21JUN01*	2
9A00000113	Complete Mid-Year Review	0			29JUN01*	29JUN01*	2
9AECAM024	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL01*	02JUL01*	2
9AENCF0149	Monthly CA Progress Report (FDF to DOE)	0			16JUL01*	16JUL01*	2
9AENCF0164	Quarterly CA Progress Report (FDF to DOE)	0			16JUL01*	16JUL01*	2
9AENCF0150	Monthly CA Progress Report (DOE to EPA)	0			23JUL01*	23JUL01*	2
9AENCF0165	Quarterly CA Progress Report (DOE to EPA)	0			23JUL01*	23JUL01*	2
9A00HR0109	Complete Historically Black College & Univ. Pla	0			31JUL01*	31JUL01*	2
9AENCF0151	Monthly CA Progress Report (FDF to DOE)	0			14AUG01*	14AUG01*	2
9AENCF0152	Monthly CA Progress Report (DOE to EPA)	0			21AUG01*	21AUG01*	2
9A00HR0111	Complete Affirm Action Plan-Veterans&Handicappe	0			04SEP01*	04SEP01*	2
9AENCF0153	Monthly CA Progress Report (FDF to DOE)	0			17SEP01*	17SEP01*	2
9AENCF0154	Monthly CA Progress Report (DOE to EPA)	0			24SEP01*	24SEP01*	2
9AENCF0231	Monthly CA Progress Report (FDF to DOE)	0			12OCT01*	12OCT01*	2
9AENCF0258	Quarterly CA Progress Report (FDF to DOE)	0			12OCT01*	12OCT01*	2
9AENCF0232	Monthly CA Progress Report (DOE to EPA)	0			19OCT01*	19OCT01*	2

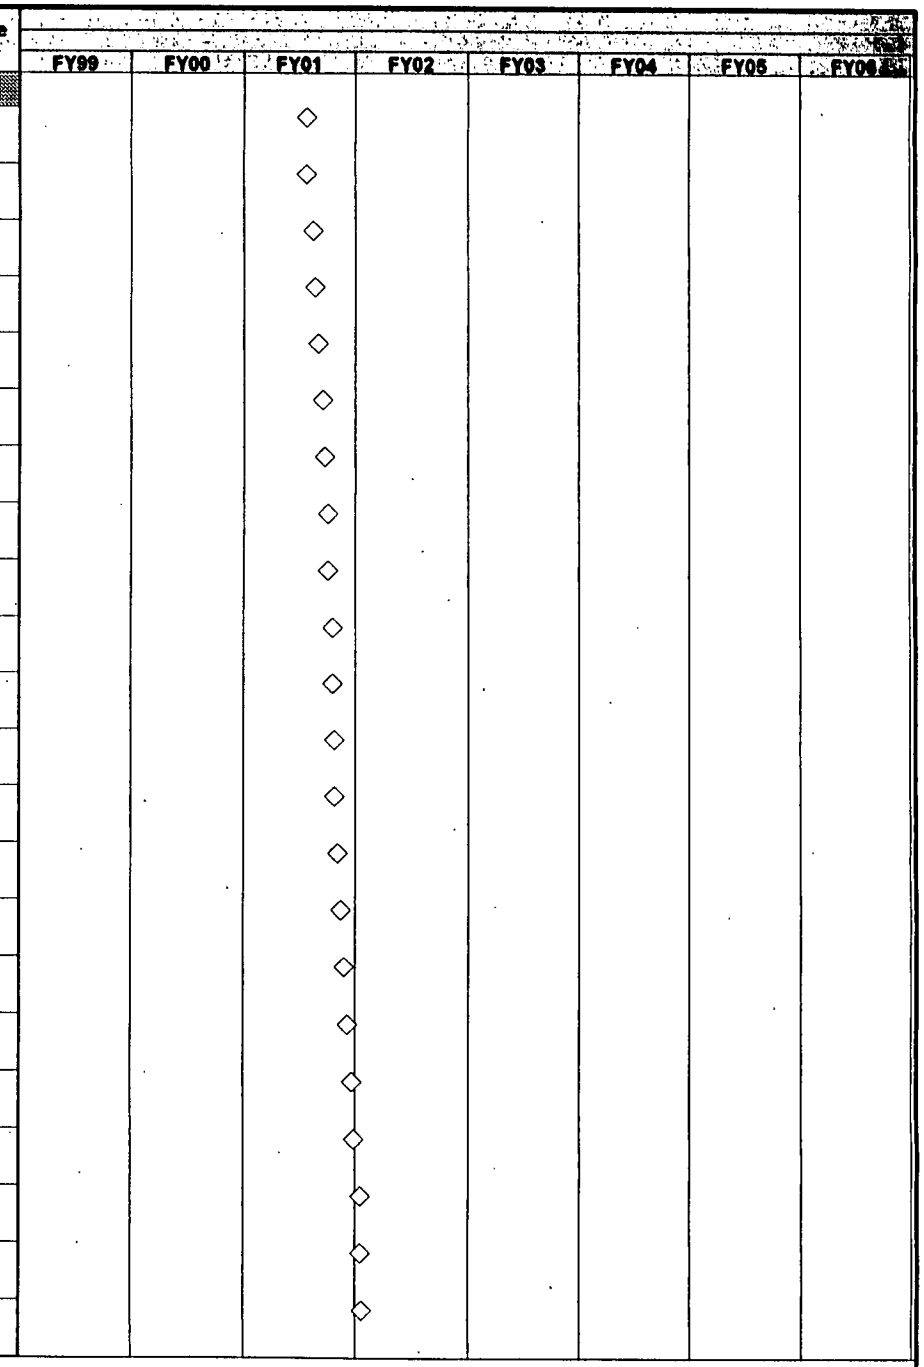

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

43

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0259	Quarterly CA Progress Report (DOE to EPA)	0			19OCT01*	19OCT01*	2
9AENCF0233	Monthly CA Progress Report (FDF to DOE)	0			15NOV01*	15NOV01*	2
9AENCF0234	Monthly CA Progress Report (DOE to EPA)	0			26NOV01*	26NOV01*	2
9AENCF0235	Monthly CA Progress Report (FDF to DOE)	0			14DEC01*	14DEC01*	2
9AENCF0236	Monthly CA Progress Report (DOE to EPA)	0			21DEC01*	21DEC01*	2
9A00000215	Conduct FY 2001 Year End Review	0			31DEC01*	31DEC01*	2
9AENCF0237	Monthly CA Progress Report (FDF to DOE)	0			15JAN02*	15JAN02*	2
9AENCF0260	Quarterly CA Progress Report (FDF to DOE)	0			15JAN02*	15JAN02*	2
9AENCF0238	Monthly CA Progress Report (DOE to EPA)	0			22JAN02*	22JAN02*	2
9AENCF0261	Quarterly CA Progress Report (DOE to EPA)	0			22JAN02*	22JAN02*	2
9A00HR0208	Complete Affirm Action Plan-Females & Minoritie	0			31JAN02*	31JAN02*	2
9AENCF0239	Monthly CA Progress Report (FDF to DOE)	0			14FEB02*	14FEB02*	2
9AENCF0240	Monthly CA Progress Report (DOE to EPA)	0			22FEB02*	22FEB02*	2
9AECAM025	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR02*	01MAR02*	2
9AENCF0241	Monthly CA Progress Report (FDF to DOE)	0			14MAR02*	14MAR02*	2
9AENCF0242	Monthly CA Progress Report (DOE to EPA)	0			21MAR02*	21MAR02*	2
9A00HR0220	Complete Annual Acct. of Salaried Savings Plans	0			25MAR02*	25MAR02*	2
9AENCF0243	Monthly CA Progress Report (FDF to DOE)	0			12APR02*	12APR02*	2
9AENCF0262	Quarterly CA Progress Report (FDF to DOE)	0			12APR02*	12APR02*	2
9AENCF0244	Monthly CA Progress Report (DOE to EPA)	0			19APR02*	19APR02*	2
9AENCF0263	Quarterly CA Progress Report (DOE to EPA)	0			19APR02*	19APR02*	2
9AENCF0245	Monthly CA Progress Report (FDF to DOE)	0			14MAY02*	14MAY02*	2

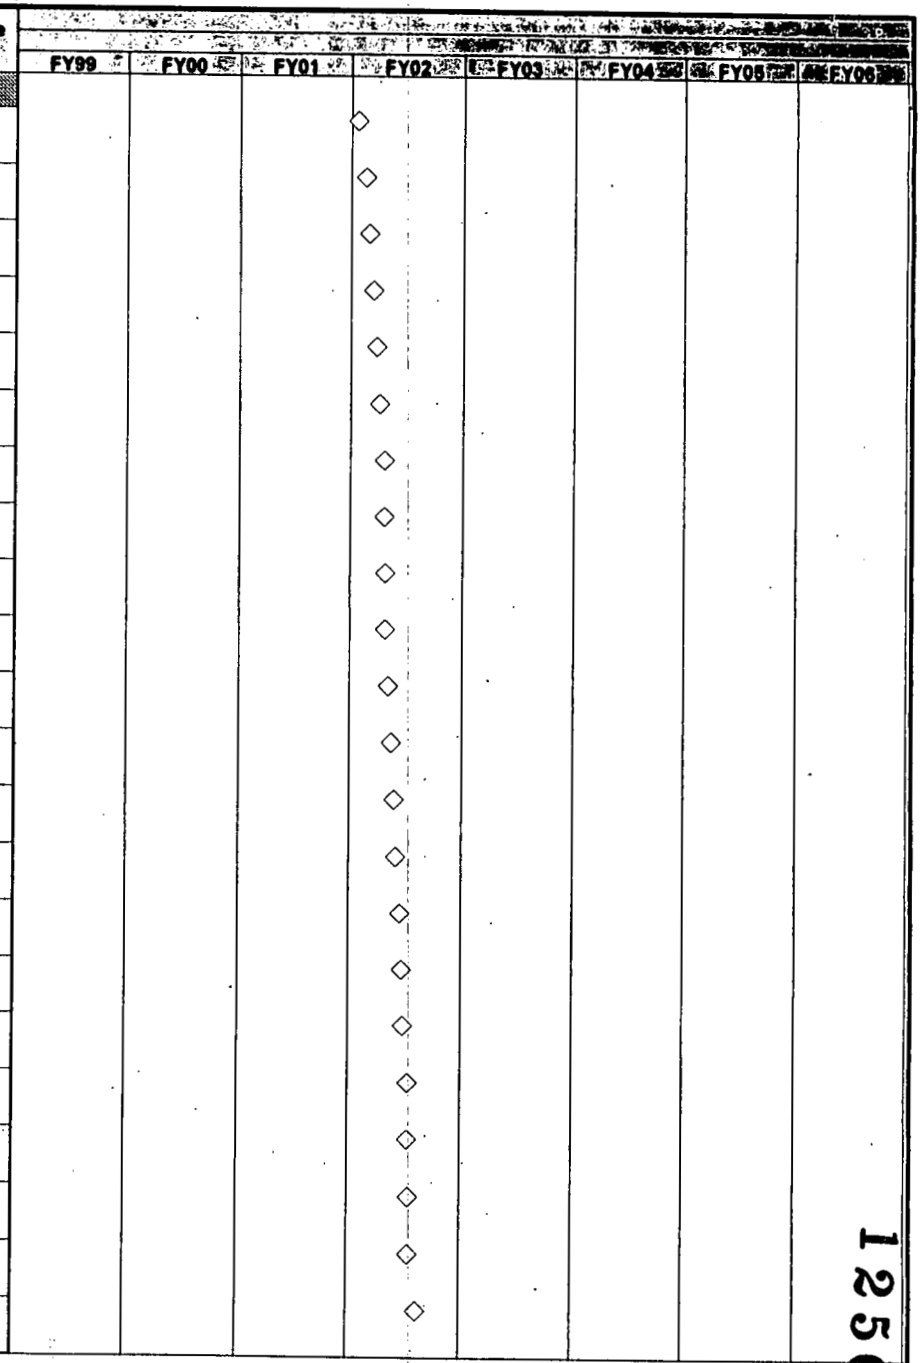

1256

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

44

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0246	Monthly CA Progress Report (DOE to EPA)	0			21MAY02*	21MAY02*	2
9A00000216	Complete Congressional Budget Submittal	0			30MAY02*	30MAY02*	2
9AENCF0247	Monthly CA Progress Report (FDF to DOE)	0			14JUN02*	14JUN02*	2
9AENCF0248	Monthly CA Progress Report (DOE to EPA)	0			21JUN02*	21JUN02*	2
9A00000213	Complete Mid-Year Review	0			28JUN02*	28JUN02*	2
9AECAM026	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL02*	02JUL02*	2
9AENCF0249	Monthly CA Progress Report (FDF to DOE)	0			15JUL02*	15JUL02*	2
9AENCF0264	Quarterly CA Progress Report (FDF to DOE)	0			15JUL02*	15JUL02*	2
9AENCF0250	Monthly CA Progress Report (DOE to EPA)	0			22JUL02*	22JUL02*	2
9AENCF0265	Quarterly CA Progress Report (DOE to EPA)	0			22JUL02*	22JUL02*	2
9A00HR0209	Complete Historically Black College & Univ. Pla	0			31JUL02*	31JUL02*	2
9AENCF0251	Monthly CA Progress Report (FDF to DOE)	0			14AUG02*	14AUG02*	2
9AENCF0252	Monthly CA Progress Report (DOE to EPA)	0			21AUG02*	21AUG02*	2
9A00HR0211	Complete Affirm Action Plan-Veterans&Handicappe	0			03SEP02*	03SEP02*	2
9AENCF0253	Monthly CA Progress Report (FDF to DOE)	0			16SEP02*	16SEP02*	2
9AENCF0254	Monthly CA Progress Report (DOE to EPA)	0			23SEP02*	23SEP02*	2
9AENCF0331	Monthly CA Progress Report (FDF to DOE)	0			14OCT02*	14OCT02*	2
9AENCF0358	Quarterly CA Progress Report (FDF to DOE)	0			14OCT02*	14OCT02*	2
9AENCF0332	Monthly CA Progress Report (DOE to EPA)	0			21OCT02*	21OCT02*	2
9AENCF0359	Quarterly CA Progress Report (DOE to EPA)	0			21OCT02*	21OCT02*	2
9AENCF0333	Monthly CA Progress Report (FDF to DOE)	0			15NOV02*	15NOV02*	2
9AENCF0334	Monthly CA Progress Report (DOE to EPA)	0			22NOV02*	22NOV02*	2

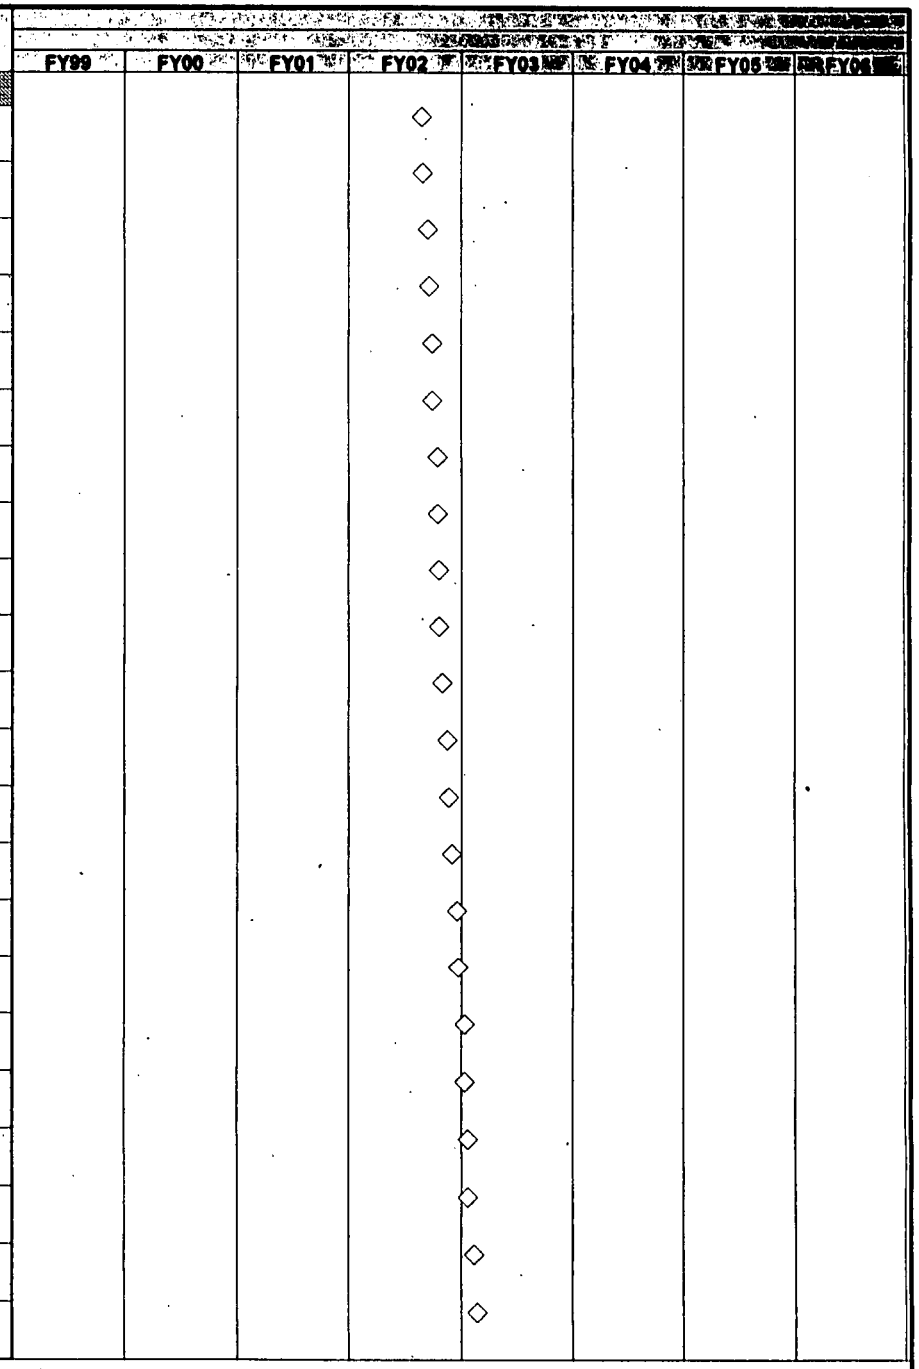

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level	FY99	FY00	FY01	FY02	FY03	FY04	FY05	FY06
Support and Oversight															
9AENCF0335	Monthly CA Progress Report (FDF to DOE)	0			13DEC02*	13DEC02*	2					◇			
9AENCF0336	Monthly CA Progress Report (DOE to EPA)	0			20DEC02*	20DEC02*	2					◇			
9A00000315	Conduct FY 2002 Year End Review	0			31DEC02*	31DEC02*	2					◇			
9AENCF0337	Monthly CA Progress Report (FDF to DOE)	0			15JAN03*	15JAN03*	2					◇			
9AENCF0360	Quarterly CA Progress Report (FDF to DOE)	0			15JAN03*	15JAN03*	2					◇			
9AENCF0338	Monthly CA Progress Report (DOE to EPA)	0			22JAN03*	22JAN03*	2					◇			
9AENCF0361	Quarterly CA Progress Report (DOE to EPA)	0			22JAN03*	22JAN03*	2					◇			
9A00HR0308	Complete Affirm Action Plan-Females & Minoritie	0			31JAN03*	31JAN03*	2					◇			
9AENCF0339	Monthly CA Progress Report (FDF to DOE)	0			14FEB03*	14FEB03*	2					◇			
9AENCF0340	Monthly CA Progress Report (DOE to EPA)	0			24FEB03*	24FEB03*	2					◇			
9AECAM027	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			03MAR03*	03MAR03*	2					◇			
9AENCF0341	Monthly CA Progress Report (FDF to DOE)	0			14MAR03*	14MAR03*	2					◇			
9AENCF0342	Monthly CA Progress Report (DOE to EPA)	0			21MAR03*	21MAR03*	2					◇			
9A00HR0320	Complete Annual Acct. of Salaried Savings Plans	0			25MAR03*	25MAR03*	2					◇			
9AENCF0343	Monthly CA Progress Report (FDF to DOE)	0			14APR03*	14APR03*	2					◇			
9AENCF0362	Quarterly CA Progress Report (FDF to DOE)	0			14APR03*	14APR03*	2					◇			
9AENCF0344	Monthly CA Progress Report (DOE to EPA)	0			22APR03*	22APR03*	2					◇			
9AENCF0363	Quarterly CA Progress Report (DOE to EPA)	0			22APR03*	22APR03*	2					◇			
9AENCF0345	Monthly CA Progress Report (FDF to DOE)	0			14MAY03*	14MAY03*	2					◇			
9AENCF0346	Monthly CA Progress Report (DOE to EPA)	0			21MAY03*	21MAY03*	2					◇			
9A00000316	Complete Congressional Budget Submittal	0			30MAY03*	30MAY03*	2					◇			
9AENCF0347	Monthly CA Progress Report (FDF to DOE)	0			13JUN03*	13JUN03*	2					◇			

- 1256

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0348	Monthly CA Progress Report (DOE to EPA)	0			20JUN03*	20JUN03*	2
9A00000313	Complete Mid-Year Review	0			30JUN03*	30JUN03*	2
9AECAM028	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL03*	02JUL03*	2
9AENCF0349	Monthly CA Progress Report (FDF to DOE)	0			15JUL03*	15JUL03*	2
9AENCF0364	Quarterly CA Progress Report (FDF to DOE)	0			15JUL03*	15JUL03*	2
9AENCF0350	Monthly CA Progress Report (DOE to EPA)	0			22JUL03*	22JUL03*	2
9AENCF0365	Quarterly CA Progress Report (DOE to EPA)	0			22JUL03*	22JUL03*	2
9A00HR0309	Complete Historically Black College & Univ. Pla	0			31JUL03*	31JUL03*	2
9AENCF0351	Monthly CA Progress Report (FDF to DOE)	0			14AUG03*	14AUG03*	2
9AENCF0352	Monthly CA Progress Report (DOE to EPA)	0			21AUG03*	21AUG03*	2
9A00HR0311	Complete Affirm Action Plan-Veterans&Handicappe	0			02SEP03*	02SEP03*	2
9AENCF0353	Monthly CA Progress Report (FDF to DOE)	0			15SEP03*	15SEP03*	2
9AENCF0354	Monthly CA Progress Report (DOE to EPA)	0			22SEP03*	22SEP03*	2
9AENCF0431	Monthly CA Progress Report (FDF to DOE)	0			14OCT03*	14OCT03*	2
9AENCF0458	Quarterly CA Progress Report (FDF to DOE)	0			14OCT03*	14OCT03*	2
9AENCF0432	Monthly CA Progress Report (DOE to EPA)	0			21OCT03*	21OCT03*	2
9AENCF0459	Quarterly CA Progress Report (DOE to EPA)	0			21OCT03*	21OCT03*	2
9AENCF0433	Monthly CA Progress Report (FDF to DOE)	0			17NOV03*	17NOV03*	2
9AENCF0434	Monthly CA Progress Report (DOE to EPA)	0			24NOV03*	24NOV03*	2
9AENCF0435	Monthly CA Progress Report (FDF to DOE)	0			12DEC03*	12DEC03*	2
9AENCF0436	Monthly CA Progress Report (DOE to EPA)	0			19DEC03*	19DEC03*	2
9A00000415	Conduct FY 2003 Year End Review	0			31DEC03*	31DEC03*	2

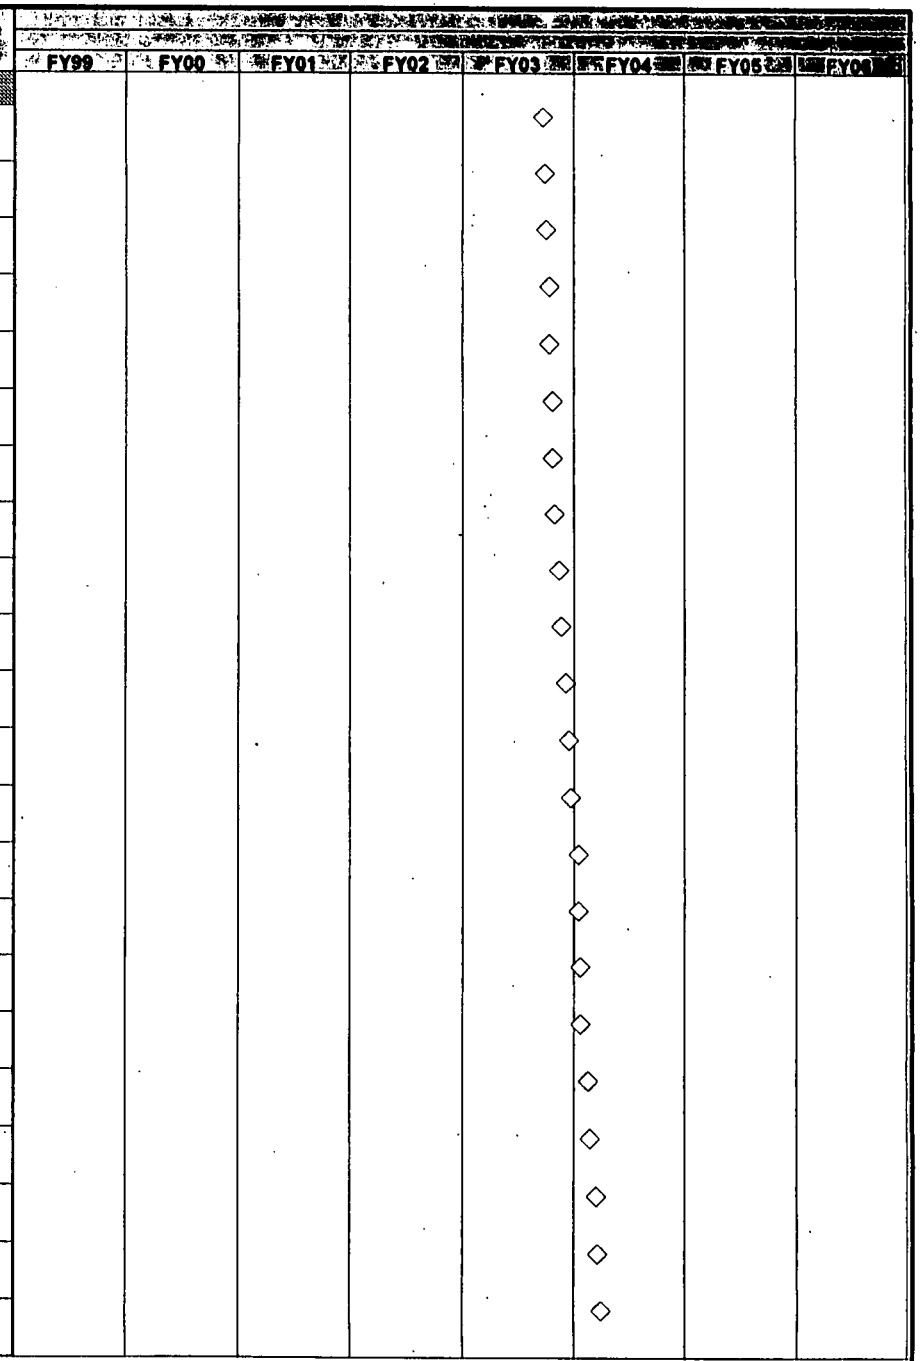

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level	FY99	FY00	FY01	FY02	FY03	FY04	FY05	FY06
Support and Oversight															
9AENCF0437	Monthly CA Progress Report (FDF to DOE)	0			15JAN04*	15JAN04*	2						◇		
9AENCF0460	Quarterly CA Progress Report (FDF to DOE)	0			15JAN04*	15JAN04*	2						◇		
9AENCF0438	Monthly CA Progress Report (DOE to EPA)	0			22JAN04*	22JAN04*	2						◇		
9AENCF0461	Quarterly CA Progress Report (DOE to EPA)	0			22JAN04*	22JAN04*	2						◇		
9A00HR0408	Complete Affirm Action Plan-Females & Minoritie	0			02FEB04*	02FEB04*	2						◇		
9AENCF0439	Monthly CA Progress Report (FDF to DOE)	0			13FEB04*	13FEB04*	2						◇		
9AENCF0440	Monthly CA Progress Report (DOE to EPA)	0			23FEB04*	23FEB04*	2						◇		
9AECAM029	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR04*	01MAR04*	2						◇		
9AENCF0441	Monthly CA Progress Report (FDF to DOE)	0			12MAR04*	12MAR04*	2						◇		
9AENCF0442	Monthly CA Progress Report (DOE to EPA)	0			19MAR04*	19MAR04*	2						◇		
9A00HR0420	Complete Annual Acct. of Salaried Savings Plans	0			25MAR04*	25MAR04*	2						◇		
9AENCF0443	Monthly CA Progress Report (FDF to DOE)	0			15APR04*	15APR04*	2						◇		
9AENCF0462	Quarterly CA Progress Report (FDF to DOE)	0			15APR04*	15APR04*	2						◇		
9AENCF0444	Monthly CA Progress Report (DOE to EPA)	0			22APR04*	22APR04*	2						◇		
9AENCF0463	Quarterly CA Progress Report (DOE to EPA)	0			22APR04*	22APR04*	2						◇		
9AENCF0445	Monthly CA Progress Report (FDF to DOE)	0			14MAY04*	14MAY04*	2						◇		
9AENCF0446	Monthly CA Progress Report (DOE to EPA)	0			21MAY04*	21MAY04*	2						◇		
9A00000416	Complete Congressional Budget Submittal	0			28MAY04*	28MAY04*	2						◇		
9AENCF0447	Monthly CA Progress Report (FDF to DOE)	0			14JUN04*	14JUN04*	2						◇		
9AENCF0448	Monthly CA Progress Report (DOE to EPA)	0			21JUN04*	21JUN04*	2						◇		
9A00000413	Complete Mid-Year Review	0			30JUN04*	30JUN04*	2						◇		
9AECAM030	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			02JUL04*	02JUL04*	2						◇		

1256

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule
Status Through 01/18/98
Level 0/1/2 Milestones (FY99 - 06)

Sheet 15 of 20

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level	FY99	FY00	FY01	FY02	FY03	FY04	FY05	FY06
Support and Oversight															
9AENCF0449	Monthly CA Progress Report (FDF to DOE)	0			15JUL04*	15JUL04*	2						◇		
9AENCF0464	Quarterly CA Progress Report (FDF to DOE)	0			15JUL04*	15JUL04*	2						◇		
9AENCF0450	Monthly CA Progress Report (DOE to EPA)	0			22JUL04*	22JUL04*	2						◇		
9AENCF0465	Quarterly CA Progress Report (DOE to EPA)	0			22JUL04*	22JUL04*	2						◇		
9A00HR0409	Complete Historically Black College & Univ. Pla	0			02AUG04*	02AUG04*	2						◇		
9AENCF0451	Monthly CA Progress Report (FDF to DOE)	0			13AUG04*	13AUG04*	2						◇		
9AENCF0452	Monthly CA Progress Report (DOE to EPA)	0			20AUG04*	20AUG04*	2						◇		
9A00HR0411	Complete Affirm Action Plan-Veterans&Handicappe	0			02SEP04*	02SEP04*	2						◇		
9AENCF0453	Monthly CA Progress Report (FDF to DOE)	0			15SEP04*	15SEP04*	2						◇		
9AENCF0454	Monthly CA Progress Report (DOE to EPA)	0			22SEP04*	22SEP04*	2						◇		
9AENCF0531	Monthly CA Progress Report (FDF to DOE)	0			14OCT04*	14OCT04*	2							◇	
9AENCF0558	Quarterly CA Progress Report (FDF to DOE)	0			14OCT04*	14OCT04*	2							◇	
9AENCF0532	Monthly CA Progress Report (DOE to EPA)	0			21OCT04*	21OCT04*	2							◇	
9AENCF0559	Quarterly CA Progress Report (DOE to EPA)	0			21OCT04*	21OCT04*	2							◇	
9AENCF0533	Monthly CA Progress Report (FDF to DOE)	0			15NOV04*	15NOV04*	2							◇	
9AENCF0534	Monthly CA Progress Report (DOE to EPA)	0			22NOV04*	22NOV04*	2							◇	
9AENCF0535	Monthly CA Progress Report (FDF to DOE)	0			14DEC04*	14DEC04*	2							◇	
9AENCF0536	Monthly CA Progress Report (DOE to EPA)	0			21DEC04*	21DEC04*	2							◇	
9A00000515	Conduct FY 2004 Year End Review	0			30DEC04*	30DEC04*	2							◇	
9AENCF0537	Monthly CA Progress Report (FDF to DOE)	0			14JAN05*	14JAN05*	2							◇	
9AENCF0560	Quarterly CA Progress Report (FDF to DOE)	0			14JAN05*	14JAN05*	2							◇	
9AENCF0538	Monthly CA Progress Report (DOE to EPA)	0			21JAN05*	21JAN05*	2							◇	

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 08)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0561	Quarterly CA Progress Report (DOE to EPA)	0			21JAN05*	21JAN05*	2
9A00HR0508	Complete Affirm Action Plan-Females & Minoritie	0			31JAN05*	31JAN05*	2
9AENCF0539	Monthly CA Progress Report (FDF to DOE)	0			14FEB05*	14FEB05*	2
9AENCF0540	Monthly CA Progress Report (DOE to EPA)	0			22FEB05*	22FEB05*	2
9AECAM031	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR05*	01MAR05*	2
9AENCF0541	Monthly CA Progress Report (FDF to DOE)	0			14MAR05*	14MAR05*	2
9AENCF0542	Monthly CA Progress Report (DOE to EPA)	0			21MAR05*	21MAR05*	2
9A00HR0520	Complete Annual Acct. of Salaried Savings Plans	0			28MAR05*	28MAR05*	2
9AENCF0543	Monthly CA Progress Report (FDF to DOE)	0			14APR05*	14APR05*	2
9AENCF0562	Quarterly CA Progress Report (FDF to DOE)	0			14APR05*	14APR05*	2
9AENCF0544	Monthly CA Progress Report (DOE to EPA)	0			21APR05*	21APR05*	2
9AENCF0563	Quarterly CA Progress Report (DOE to EPA)	0			21APR05*	21APR05*	2
9AENCF0545	Monthly CA Progress Report (FDF to DOE)	0			13MAY05*	13MAY05*	2
9AENCF0546	Monthly CA Progress Report (DOE to EPA)	0			20MAY05*	20MAY05*	2
9A00000516	Complete Congressional Budget Submittal	0			31MAY05*	31MAY05*	2
9AENCF0547	Monthly CA Progress Report (FDF to DOE)	0			14JUN05*	14JUN05*	2
9AENCF0548	Monthly CA Progress Report (DOE to EPA)	0			21JUN05*	21JUN05*	2
9A00000513	Complete Mid-Year Review	0			30JUN05*	30JUN05*	2
9AECAM032	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			05JUL05*	05JUL05*	2
9AENCF0549	Monthly CA Progress Report (FDF to DOE)	0			15JUL05*	15JUL05*	2
9AENCF0564	Quarterly CA Progress Report (FDF to DOE)	0			15JUL05*	15JUL05*	2
9AENCF0550	Monthly CA Progress Report (DOE to EPA)	0			22JUL05*	22JUL05*	2

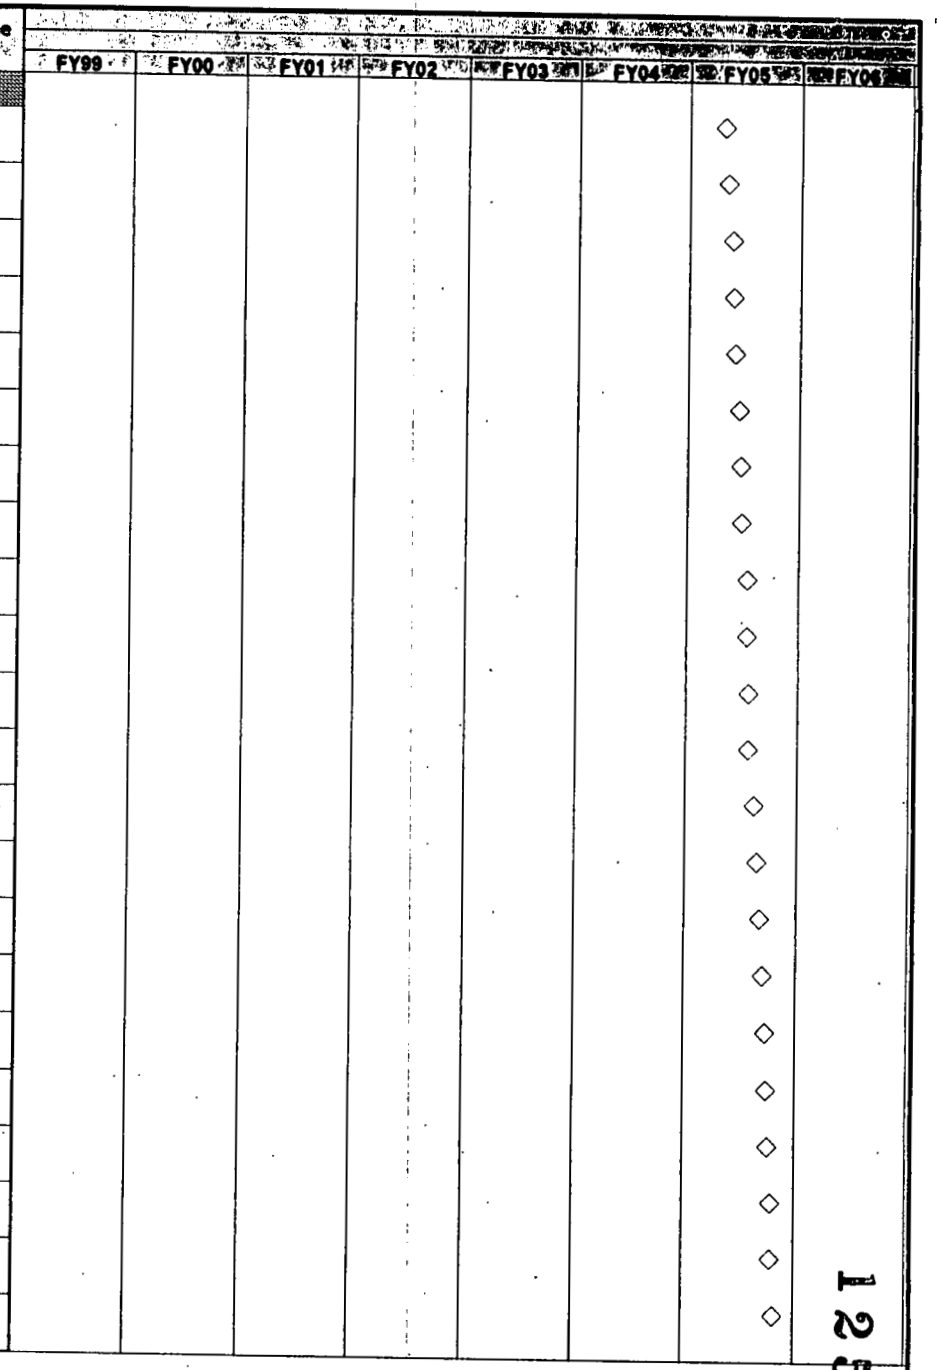

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

Sheet 17 of 20

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

1256

58

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0565	Quarterly CA Progress Report (DOE to EPA)	0			22JUL05*	22JUL05*	2
9A00HR0509	Complete Historically Black College & Univ. Pla	0			01AUG05*	01AUG05*	2
9AENCF0551	Monthly CA Progress Report (FDF to DOE)	0			12AUG05*	12AUG05*	2
9AENCF0552	Monthly CA Progress Report (DOE to EPA)	0			19AUG05*	19AUG05*	2
9A00HR0511	Complete Affirm Action Plan-Veterans&Handicappe	0			02SEP05*	02SEP05*	2
9AENCF0553	Monthly CA Progress Report (FDF to DOE)	0			15SEP05*	15SEP05*	2
9AENCF0554	Monthly CA Progress Report (DOE to EPA)	0			22SEP05*	22SEP05*	2
9AENCF0631	Monthly CA Progress Report (FDF to DOE)	0			14OCT05*	14OCT05*	2
9AENCF0658	Quarterly CA Progress Report (FDF to DOE)	0			14OCT05*	14OCT05*	2
9AENCF0632	Monthly CA Progress Report (DOE to EPA)	0			21OCT05*	21OCT05*	2
9AENCF0659	Quarterly CA Progress Report (DOE to EPA)	0			21OCT05*	21OCT05*	2
9AENCF0633	Monthly CA Progress Report (FDF to DOE)	0			15NOV05*	15NOV05*	2
9AENCF0634	Monthly CA Progress Report (DOE to EPA)	0			22NOV05*	22NOV05*	2
9AENCF0635	Monthly CA Progress Report (FDF to DOE)	0			14DEC05*	14DEC05*	2
9AENCF0636	Monthly CA Progress Report (DOE to EPA)	0			21DEC05*	21DEC05*	2
9A00000615	Conduct FY 2005 Year End Review	0			30DEC05*	30DEC05*	2
9AENCF0637	Monthly CA Progress Report (FDF to DOE)	0			16JAN06*	16JAN06*	2
9AENCF0660	Quarterly CA Progress Report (FDF to DOE)	0			16JAN06*	16JAN06*	2
9AENCF0638	Monthly CA Progress Report (DOE to EPA)	0			23JAN06*	23JAN06*	2
9AENCF0661	Quarterly CA Progress Report (DOE to EPA)	0			23JAN06*	23JAN06*	2
9A00HR0608	Complete Affirm Action Plan-Females & Minoritie	0			31JAN06*	31JAN06*	2
9AENCF0639	Monthly CA Progress Report (FDF to DOE)	0			14FEB06*	14FEB06*	2

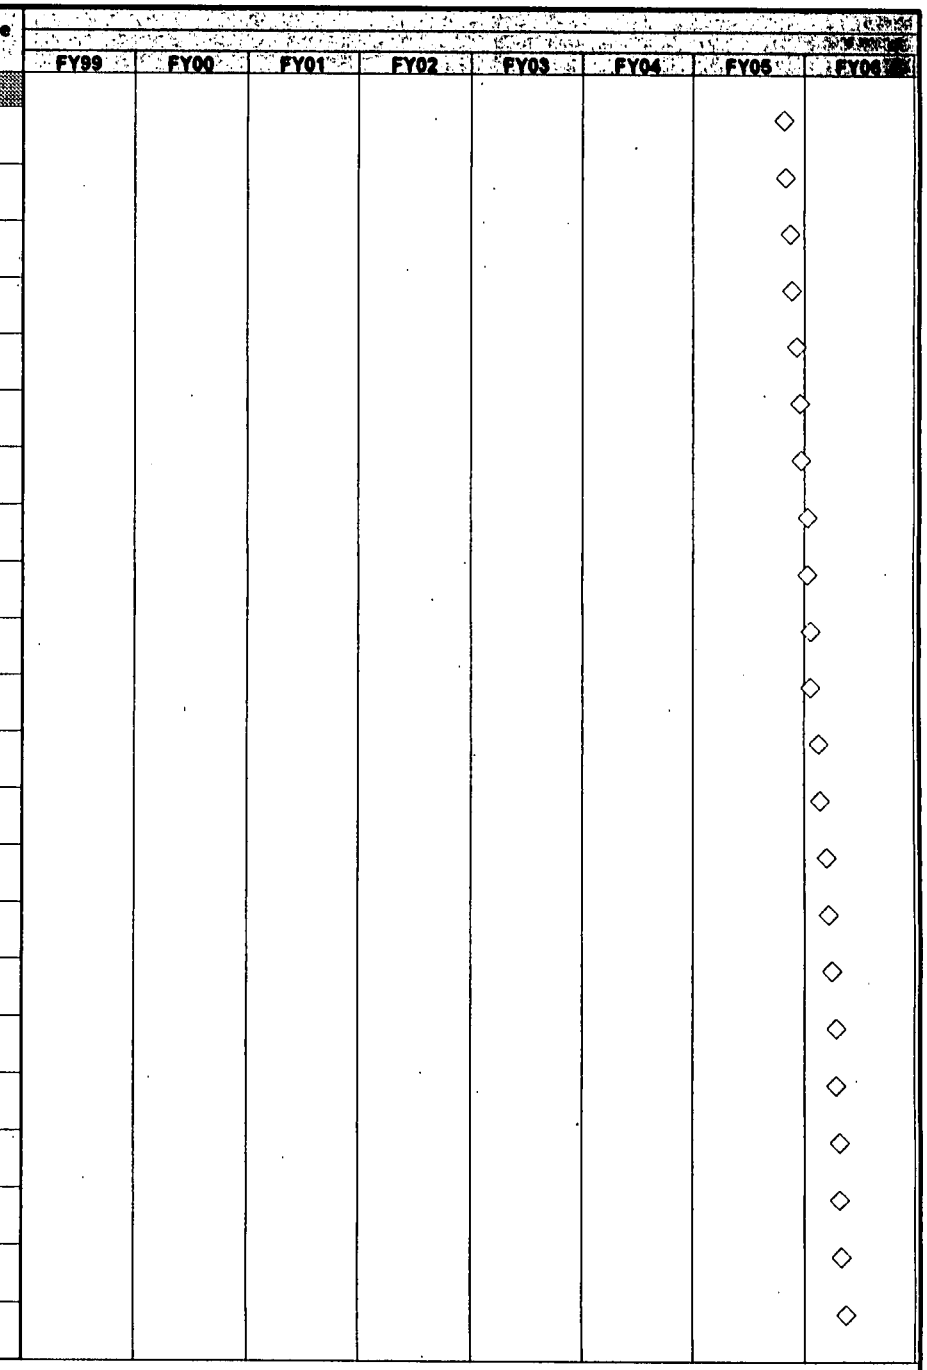

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

5

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0640	Monthly CA Progress Report (DOE to EPA)	0			22FEB06*	22FEB06*	2
9AECAM033	PREPARE/SUBMIT SARA 312 RPT. TO SERC, LEPC & JF	0			01MAR06*	01MAR06*	2
9AENCF0641	Monthly CA Progress Report (FDF to DOE)	0			14MAR06*	14MAR06*	2
9AENCF0642	Monthly CA Progress Report (DOE to EPA)	0			21MAR06*	21MAR06*	2
9A00HR0620	Complete Annual Acct. of Salaried Savings Plans	0			27MAR06*	27MAR06*	2
9AENCF0643	Monthly CA Progress Report (FDF to DOE)	0			17APR06*	17APR06*	2
9AENCF0662	Quarterly CA Progress Report (FDF to DOE)	0			17APR06*	17APR06*	2
9AENCF0644	Monthly CA Progress Report (DOE to EPA)	0			24APR06*	24APR06*	2
9AENCF0663	Quarterly CA Progress Report (DOE to EPA)	0			24APR06*	24APR06*	2
9AENCF0645	Monthly CA Progress Report (FDF to DOE)	0			12MAY06*	12MAY06*	2
9AENCF0646	Monthly CA Progress Report (DOE to EPA)	0			19MAY06*	19MAY06*	2
9A00000616	Complete Congressional Budget Submittal	0			30MAY06*	30MAY06*	2
9AENCF0647	Monthly CA Progress Report (FDF to DOE)	0			14JUN06*	14JUN06*	2
9AENCF0648	Monthly CA Progress Report (DOE to EPA)	0			21JUN06*	21JUN06*	2
9A00000613	Complete Mid-Year Review	0			30JUN06*	30JUN06*	2
9AECAM034	PREPARE/SUBMIT SARA 313 RPT. TO OHIO & U.S. EPA	0			03JUL06*	03JUL06*	2
9AENCF0649	Monthly CA Progress Report (FDF to DOE)	0			17JUL06*	17JUL06*	2
9AENCF0664	Quarterly CA Progress Report (FDF to DOE)	0			17JUL06*	17JUL06*	2
9AENCF0650	Monthly CA Progress Report (DOE to EPA)	0			24JUL06*	24JUL06*	2
9AENCF0665	Quarterly CA Progress Report (DOE to EPA)	0			24JUL06*	24JUL06*	2
9A00HR0609	Complete Historically Black College & Univ. Pla	0			31JUL06*	31JUL06*	2
9AENCF0651	Monthly CA Progress Report (FDF to DOE)	0			14AUG06*	14AUG06*	2

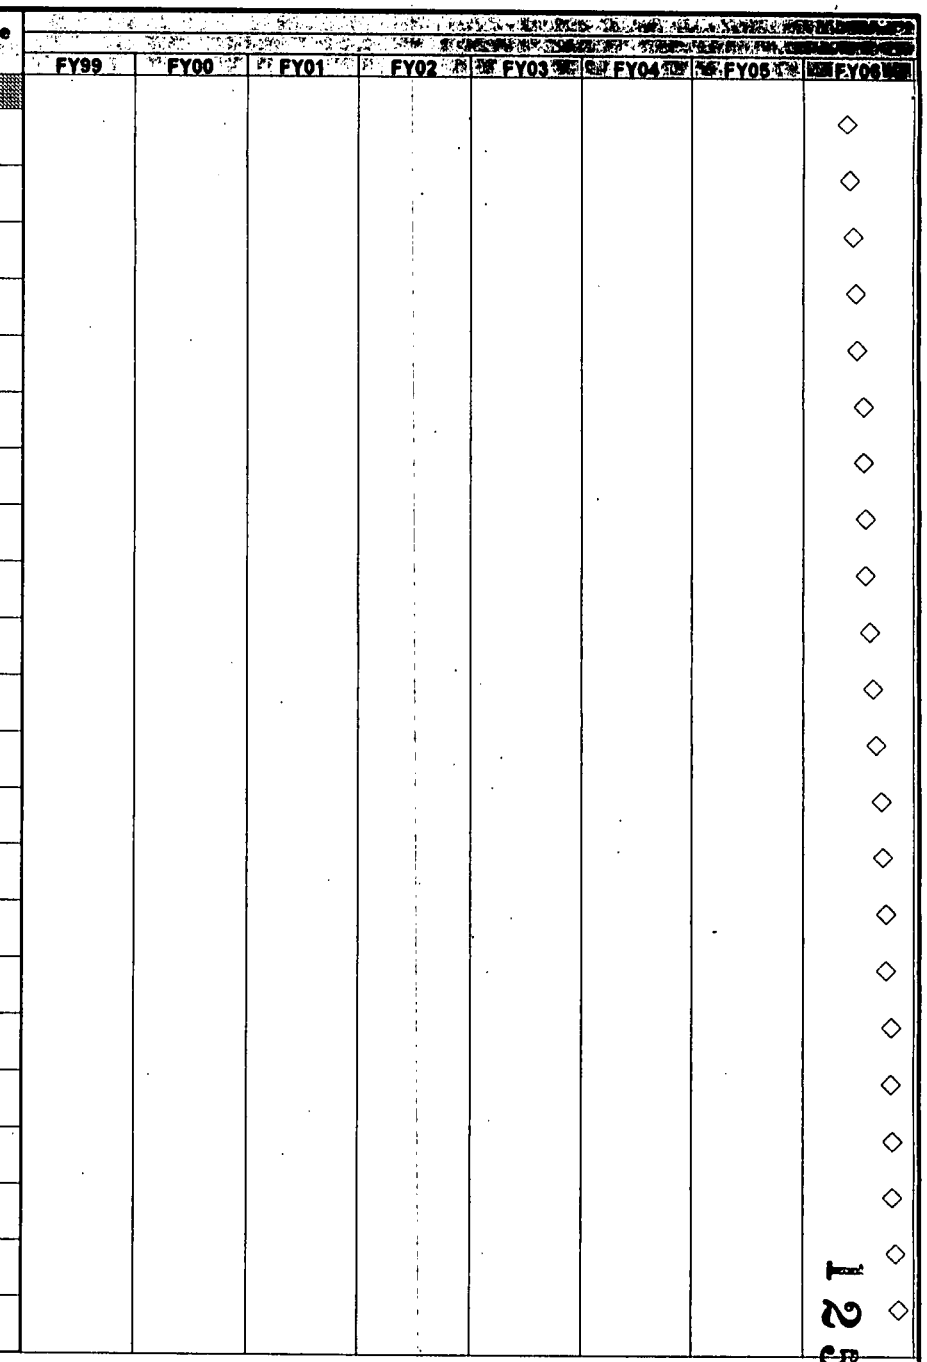

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

1259

57

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Support and Oversight							
9AENCF0652	Monthly CA Progress Report (DOE to EPA)	0			21AUG06*	21AUG06*	2
9A00HR0611	Complete Affirm Action Plan-Veterans&Handicappe	0			01SEP06*	01SEP06*	2
9AENCF0653	Monthly CA Progress Report (FDF to DOE)	0			15SEP06*	15SEP06*	2
9AENCF0654	Monthly CA Progress Report (DOE to EPA)	0			22SEP06*	22SEP06*	2

FY99 FY00 FY01 FY02 FY03 FY04 FY05 FY06

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

© Primavera Systems, Inc.

Current Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

Level 0/1/2 Milestones (FY99 - 06)

FERNALD
Environmental Management Project

EA Milestones

FY 1998

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Facilities Closure & Demolition							
3WNGU012	SUBMIT QUARTERLY NATURAL GAS USAGE	100			24OCT97A	14NOV97*	4
3WNOX012	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	100			31OCT97A	14NOV97*	4
3D08C01M01	BP/WP D&D NOTICE TO PROCEED	0	19JAN98*	10MAR97*			2
3WNGU014	SUBMIT QUARTERLY NATURAL GAS USAGE	0			19JAN98*	13FEB98*	4
3WGDF012	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			13FEB98*	13FEB98*	4
3WHAM012	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			13FEB98*	13FEB98*	4
3D09M01001	MAINT/TANK FARM D&D IMPLEMENTATION PLAN TO	0	04MAR98*	04MAR98*			1
3D17M01001	STP IMPLEMENTATION PLAN TO EPA	0	02APR98*	02APR98			1
3WOEP012	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR98*	15APR98*	4
3WNGU016	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15MAY98*	15MAY98*	4
3WNES012	SUBMIT NESHAP ANNUAL REPORT	0			30JUN98*	30JUN98*	2
3D17C01M01	STP D&D NOTICE TO PROCEED	0	01JUL98*	01JUL98*			2
3D09C01M01	MX/TF & NEW WATER STORAGE NOTICE TO	0	15JUL98*	15JUL98*			2
3D05M01001	PLANT 5 IMPLEMENTATION PLAN TO EPA	0	18JUL98	18JUL98			1
3WNGU018	SUBMIT QUARTERLY NATURAL GAS USAGE	0			14AUG98*	14AUG98*	4
3D08E02M15	BP/WP D&D - CONSTRUCTION FIELD COMPLETION	0			26SEP98*	26SEP98*	2
Soils and Water							
5AFCW2M101	Submit NPDES DMR for 9/97 to Ohio EPA	100			14OCT97A	15OCT97*	2
5CD51598	SWU: SUBMIT PREFNL/90% DSGN PKG TO EPA(CA)	100			23OCT97A	20OCT97	1
5CF63512	SWU IMPLEMNT PLAN: SUBMIT DRAFT PKG TO	100			23OCT97A	20OCT97	1
5AFCW2M102	Submit NPDES DMR for 10/97 to Ohio EPA	100			14NOV97A	15NOV97*	2
5C2D51595	Area 1-II:Submit 90%/Prefnl Dsgn Pkg to EPA (CA)	100			21NOV97A	21NOV97	1
5AARD1M003	OU5 ROD MS-Discharge 20 PPB Limit (JAN 1 98)	100			01DEC97A	31DEC97	2

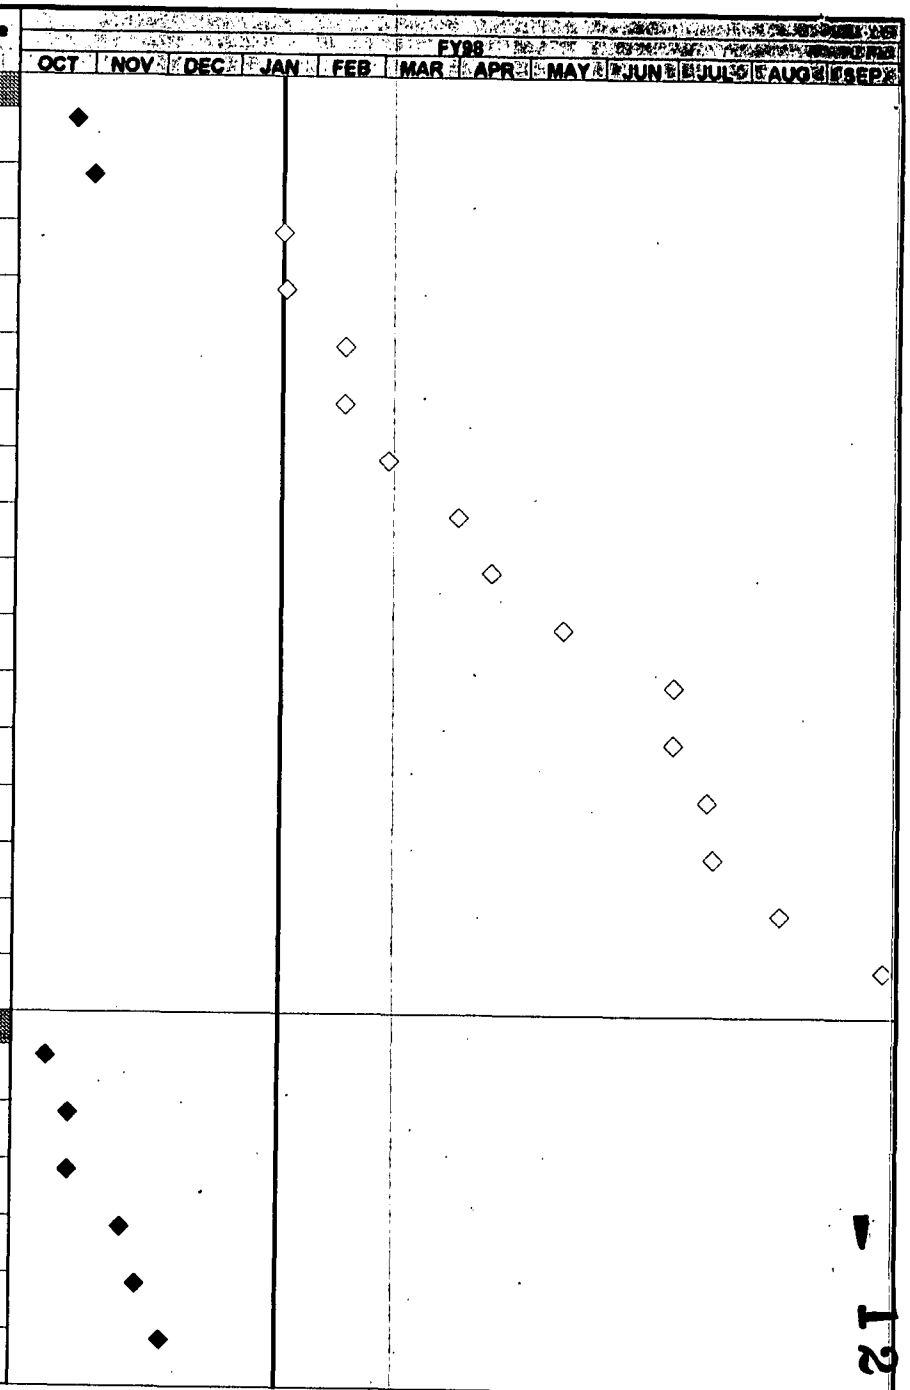

Project Start	01JAN95	Current Bar
Project Finish	30SEP08	Progress Bar
Data Date	19JAN98	Critical Activity
Run Date	04FEB98	

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY98)

Sheet 1 of 2

FERNALD
Environmental Management Project

1236

35

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish	Milestone Level
Soils and Water							
2AD42478	Complete Construction of Roads(EA)	100			05DEC97A	27MAR98*	2
5AFCW2M103	Submit NPDES DMR for 11/97 to Ohio EPA	100			12DEC97A	15DEC97*	2
5CD515M02	SWU: SUBMIT FINAL/CFC DSGN PKG TO EPA(CA)	100			17DEC97A		1
2AN7250	Initiate First Waste Placement in the OSDF(EA)	100	23DEC97A	27MAR98			3
2AN72M4	Place Seasonal Cover On OSDF (1997)(EA)	100			02JAN98A	31DEC97	3
5AFCW2M104	Submit NPDES DMR for 12/97 to Ohio EPA	100			15JAN98A	15JAN98*	2
5AFCW2M105	Submit NPDES DMR for 1/98 to Ohio EPA	0			15FEB98*	15FEB98*	2
5CF63513	SWU : SBMT FNL IMPLEMNT PLN/DESGN PKG TO EPA(CA)	0			25FEB98	13FEB98	1
5AFCW1M002	ODNR Annual Water Withdrawal Report	0			01MAR98*	01MAR98*	4
5AFCW2M106	Submit NPDES DMR for 2/98 to Ohio EPA	0			15MAR98*	15MAR98*	2
5AFCW2M107	Submit NPDES DMR for 3/98 to Ohio EPA	0			15APR98*	15APR98*	2
1C1DEC1779	TRANSPORTATION AND DISPOSAL PLAN (EA	0			27APR98*	27APR98*	2
5BCTP4M001	AWWT Expansion - Commence Operations (CA)	0	30APR98*	30APR98*			2
5AFCW2M108	Submit NPDES DMR for 4/98 to Ohio EPA	0			15MAY98*	15MAY98*	2
5ACSF4M003	SFES Phase I - Commence Operations (CA)	0	16MAY98	30SEP98*			2
5AFCW2M109	Submit NPDES DMR for 5/98 to Ohio EPA	0			15JUN98*	15JUN98*	2
5AFCW2M110	Submit NPDES DMR for 6/98 to Ohio EPA	0			15JUL98*	15JUL98*	2
5AFCW2M111	Submit NPDES DMR for 7/98 to Ohio EPA	0			15AUG98*	15AUG98*	2
5ACGW6M009	South Plume Opt - Commence Operations (CA)	0	01SEP98*	01SEP98*			2
5AFCW2M112	Submit NPDES DMR for 8/98 to Ohio EPA	0			15SEP98*	15SEP98*	2
Waste Management and Sites							
W8ABBAM03	TSCA PCB ANNUAL DOCUMENT LOG	0			02JUL98*	02JUL98*	3

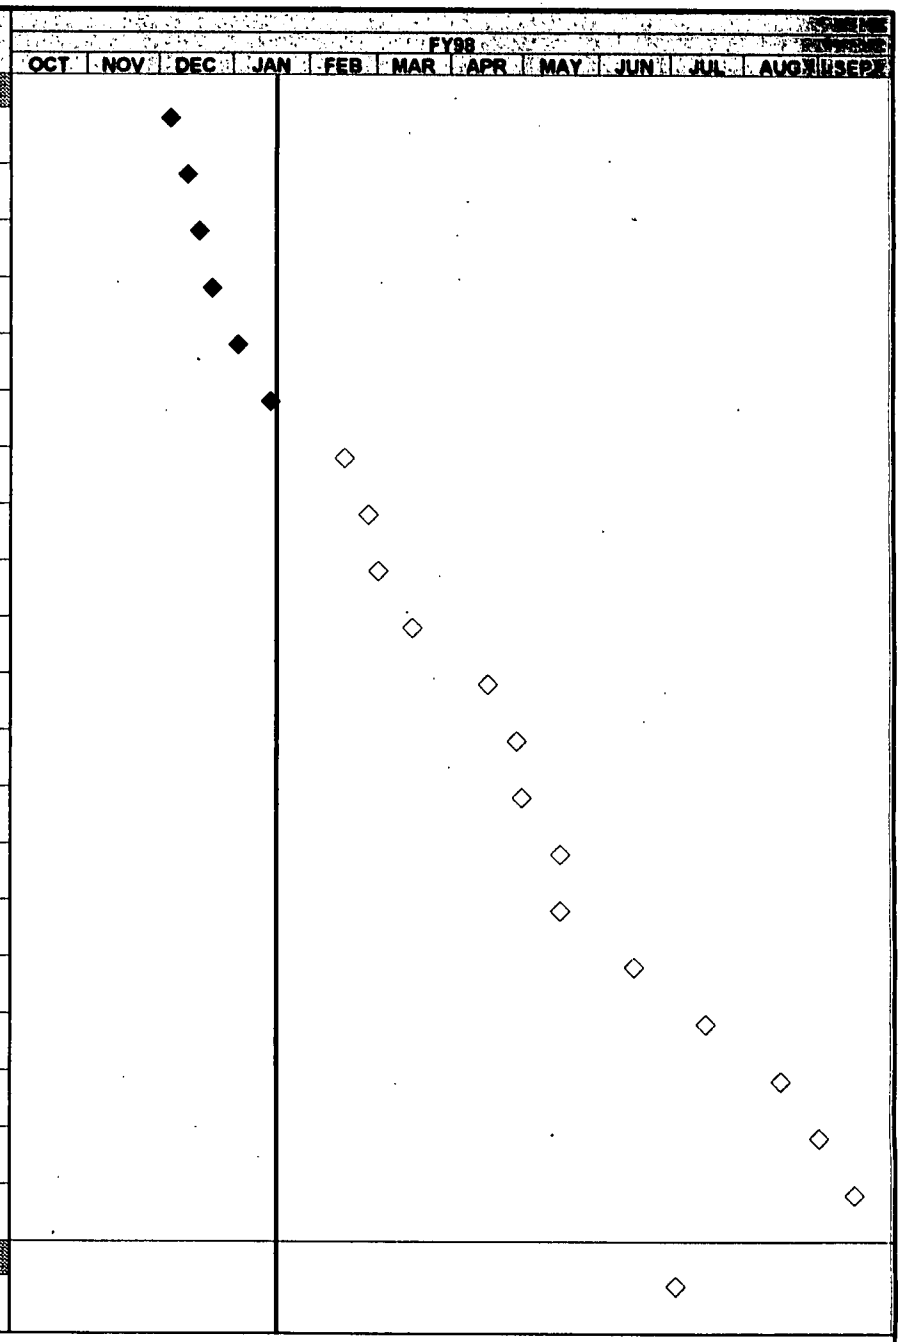

Project Start 01JAN95
Project Finish 30SEP08
Data Date 19JAN98
Run Date 04FEB98

Current Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Sheet 2 of 2

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY98)

FERNALD
Environmental Management Project

EA Milestones

FY 1999 - FY 2006

12256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
Facilities Closure & Demolition						
3D17E02M15	TO OU5: STP D&D - CONSTRUCTION FIELD	0			14OCT98	01MAY00
3D05E01M05	PLANT 5 D&D NOTICE TO PROCEED	0	16OCT98	02DEC98		
3WNGU022	SUBMIT QUARTERLY NATURAL GAS USAGE	0			13NOV98*	13NOV98*
3WNOX022	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			13NOV98*	13NOV98*
3D02M01001	PLANT 3 IMPLEMENTATION PLAN TO EPA	0	18NOV98	02DEC98*		
3D08E03M25	BP/WP D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			23NOV98	13FEB99*
3D17E03M25	STP D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			14DEC98	30JUN00*
3D07PL9M02	TO OU5: TH/PLANT 9 D&D - CONSTRUCTION FIELD COMP	0			31DEC98	17AUG99*
3WGDF022	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			16FEB99*	16FEB99*
3WHAM022	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			16FEB99*	16FEB99*
3WNGU024	SUBMIT QUARTERLY NATURAL GAS USAGE	0			16FEB99*	16FEB99*
3D02C01M01	PLANT 3 D&D NOTICE TO PROCEED	0	01APR99	15APR99		
3D06M01001	PLANT 6 COMPLEX IMPLEMENTATION PLAN TO	0	02APR99	02APR99*		
3WOEP022	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR99*	15APR99*
3WNGU026	SUBMIT QUARTERLY NATURAL GAS USAGE	0			14MAY99*	14MAY99*
3D07E03M25	TH/PLANT 9 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			24MAY99	16OCT99*
3WNES022	SUBMIT NESHAP ANNUAL REPORT	0			30JUN99*	30JUN99*
3D06C01M01	PLANT 6 D&D NOTICE TO PROCEED	0	01JUL99	20JUL99		
3D12M01001	EAST WAREHOUSE IMPLEMENTATION PLAN TO	0	16JUL99	16JUL99*		
3D03M01001	PLANT 2 COMPLEX IMPLEMENTATION PLAN TO	0	30JUL99	14AUG99*		
3WNGU028	SUBMIT QUARTERLY NATURAL GAS USAGE	0			13AUG99*	13AUG99*
3D11M01001	PLANT 8 COMPLEX IMPLEMENTATION PLAN TO	0	15SEP99	15SEP99*		
3D19M01001	PLANT 1 PHASE II IMPLEMENTATION PLAN TO	0	29SEP99	06OCT99*		

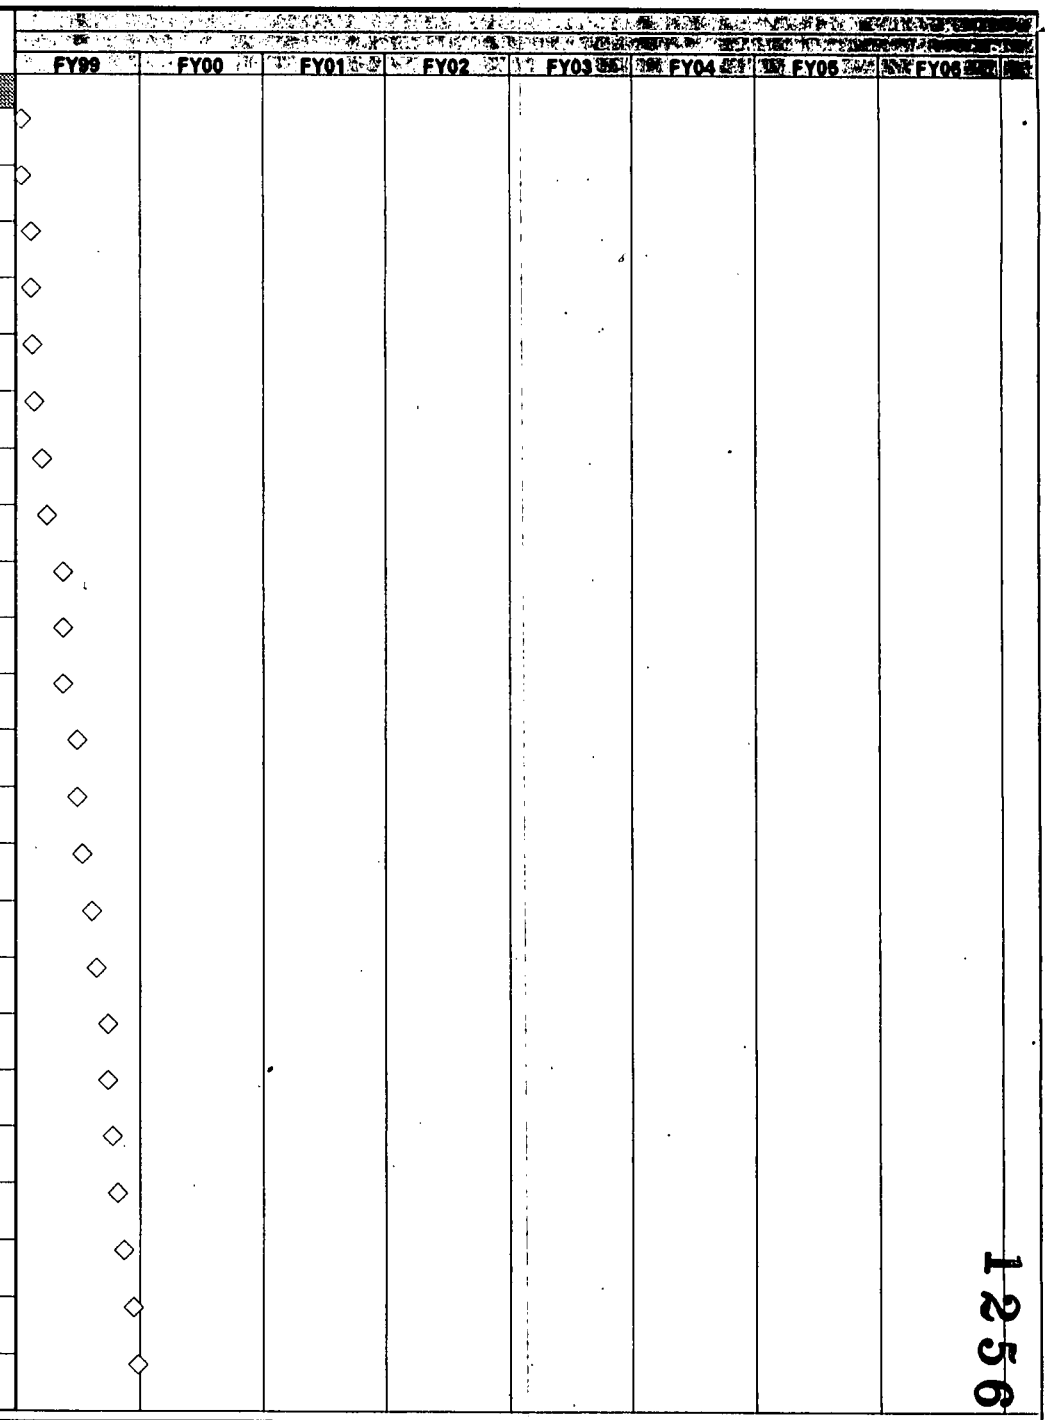

1256

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

FERNALD
Environmental Management Project

58

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
3D12C01M01	EAST WAREHOUSE D&D NOTICE TO PROCEED	0	14OCT99	06DEC99		
3D03C01M01	PLANT 2 D&D NOTICE TO PROCEED	0	28OCT99	21DEC99		
3WNGU032	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15NOV99*	15NOV99*
3WNOX032	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			15NOV99*	15NOV99*
3D11C01M01	PLANT 8 D&D NOTICE TO PROCEED	0	14DEC99	03FEB00		
3D20M01001	GENERAL SUMP COMP. IMPLEMENTATION PLN TO	0	15DEC99	20DEC99*		
3D09E02M15	MAINT/TANK FARM D&D - CONSTR FIELD COMPLETION	0			27DEC99	15JUN01
3D04M01001	PILOT PLANT COMPLEX IMPLEMENTATION PLN TO	0	13JAN00	17JAN00*		
3WGDF032	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			15FEB00*	15FEB00*
3WHAM032	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			15FEB00*	15FEB00*
3WNGU034	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15FEB00*	15FEB00*
3D09E03M25	MAINT/TANK FARM D&D - DRAFT CLOSEOUT REP TO	0			25FEB00	30SEP08
3D19C01M01	PLANT 1 PHASE II D&D NOTICE TO PROCEED	0	01APR00	13APR00		
3WOEP032	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			14APR00*	14APR00*
3D04C01M01	PILOT PLANT D&D NOTICE TO PROCEED	0	29APR00	07JUN00		
3WNGU036	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15MAY00*	15MAY00*
3D12E02M15	EAST WHSE D&D - CONSTRUCTION FIELD	0			22MAY00	02JUN00
3WNES032	SUBMIT NESHAP ANNUAL REPORT	0			30JUN00*	30JUN00*
3D12E03M25	EAST WHSE D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			19JUL00	31JUL00*
3WNGU038	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15AUG00*	15AUG00*
3D21M01001	LIQUID STOR COMPLEX IMPLEMENTATION PLN TO	0	30SEP00	04OCT00*		
3WNGU042	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15NOV00*	15NOV00*
3WNOX042	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			15NOV00*	15NOV00*

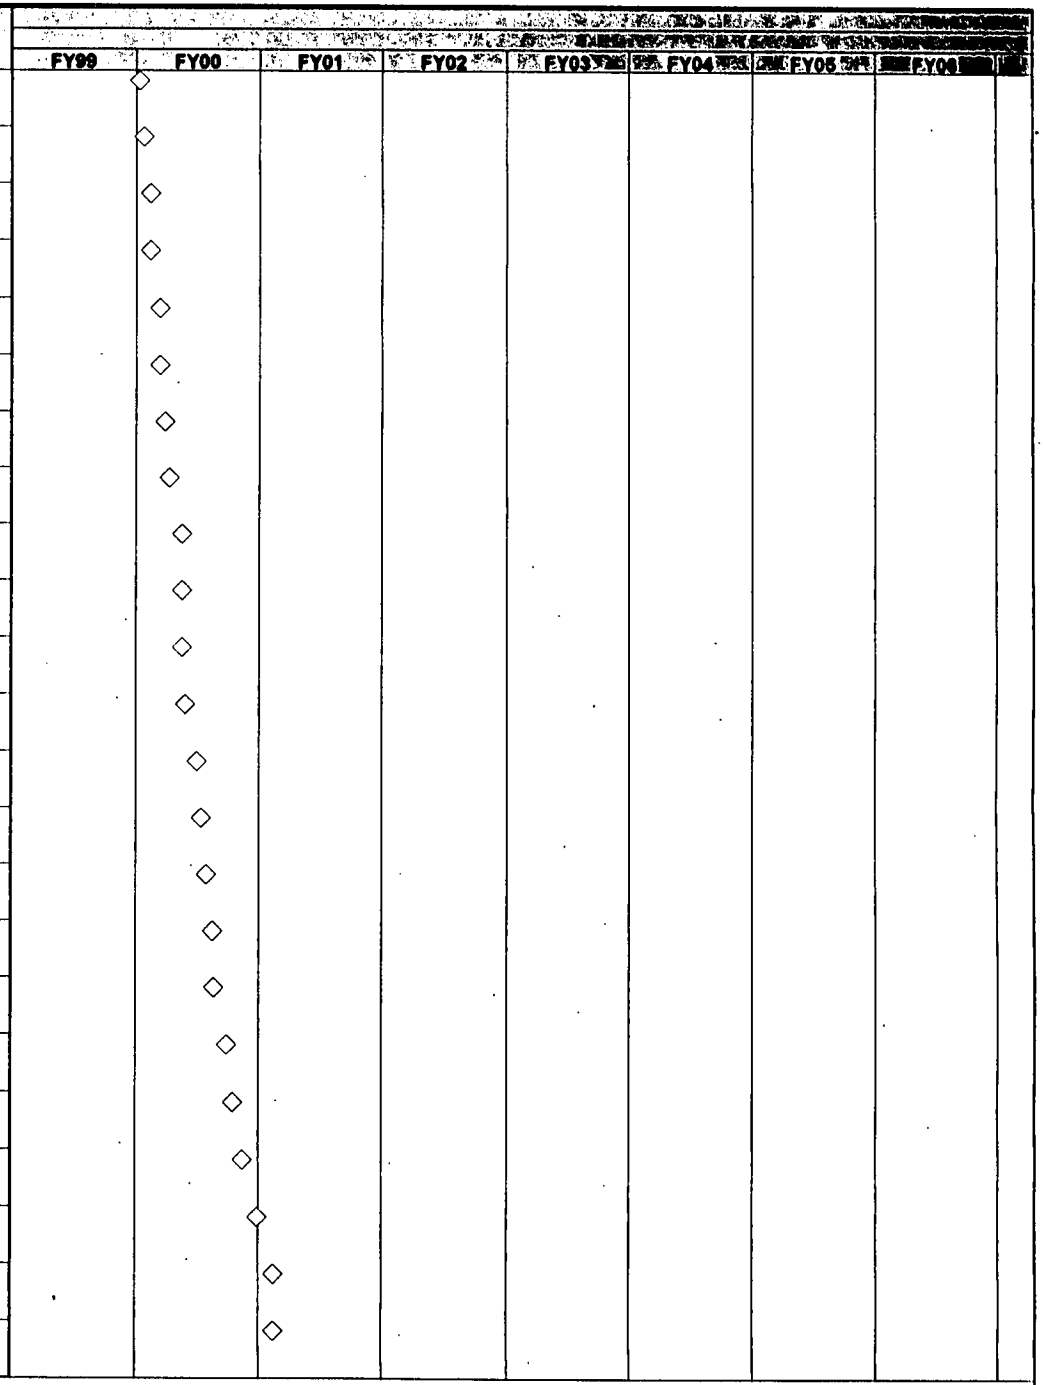

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

© Primavera Systems, Inc.

Early Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

FERNALD
Environmental Management Project

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
3D10M01001	ADMIN. COMPLEX IMPLEMENTATION PLN TO	0	12DEC00	18DEC00*		
3WGDF042	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			15FEB01*	15FEB01*
3WHAM042	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			15FEB01*	15FEB01*
3WNGU044	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15FEB01*	15FEB01*
3D02E02M15	PLANT 3 D&D - CONSTRUCTION FIELD	0			01MAR01	16MAR01
3D05C01M10	PLANT 5 D&D - CONSTRUCTION FIELD	0	28MAR01	12APR01		
3D16M01001	ELECTRICAL COMPLEX IMPLEMENTATION PLN TO	0	31MAR01	03APR01*		
3D19000301	TO OU5: PLANT 1 PHASE II D&D - CONSTR FIELD COMP	0	02APR01	12APR01		
3WOEP042	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			16APR01*	16APR01*
3D14M01001	LABORATORY COMPLEX IMPLEMENTATION PLN TO	0	28APR01	01MAY01*		
3WNGU046	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15MAY01*	15MAY01*
3D19E03M25	PLANT 1 PHASE II D&D - DRAFT CLOSE REP TO EPAS	0			25MAY01	07JUN01*
3D02E03M25	PLANT 3 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			31MAY01	15JUN01*
3D05C01M12	PLANT 5 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			28JUN01	13JUL01*
3WNES042	SUBMIT NESHAP ANNUAL REPORT	0			28JUN01*	28JUN01*
3D06M00100	TO OU5: PLANT 6 D&D - CONSTRUCTION FIELD	0			29JUN01	18JUL01
3WNGU048	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15AUG01*	15AUG01*
3D06E03M25	PLANT 6 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			28AUG01	14SEP01*
3D11E02M15	PLANT 8 D&D - CONSTRUCTION FIELD	0			12OCT01	25OCT01
3WNGU052	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15NOV01*	15NOV01*
3WNOX052	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			15NOV01*	15NOV01*
3D11E03M25	PLANT 8 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			14DEC01	31DEC01*
3D20C01M01	GENERAL SUMP D&D NOTICE TO PROCEED	0	05JAN02*	28JUN02		

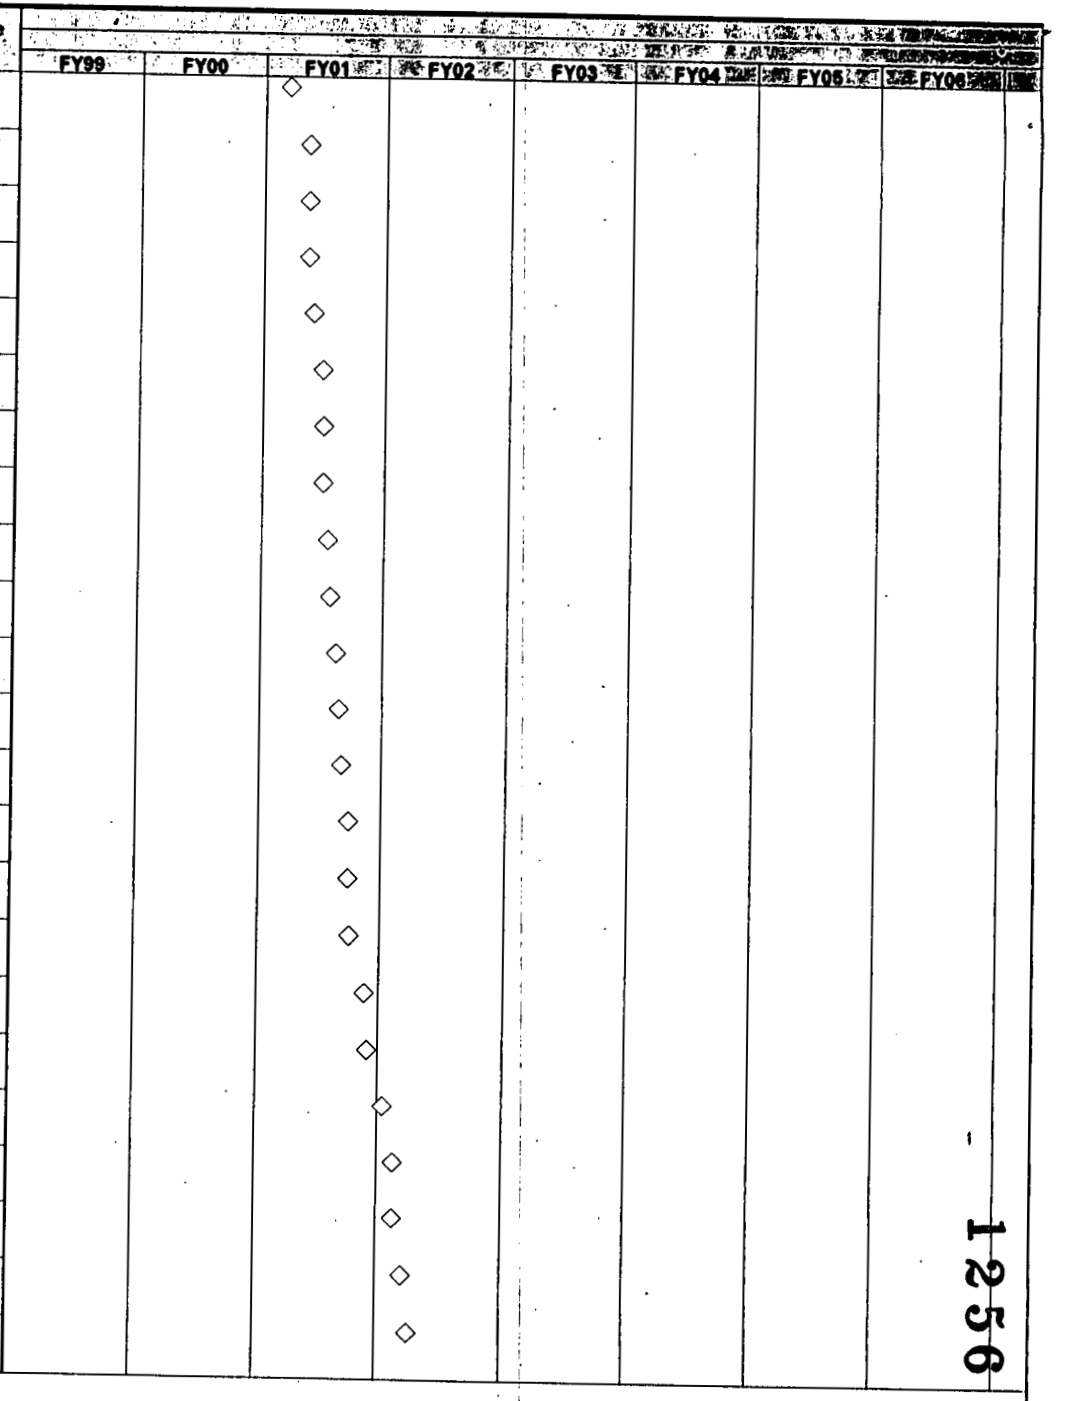

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Early Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

Sheet 3 of 6

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
3WGDF052	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			15FEB02*	15FEB02*
3WHAM052	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			15FEB02*	15FEB02*
3WNGU054	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15FEB02*	15FEB02*
3D21C01M01	LIQUID STORAGE D&D NOTICE TO PROCEED	0	02APR02	02MAY02		
3WOEP052	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR02*	15APR02*
3D10C01M01	ADMIN D&D NOTICE TO PROCEED	0	09MAY02	02JUL02		
3D14C01M01	CHEMICAL LAB D&D NOTICE TO PROCEED	0	09MAY02	01OCT02		
3WNGU056	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15MAY02*	15MAY02*
3D04000301	TO OU5: PILOT PLANT D&D - CONSTR FIELD COMPLETIO	0			17MAY02	04JUN02
3D03E02M15	PLANT 2 D&D - CONSTRUCTION FIELD	0			06JUN02	20JUN02
3WNES052	SUBMIT NESHAP ANNUAL REPORT	0			28JUN02*	28JUN02*
3D04E03M25	PILOT PLANT D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			16JUL02	31JUL02*
3D03E03M25	PLANT 2 D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			05AUG02	19AUG02*
3WNGU058	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15AUG02*	15AUG02*
3D21E02M15	LIQUID STG D&D - CONSTRUCTION FIELD	0			26SEP02	28OCT02
3WNGU062	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15NOV02*	15NOV02*
3WNOX062	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			15NOV02*	15NOV02*
3D21E03M25	LIQUID STG D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			25NOV02	31DEC02*
3DOU4M1001	OU4 COMPLEX IMPLEMENTATION PLAN TO	0	15JAN03*	06MAR07		
3WGDF062	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			14FEB03*	14FEB03*
3WHAM062	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			14FEB03*	14FEB03*
3WNGU064	SUBMIT QUARTERLY NATURAL GAS USAGE	0			14FEB03*	14FEB03*
3D20002000	TO OU5: GENERAL SUMP D&D - CONSTR FIELD COMPLETI	0			03APR03	25SEP03

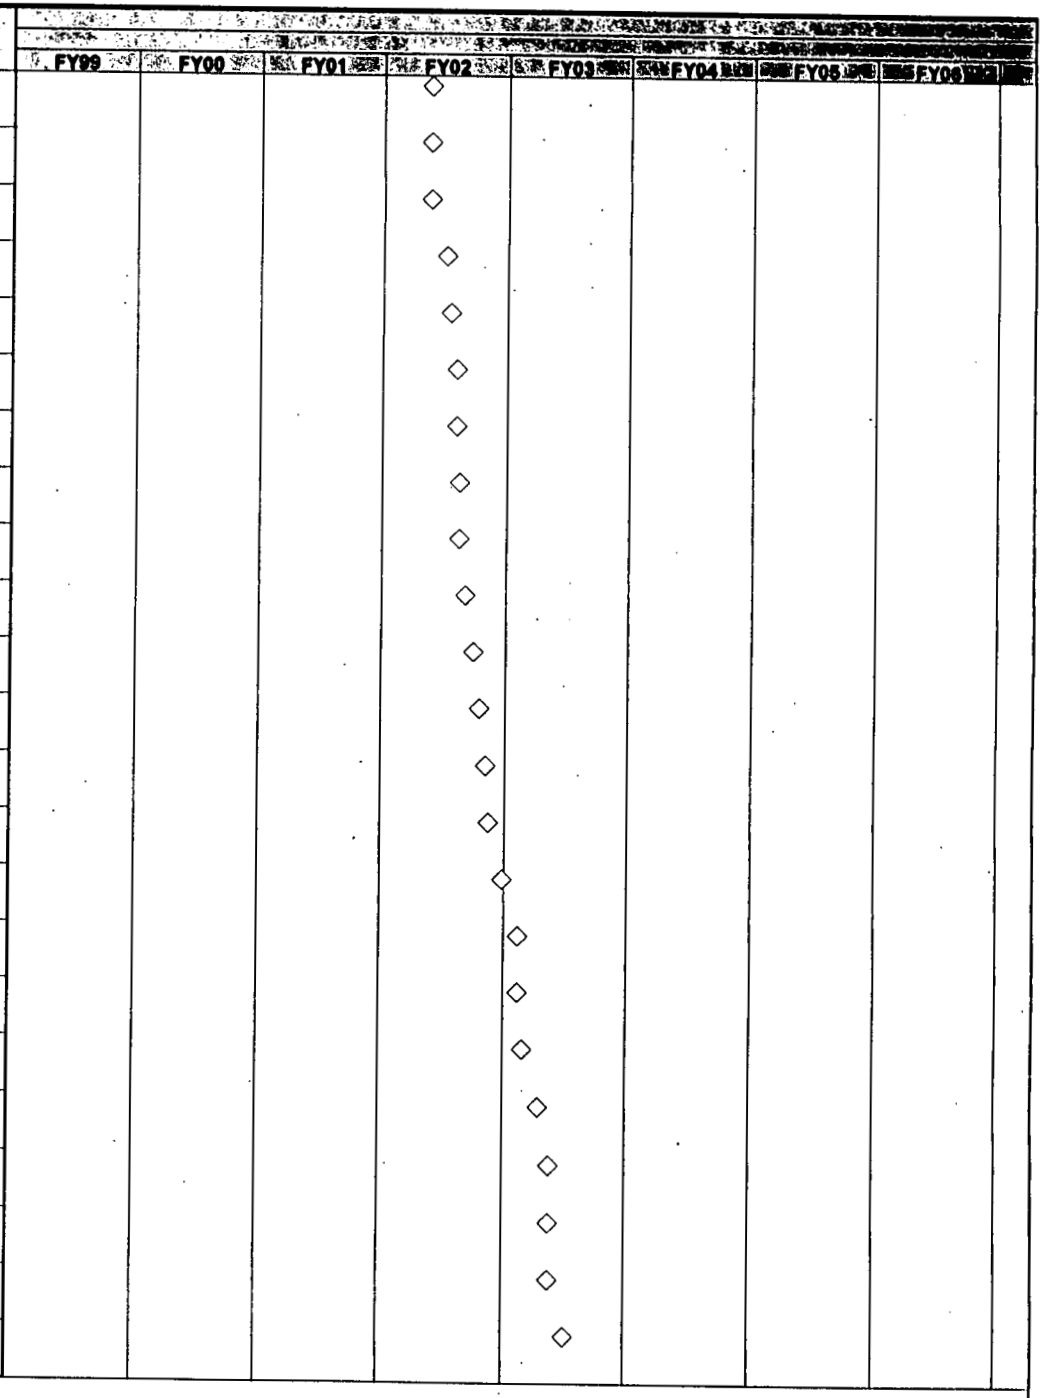

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Early Bar
Progress Bar
Critical Activity

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

FERNALD
Environmental Management Project

© Primavera Systems, Inc.

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
3WOEP062	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR03*	15APR03*
3D14E02M15	LAB D&D - CONSTRUCTION FIELD COMPLETION	0			07MAY03	29SEP03
3WNGU066	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15MAY03*	15MAY03*
3D20E03M25	GENERAL SUMP D&D - DRAFT CLOSEOUT REPORT TO EPA	0			05JUN03	26NOV03*
3WNES062	SUBMIT NESHAP ANNUAL REPORT	0			30JUN03*	30JUN03*
3D14E03M25	LAB D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			07JUL03	26NOV03*
3WNGU068	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15AUG03*	15AUG03*
3WNGU072	SUBMIT QUARTERLY NATURAL GAS USAGE	0			14NOV03*	14NOV03*
3WNOX072	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			14NOV03*	14NOV03*
3D10M00100	TO OU5: ADMIN D&D - CONSTRUCTION FIELD	0			06FEB04	31MAR04
3D0U1M1001	OU1 COMPLEX IMPLEMENTATION PLAN TO	0	11FEB04	11FEB04*		
3WGDF072	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			13FEB04*	13FEB04*
3WHAM072	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			13FEB04*	13FEB04*
3WNGU074	SUBMIT QUARTERLY NATURAL GAS USAGE	0			13FEB04*	13FEB04*
3D10E03M25	ADMIN D&D - DRAFT CLOSEOUT REPORT TO EPAs	0			06APR04	28MAY04*
3WOEP072	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR04*	15APR04*
3WNGU076	SUBMIT QUARTERLY NATURAL GAS USAGE	0			14MAY04*	14MAY04*
3WNES072	SUBMIT NESHAP ANNUAL REPORT	0			30JUN04*	30JUN04*
3WNGU078	SUBMIT QUARTERLY NATURAL GAS USAGE	0			16AUG04*	16AUG04*
3WNGU082	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15NOV04*	15NOV04*
3WNOX082	SUBMIT NITROGEN OXIDE EMISSION STATEMENT	0			15NOV04*	15NOV04*
3WGDF082	SUBMIT GASOLINE DISPENS FAC ANNUAL DELIV REPORT	0			15FEB05*	15FEB05*
3WHAM082	SUBMIT HAMILTON CO. D.E.S. EMISSION INVENTORY	0			15FEB05*	15FEB05*

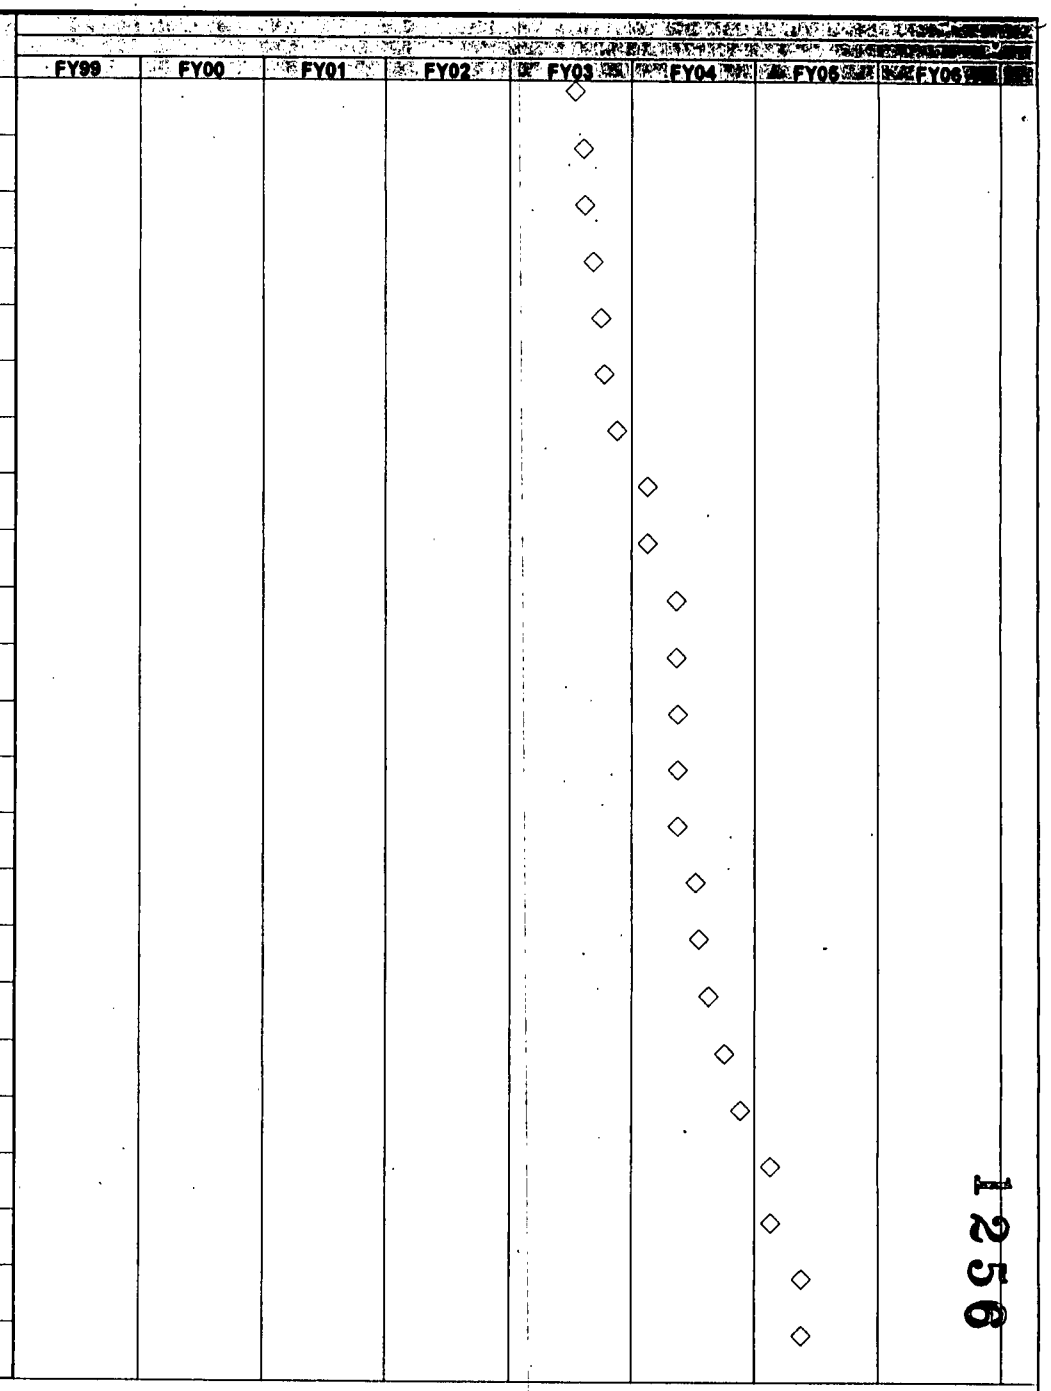

Project Start	01JAN95	Early Bar
Project Finish	30SEP08	Progress Bar
Data Date	19JAN98	Critical Activity
Run Date	04FEB98	

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

FERNALD Environmental Management Project

1256

Activity ID	Activity Description	Percent Complete	Forecast Start	Baseline Start	Forecast Finish	Baseline Finish
3WNGU084	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15FEB05*	15FEB05*
3WOEP082	SUBMIT OEPA AIR POLLTN CONTROL FEE EMISSION RPT	0			15APR05*	15APR05*
3WNGU086	SUBMIT QUARTERLY NATURAL GAS USAGE	0			16MAY05*	16MAY05*
3WNES082	SUBMIT NESHAP ANNUAL REPORT	0			30JUN05*	30JUN05*
3WNGU088	SUBMIT QUARTERLY NATURAL GAS USAGE	0			15AUG05*	15AUG05*
Soils and Water						
1CB0010055	INITIATION OF OPERATIONS	0	25FEB99	01MAR99*		
5AFCW1M003	ODNR Annual Water Withdrawal Report	0			01MAR99*	01MAR99*
5AFCW1M004	ODNR Annual Water Withdrawal Report	0			01MAR00*	01MAR00*
5CCSD1M030	AREA 3 AND LSP: PREFINAL DESIGN PKG TO EPA-L1	0			31MAR00	31MAR00*
5CCSDX4M01	Area 4/5: Submit Prefinal Design Pkg to EPA (L1)	0			15NOV00*	15NOV00*
5CCSDX6M01	Area 6,7,1-III,2-II-2,SWL:Submit Pre Dsgn to EPA	0			15JAN01*	15JAN01*
5AXR2M010	EPA receives Waste Stor Area Prelim Design Pkg	0	15JUN01	15JUN01*		
5AXR3M010	EPA receives Plant 6 Area Prelim Design Pkg	0	15AUG01	15AUG01*		
5AXR2M020	EPA receives Waste Stor Area Pre-Final Dsgn Pkg	0	30NOV01	30NOV01*		
5AXR3M020	EPA receives Plant 6 Area Pre-Final Design Pkg	0	30NOV01	30NOV01*		
1CB0010318	COMPLETION OF OPERATIONS	0			31MAY05*	31MAY05*
Waste Management and Sites						
W8ABBAM05	TSCA PCB ANNUAL DOCUMENT LOG	0			01JUL99*	01OCT99*
W8REGDD9C	CHEMICAL TREATMENT PROJ. - All Chem Treatmt Cmpl	0			28SEP01*	28SEP01*

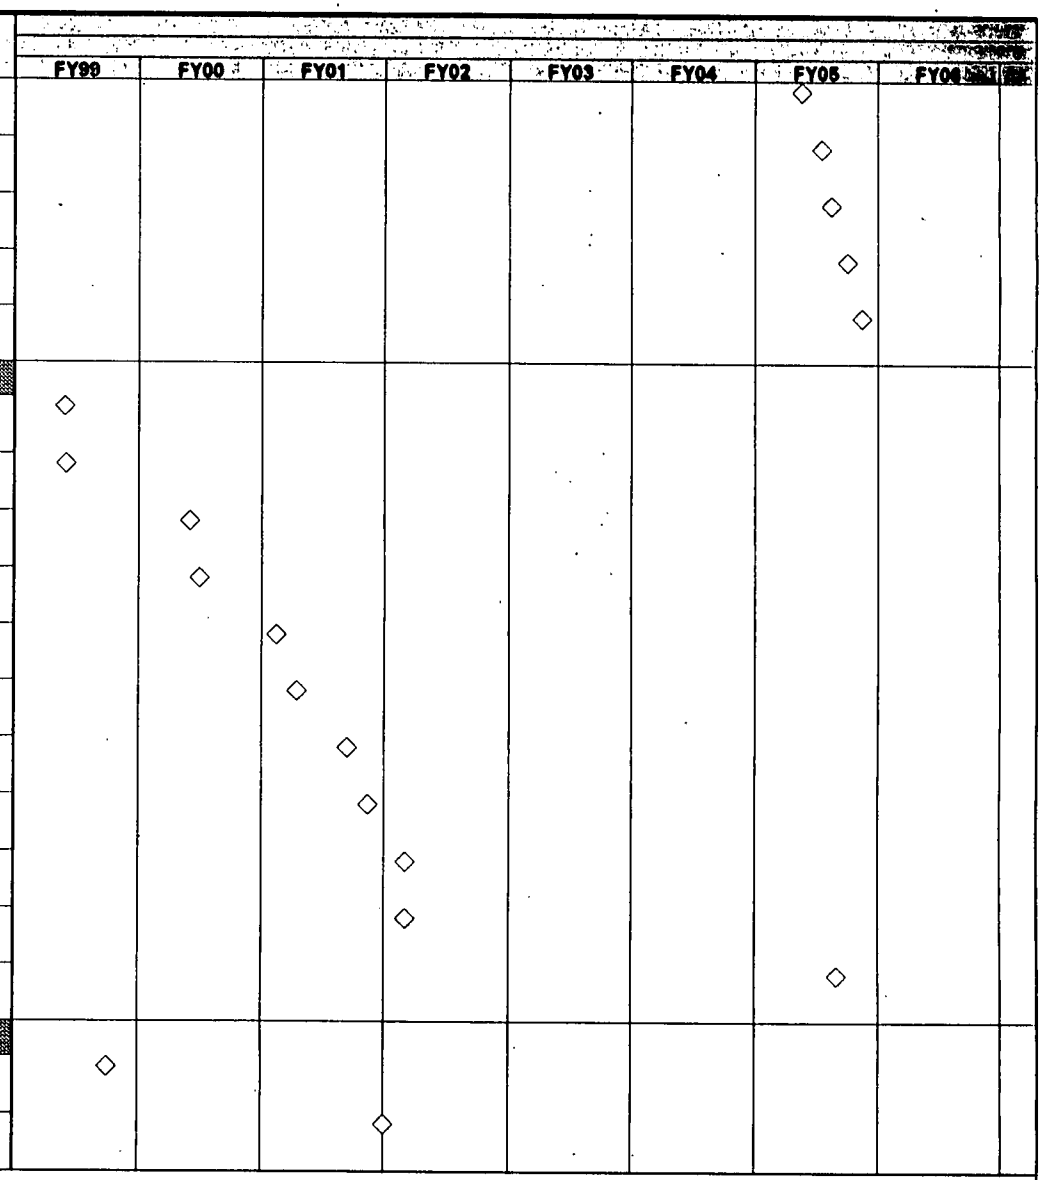

Project Start	01JAN95
Project Finish	30SEP08
Data Date	19JAN98
Run Date	04FEB98

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

C00F

Integrated Site Master Schedule

Status Through 01/18/98

EA Milestones (FY99 - 06)

FERNALD
Environmental Management Project

13
