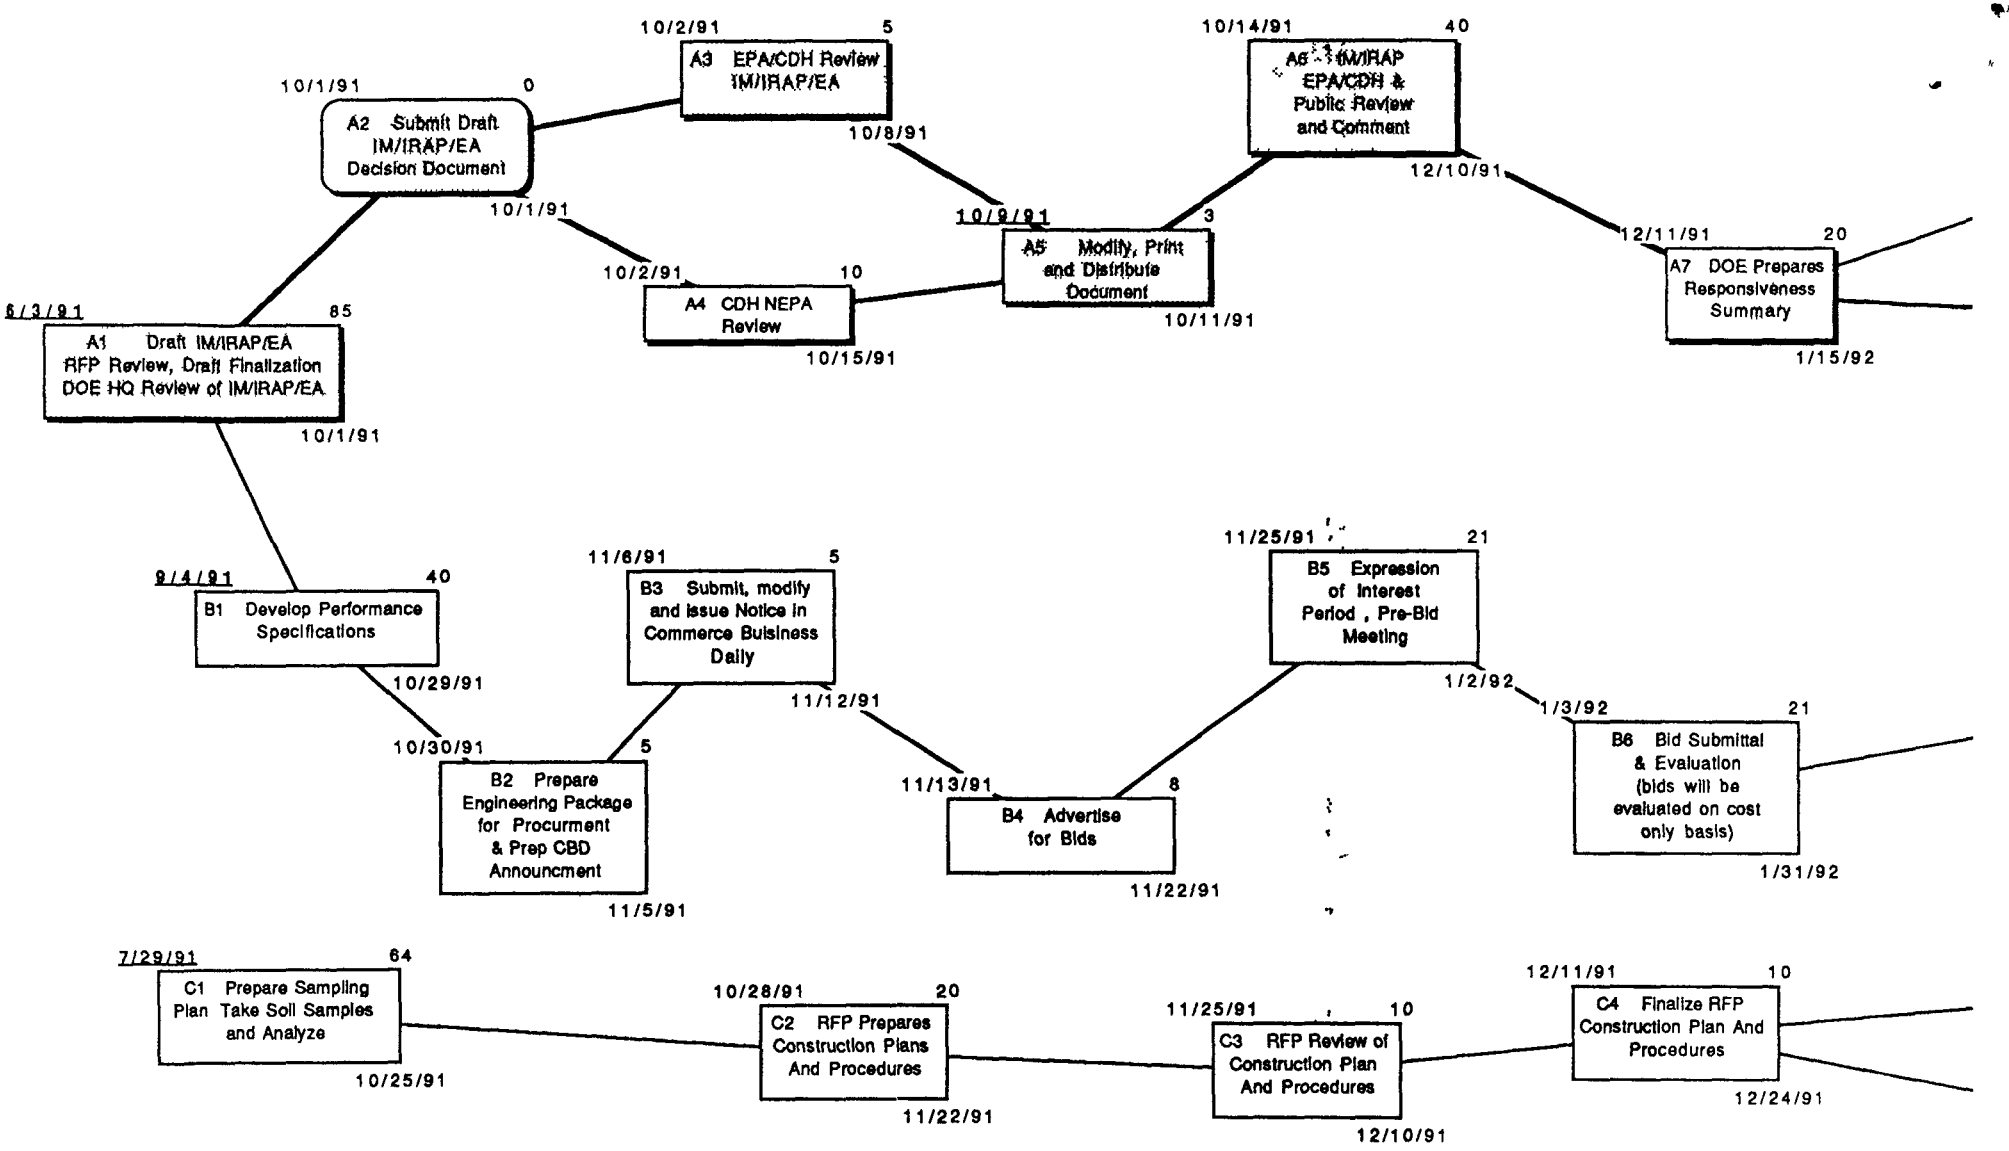

PROPOSED OU2 WOMAN CREEK SCHEDULE

8/6/91

NOTE Design & construction activities scheduled to start after completion of Task A1 assume DOE/RFO commitment to the collection/transport system described in the IRAP

ADMIN RECORD

A-OU02-000178

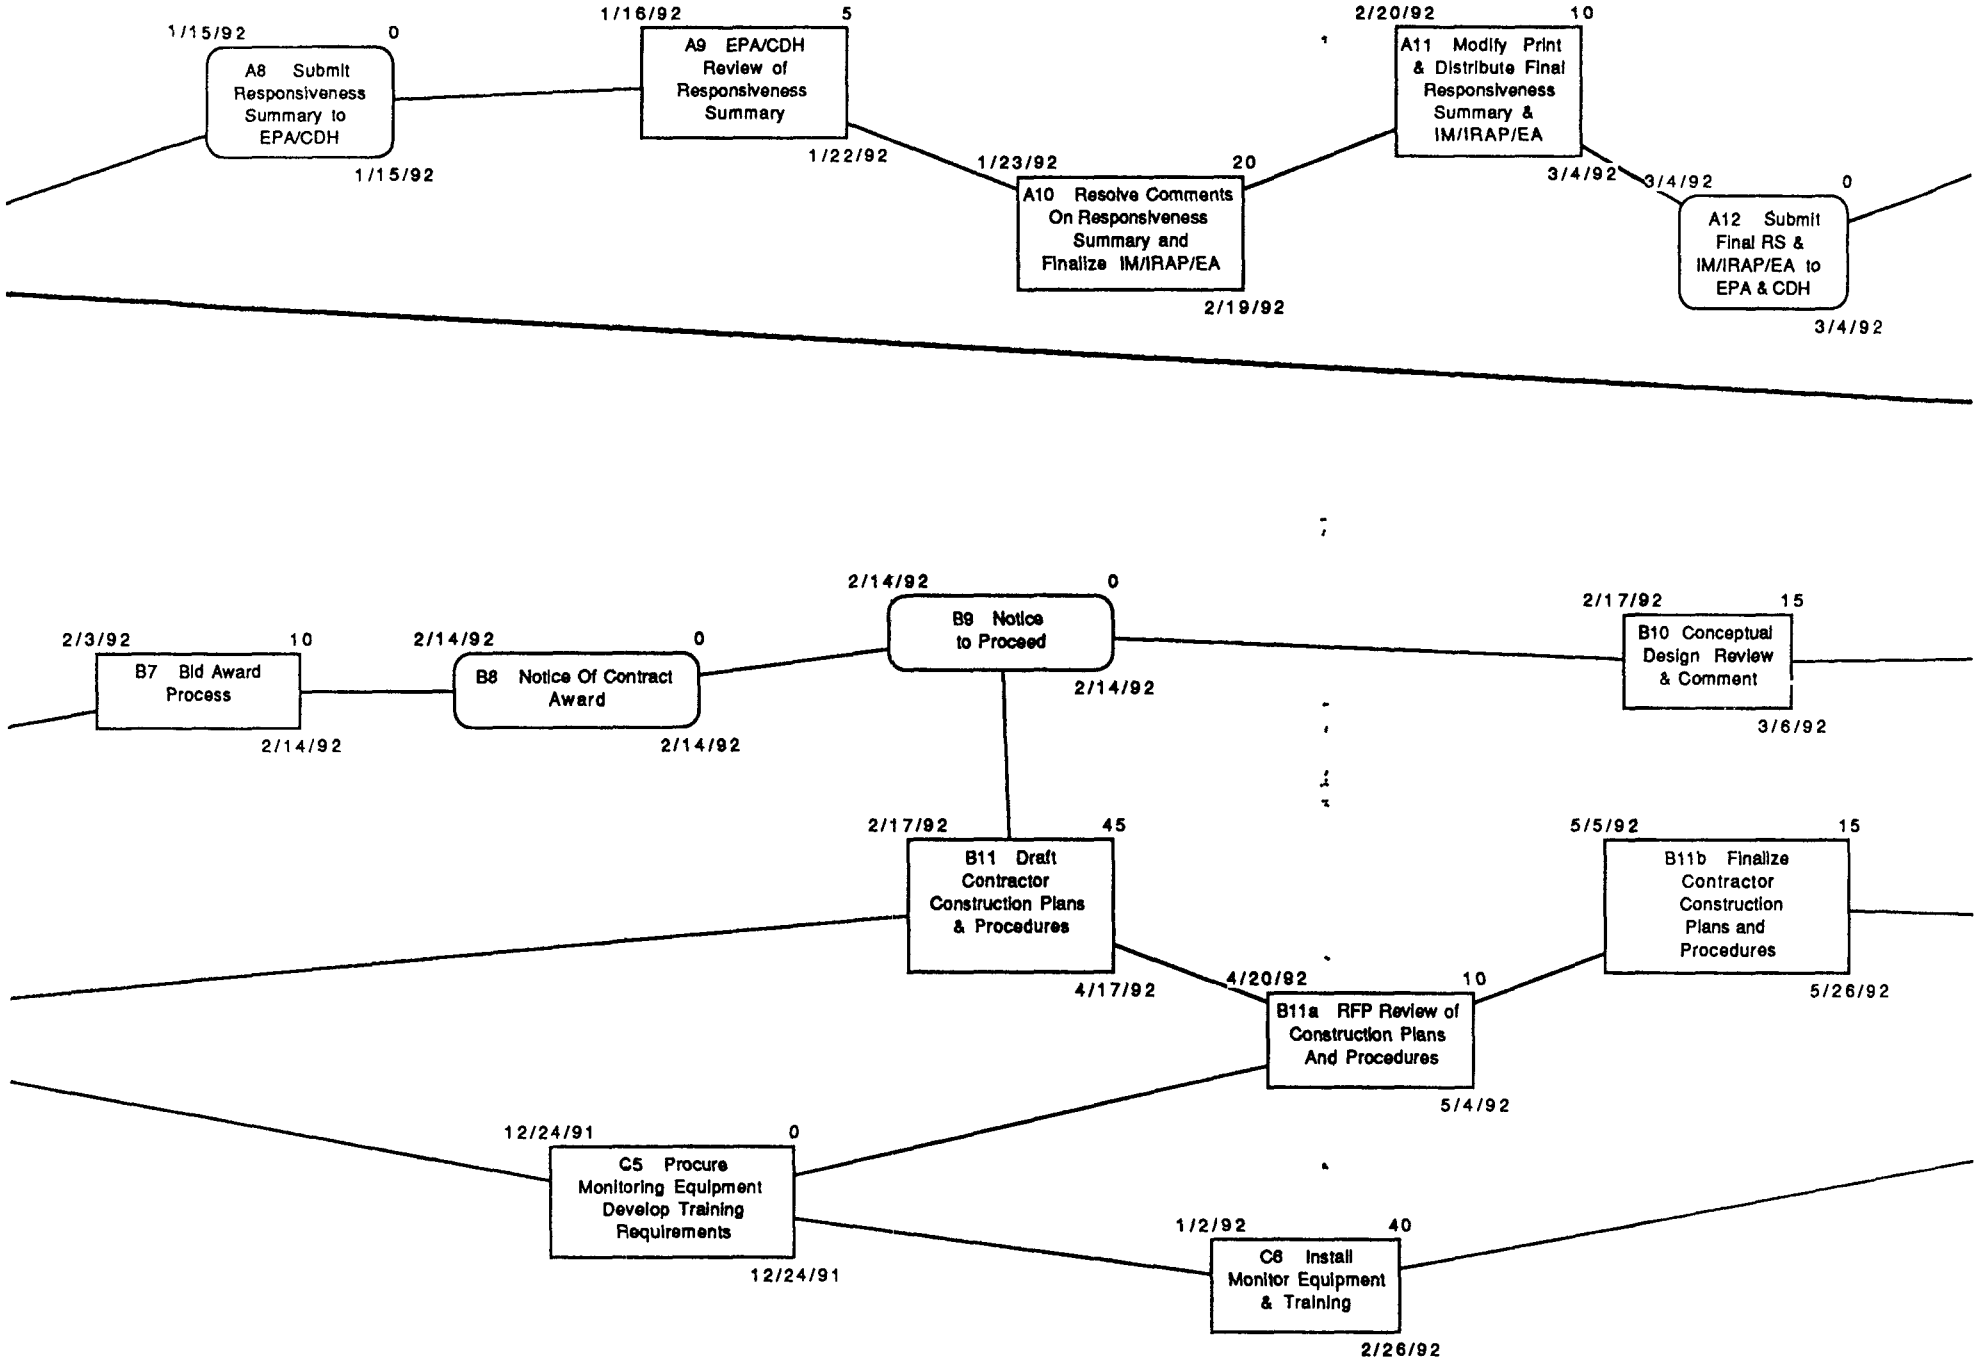
1/15/92
0
A8 Submit Responsiveness Summary to EPA/CDH
1/15/92
1/16/92
5
A9 EPA/CDH Review of Responsiveness Summary
1/22/92
1/23/92
20
A10 Resolve Comments On Responsiveness Summary and Finalize IM/IRAP/EA
2/19/92
2/20/92
10
A11 Modify Print & Distribute Final Responsiveness Summary & IM/IRAP/EA
3/4/92
3/4/92
0
A12 Submit Final RS & IM/IRAP/EA to EPA & CDH
3/4/92
2/3/92
10
B7 Bid Award Process
2/14/92
2/14/92
0
B8 Notice Of Contract Award
2/14/92
2/14/92
0
B9 Notice to Proceed
2/14/92
2/17/92
15
B10 Conceptual Design Review & Comment
3/6/92
2/17/92
45
B11 Draft Contractor Construction Plans & Procedures
4/17/92
5/5/92
15
B11b Finalize Contractor Construction Plans and Procedures
5/26/92
4/20/92
10
B11a RFP Review of Construction Plans And Procedures
5/4/92
12/24/91
0
C5 Procure Monitoring Equipment Develop Training Requirements
12/24/91
1/2/92
40
C6 Install Monitor Equipment & Training
2/26/92

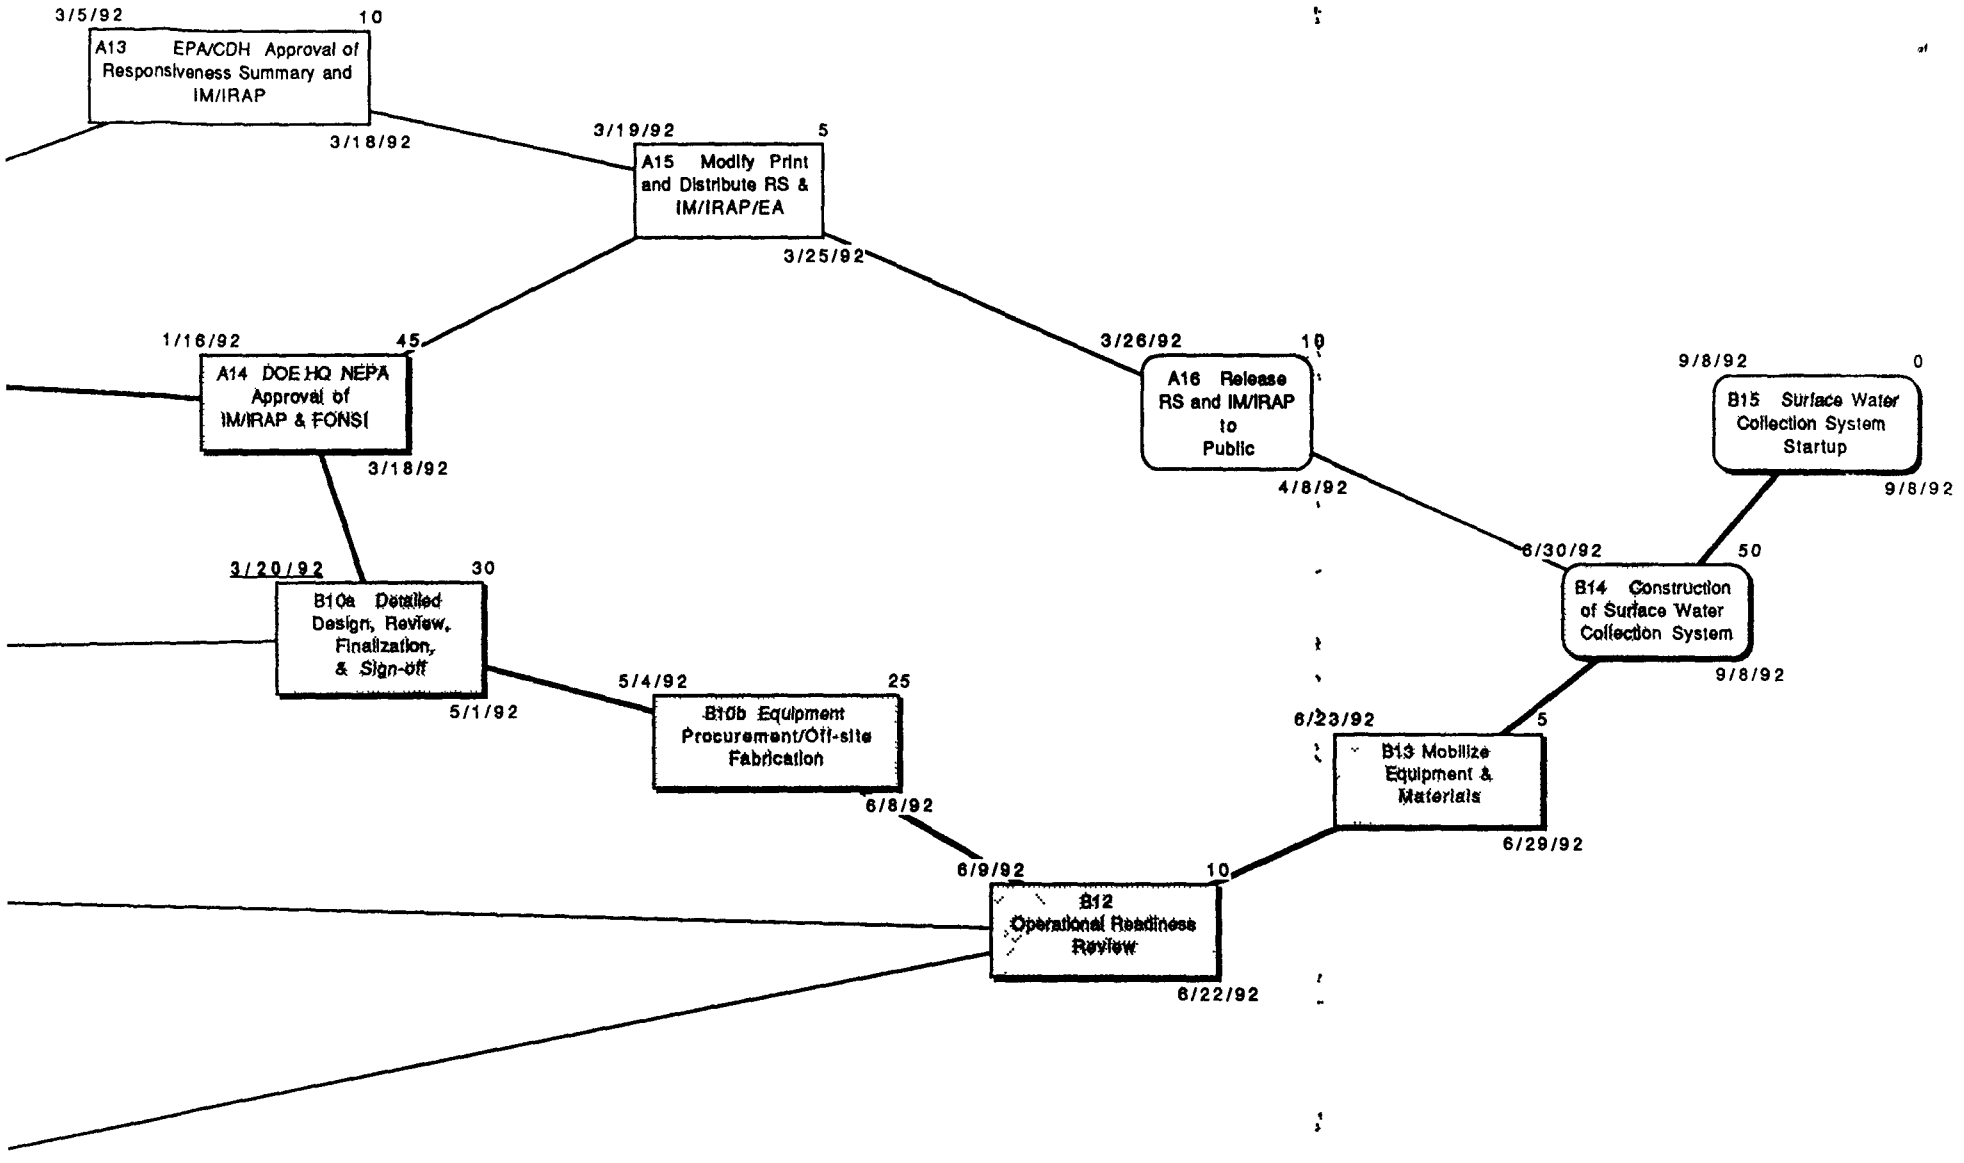
3/5/92
10
A13 EPA/CDH Approval of Responsiveness Summary and IM/IRAP
3/18/92
3/19/92
5
A15 Modify Print and Distribute RS & IM/IRAP/EA
3/25/92
1/16/92
45
A14 DOE HQ NEPA Approval of IM/IRAP & FONSI
3/18/92
3/26/92
10
A16 Release RS and IM/IRAP to Public
4/8/92
9/8/92
0
B15 Surface Water Collection System Startup
9/8/92
6/30/92
50
B14 Construction of Surface Water Collection System
9/8/92
3/20/92
30
B10a Detailed Design, Review, Finalization, & Sign-off
5/1/92
5/4/92
25
B10b Equipment Procurement/Off-site Fabrication
6/8/92
6/23/92
5
B13 Mobilize Equipment & Materials
6/29/92
6/9/92
10
B12 Operational Readiness Review
6/22/92
