Activity ID	Activity Description	Orig Dur	Baseline Start	Baseline Finish
FCE SNM Removal				
1FCEM20100	Unclassified Metal Shipment #1 - Make Ready	22	22JAN01	22FEB01
1FCEM20200	Unclassified Metal Shipment #2 - Make Ready	22	23FEB01	28MAR01
1FCEM20300	Unclassified Metal Shipment #3 - Make Ready	22	23FEB01	28MAR01
1FCEM20400	Unclassified Metal Shipment #4 - Make Ready	22	23FEB01	28MAR01
1FCEM20500	Unclassified Metal Shipment #5 - Make Ready	24	29MAR01	04MAY01
1FCEM20600	Unclassified Metal Shipment #6 - Make Ready	24	29MAR01	04MAY01
1FCEO30100	Unclassified Oxide Shipment #1 - Make Ready	24	07MAY01	13JUN01
1FCEO30200	Unclassified Oxide Shipment #2 - Make Ready	24	07MAY01	13JUN01
1FCEO30300	Unclassified Oxide Shipment #3 - Make Ready	21	14JUN01	17JUL01
1FCEO30400	Unclassified Oxide Shipment #4 - Make Ready	21	14JUN01	17JUL01
1FCEO30500	Unclassified Oxide Shipment #5 - Make Ready	22	18JUL01	21AUG01
1FCEO30600	Unclassified Oxide Shipment #6 - Make Ready	20	22AUG01	21SEP01
1FCEO30700	Unclassified Oxide Shipment #7 - Make Ready	20	22AUG01	21SEP01
1FCEO30800	Unclassified Oxide Shipment #8 - Make Ready	24	24SEP01	30OCT01
1FCEO30900	Unclassified Oxide Shipment #9 - Make Ready	24	24SEP01	30OCT01
1FCEO31000	Unclassified Oxide Shipment #10 - Make Ready	21	31OCT01	04DEC01
1FCEO31100	Unclassified Oxide Shipment #11 - Make Ready	21	05DEC01	09JAN02
1FCEO31200	Unclassified Oxide Shipment #12 - Make Ready	24	10JAN02	14FEB02
1FCEO31300	Unclassified Oxide Shipment #13 - Make Ready	24	10JAN02	14FEB02
1FCEO31400	Unclassified Oxide Shipment #14 - Make Ready	21	18FEB02	20MAR02
1FCEO31500	Unclassified Oxide Shipment #15 - Make Ready	22	21MAR02	23APR02
1FCEO31600	Unclassified Oxide Shipment #16 - Make Ready	22	21MAR02	23APR02
1FCEO31700	Unclassified Oxide Shipment #17 - Make Ready	22	21MAR02	23APR02
1FCEO31800	Unclassified Oxide Shipment #18 - Make Ready	22	24APR02	29MAY02
1FCEO31900	Unclassified Oxide Shipment #19 - Make Ready	22	24APR02	29MAY02
1FCEO32000	Unclassified Oxide Shipment #20 - Make Ready	22	30MAY02	02JUL02
1FCEO32100	Unclassified Oxide Shipment #21 - Make Ready	22	30MAY02	02JUL02
1FCEO32200	Unclassified Oxide Shipment #22 - Make Ready	22	30MAY02	02JUL02
1FCEO32300	Unclassified Oxide Shipment #23 - Make Ready	22	30MAY02	02JUL02
1FCEO32400	Unclassified Oxide Shipment #24 - Make Ready	22	03JUL02	07AUG02
1FCEO32500	Unclassified Oxide Shipment #25 - Make Ready	22	03JUL02	07AUG02
1FCEO32600	Unclassified Oxide Shipment #26 - Make Ready	22	03JUL02	07AUG02
1FCEO32700	Unclassified Oxide Shipment #27 - Make Ready	22	03JUL02	07AUG02
1FCEO32800	Unclassified Oxide Shipment #28 - Make Ready	22	08AUG02	11SEP02
1FCEO32900	Unclassified Oxide Shipment #29 - Make Ready	22	08AUG02	11SEP02
1FCEO33000	Unclassified Oxide Shipment #30 - Make Ready	22	08AUG02	11SEP02

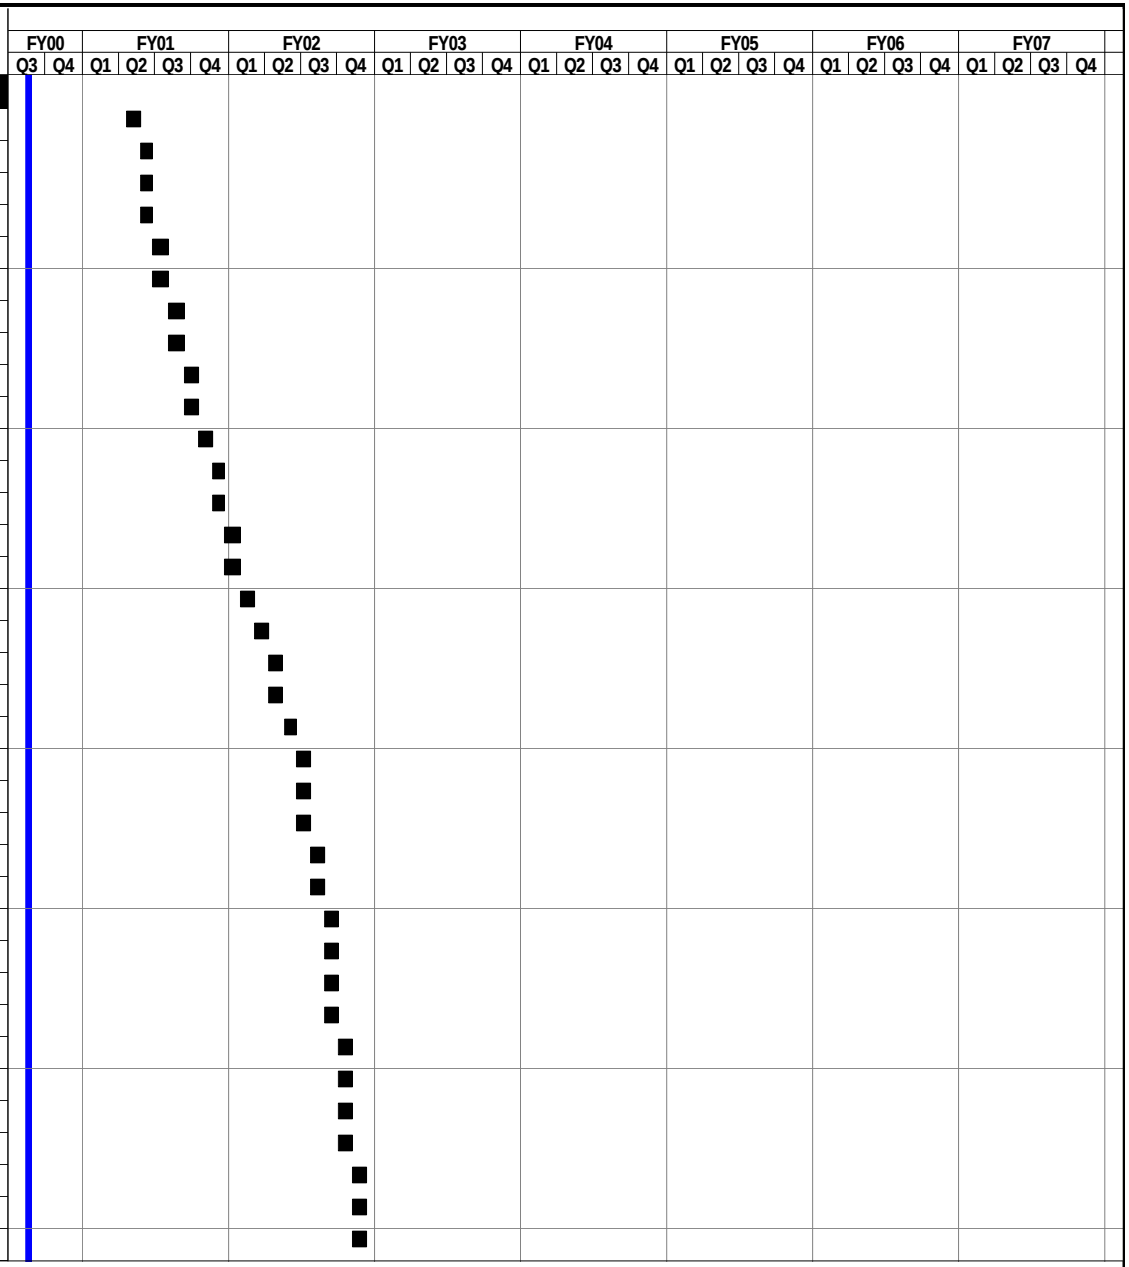

Start Date 01FEB99
Finish Date 14DEC06
Data Date 22MAY00
Run Date 26JUN00 15:33

© Primavera Systems, Inc.

CPBB

ROCKY FLATS
CLOSURE PROJECT BASELINE

Cost Account Critical Path

KAISER•HILL COMPANY

CLOSURE 2006 KAISER-HILL ROCKY FLATS CLOSURE PROJECT

Activity ID	Activity Description	Orig Dur	Baseline Start	Baseline Finish
FCE SNM Removal				
1FCEO33100	Unclassified Oxide Shipment #31 - Make Ready	22	08AUG02	11SEP02
1FCEO33200	Unclassified Oxide Shipment #32 - Make Ready	22	12SEP02	16OCT02
1FCEO33300	Unclassified Oxide Shipment #33 - Make Ready	22	12SEP02	16OCT02
1FCEO33400	Unclassified Oxide Shipment #34 - Make Ready	22	12SEP02	16OCT02
1FCEO33500	Unclassified Oxide Shipment #35 - Make Ready	22	12SEP02	16OCT02
1FCEO33600	Unclassified Oxide Shipment #36 - Make Ready	22	17OCT02	19NOV02
1FCEO33700	Unclassified Oxide Shipment #37 - Make Ready	22	17OCT02	19NOV02
1FCEO33800	Unclassified Oxide Shipment #38 - Make Ready	22	17OCT02	19NOV02
1FCEO33900	Unclassified Oxide Shipment #39 - Make Ready	22	17OCT02	19NOV02
1FCEO34000	Unclassified Oxide Shipment #40 - Make Ready	22	20NOV02	27DEC02
1FCEO34100	Unclassified Oxide Shipment #41 - Make Ready	22	20NOV02	27DEC02
1FCEO34200	Unclassified Oxide Shipment #42 - Make Ready	22	20NOV02	27DEC02
1FCEO34300	Unclassified Oxide Shipment #43 - Make Ready	22	20NOV02	27DEC02
1FCEO34400	Unclassified Oxide Shipment #44 - Make Ready	22	30DEC02	03FEB03
1FCEO34500	Unclassified Oxide Shipment #45 - Make Ready	22	30DEC02	03FEB03
1FCEO34600	Unclassified Oxide Shipment #46 - Make Ready	22	30DEC02	03FEB03
1FCEO34700	Unclassified Oxide Shipment #47 - Make Ready	22	30DEC02	03FEB03
1FCEO34800	Unclassified Oxide Shipment #48 - Make Ready	22	04FEB03	07MAR03
1FCEO34900	Unclassified Oxide Shipment #49 - Make Ready	22	04FEB03	07MAR03
1FCEO35000	Unclassified Oxide Shipment #50 - Make Ready	22	04FEB03	07MAR03
1FCEO35100	Unclassified Oxide Shipment #51 - Make Ready	22	04FEB03	07MAR03
1FCEO35200	Unclassified Oxide Shipment #52 - Make Ready	14	10MAR03	31MAR03
1FCEO35300	Unclassified Oxide Shipment #53 - Make Ready	14	10MAR03	31MAR03
1FCEO35400	Unclassified Oxide Shipment #54 - Make Ready	14	10MAR03	31MAR03
1FCEO35500	Unclassified Oxide Shipment #55 - Make Ready	14	10MAR03	31MAR03

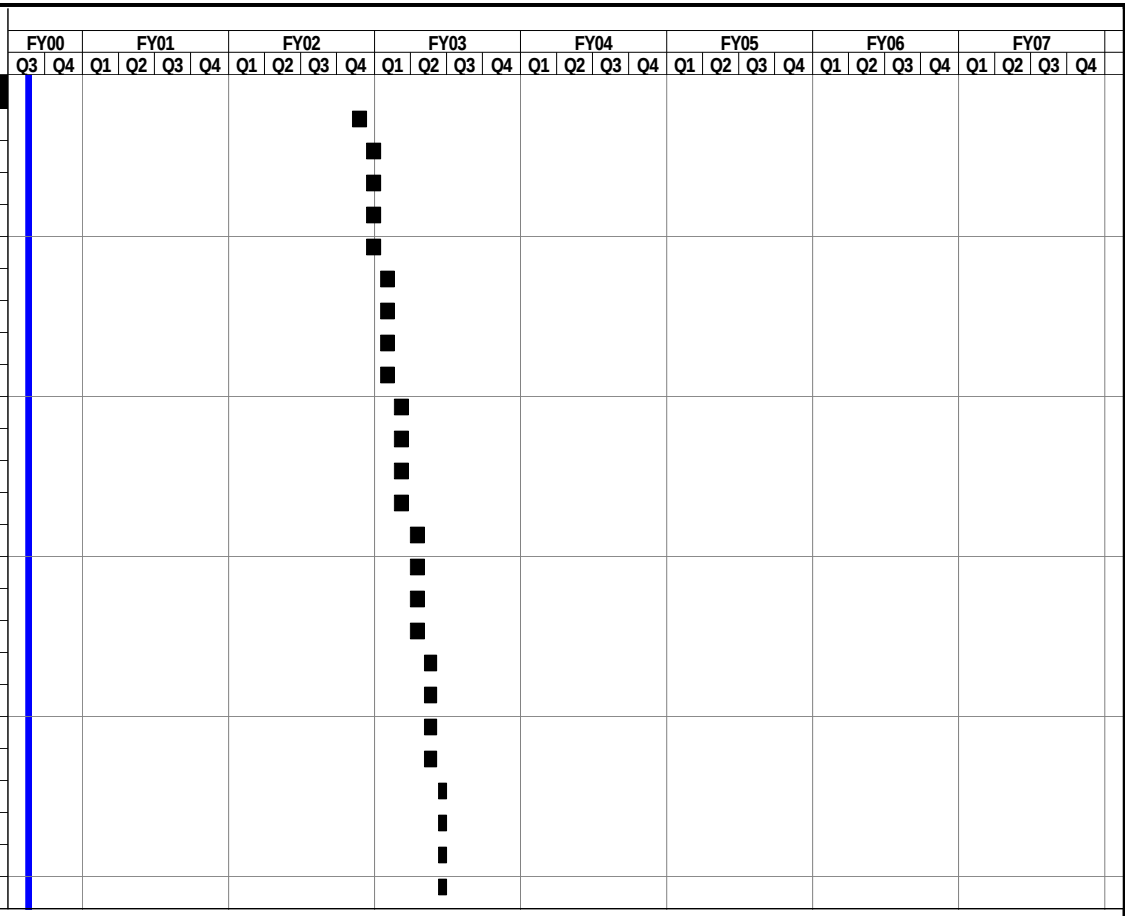

Start Date	01FEB99
Finish Date	14DEC06
Data Date	22MAY00
Run Date	26JUN00 15:33

© Primavera Systems, Inc.

CPBB

Sheet 2 of 2

ROCKY FLATS
CLOSURE PROJECT BASELINE

Cost Account Critical Path

KAISER•HILL COMPANY

CLOSURE 2006 KAISER-HILL ROCKY FLATS CLOSURE PROJECT
