

CORRES. CONTROL  
OUTGOING LTR NO

89 RF 0613

DIST.

LTR

Rocky Flats Plant  
Aerospace Operations  
Rockwell International Corporation  
P.O. Box 464  
Golden, Colorado 80402-0464  
(303) 966-7000



Rockwell  
International

Contractor to U.S. Department of Energy

89-RF-0613

Albert E. Whiteman  
Area Manager  
DOE, RFAO

SCHEDULE FOR INTERIM REMEDIAL ACTION FOR THE HIGH PRIORITY SITES  
(881 HILLSIDE)

Attached is the present accelerated schedule from Facilities Project Management for the interim remedial action on the 881 Hillside. As you know, the critical path is dependent on DOE-HQ issuing a Finding Of No Significant Impact (FONSI) on the Environmental Assessment (EA). The schedule reflects issuing the FONSI by May 1, 1989, which will allow procurement in time for trenching and construction to take place in the dry summer months. The treatment system would be operational in January, 1990. If the FONSI is not issued by May 1, 1989, the schedule will expand as it is delayed to compensate for adverse weather conditions, perhaps delaying treatment for another year.

In order to expedite the EA review process, time commitments for comments/approvals from ALO and HQ are appropriate. Connie Soden has been RFAO's primary contact in ALO. HQ review will be in the Office of NEPA Compliance (EH-25) which is directed by Carol Borgstrom, who reports to Ray Berube (EH-20). To our knowledge, contact with EH-25 on this issue has not been initiated. According to their guidance at the NEPA Compliance Conference in October, 1988, EH-25 welcomes informal drafts and forewarning of critical issues; we should be taking advantage of that mechanism to expedite their review, and request time commitments from them.

SANCHINI, D. J. ☒  
BADER, C. P. ☐  
ERFURDT, R. J. ☐  
HEINTZ, E. R. ☐  
HOOD, R. C. ☐  
IDEKER, E. H. ☐  
KINZER, J. E. ☐  
KIRBY, W. A. ☐  
MCNETT, J. F. ☐  
MEYERS, G. W. ☐  
ROECKER, J. H. ☐  
SHANNON, W. M. ☐  
SMITH, R. E. ☐  
WESTON, W. F. ☒  
WOZNAK, B. D. ☐  
YOUNG, E. R. ☐  
  
BETCHER, D. H. ☐  
CARNIVAL, G. J. ☐  
FERRERA, D. W. ☐  
HARMAN, L. K. ☐  
HEBERT, J. L. ☐  
HOEY, J. B. ☐  
HOFFMAN, R. B. ☐  
KLAMANN, R. L. ☐  
KRIEG, D. M. ☐  
LOUDENBURG, G. E. ☐  
MCKINLEY, K. B. ☒  
NAIMON, E. R. ☐  
NEWBY, R. L. ☐  
TURNER, H. L. ☐  
VELASQUEZ, R. N. ☐  
RICK, L. S. O. ☒  
REINGARD ☒  
  
CORRES. CONTROL ☒  
  
CLASSIFICATION  
UNCLASSIFIED ☒  
CONFIDENTIAL ☐  
SECRET ☐

AUTH. CLASSIFIER SIG

*BKG*

DATE *2-17-89*  
IN REPLY TO LTR NO.

Dominick J. Sanchini  
President

Orig. & 1 cc - A. E. Whiteman  
Enc.

\*REVIEWED FOR CLASSIFICATION

By R. B. Hoffman

Date *6-19-90*

REVIEWED FOR CLASSIFICATION/UCM

By *George H. Setlock*

Date *6/15/90*

ADMIN RECORD


A-OU01-000023

*2-17-89*  
*Shirley*  
*Please call*  
*when*  
*signed -*  
*will pick*  
*up for DOE*  
*Rec*

# 986147 - REMEDIAL ACTION 881 HILLSIDE

1101 ENGINEERING - UV CONSTR. PKB. 8 D  
 1102 ENGINEERING - ION EXCH. BYS. (S.O.M.) 8 D  
 1103 EXPD. START - BOA 3 D  
 1104 BOA TITLE I/II DESIGN 49 D  
 1105 TITLE II REVIEW 20 D  
 1106 CONSTR. PKB. ISSUE 9 D  
 1107 DIVERSION STRUCTURE CONST. PKB. 25 D  
 2101 PROCUREMENT - SOLICITATION TO AWARD 50 D  
 2102 UV & ION EXCH. DELIVERY 58 D  
 2103 TANK DEL. 82 D  
 3104 CONSTRUCTION PP (DIVERSION STRUCT. BID - AWARD) 58 D  
 3105 CONSTRUCTION PP (DIVERSION STRUCT. CONSTR.) 141 D  
 3106 CONSTRUCTION PP (DIVERSION STRUCT. TEST) 9 D

Legend  
 EMERGENCY CPM ☐

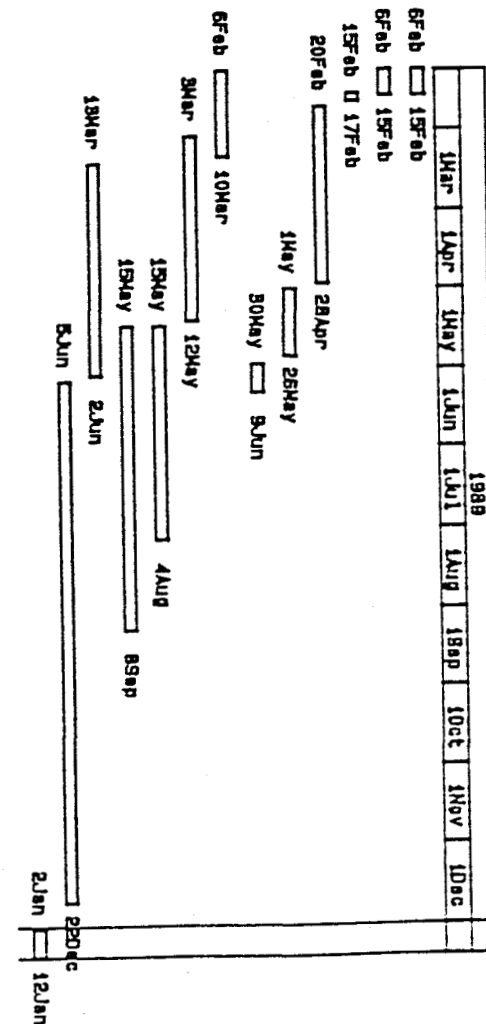

Project: 986147 986147-B.DWB Date: 16Feb89 R: 12  
 REMEDIAL ACTION 881 HILLSIDE  
 Page: 1 Drawn by GRIFFIN Graphics

REVIEWED FOR CLASSIFICATION  
 By R. B. Hoffman  
 Date 4-19-90

NO COMMENT
