

CORRES CONTROL

39 0613



Rocky Flats Plant
Aerospace Operations
Rockwell International Corporation
P O Box 484
Golden Colorado 80402-0464
(303) 966-7000

Rockwell
International

Contractor to U S Department of Energy

FEB 23 1989

89 RF 0613

Albert E Whiteman
Area Manager
DOE RFAO

SCHEDULE FOR INTERIM REMEDIAL ACTION FOR THE HIGH PRIORITY SITES
(881 HILLSIDE)

Attached is the present accelerated schedule from Facilities Project Management for the interim remedial action on the 881 Hillside. As you know the critical path is dependent on DOE HQ issuing a Finding Of No Significant Impact (FONSI) on the Environmental Assessment (EA). The schedule reflects issuing the FONSI by May 1 1989 which will allow procurement in time for trenching and construction to take place in the dry summer months. The treatment system would be operational in January 1990. If the FONSI is not issued by May 1 1989 the schedule will expand as it is delayed to compensate for adverse weather conditions perhaps delaying treatment for another year.

In order to expedite the EA review process time commitments for comments/approvals from ALO and HQ are appropriate. Connie Soden has been RFAO's primary contact in ALO. HQ review will be in the Office of NEPA Compliance (EH 25) which is directed by Carol Borgstrom who reports to Ray Berube (EH 20). To our knowledge contact with EH 25 on this issue has not been initiated. According to their guidance at the NEPA Compliance Conference in October 1988 EH 25 welcomes informal drafts and forewarning of critical issues we should be taking advantage of that mechanism to expedite their review and request time commitments from them.

Dominick J Sanchini
President

Orig & 1 cc A E Whiteman
Enc

| | |
|----------------|---|
| DST | |
| SANCHINI D | X |
| BADER C P | |
| ERFURDT | |
| E ZER | |
| HOOD R C | |
| DEERE | |
| KINZER J E | |
| KIRBY W | |
| McNETT J F | |
| MEYERS G W | |
| ROECKER J H | |
| SHANNON W M | |
| SMITH R E | |
| WESTON W F | X |
| WOZNIAK B D | |
| YOUNG R | |
| BETCHER D H | |
| CARNV L G J | |
| FERRER D W | |
| HARM N L K | |
| HEBERT J L | |
| OEY B | |
| OFFM N R B | |
| LAMAN R L | |
| KRIEG D M | |
| LOUDENBURG G E | |
| McK L E K B | X |
| NAIMON E R | |
| NEWBY R L | |
| TURNER | |
| ELASQUEZ R N | |
| FRISK I S D | X |
| GREENGARD | X |
| CORRES CONTROL | |
| CLASSIF CATIO | |
| UNCLASSIF ED | X |
| CONF DENT L | |
| SECRET | |

AUTH CLASS FERS G
DATE 2-17-89
NREP TO TR O

DEC
LTP P O L S
KBM - [initials]
WFWA - [initials]


LWOF/ [initials]
RF 76 R

ADMIN RECORD

REVIEWED FOR CLASSIFICATION/UCNI
BY G T Ostdiek 672
DATE 7-12-93

A-QU01-000549

986147 - REMEDIAL ACTION 881 HILLSIDE

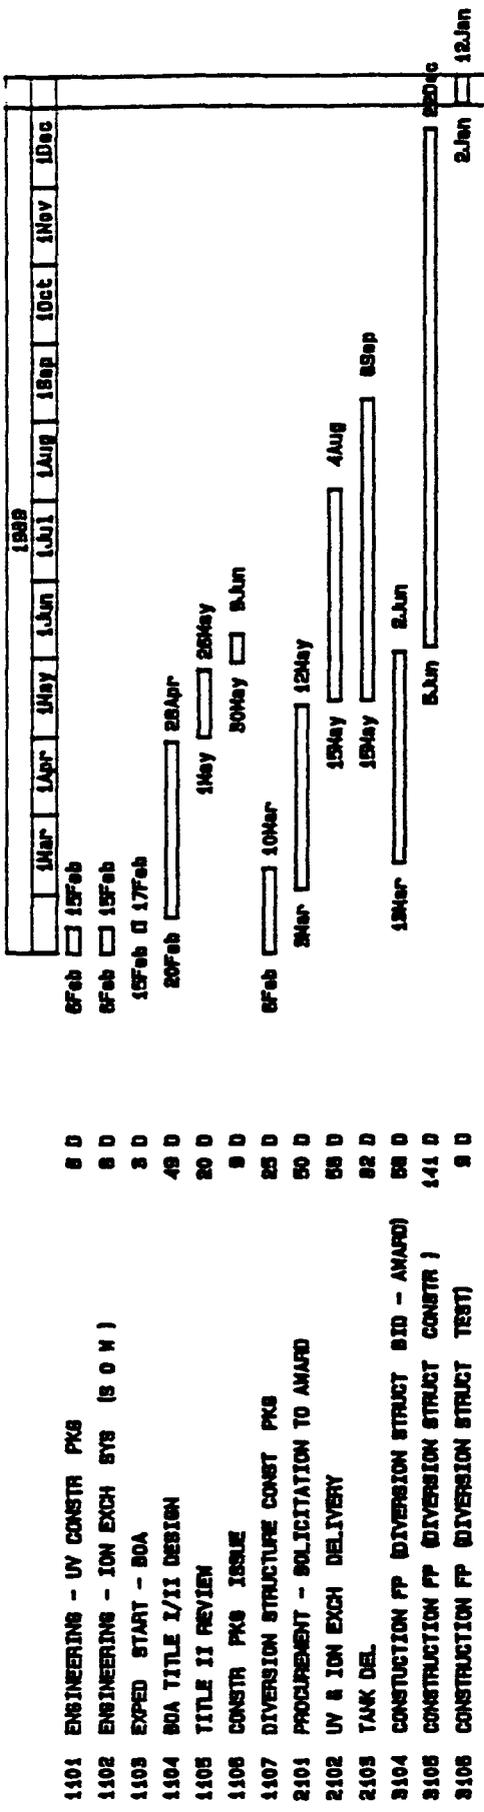

Project: 986147 986147-B DWG Date: 16Feb89 8:12
 REMEDIAL ACTION 881 HILLSIDE
 Page: 1 Drawn by: SMFKMET Graphics

Legend
 EARLY CPH
